



# Section G Fast Flux Test Facility Closure (RL-0042)



K. L. Kehler Vice President and Project Manager for D&D Project



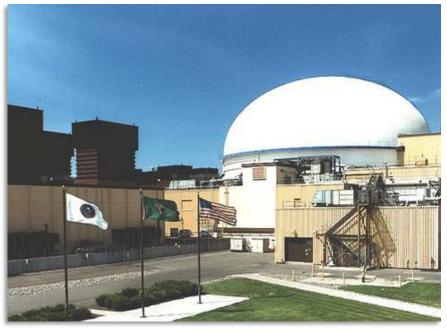

**Fast Flux Test Facility** 

# **PROJECT SUMMARY**

The Fast Flux Test Facility (FFTF) is being maintained in a low-cost surveillance and maintenance (S&M) condition. The 400 Area water system continues to operate providing service to other occupants of the 400 Area and water for fire protection.

All scope within the FFTF Closure (RL-0042) project is base funded. There is no funding from the American Recovery and Reinvestment Act.

	CM Quantity	FYTD Quantity	Comment
Days Away, Restricted or Transferred	0	0	N/A
Total Recordable Injuries	0	0	N/A
First Aid Cases	0	0	N/A
Near-Misses	0	0	N/A

# TARGET ZERO PERFORMANCE

# **KEY ACCOMPLISHMENTS**

None identified.

# **MAJOR ISSUES**

None identified.

# **KEY RISKS AND CHALLENGES**

None identified.



## PROJECT BASELINE PERFORMANCE Current Month (\$M)

RL-0042	Cost of Work			Variance	Schedule Variance (%)			Budget at Completion (BAC)
Base	0.1	0.1	0.0	0.0	0.0	0.1	66.7	25.0

Numbers are rounded to the nearest \$0.1M.

#### CM Schedule Performance: (\$0.0M/0.0%)

The current month schedule variance is within reporting thresholds.

#### CM Cost Performance: (+\$0.1M/+66.7%)

The current month cost variance is within reporting thresholds.

# Contract-to-Date (\$M)

RL-0042	Cost of Work	Work	Cost of	Variance	Schedule Variance (%)			Budget at Completion (BAC)
Base	8.7	8.7	8.3	0.0	0.0	0.4	4.7	25.1

Numbers are rounded to the nearest \$0.1M.

#### CTD Schedule Performance (\$0.0M/0.0%)

The schedule variance is within reporting thresholds.

#### CTD Cost Performance (+\$0.4M /+4.7%)

The cost variance is within reporting thresholds.

#### Contract Performance Report Formats are provided in Appendix A.



FUNDS vs. SPEND FORECAST (\$M)							
	FY						
RL-0042 FFTF Closure	Projected Funding	Spending Forecast	Variance				
Base	2.5	1.1	1.4				

#### **Funds Analysis:**

Projected Funding includes FY 2009 uncosted and FY 2010 expected new Budget Authority (BA).

#### **Critical Path Schedule**

Critical path analysis is not applicable to this project. Remaining contract scope is performance of interim surveillance and maintenance activities.

#### **Estimate at Completion (EAC)**

The BAC and EAC now include FY 2009 through FY 2018, the PRC contract period.

**Baseline Change Requests** None.

## **MILESTONE STATUS**

None currently identified.

# SELF-PERFORMED WORK

The Section H clause entitled, "Self-Performed Work," is addressed in the Monthly Report Overview.

# GOVERNMENT FURNISHED SERVICES AND ITEMS (GFS/I)

None currently identified.

