



Barrier Berm Project – Daily Report

Day 61

Document: 139551-PMD-061-S

Date Prepared: August 1, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



Pass A Loutre– July 27th, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 31 July

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	36,458	
Cutter Texas	0	
Subtotal East	36,458	
West		
Cutter California	26,102	
Cutter EW Ellefsen	0	
Cutter RS Weeks	72,250	
Hopper Stuyvesant	14,882	2
Hopper Liberty Island	8,381	2
Hopper Terrapin Island	10,853	3
Hopper Padre Island	5,402	2
Hopper BE Lindholm	8,561	3
Hopper Bayport	7,478	2
Hopper RN Weeks	2,599	1
Hopper Glen Edwards	8,480	1
Subtotal West	164,988	16
Total	201,446	16

Today – 1 August

- Borrow operations to continue at Pass a Loutre and West.
- Placement operations to continue at E4 North and W9.

Tomorrow – 2 August

- Today’s operational activities to continue through tomorrow.


Near-Term Milestones

- Forecast completion of first mile of berm approximately 3 August.
- Start of W10 berm construction forecast to begin 24 August.


Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Equipment rotation, uptime maximization and timely remaining operations.
- Additional permit conditions to refill borrow area 6A by early August.

Fleet Mix
(total vessel count)

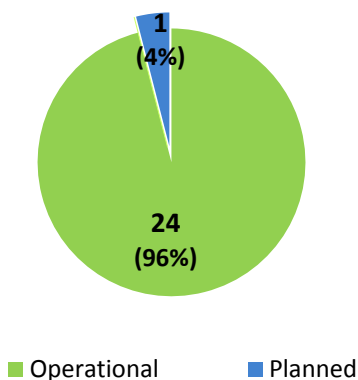

All Dredges Weekly Volume

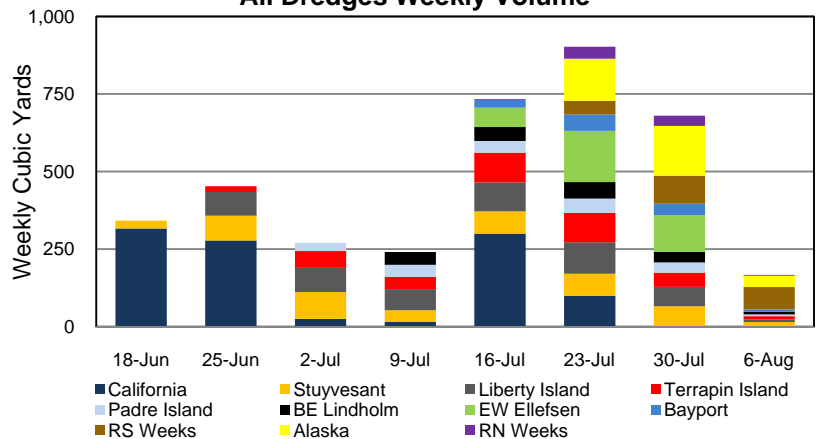

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,083,645	
Cutter EW Ellefsen	345,685	
Cutter RS Weeks	206,292	
Cutter Alaska	332,491	
Hopper Stuyvesant	453,991	70
Hopper Liberty Island	487,211	112
Hopper Terrapin Island	360,215	107
Hopper Padre Island	186,429	71
Hopper BE Lindholm	181,650	62
Hopper Bayport	122,932	34
Hopper RN Weeks	77,010	28
Hopper Glen Edwards	8,480	1
Total	3,846,031	485

Progress by Berm and Borrow Operations

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	11-Aug-10	21-Oct-10	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	1-Nov-10	8,345,969	1,366,767	6,979,202	16.38%
W8	6-Sep-10	28-Nov-10	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	27-Aug-10	1,130,870	206,292	924,578	18.24%
W10	24-Aug-10	21-Sep-10	1,327,543	0	1,327,543	0.00%
W11	13-Oct-10	1-Nov-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	18-Oct-10	13,088,593	2,272,972	10,815,621	17.37%
Totals			31,081,372	3,846,031	27,235,341	12.37%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.



Pass A Loutre Aerial Photo - July 27, 2010
