



Barrier Berm Project – Daily Report

Day 117

Document: 139551-PMD-117-S

Date Prepared: September 26, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm – September 23, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 25 September

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	17,862	
Subtotal East	17,862	
West		
Cutter California	33,228	10 Scows
Cutter EW Ellefsen	41,935	
Cutter Texas	22,951	
Hopper Glenn Edwards	18,766	2
Subtotal West	116,880	2
Total	134,742	2

Today – 26 September

- Borrow operations at Pass a Loure and West to continue.
- Berm placement operations to continue on E4 North, W9 and W10.

Tomorrow – 27 September

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- Completion of W9 berm construction forecast for tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- New tropical storm developed in Caribbean with potential impact to the Gulf of Mexico.

All Dredges Weekly Volume

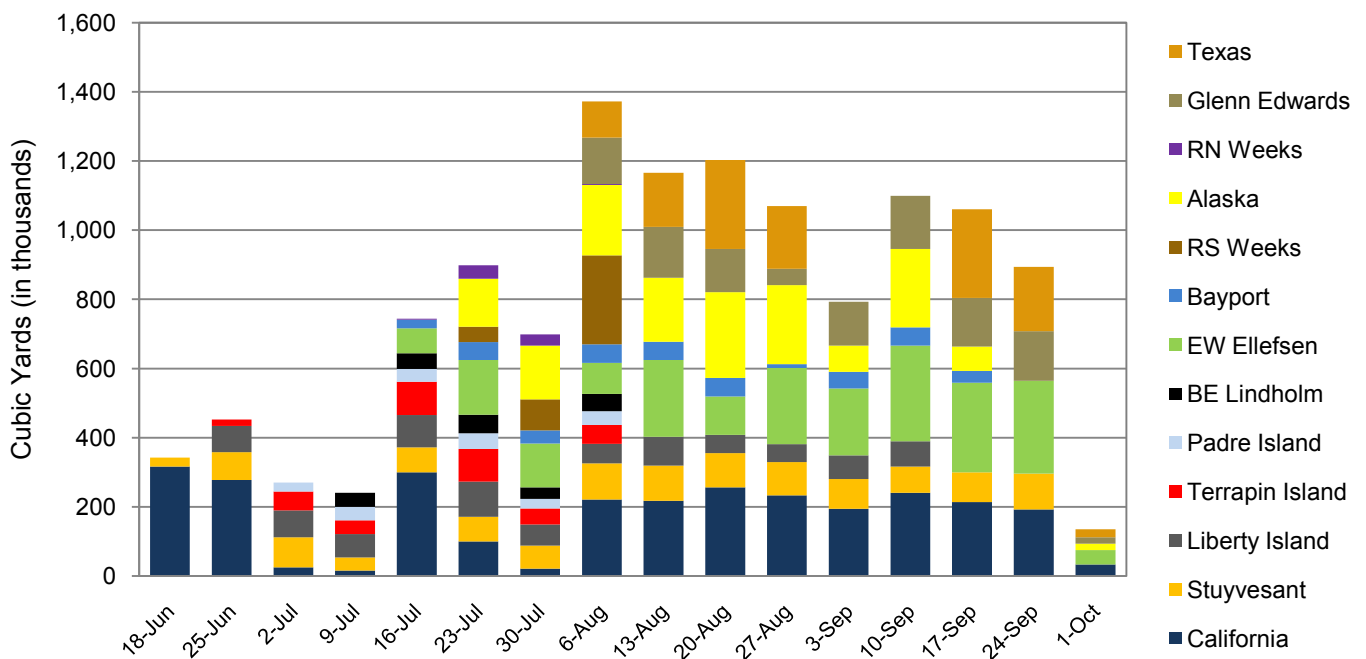

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	2,857,077	
Cutter EW Ellefsen	2,039,738	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,550,907	
Cutter Texas	1,163,883	
Hopper Stuyvesant *	1,191,480	174
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,038,129	106
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	12,437,845	894

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Start	End	Forecast (cy)**	Actual (cy)	To Go (cy)	Complete
E3	30-Dec-10	3-Apr-11	1,200,000	0	1,200,000	0.00%
E4	14-Jun-10 A	8-Feb-11	9,978,900	3,284,694	6,694,206	32.92%
W8	4-Oct-10	1-Jan-11	1,243,548	0	1,243,548	0.00%
W9	18-Jul-10 A	27-Sep-10	1,929,494	2,073,093	***	99.32%
W10	13-Sep-10 A	3-Nov-10	1,588,710	464,372	1,124,338	29.23%
W11	10-Nov-10	14-Dec-10	2,729,032	0	2,729,032	0.00%
Borrow Operations	16-Jun-10 A	7-Dec-10	9,162,418	6,615,686	2,546,732	72.20%
Totals			27,832,102	12,437,845	15,537,856	44.69%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

***Quantity variance as a result of field conditions and material variations; W9 nearing completion.

Progress by Berm (distance)

Location	Forecast (LF)**	Under Construction (LF)	To Go (LF)	Complete
E3	8,500	0	8,500	0.00%
E4	63,280	16,395	46,885	25.91%
W8	9,480	0	9,480	0.00%
W9	13,030	11,704	1,326	89.82%
W10	15,700	900	14,800	5.73%
W11	23,000	0	23,000	0.00%
Totals	132,990	28,999	103,991	21.81%

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.

** Tended project completion quantities.



W9 Berm Operations – September 23, 2010



W10 Berm Operations – September 23, 2010
