



Barrier Berm Project – Daily Report

Day 129

Document: 139551-PMD-129-S

Date Prepared: October 8, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W9 & W10 Berm – October 6, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 7 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	4,973	
Subtotal East	4,973	
West		
Cutter California	43,216	11 Scows
Cutter EW Ellefsen	0	
Cutter Texas	20,900	
Hopper Glenn Edwards	19,961	2
Subtotal West	84,077	2
Total	89,050	2

- Alaska returned to production.
- EW Ellefsen continues pipeline repositioning for W8 berm construction.

Today – 8 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North and W10.
- Preparations for W8 berm construction to continue.

Tomorrow – 9 October

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- W8 berm construction forecast to start on 17 October.
 - Repositioning pipeline began 3 October; pad construction to begin on 11 October.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

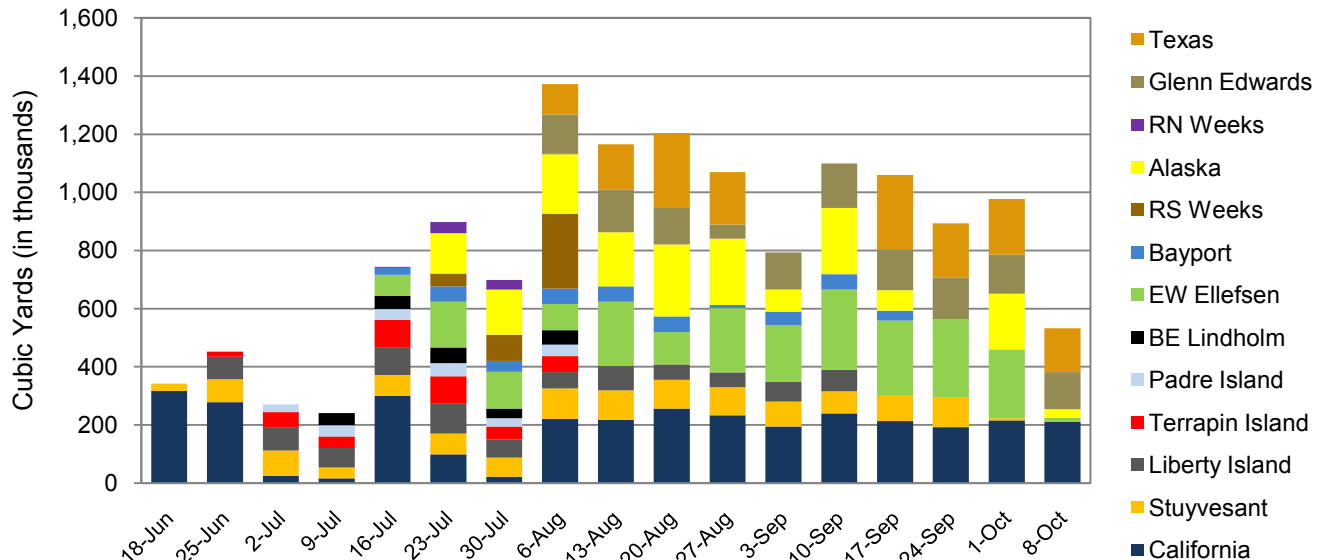

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,250,864	
Cutter EW Ellefsen	2,247,959	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,754,144	
Cutter Texas	1,482,433	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,281,941	129
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	13,812,664	918

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,487,931
W8	0
W9	2,281,314
W10	782,922
W11	0
Borrow Operations	7,260,497
Totals	13,812,664

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	18,471
W8	0
W9	12,449
W10	4,200
W11	0
Totals	35,120

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W10 Berm Operations – October 6, 2010



E4 North Berm Operations – October 6, 2010
