



# Barrier Berm Project – Daily Report

## Day 130

---

Document: 139551-PMD-130-S

Date Prepared: October 9, 2010

Prepared by:

Shaw Environmental & Infrastructure Group

---



*W9 & W10 Berm – October 7, 2010*

# Barrier Berm Project 139551 – Daily Information

## Yesterday – 8 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
<b>East</b>		
Cutter Alaska	22,326	
<b>Subtotal East</b>	<b>22,326</b>	
<b>West</b>		
Cutter California	44,667	15 Scows
Cutter EW Ellefsen	0	
Cutter Texas	35,100	
Hopper Glenn Edwards	30,450	3
<b>Subtotal West</b>	<b>110,217</b>	<b>3</b>
<b>Total</b>	<b>132,543</b>	<b>3</b>

- EW Ellefsen continues pipeline repositioning for W8 berm construction.

## Today – 9 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North and W10.
- Preparations for W8 berm construction to continue.

## Tomorrow – 10 October

- Today's operational activities to continue through tomorrow.


## Near-Term Milestones

- W8 berm construction forecast to start on 17 October.
  - Repositioning pipeline began 3 October; pad construction to begin on 11 October.

## Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

**All Dredges Weekly Volume**

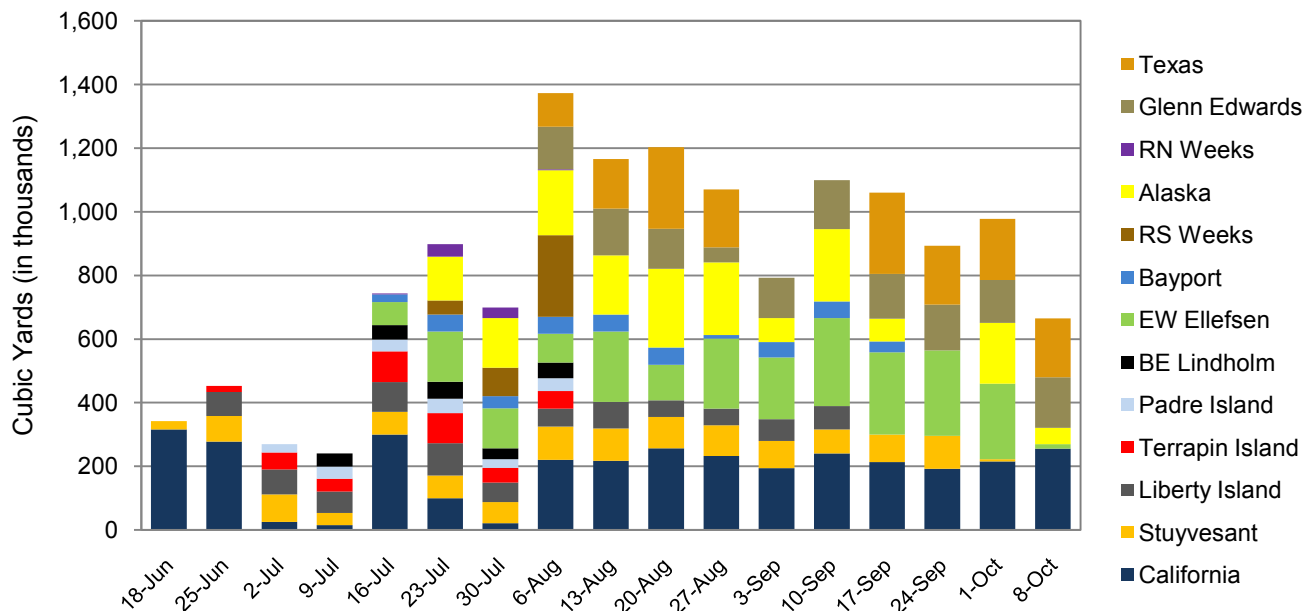

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,295,531	
Cutter EW Ellefsen	2,247,959	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,776,470	
Cutter Texas	1,517,533	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,312,391	132
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>13,945,207</b>	<b>921</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,510,257
W8	0
W9	2,281,314
W10	818,022
W11	0
Borrow Operations	7,335,614
<b>Totals</b>	<b>13,945,207</b>

### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	19,255
W8	0
W9	12,449
W10	4,600
W11	0
<b>Totals</b>	<b>36,304</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 & W10 – October 7, 2010



E4 North Berm Operations – October 7, 2010
