



Barrier Berm Project – Daily Report

Day 141

Document: 139551-PMD-141-S

Date Prepared: October 20, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W8, W9, & W10 Berms – October 19, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 19 October

| Vessel | Cubic Yards (CY) Handled | Hopper Loads |
|----------------------|--------------------------|--------------|
| East | | |
| Cutter Alaska | 57,179 | |
| Subtotal East | 57,179 | |
| West | | |
| Cutter California | 33,506 | 9 Scows |
| Cutter EW Ellefsen | 31,887 | |
| Cutter Texas | 17,930 | |
| Hopper Glenn Edwards | 0 | 0 |
| Subtotal West | 83,323 | 0 |
| Total | 140,502 | 0 |

- Glenn Edwards still down for repairs, and is expected to return October 25th.
- Barge loading operations switched from the GL55 to the Weeks spider barge.

Today – 20 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 21 October

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

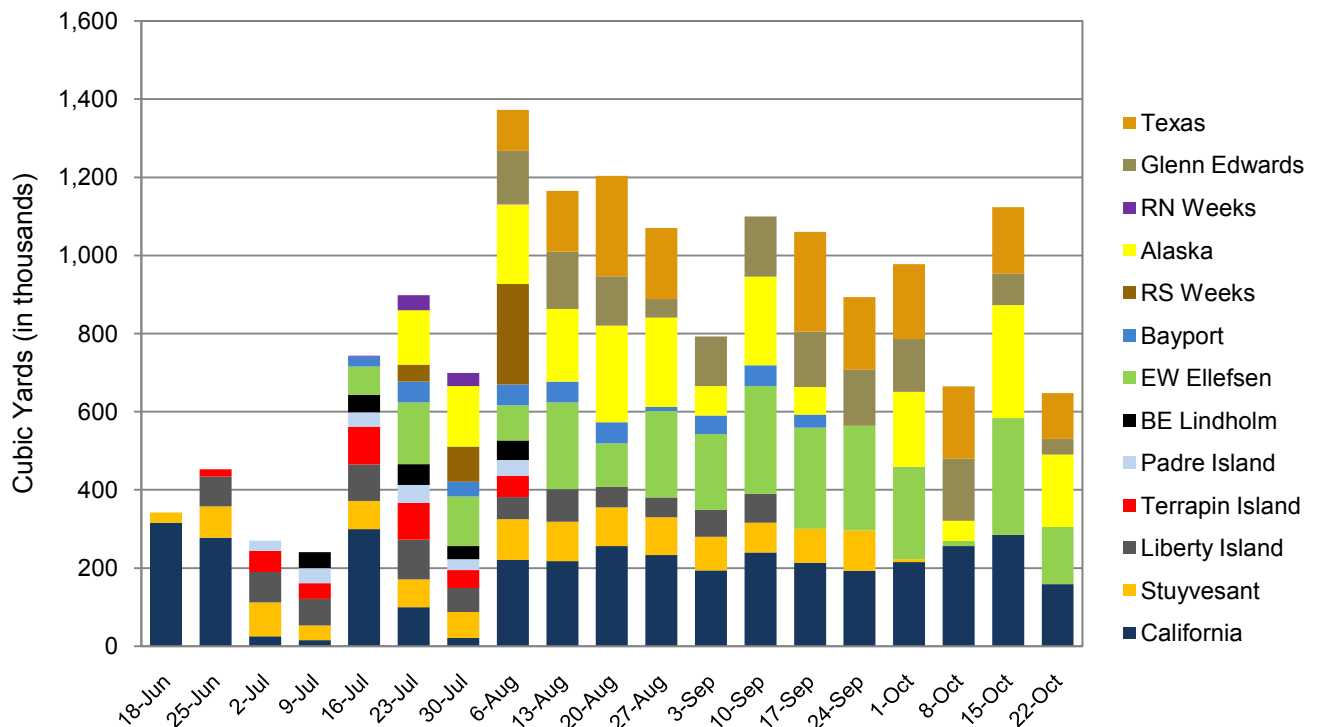

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

| Vessel | Handled - ITD (cy) | Hopper Loads - ITD |
|--------------------------|--------------------|--------------------|
| Cutter California | 3,739,207 | |
| Cutter EW Ellefsen | 2,693,652 | |
| Cutter RS Weeks * | 391,350 | |
| Cutter Alaska | 2,250,246 | |
| Cutter Texas | 1,805,130 | |
| Hopper Stuyvesant * | 1,198,692 | 175 |
| Hopper Liberty Island * | 864,508 | 192 |
| Hopper Bayport * | 421,280 | 114 |
| Hopper Glenn Edwards | 1,432,852 | 144 |
| Hopper Terrapin Island * | 403,823 | 119 |
| Hopper Padre Island * | 216,133 | 84 |
| Hopper BE Lindholm * | 222,527 | 76 |
| Hopper RN Weeks * | 77,010 | 29 |
| Total | 15,716,410 | 933 |

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

| Location | Actuals (CY) |
|-------------------|-------------------|
| E3 | 0 |
| E4 | 3,984,033 |
| W8 | 445,693 |
| W9 | 2,281,314 |
| W10 | 1,105,619 |
| W11 | 0 |
| Borrow Operations | 7,899,751 |
| Totals | 15,716,410 |

Progress by Berm (distance)

| Location | Under Construction (LF) |
|---------------|-------------------------|
| E3 | 0 |
| E4 | 22,667 |
| W8 | 1,050 |
| W9 | 12,449 |
| W10 | 7,790 |
| W11 | 0 |
| Totals | 43,956 |

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 19, 2010



W8 Berm Operations – October 18, 2010
