



# Barrier Berm Project – Daily Report

## Day 144

---

Document: 139551-PMD-144-S

Date Prepared: October 23, 2010

Prepared by:

Shaw Environmental & Infrastructure Group

---



*E4 Berm – October 19, 2010*

# Barrier Berm Project 139551 – Daily Information

## Yesterday – 22 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
<b>East</b>		
Cutter Alaska	20,967	
<b>Subtotal East</b>	<b>20,967</b>	
<b>West</b>		
Cutter California	33,205	12 Scows
Cutter EW Ellefsen	28,624	
Cutter Texas	0	
Hopper Glenn Edwards	0	0
<b>Subtotal West</b>	<b>61,829</b>	<b>0</b>
<b>Total</b>	<b>82,796</b>	<b>0</b>

- Glenn Edwards still down for repairs, and is expected to return to operations October 27<sup>th</sup>.
- Texas down for repairs; forecast to return to production tomorrow.

## Today – 23 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


## Tomorrow – 24 October

- Today's operational activities to continue through tomorrow.

## Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

**All Dredges Weekly Volume**

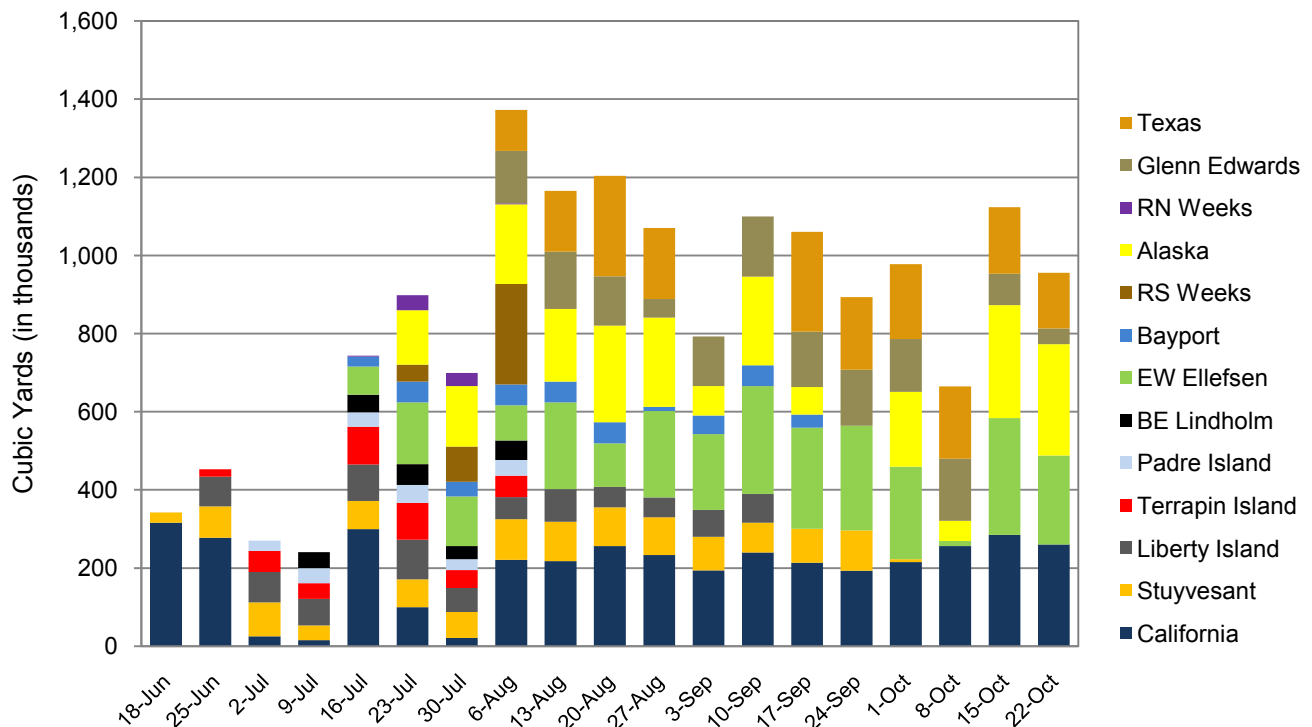

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,840,267	
Cutter EW Ellefsen	2,775,302	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,350,229	
Cutter Texas	1,830,530	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,432,852	144
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>16,024,503</b>	<b>933</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,084,016
W8	527,343
W9	2,281,314
W10	1,131,019
W11	0
Borrow Operations	8,000,811
<b>Totals</b>	<b>16,024,503</b>

### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	23,997
W8	2,050
W9	12,449
W10	7,630
W11	0
<b>Totals</b>	<b>46,126</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 19, 2010



W8 & W9 Berm Operations – October 19, 2010
