



# Barrier Berm Project – Daily Report

## Day 146

---

**Document:** 139551-PMD-146-S

**Date Prepared:** October 25, 2010

**Prepared by:**

Shaw Environmental & Infrastructure Group

---



*W8 Berm – October 24, 2010*

# Barrier Berm Project 139551 – Daily Information

## Yesterday – 24 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
<b>East</b>		
Cutter Alaska	25,811	
<b>Subtotal East</b>	<b>25,811</b>	
<b>West</b>		
Cutter California	16,038	6 Scows
Cutter EW Ellefsen	8,043	
Cutter Texas	16,500	
Hopper Glenn Edwards	0	0
<b>Subtotal West</b>	<b>40,581</b>	<b>0</b>
<b>Total</b>	<b>66,392</b>	<b>0</b>

- Glenn Edwards down for repairs, and is expected to return to operations October 27<sup>th</sup>.
- California moved operations to South Pass.
- High seas also hindered production yesterday.

## Today – 25 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


## Tomorrow – 26 October

- Today's operational activities to continue through tomorrow.

## Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

**All Dredges Weekly Volume**

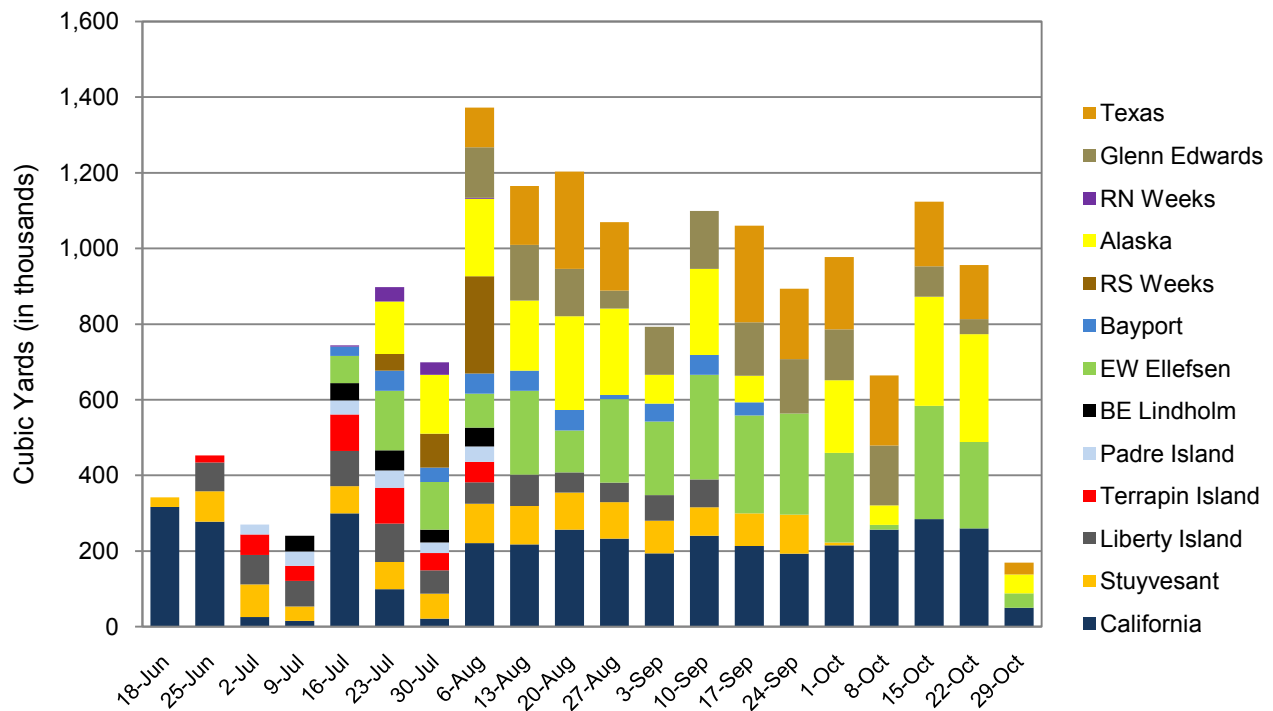

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,890,522	
Cutter EW Ellefsen	2,812,914	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,400,431	
Cutter Texas	1,862,030	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,432,852	144
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>16,194,072</b>	<b>933</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,134,218
W8	564,955
W9	2,281,314
W10	1,162,519
W11	0
Borrow Operations	8,051,066
<b>Totals</b>	<b>16,194,072</b>


### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	24,407
W8	2,550
W9	12,449
W10	8,230
W11	0
<b>Totals</b>	<b>47,636</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 24, 2010

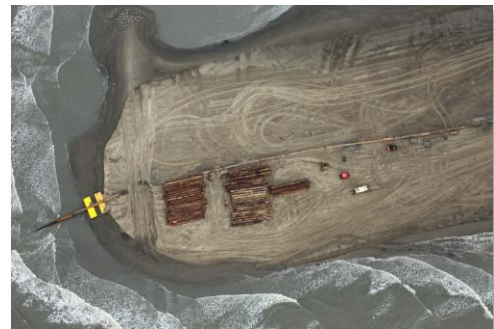

W8 Berm Operations – October 24, 2010
