



Barrier Berm Project – Daily Report

Day 149

Document: 139551-PMD-149-S

Date Prepared: October 28, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W10 Berm – October 26, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 27 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	33,788	
Subtotal East	33,788	
West		
Cutter California	0	0 Scows
Cutter EW Ellefsen	0	
Cutter Texas	7,000	
Hopper Glenn Edwards	19,601	2
Subtotal West	26,601	2
Total	60,389	2

- Lowered dredge production due to poor weather and rough seas.

Today – 28 October

- Borrow operations at South Pass to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 29 October

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

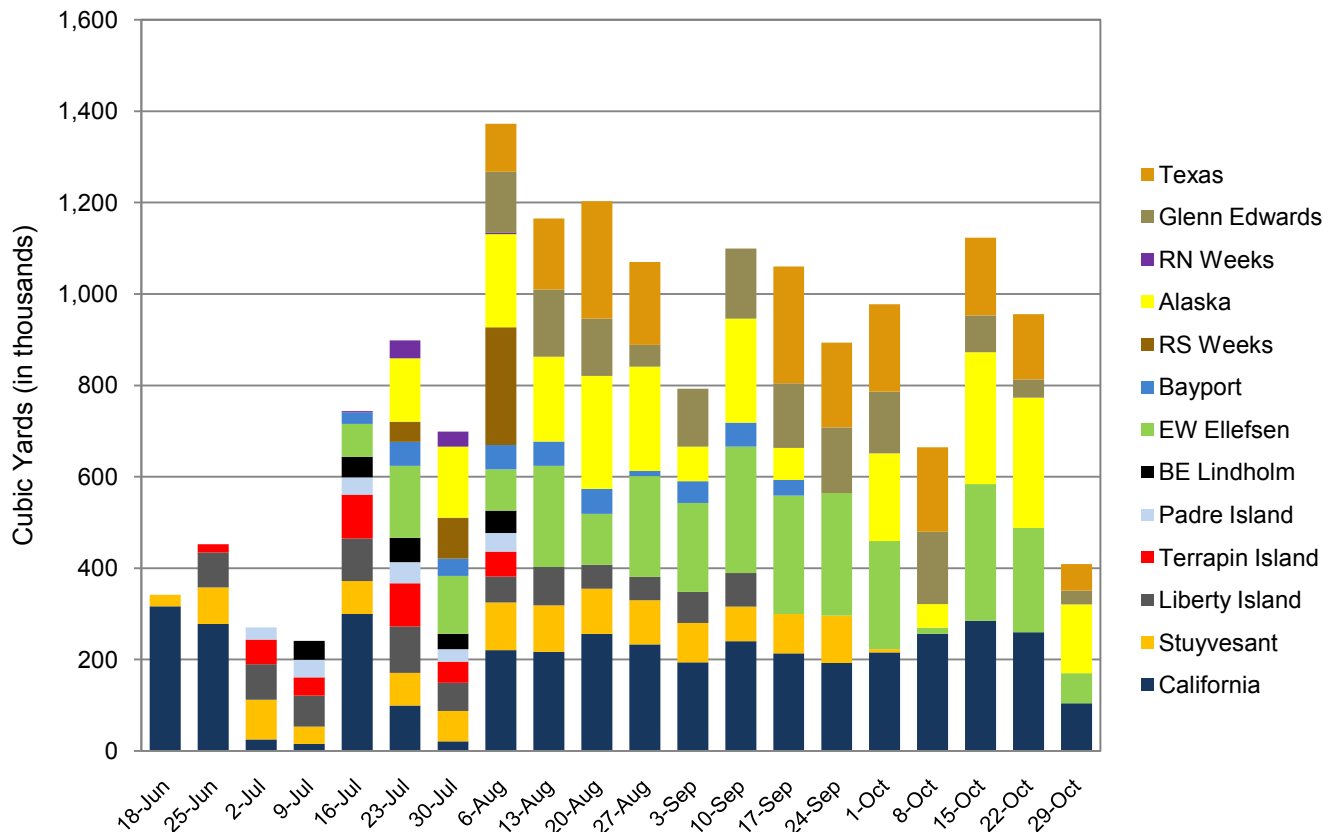

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,944,877	
Cutter EW Ellefsen	2,840,715	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,501,242	
Cutter Texas	1,888,630	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,462,398	147
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	16,433,185	936

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,235,029
W8	592,756
W9	2,281,314
W10	1,189,119
W11	0
Borrow Operations	8,134,967
Totals	16,433,185

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	24,996
W8	2,790
W9	12,449
W10	8,530
W11	0
Totals	48,765

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 26, 2010



W10 Berm Operations – October 24, 2010
