



# Barrier Berm Project – Daily Report

## Day 155

---

Document: 139551-PMD-155-S

Date Prepared: November 3, 2010

Prepared by:

Shaw Environmental & Infrastructure Group

---



*Eastern end of W8 Berm – October 31, 2010*

# Barrier Berm Project 139551 – Daily Information

## Yesterday – 2 November

Vessel	Cubic Yards (CY) Handled	Hopper Loads
<b>East</b>		
Cutter Alaska	31,047	
<b>Subtotal East</b>	<b>31,047</b>	
<b>West</b>		
Cutter California	36,487	9 Scows
Cutter EW Ellefsen	12,948	
Cutter Texas	14,600	
Hopper Glenn Edwards	20,434	2
<b>Subtotal West</b>	<b>84,469</b>	<b>2</b>
<b>Total</b>	<b>115,516</b>	<b>2</b>


## Today – 3 November

- Borrow operations at South Pass to continue throughout the day and complete operations at midnight.
- Hopper Glenn Edwards to continue operating throughout the day and demobilize at midnight.
- Berm placement operations to continue on E4 North and W10.
- EW Ellefsen down for repairs. W8 Berm placement operations to resume tomorrow.

## Tomorrow – 4 November

- Berm placement operations to continue.

**All Dredges Weekly Volume**

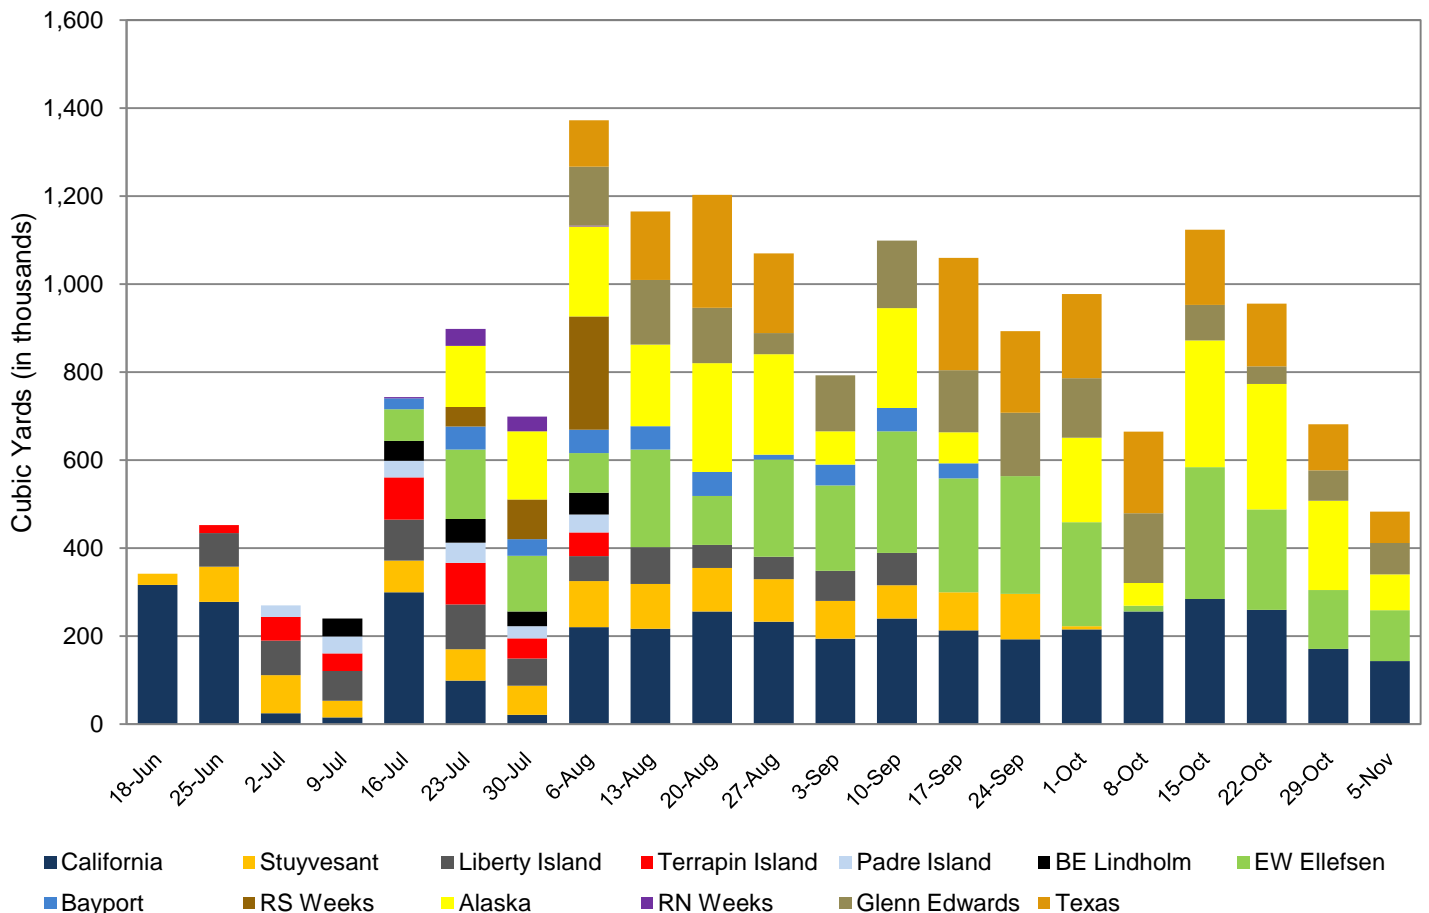

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	4,154,779	
Cutter EW Ellefsen	3,024,720	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,635,106	
Cutter Texas	2,006,430	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,572,586	160
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>17,188,944</b>	<b>949</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,368,893
W8	776,761
W9	2,281,314
W10	1,306,919
W11	0
Borrow Operations	8,455,057
<b>Totals</b>	<b>17,188,944</b>

### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	26,096
W8	4,939
W9	12,449
W10	10,130
W11	0
<b>Totals</b>	<b>53,614</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 31, 2010



W8 Berm – October 31, 2010
