



# Barrier Berm Project – Daily Report

## Day 161

---

**Document:** 139551-PMD-161-S

**Date Prepared:** November 9, 2010

**Prepared by:**

Shaw Environmental & Infrastructure Group

---



*E4 North Berm – November 7, 2010*

# Barrier Berm Project 139551 – Daily Information

Yesterday – 8 November

Vessel	Cubic Yards (CY) Handled
<b>East</b>	
Cutter Alaska	50,681
<b>Subtotal East</b>	<b>50,681</b>
<b>West</b>	
Cutter EW Ellefsen	34,641
Cutter Texas	27,000
<b>Subtotal West</b>	<b>61,641</b>
<b>Total</b>	<b>112,322</b>


Today – 9 November

- Berm placement operations to continue on E4, W8 and W10.

Tomorrow – 10 November

- Today's operational activities to continue tomorrow.

**All Dredges Weekly Volume**

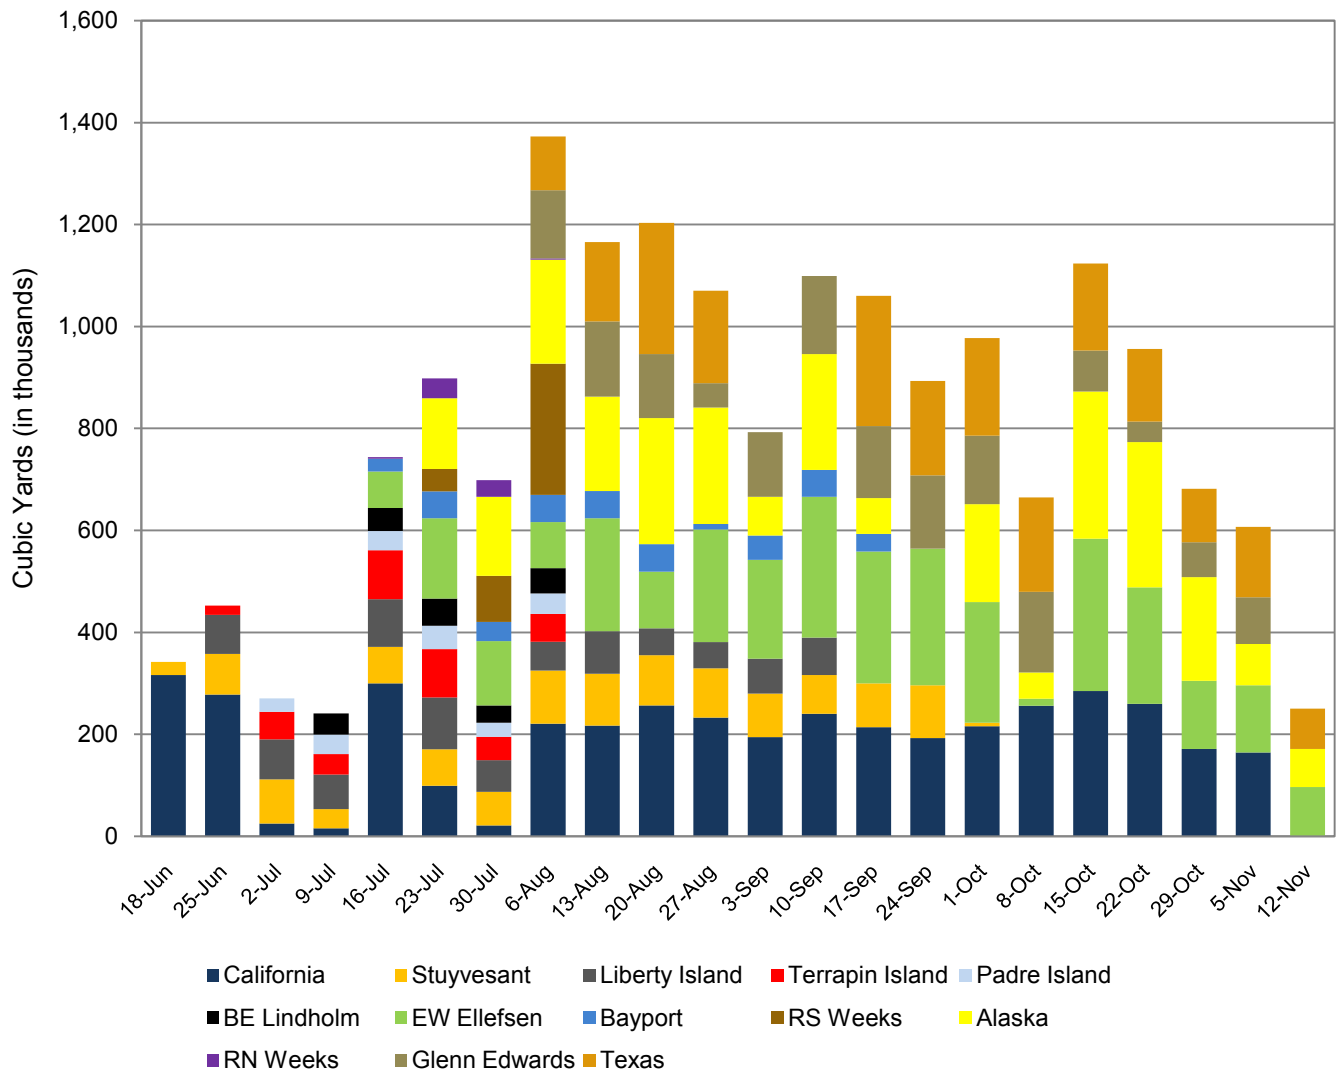

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California*	4,175,650	
Cutter EW Ellefsen	3,137,237	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,709,599	
Cutter Texas	2,152,230	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards*	1,593,128	162
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>17,563,167</b>	<b>951</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,443,386
W8	889,278
W9	2,281,314
W10	1,452,719
W11	0
Borrow Operations	8,496,470
<b>Totals</b>	<b>17,563,167</b>

### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	26,446
W8	6,339
W9	12,449
W10	11,130
W11	0
<b>Totals</b>	<b>56,364</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W10 Berm Operations – November 7, 2010



W8 Berm – November 7, 2010
