



# Barrier Berm Project – Daily Report

## Day 166

---

Document: 139551-PMD-166-S

Date Prepared: November 14, 2010

Prepared by:

Shaw Environmental & Infrastructure Group

---



*W10 Berm – November 10, 2010*

# Barrier Berm Project 139551 – Daily Information

Yesterday – 13 November

Vessel	Cubic Yards (CY) Handled
<b>East</b>	
Cutter Alaska	33,606
<b>Subtotal East</b>	<b>33,606</b>
<b>West</b>	
Cutter EW Ellefsen	41,789
Cutter Texas	32,100
<b>Subtotal West</b>	<b>73,889</b>
<b>Total</b>	<b>107,495</b>


Today – 14 November

- Berm placement operations to continue on E4, W8 and W10.

Tomorrow – 15 November

- Today's operational activities to continue tomorrow.

**All Dredges Weekly Volume**

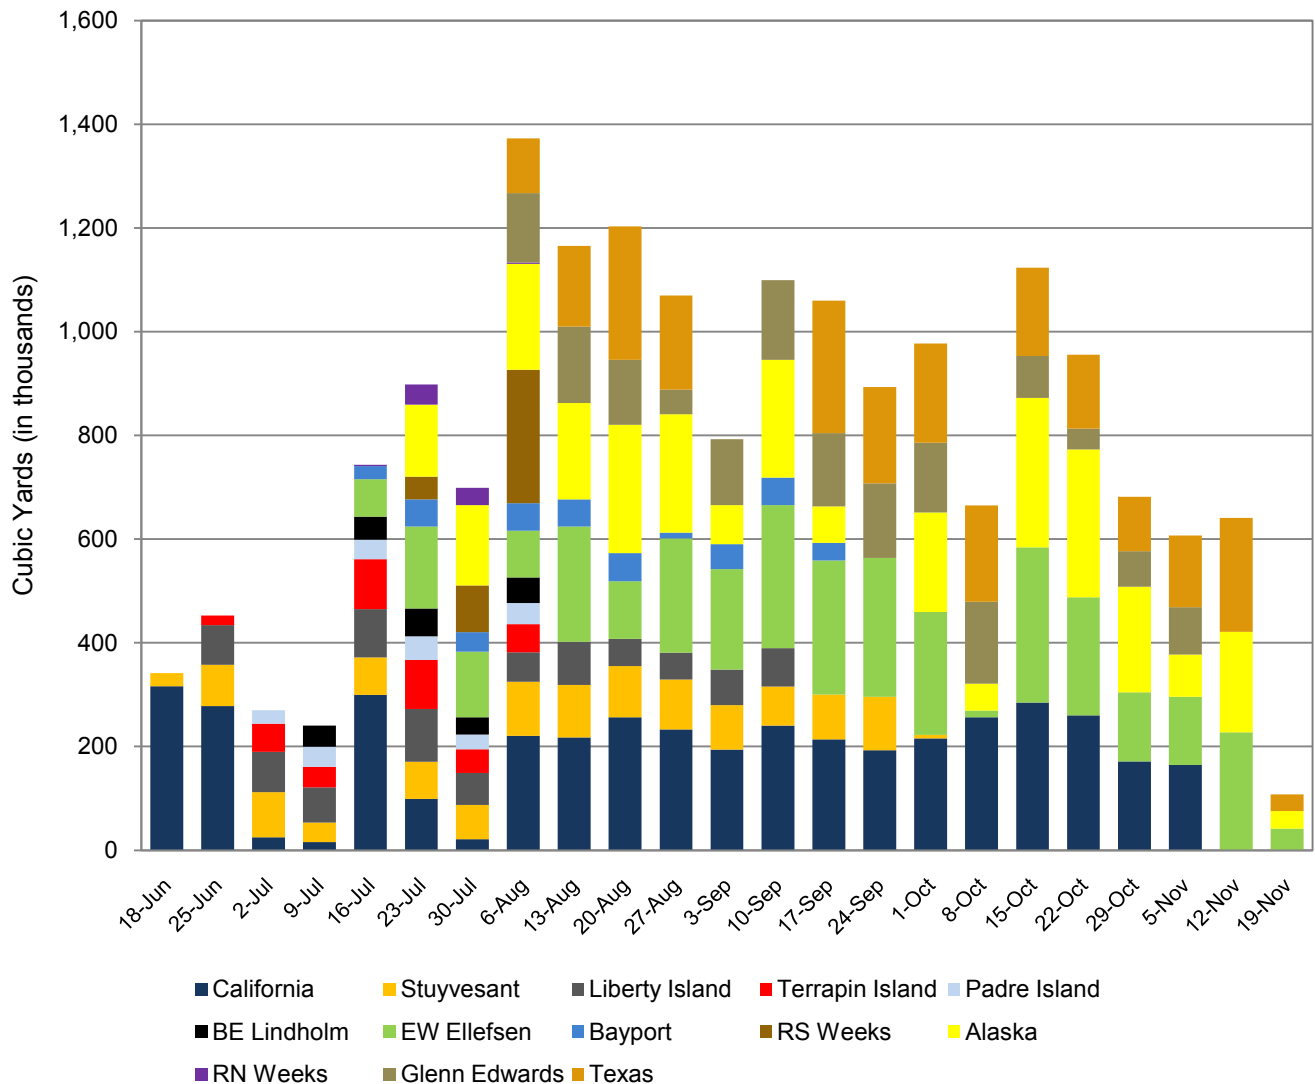

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California*	4,175,650	
Cutter EW Ellefsen	3,309,565	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,862,937	
Cutter Texas	2,324,982	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards*	1,593,128	162
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>18,061,585</b>	<b>951</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,596,724
W8	1,061,606
W9	2,281,314
W10	1,625,471
W11	0
Borrow Operations	8,496,470
<b>Totals</b>	<b>18,061,585</b>

### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	28,546
W8	7,339
W9	12,449
W10	12,130
W11	0
<b>Totals</b>	<b>60,464</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W10 Berm – November 10, 2010



E4 North Berm – November 10, 2010
