



Barrier Berm Project – Daily Report

Day 68

Document: 139551-PMD-068-S

Date Prepared: August 8, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W9 Berm (Pelican Island) – August 5, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 7 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	56,161	
Cutter Texas	11,400	
Subtotal East	67,561	
West		
Cutter California	51,357	14 Scows
Cutter EW Ellefsen	51,916	
Hopper Stuyvesant	15,720	2
Hopper Liberty Island	9,854	2
Hopper Bayport	7,666	2
Hopper Glen Edwards	20,192	2
Subtotal West	156,705	8
Total	224,266	8

Today – 8 August

- Borrow operations to continue at Pass a Loutre and West, placement operations to continue at E4 North and W9.

Tomorrow – 9 August


- Today's operational activities expected to continue through tomorrow.

Near-Term Milestones

- Start E4 south berm construction forecast to begin 11 August.
- Start W10 berm construction forecast to begin 24 August.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Variations from current fleet configuration.

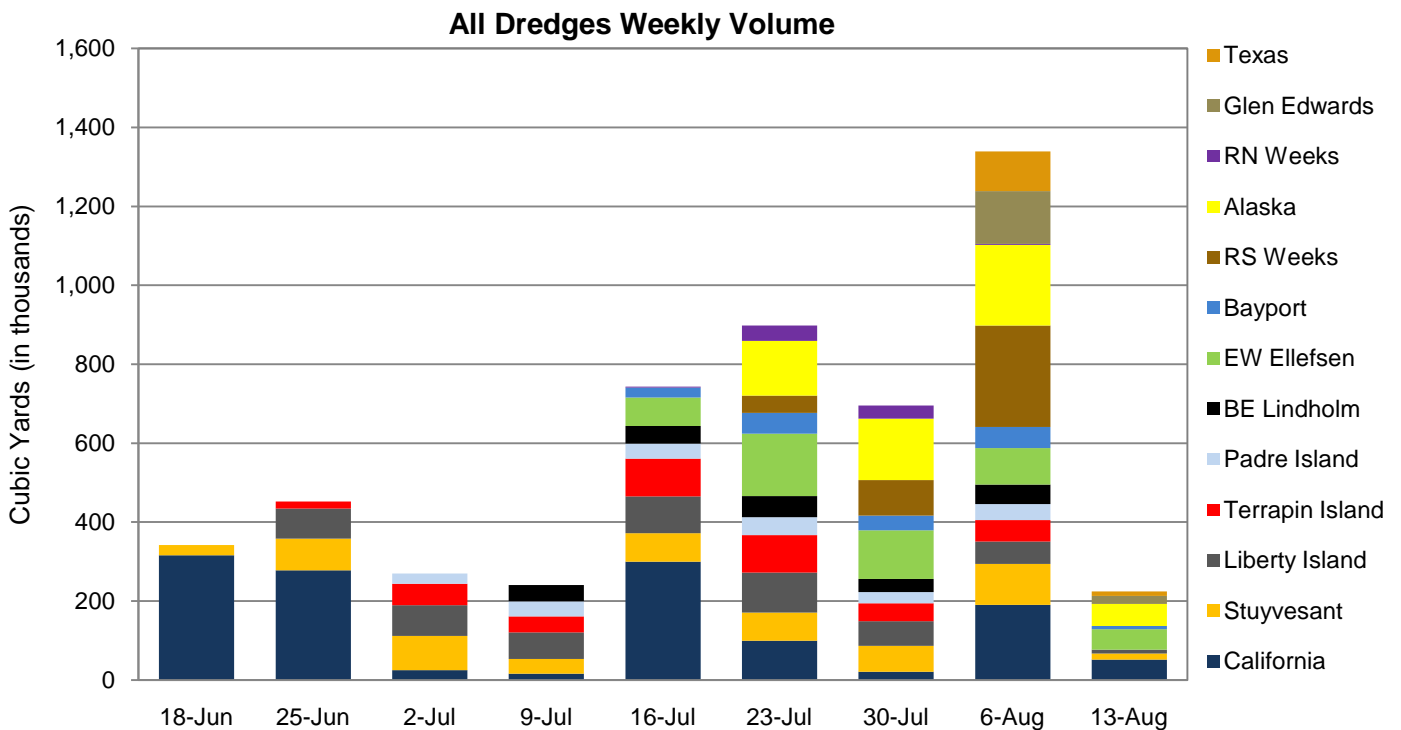

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,296,643	
Cutter EW Ellefsen	497,590	
Cutter RS Weeks	391,350	
Cutter Alaska	554,309	
Cutter Texas	112,158	
Hopper Stuyvesant	559,072	84
Hopper Liberty Island	545,044	124
Hopper Terrapin Island	403,843	119
Hopper Padre Island	216,129	84
Hopper BE Lindholm	222,527	76
Hopper Bayport	176,288	48
Hopper RN Weeks	77,010	28
Hopper Glen Edwards	153,927	16
Total	5,205,890	579

Progress by Berm and Borrow Operations

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	11-Aug-10	21-Oct-10	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	1-Nov-10	8,345,969	1,700,743	6,645,226	20.38%
W8	6-Sep-10	28-Nov-10	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	27-Aug-10	1,130,870	531,934	598,936	47.04%
W10	24-Aug-10	21-Sep-10	1,327,543	0	1,327,543	0.00%
W11	13-Oct-10	1-Nov-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	18-Oct-10	13,088,593	2,973,213	10,115,380	22.72%
Totals			31,081,372	5,205,890	25,875,482	16.75%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.




W9 Berm Construction – August 5, 2010



W9 Berm – August 5, 2010



E4 Berm – August 5, 2010

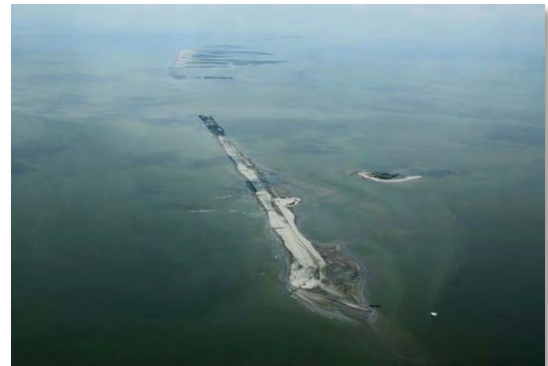

E4 Berm Construction – August 5, 2010
