



Barrier Berm Project – Daily Report

Day 69

Document: 139551-PMD-069-S

Date Prepared: August 9, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm – August 8, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 8 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	37,669	
Cutter Texas	44,700	
Subtotal East	82,369	
West		
Cutter California	40,661	11 Scows
Cutter EW Ellefsen	48,105	
Hopper Stuyvesant	15,128	2
Hopper Liberty Island	14,605	3
Hopper Bayport	11,446	3
Hopper Glen Edwards	30,439	3
Subtotal West	160,384	11
Total	242,753	11

Today – 9 August

- Borrow operations to continue at Pass a Loutre and West, placement operations to continue at E4 North and W9.

Tomorrow – 10 August


- Today's operational activities expected to continue through tomorrow.

Near-Term Milestones

- Complete refilling borrow area 6A on 11 August.
- Start E4 south berm construction forecast to begin 11 August.
- Start W10 berm construction forecast to begin 24 August.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Variations from current fleet configuration.
- Additional berm alignment authorization in advance of construction operations.

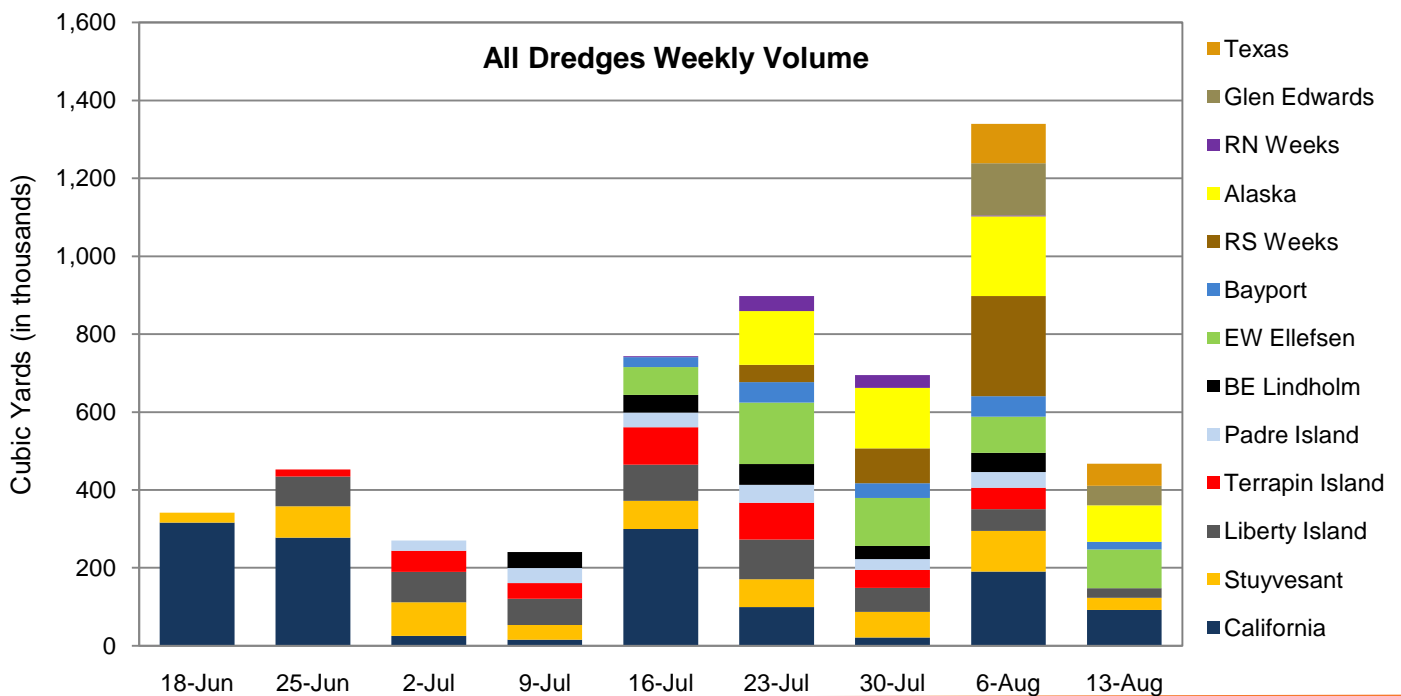

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,337,304	
Cutter EW Ellefsen	545,695	
Cutter RS Weeks *	391,350	
Cutter Alaska	591,978	
Cutter Texas	156,858	
Hopper Stuyvesant	574,200	86
Hopper Liberty Island	559,649	127
Hopper Bayport	187,734	51
Hopper Glen Edwards	184,366	19
Hopper Terrapin Island *	403,843	119
Hopper Padre Island *	216,129	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	28
Total	5,448,643	590

* Demobilized on or before August 6th.

Progress by Berm and Borrow Operations

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	11-Aug-10	21-Oct-10	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	1-Nov-10	8,345,969	1,783,112	6,562,857	21.36%
W8	6-Sep-10	28-Nov-10	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	27-Aug-10	1,130,870	580,039	550,831	51.29%
W10	24-Aug-10	21-Sep-10	1,327,543	0	1,327,543	0.00%
W11	13-Oct-10	1-Nov-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	18-Oct-10	13,088,593	3,085,492	10,003,101	23.57%
Totals			31,081,372	5,448,643	25,632,729	17.53%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.




W9 Berm Construction – August 5, 2010



W9 Berm – August 5, 2010



E4 Berm – August 5, 2010

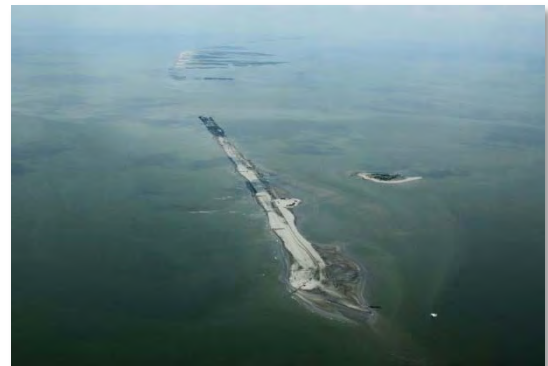

E4 Berm Construction – August 5, 2010
