



Barrier Berm Project – Daily Report

Day 53

Document: 139551-PMD-053-S

Date Prepared: July 24, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W9 Operations – July 22nd, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 23 July

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter California	0	
Cutter Alaska	33,140	
Hopper Liberty Island	11,417	3
Hopper Terrapin Island	9,865	3
Hopper Padre Island	10,153	4
Subtotal East	64,575	10
West		
Cutter EW Ellefsen	25,920	
Cutter RS Weeks	0	
Hopper Stuyvesant	15,356	1
Hopper BE Lindholm	11,110	4
Hopper Bayport	13,618	3
Hopper RN Weeks	5,163	2
Subtotal West	71,167	10
Total	135,742	20

- California continues mobilization to PAL as weather permits.
- Safe evacuation of Venice and Expo Clipper field locations in preparation for TD Bonnie.

Today – 24 July

- Pass a Loutre and hopper operations to continue to support west borrow operations as weather permits.
- Cutter dredges idled seeking safe harbor for due to storm activity.

Tomorrow – 25 July

- Hopper operations to continue until weather interruptions.
- Minimal cutter work occurring due to storm activity.


Near-Term Milestones

- Start of E4 South berm construction forecast to begin 27 July.
- Forecast completion of first mile of berm approximately 29 July.
- Start of W10 berm construction forecast to begin 10 August.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Equipment rotation, uptime maximization and timely remaining operations.
- Additional permit conditions to refill borrow area 6A by early August.
- Tropical Depression Bonnie site shutdown.

Fleet Mix
(total vessel count)

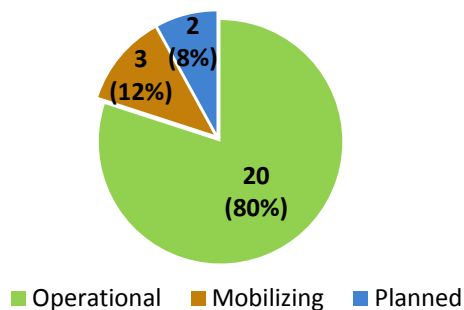

All Dredges Weekly Volume

