

Barrier Berm Project – Daily Report

Day 103

Document: 139551-PMD-103-S

Date Prepared: September 12, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm - September 9, 2010



Barrier Berm Project 139551 – Daily Information

Yesterday - 11 September

Vessel	Cubic Yards (CY) Handled	Hopper Loads				
East						
Cutter Alaska	10,653					
Subtotal East	10,653					
West						
Cutter California	13,173	3 Scows				
Cutter EW Ellefsen	56,386					
Cutter Texas	0					
Hopper Stuyvesant	7,011	1				
Hopper Bayport	7,559	2				
Hopper Glenn Edwards	20,525	2				
Subtotal West	104,654	5				
Total	115,307	5				

- Alaska down most of the day repairing a leak on the shore pipe; returned to production today.
- California performing repairs to main engine; expected to be fully operational tomorrow.

Today – 12 September

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North and W9.
- W10 berm construction to begin.

Tomorrow – 13 September

· Today's operational activities to continue through tomorrow.


Near-Term Milestones

Completion of W9 berm construction forecast for 26 September.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Project execution revision based on St. Bernard Shoals availability.
- Increased weather system activity in the Atlantic Ocean.

All Dredges Weekly Volume

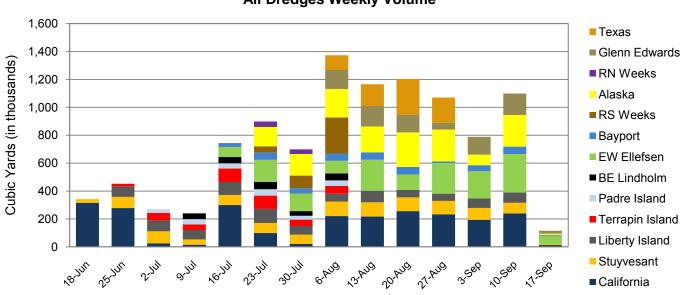



1

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD	
Cutter California	2,430,188		
Cutter EW Ellefsen	1,527,597		
Cutter RS Weeks *	391,350		
Cutter Alaska	1,473,284		
Cutter Texas	699,511		
Hopper Stuyvesant	1,008,144	150	
Hopper Liberty Island *	864,508	192	
Hopper Bayport	390,889	107	
Hopper Glenn Edwards	755,166	77	
Hopper Terrapin Island *	403,823	119	
Hopper Padre Island *	216,133	84	
Hopper BE Lindholm *	222,527	76	
Hopper RN Weeks *	77,010	29	
Total	10,460,130	834	

Progress by Berm and Borrow Operations (cubic yards)

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	29-Dec-10	2-Apr-11	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	7-Feb-11	8,345,969	3,207,071	5,138,898	38.43%
W8	4-Oct-10	1-Jan-11	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	26-Sep-10	1,929,494**	1,560,952	368,542	80.90%
W10	12-Sep-10	2-Nov-10	1,327,543	0	1,327,543	0.00%
W11	9-Nov-10	13-Dec-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	7-Dec-10	10,917,069**	5,692,107	5,224,962	52.14%
Totals			29,708,472	10,460,130	19,248,342	35.21%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

Progress by Berm (linear feet)

Location	Forecast (LF)	Under Construction (LF)*	To Go (LF)	Complete
E3	35,482	0	35,482	0.00%
E4	80,520	15,699	64,821	19.50%
W8	30,096	0	30,096	0.00%
W9	13,030**	7,830	5,200	60.09%
W10	14,256	0	14,256	0.00%
W11	11,616	0	11,616	0.00%
Totals	185,000	23,529	161,471	12.72%

Note: Data subject to one day lag. Under normal field conditions, berm is advancing approximately 500 LF per reach per day. *Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.

^{**} Revised quantities based on project change control program.



W9 Berm Operations - September 9, 2010



E4 North Berm - September 9, 2010

