



Barrier Berm Project – Daily Report

Day 108

Document: 139551-PMD-108-S

Date Prepared: September 17, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W9 Berm – September 13, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 16 September

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	0	
Subtotal East	0	
West		
Cutter California	41,408	11 Scows
Cutter EW Ellefsen	41,139	
Cutter Texas	38,200	
Hopper Stuyvesant	14,216	2
Hopper Glenn Edwards	19,678	2
Subtotal West	154,641	4
Total	154,641	4

- Alaska down for repairs on the cutter; expected to return to production on 20 September.

Today – 17 September

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on W9 and W10.

Tomorrow – 18 September


- Today's operational activities to continue through tomorrow.

Near-Term Milestones

- Completion of W9 berm construction forecast for 26 September.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Project execution revision based on St. Bernard Shoals availability.
- Increased weather system activity in the Atlantic Ocean.

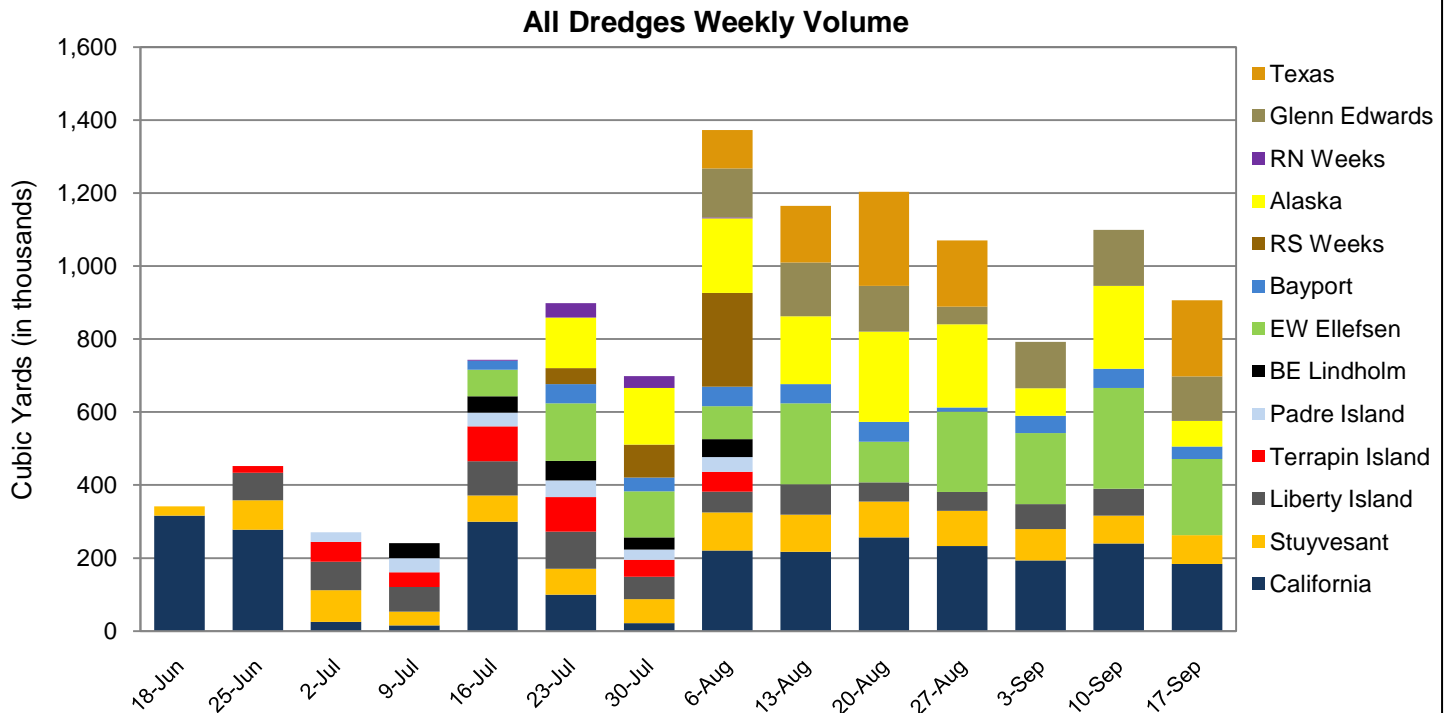

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	2,600,630	
Cutter EW Ellefsen	1,679,635	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,533,045	
Cutter Texas	908,811	
Hopper Stuyvesant	1,080,827	159
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	856,235	87
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	11,255,814	860

* Demobilized from Project on or before September 15th.

Progress by Berm and Borrow Operations (cubic yards)

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	30-Dec-10	3-Apr-11	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	8-Feb-11	8,345,969	3,266,832	5,079,137	39.14%
W8	4-Oct-10	1-Jan-11	1,243,548**	0	1,243,548	0.00%
W9	18-Jul-10 A	26-Sep-10	1,929,494**	1,712,990	216,504	88.78%
W10	13-Sep-10 A	3-Nov-10	1,588,710**	209,300	1,379,410	13.17%
W11	10-Nov-10	14-Dec-10	2,729,032**	0	2,729,032	0.00%
Borrow Operations	16-Jun-10 A	7-Dec-10	11,266,525**	6,066,692	5,199,833	53.85%
Totals			30,407,385	11,255,814	19,151,571	37.02%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

Progress by Berm (linear feet)

Location	Forecast (LF)	Under Construction (LF)*	To Go (LF)	Complete
E3	35,482	0	35,482	0.00%
E4	80,520	16,395	64,125	20.36%
W8	9,480 **	0	9,480	0.00%
W9	13,030**	8,924	4,106	68.49%
W10	15,700**	0	15,700	0.00%
W11	23,000**	0	23,000	0.00%
Totals	177,212	25,319	151,893	14.29%

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.

** Trended project completion quantities.



W9 Berm Operations – September 13, 2010



E4 North Berm – September 13, 2010
