



Barrier Berm Project – Daily Report

Day 122

Document: 139551-PMD-122-S

Date Prepared: October 1, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W9 Berm – September 28, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 30 September

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	27,284	
Subtotal East	27,284	
West		
Cutter California	30,834	10 Scows
Cutter EW Ellefsen	42,350	
Cutter Texas	30,000	
Hopper Glenn Edwards	19,192	2
Subtotal West	122,376	2
Total	149,660	2

Today – 1 October

- Borrow operations at Pass a Loure and West to continue.
- Berm placement operations to continue on E4 North, W9 and W10.

Tomorrow – 2 October

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- W9 berm constructed to final distance; additional filling continues as directed.
- W8 berm construction forecast to start on 15 October.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

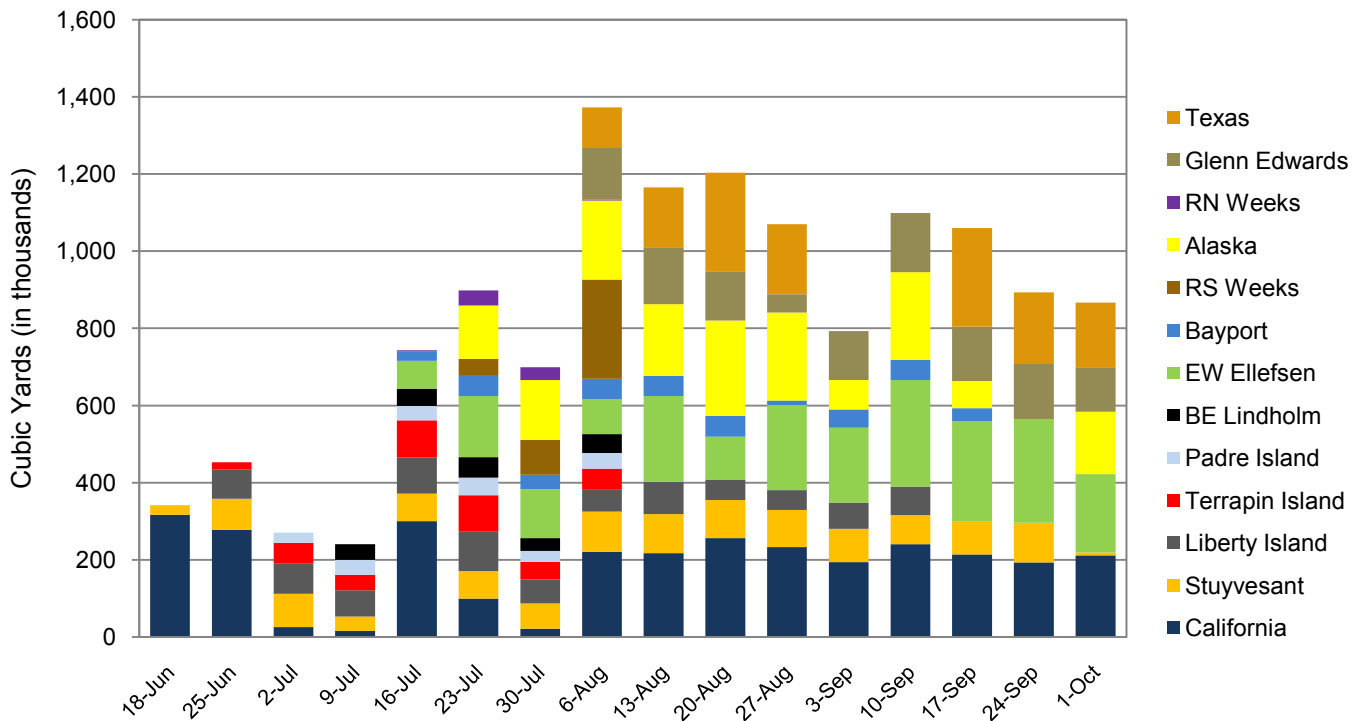

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,035,453	
Cutter EW Ellefsen	2,201,006	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,694,971	
Cutter Texas	1,308,533	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,134,871	116
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	13,170,157	905

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,428,758
W8	0
W9	2,234,361
W10	609,022
W11	0
Borrow Operations	6,898,016
Totals	13,170,157

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	18,015
W8	0
W9	12,449
W10	1,800
W11	0
Totals	32,264

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



Stuyvesant Borrow Operations – September 23, 2010



W10 Berm Operations– September 28, 2010
