



Barrier Berm Project – Daily Report

Day 124

Document: 139551-PMD-124-S

Date Prepared: October 3, 2010

Prepared by:
Shaw Environmental & Infrastructure Group



W9 Berm – September 28, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 2 October

| Vessel | Cubic Yards (CY) Handled | Hopper Loads |
|----------------------|--------------------------|--------------|
| East | | |
| Cutter Alaska | 13,173 | |
| Subtotal East | 13,173 | |
| West | | |
| Cutter California | 2,650 | 1 Scows |
| Cutter EW Ellefsen | 13,410 | |
| Cutter Texas | 25,000 | |
| Hopper Glenn Edwards | 19,343 | 2 |
| Subtotal West | 60,403 | 2 |
| Total | 73,576 | 2 |

- California down most of the day to replace pump impeller; operational as of 8:30 PM.
- W9 berm construction completed.

Today – 3 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North and W10.
- Preparations for W8 berm construction to continue.

Tomorrow – 4 October

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- W8 berm construction forecast to start on 17 October.
 - Repositioning pipeline to begin today; pad construction to begin on 11 October.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

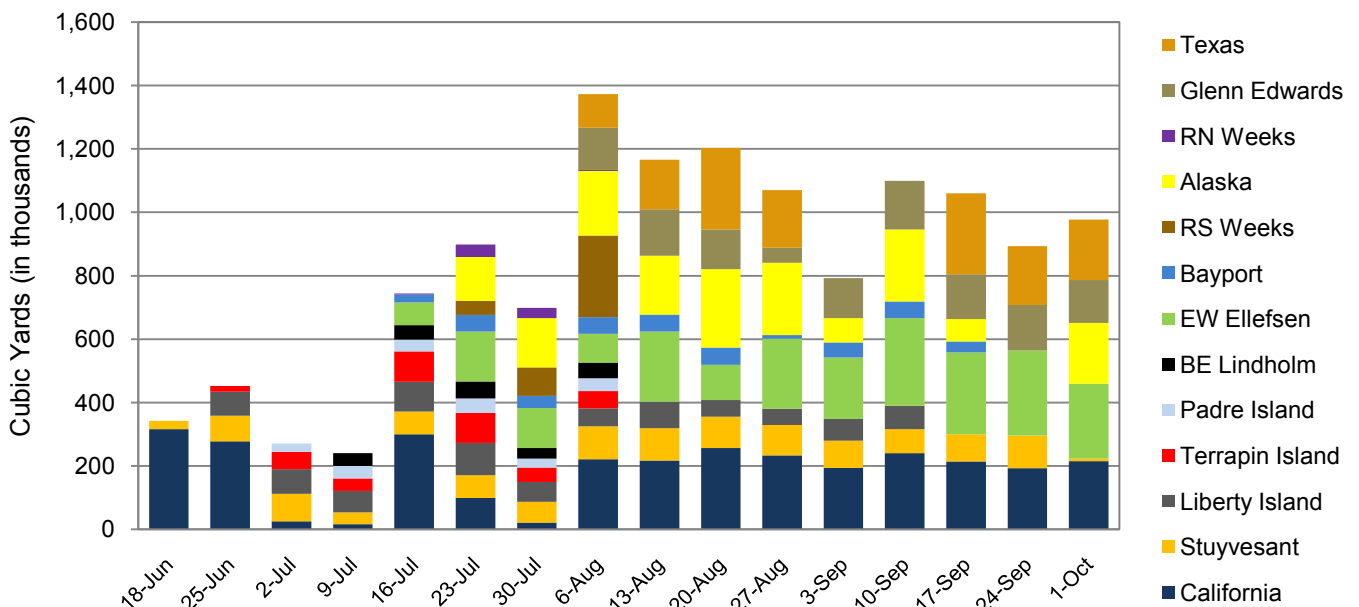

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

| Vessel | Handled - ITD (cy) | Hopper Loads - ITD |
|--------------------------|--------------------|--------------------|
| Cutter California | 3,042,025 | |
| Cutter EW Ellefsen | 2,247,959 | |
| Cutter RS Weeks * | 391,350 | |
| Cutter Alaska | 1,738,005 | |
| Cutter Texas | 1,357,233 | |
| Hopper Stuyvesant * | 1,198,692 | 175 |
| Hopper Liberty Island * | 864,508 | 192 |
| Hopper Bayport * | 421,280 | 114 |
| Hopper Glenn Edwards | 1,173,498 | 116 |
| Hopper Terrapin Island * | 403,823 | 119 |
| Hopper Padre Island * | 216,133 | 84 |
| Hopper BE Lindholm * | 222,527 | 76 |
| Hopper RN Weeks * | 77,010 | 29 |
| Total | 13,354,043 | 905 |

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

| Location | Actuals (CY) |
|-------------------|-------------------|
| E3 | 0 |
| E4 | 3,471,792 |
| W8 | 0 |
| W9 | 2,281,314 |
| W10 | 657,722 |
| W11 | 0 |
| Borrow Operations | 6,943,215 |
| Totals | 13,354,043 |

Progress by Berm (distance)

| Location | Under Construction (LF) |
|---------------|-------------------------|
| E3 | 0 |
| E4 | 18,395 |
| W8 | 0 |
| W9 | 12,449 |
| W10 | 2,300 |
| W11 | 0 |
| Totals | 33,144 |

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



Stuyvesant Borrow Operations – September 23, 2010



W10 Berm Operations– September 28, 2010
