



# Barrier Berm Project – Daily Report

## Day 128

---

Document: 139551-PMD-127-S

Date Prepared: October 7, 2010

Prepared by:

Shaw Environmental & Infrastructure Group

---



*W9 & W10 Berm – October 6, 2010*

# Barrier Berm Project 139551 – Daily Information

## Yesterday – 6 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
<b>East</b>		
Cutter Alaska	0	
<b>Subtotal East</b>	<b>0</b>	
<b>West</b>		
Cutter California	35,585	12 Scows
Cutter EW Ellefsen	0	
Cutter Texas	18,500	
Hopper Glenn Edwards	20,034	2
<b>Subtotal West</b>	<b>74,119</b>	<b>2</b>
<b>Total</b>	<b>74,119</b>	<b>2</b>

- Rough Seas persisting on the East side, prohibiting the Alaska from operating; weather expected to break later today, which should allow the Alaska to return to production.
- EW Ellefsen continues pipeline repositioning for W8 berm construction.

## Today – 7 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North and W10.
- Preparations for W8 berm construction to continue.

## Tomorrow – 8 October

- Today's operational activities to continue through tomorrow.


## Near-Term Milestones

- W8 berm construction forecast to start on 17 October.
  - Repositioning pipeline began 3 October; pad construction to begin on 11 October.

## Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

**All Dredges Weekly Volume**

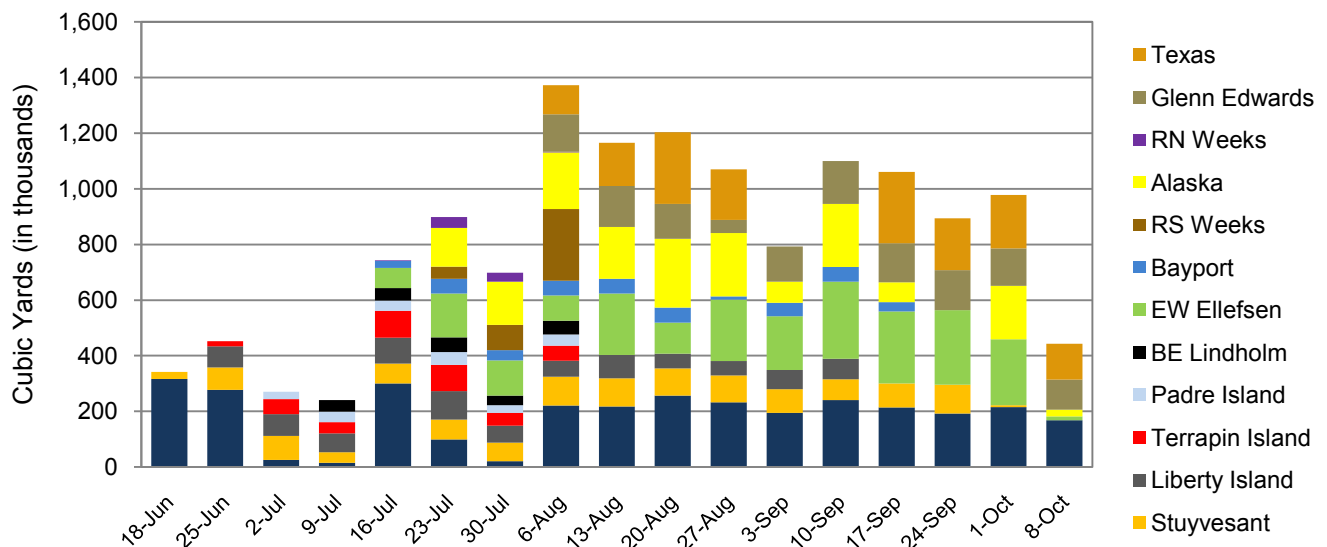

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,207,648	
Cutter EW Ellefsen	2,247,959	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,749,171	
Cutter Texas	1,461,533	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,261,980	127
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>13,723,614</b>	<b>916</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,482,958
W8	0
W9	2,281,314
W10	762,022
W11	0
Borrow Operations	7,197,320
<b>Totals</b>	<b>13,723,614</b>

### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	18,435
W8	0
W9	12,449
W10	3,950
W11	0
<b>Totals</b>	<b>34,834</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W10 Berm Operations – October 6, 2010



E4 North Berm Operations – October 6, 2010
