

Barrier Berm Project – Daily Report

Day 131

Document: 139551-PMD-131-S

Date Prepared: October 10, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W9 & W10 Berm - October 7, 2010



Barrier Berm Project 139551 – Daily Information

Yesterday - 9 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads		
East				
Cutter Alaska	29,554			
Subtotal East	29,554			
West				
Cutter California	27,326	8 Scows		
Cutter EW Ellefsen	13,409			
Cutter Texas	32,000			
Hopper Glenn Edwards	20,071	2		
Subtotal West	92,806	2		
Total	122,360	2		

EW Ellefsen began pad construction on W8.

Today - 10 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.

Tomorrow – 11 October

• Today's operational activities to continue through tomorrow.


Near-Term Milestones

- W8 berm construction forecast to start on 17 October.
 - o Repositioning pipeline began 3 October; pad construction began on 9 October.

Potential Schedule Variability Items

• Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

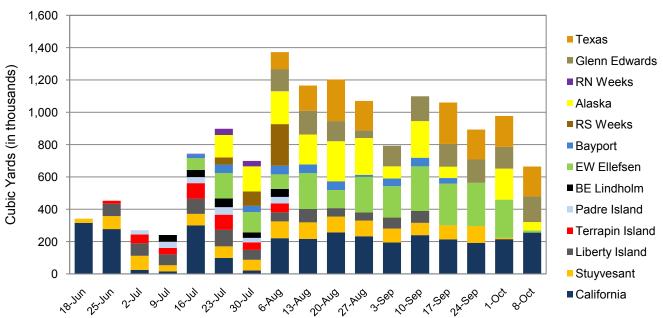



Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,322,857	
Cutter EW Ellefsen	2,261,368	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,806,024	
Cutter Texas	1,549,533	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,332,462	134
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	14,067,567	923

^{*} Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,539,811
W8	0
W9	2,294,723
W10	850,022
W11	0
Borrow Operations	7,383,011
Totals	14,067,567

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	19,597
W8	0
W9	12,449
W10	4,900
W11	0
Totals	36,946

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 & W10 - October 7, 2010



E4 North Berm Operations - October 7, 2010
