



Barrier Berm Project – Daily Report

Day 137

Document: 139551-PMD-137-S

Date Prepared: October 16, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W8 Initial Pad – October 13, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 15 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	55,683	
Subtotal East	55,683	
West		
Cutter California	44,892	13 Scows
Cutter EW Ellefsen	41,833	
Cutter Texas	26,000	
Hopper Glenn Edwards	10,181	1
Subtotal West	122,906	1
Total	178,589	1

Today – 16 October

- Borrow operations at Pass a Loure and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 17 October

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

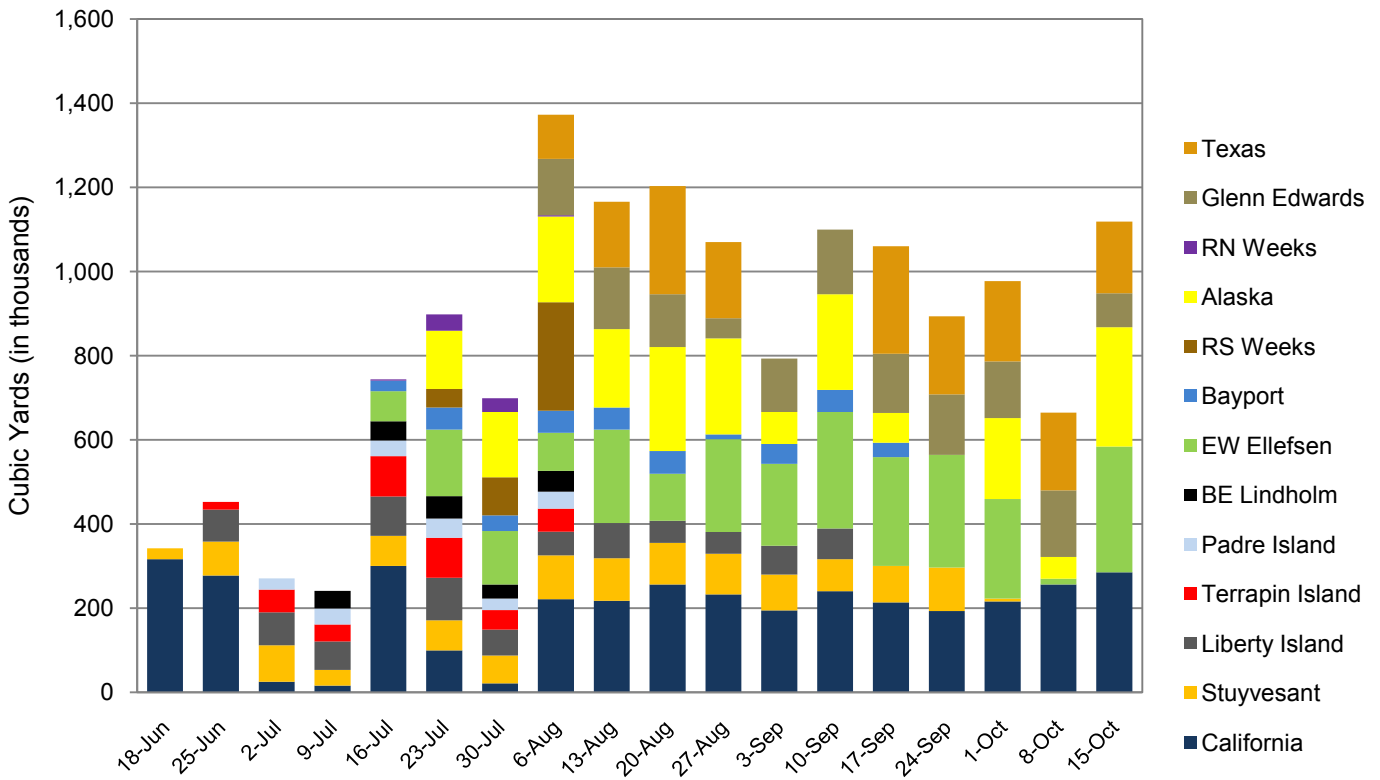

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,580,312	
Cutter EW Ellefsen	2,547,139	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,060,066	
Cutter Texas	1,687,908	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,392,946	140
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	15,063,694	929

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,793,853
W8	299,180
W9	2,281,314
W10	988,397
W11	0
Borrow Operations	7,700,950
Totals	15,063,694

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	21,257
W8	0
W9	12,449
W10	6,630
W11	0
Totals	40,336

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 Berm – October 13, 2010



W8 Berm Operations – October 13, 2010
