



Barrier Berm Project – Daily Report

Day 138

Document: 139551-PMD-138-S

Date Prepared: October 17, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm – October 13, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 16 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	52,450	
Subtotal East	52,450	
West		
Cutter California	48,910	14 Scows
Cutter EW Ellefsen	44,965	
Cutter Texas	21,005	
Hopper Glenn Edwards	29,943	3
Subtotal West	144,823	3
Total	197,273	3

Today – 17 October

- Borrow operations at Pass a Loure and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 18 October

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

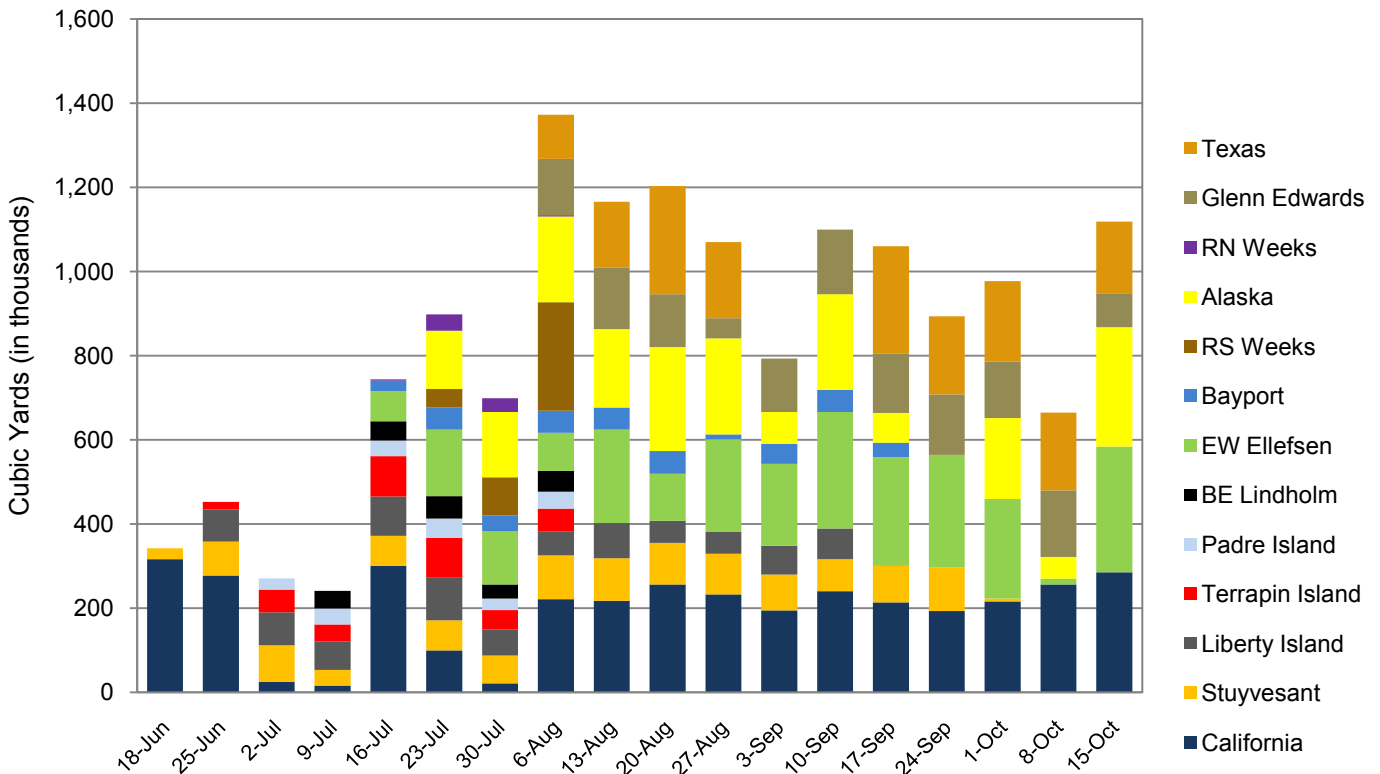

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,629,222	
Cutter EW Ellefsen	2,592,104	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,112,516	
Cutter Texas	1,708,913	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,422,889	143
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	15,260,967	932

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,846,303
W8	344,145
W9	2,281,314
W10	1,009,402
W11	0
Borrow Operations	7,779,803
Totals	15,260,967

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	21,557
W8	0
W9	12,449
W10	6,780
W11	0
Totals	40,786

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 Berm – October 13, 2010



W8 Berm Operations – October 13, 2010
