

Barrier Berm Project – Daily Report

Day 139

Document: 139551-PMD-139-S

Date Prepared: October 18, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W10 Berm - October 17, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday - 17 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads	
East			
Cutter Alaska	38,278		
Subtotal East	38,278		
West			
Cutter California	32,395	9 Scows	
Cutter EW Ellefsen	42,013		
Cutter Texas	46,000		
Hopper Glenn Edwards	9,963	1	
Subtotal West	130,371	1	
Total	168,649	1	

Today - 18 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow - 19 October

Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

• Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

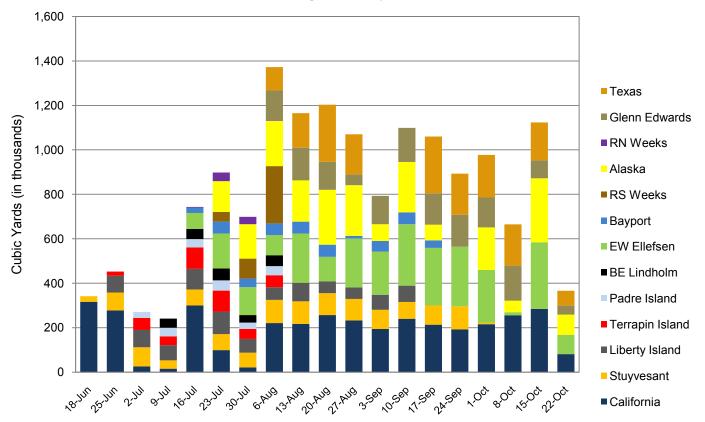

1

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,661,617	
Cutter EW Ellefsen	2,634,117	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,155,757	
Cutter Texas	1,754,913	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,432,852	144
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	15,434,579	933

^{*} Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	3,889,544
W8	386,158
W9	2,281,314
W10	1,055,402
W11	0
Borrow Operations	7,822,161
Totals	15,434,579

Progress by Berm (distance)

Location	Under Construction (LF)	
E3	0	
E4	21,987	
W8	0	
W9	12,449	
W10	6,930	
W11	0	
Totals	41,366	

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 Berm - October 13, 2010



W8 Berm Operations - October 13, 2010
