



# Barrier Berm Project – Daily Report

## Day 145

---

Document: 139551-PMD-145-S

Date Prepared: October 24, 2010

Prepared by:

Shaw Environmental & Infrastructure Group

---



*W10 Berm – October 19, 2010*

# Barrier Berm Project 139551 – Daily Information

## Yesterday – 23 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
<b>East</b>		
Cutter Alaska	24,391	
<b>Subtotal East</b>	<b>24,391</b>	
<b>West</b>		
Cutter California	34,217	12 Scows
Cutter EW Ellefsen	29,569	
Cutter Texas	15,000	
Hopper Glenn Edwards	0	0
<b>Subtotal West</b>	<b>78,786</b>	<b>0</b>
<b>Total</b>	<b>103,177</b>	<b>0</b>

- Glenn Edwards down for repairs, and is expected to return to operations October 27<sup>th</sup>.
- Texas returned to operations.

## Today – 24 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


## Tomorrow – 25 October

- Today's operational activities to continue through tomorrow.

## Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

**All Dredges Weekly Volume**

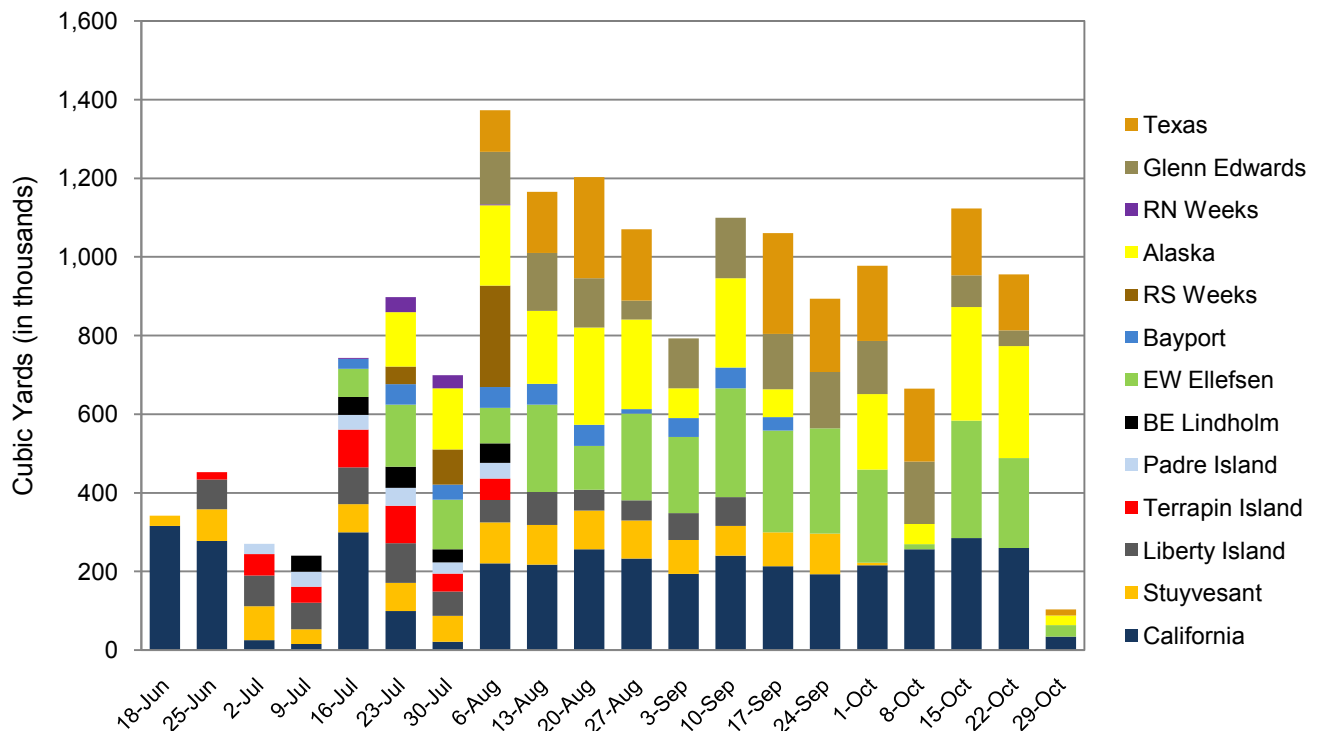

## Barrier Berm Project 139551 – Cumulative Information

### Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,874,484	
Cutter EW Ellefsen	2,804,871	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,374,620	
Cutter Texas	1,845,530	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,432,852	144
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
<b>Total</b>	<b>16,127,680</b>	<b>933</b>

\* Demobilized from Project.

### Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,108,407
W8	556,912
W9	2,281,314
W10	1,146,019
W11	0
Borrow Operations	8,035,028
<b>Totals</b>	<b>16,127,680</b>

### Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	24,247
W8	2,430
W9	12,449
W10	7,830
W11	0
<b>Totals</b>	<b>46,956</b>

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 19, 2010



W8 & W9 Berm Operations – October 19, 2010
