



Barrier Berm Project – Daily Report

Day 150

Document: 139551-PMD-150-S

Date Prepared: October 29, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W8 Berm – October 26, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 28 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	52,386	
Subtotal East	52,386	
West		
Cutter California	31,458	8 Scows
Cutter EW Ellefsen	24,380	
Cutter Texas	23,000	
Hopper Glenn Edwards	19,744	2
Subtotal West	98,582	2
Total	150,968	2

- Strong production day despite rough weather conditions

Today – 29 October

- Borrow operations at South Pass to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 30 October

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

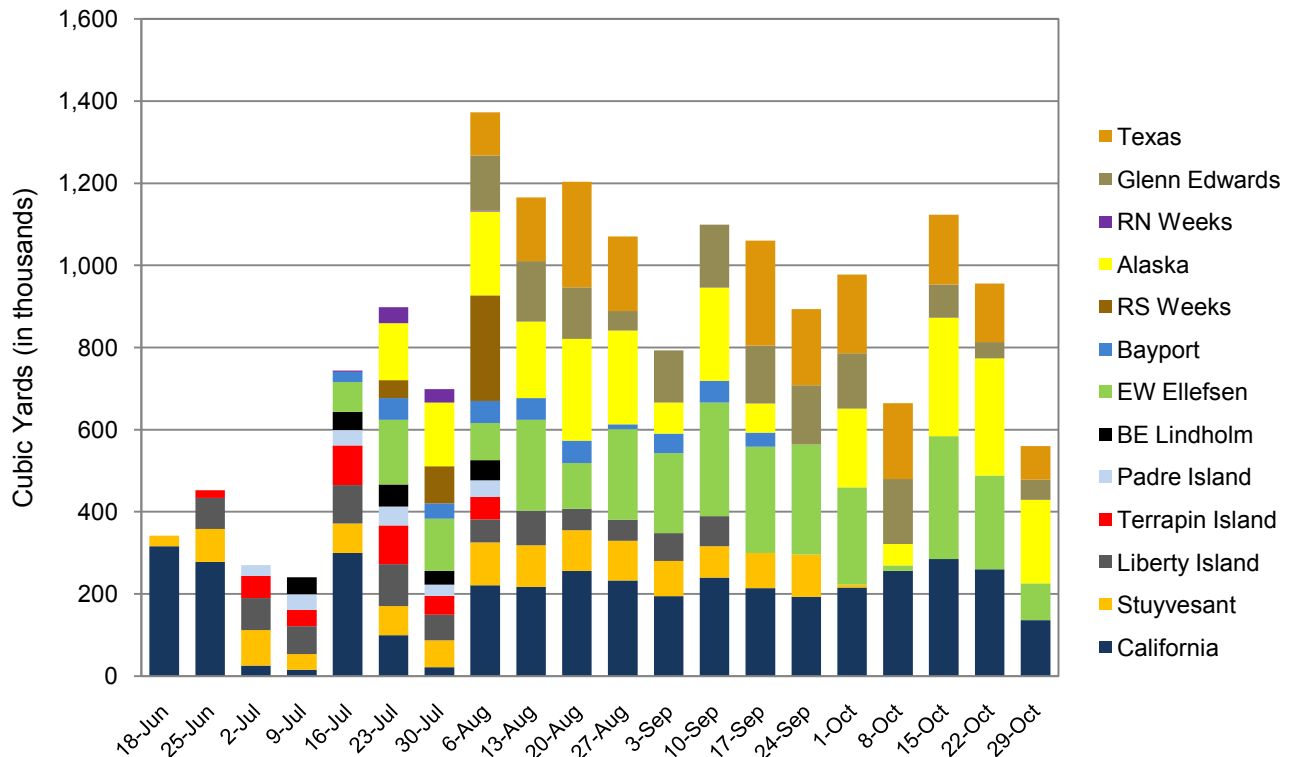

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,976,335	
Cutter EW Ellefsen	2,865,095	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,553,628	
Cutter Texas	1,911,630	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,482,142	149
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	16,584,153	938

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,287,415
W8	617,136
W9	2,281,314
W10	1,212,119
W11	0
Borrow Operations	8,186,169
Totals	16,584,153

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	25,391
W8	3,050
W9	12,449
W10	8,830
W11	0
Totals	49,720

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 26, 2010



W10 Berm Operations – October 24, 2010
