



Barrier Berm Project – Daily Report

Day 151

Document: 139551-PMD-151-S

Date Prepared: October 30, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W10 Berm – October 26, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 29 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	0	
Subtotal East	0	
West		
Cutter California	34,907	9 Scows
Cutter EW Ellefsen	43,998	
Cutter Texas	16,356	
Hopper Glenn Edwards	19,489	2
Subtotal West	114,750	2
Total	114,750	2

- Alaska down all day due to weather; operational as of 12:30 AM.

Today – 30 October

- Borrow operations at South Pass to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 31 October

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

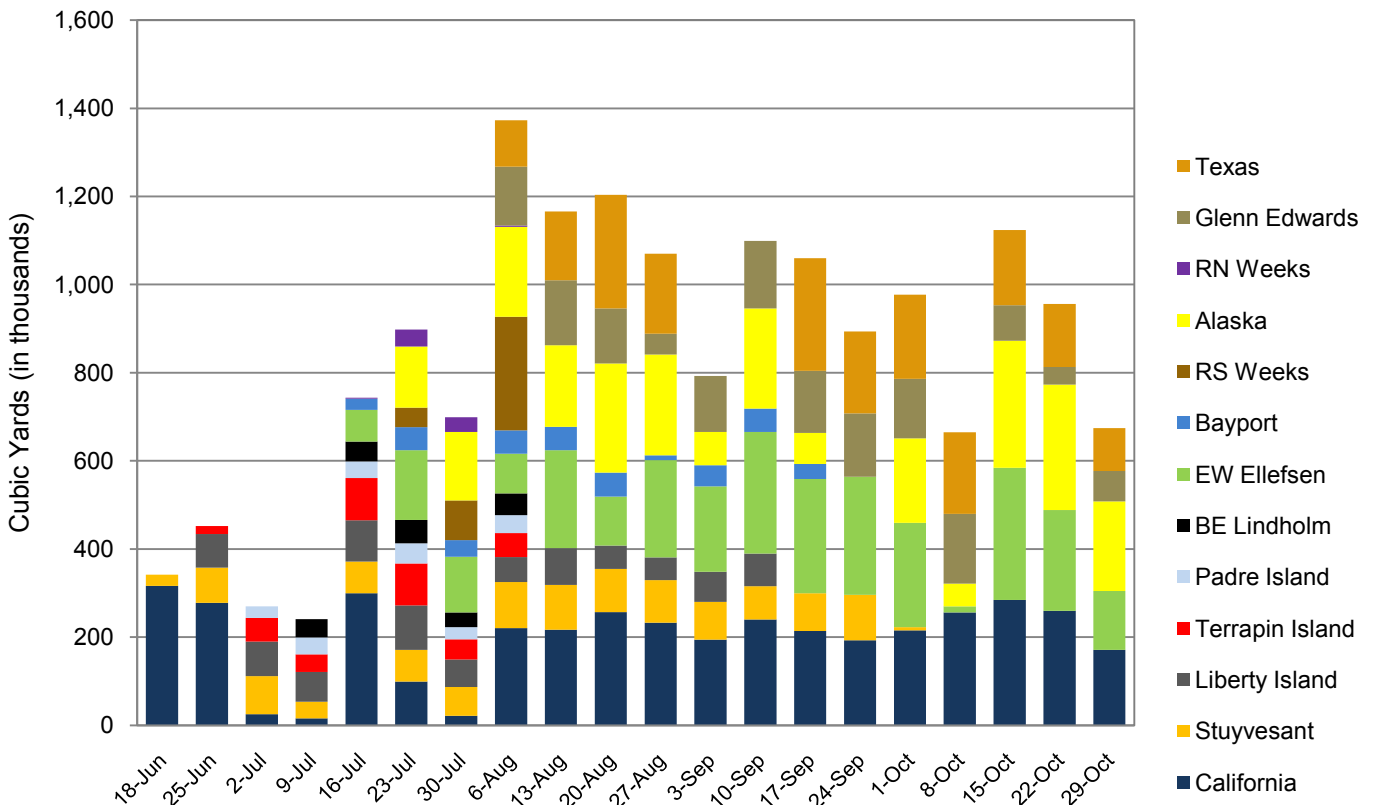

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	4,011,242	
Cutter EW Ellefsen	2,909,093	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,553,628	
Cutter Texas	1,927,986	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,501,631	153
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	16,698,903	942

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,287,415
W8	661,134
W9	2,281,314
W10	1,228,475
W11	0
Borrow Operations	8,240,565
Totals	16,698,903

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	25,391
W8	3,400
W9	12,449
W10	9,180
W11	0
Totals	50,420

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 26, 2010



W10 Berm Operations – October 24, 2010
