



Barrier Berm Project – Daily Report

Day 152

Document: 139551-PMD-152-S

Date Prepared: October 31, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm – October 26, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 30 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	35,708	
Subtotal East	35,708	
West		
Cutter California	31,474	9 Scows
Cutter EW Ellefsen	36,648	
Cutter Texas	14,700	
Hopper Glenn Edwards	19,998	2
Subtotal West	102,820	2
Total	138,528	2

Today – 31 October

- Borrow operations at South Pass to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 1 November

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

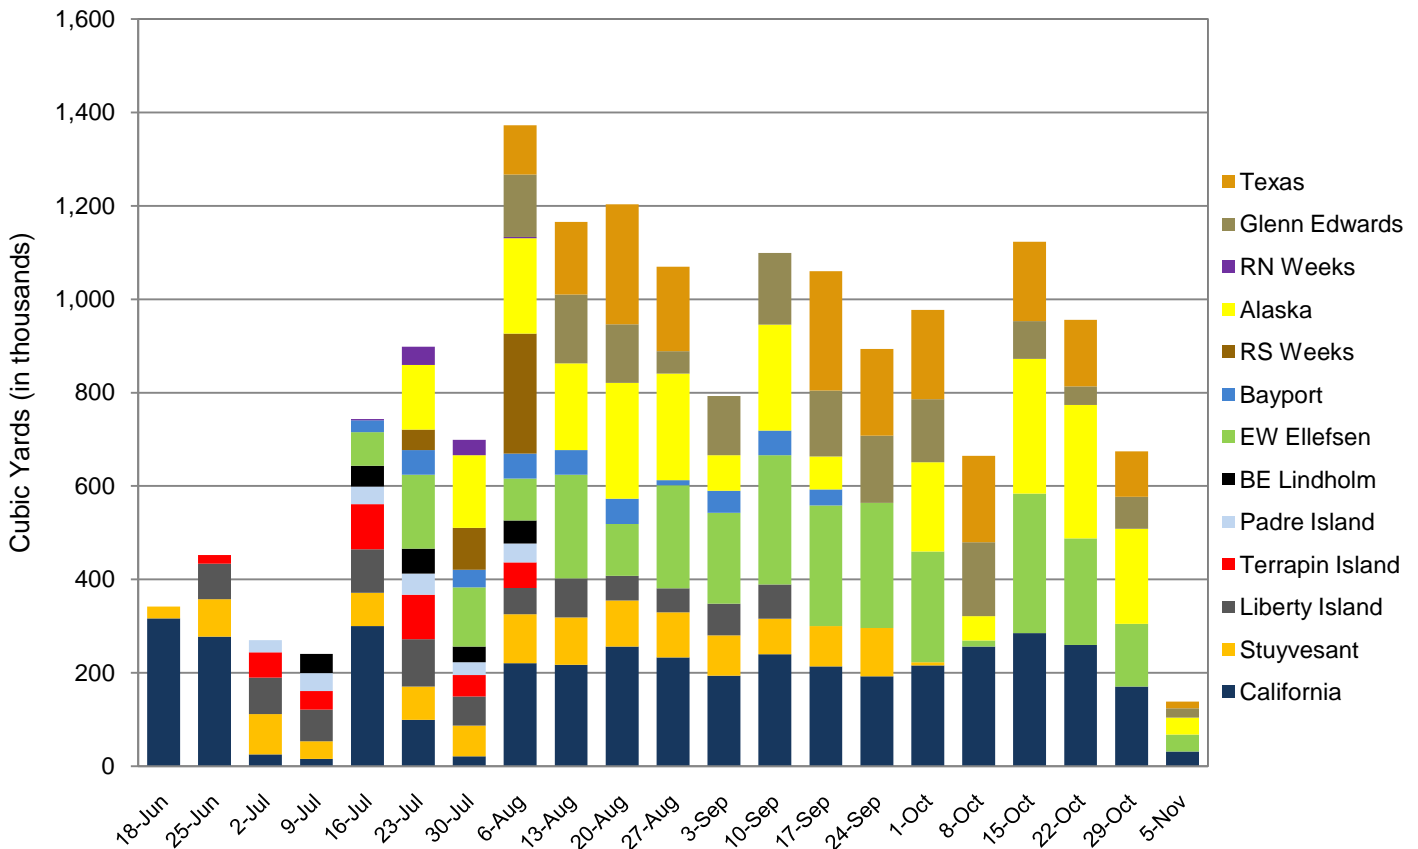

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	4,042,716	
Cutter EW Ellefsen	2,945,741	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,589,336	
Cutter Texas	1,942,686	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,521,629	155
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	16,837,431	944


Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,323,123
W8	697,782
W9	2,281,314
W10	1,243,175
W11	0
Borrow Operations	8,292,037
Totals	16,837,431

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	25,746
W8	3,650
W9	12,449
W10	9,380
W11	0
Totals	51,225

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.

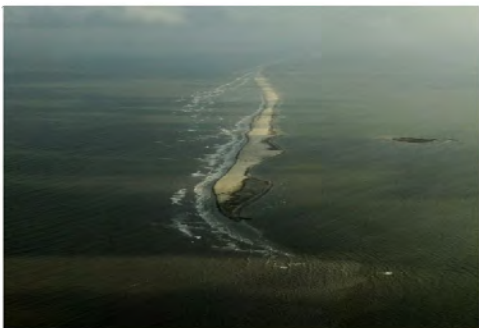

E4 Berm – October 26, 2010



W10 Berm Operations – October 24, 2010
