



Barrier Berm Project – Daily Report

Day 154

Document: 139551-PMD-154-S

Date Prepared: November 2, 2010

Prepared by:
Shaw Environmental & Infrastructure Group



E4 North Berm – October 31, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 1 November

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	4,425	
Subtotal East	4,425	
West		
Cutter California	37,512	11 Scows
Cutter EW Ellefsen	24,098	
Cutter Texas	24,900	
Hopper Glenn Edwards	20,252	2
Subtotal West	106,762	2
Total	111,187	2

- Alaska returned from repairs at 22:00 hours


Today – 2 November

- Borrow operations at South Pass to continue.
- Berm placement operations to continue on E4 North, W10, and W8.

Tomorrow – 3 November

- Today's operational activities to continue through tomorrow.

All Dredges Weekly Volume

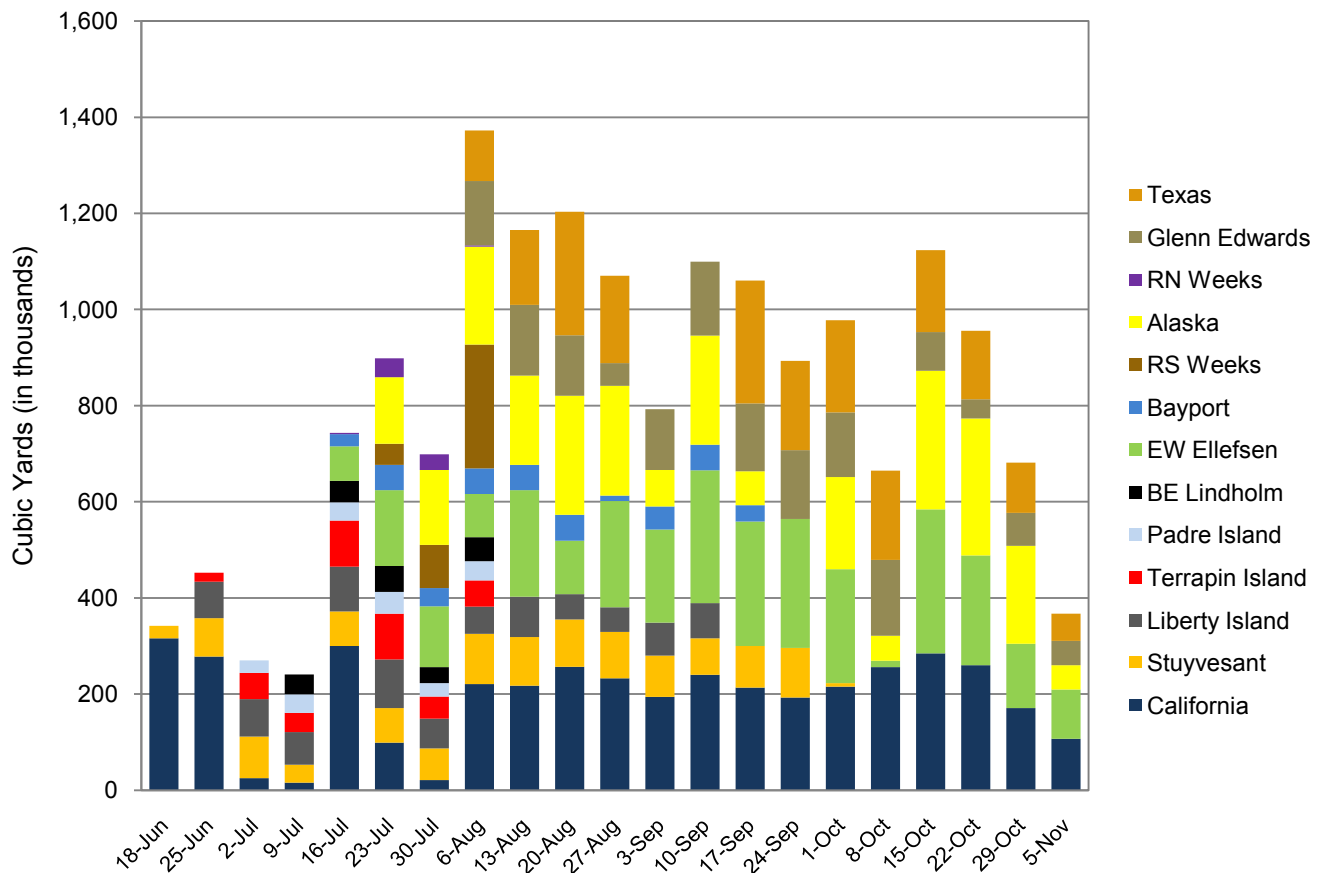

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	4,118,292	
Cutter EW Ellefsen	3,011,772	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,604,059	
Cutter Texas	1,991,830	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,552,152	158
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	17,073,428	947

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,337,846
W8	763,813
W9	2,281,314
W10	1,292,319
W11	0
Borrow Operations	8,398,136
Totals	17,073,428

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	25,946
W8	4,580
W9	12,449
W10	10,030
W11	0
Totals	53,005

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 31, 2010



W8 Berm – October 31, 2010
