



Barrier Berm Project – Daily Report

Day 160

Document: 139551-PMD-160-S

Date Prepared: November 8, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W10 Berm – November 7, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 7 November

| Vessel | Cubic Yards (CY) Handled |
|----------------------|--------------------------|
| East | |
| Cutter Alaska | 5,538 |
| Subtotal East | 5,538 |
| West | |
| Cutter EW Ellefsen | 35,607 |
| Cutter Texas | 30,500 |
| Subtotal West | 66,107 |
| Total | 71,645 |

- Alaska down 19.25 hours for repairs, returned to operations Monday morning.


Today – 8 November

- Berm placement operations to continue on E4, W8 and W10.

Tomorrow – 9 November

- Today's operational activities to continue tomorrow.

All Dredges Weekly Volume

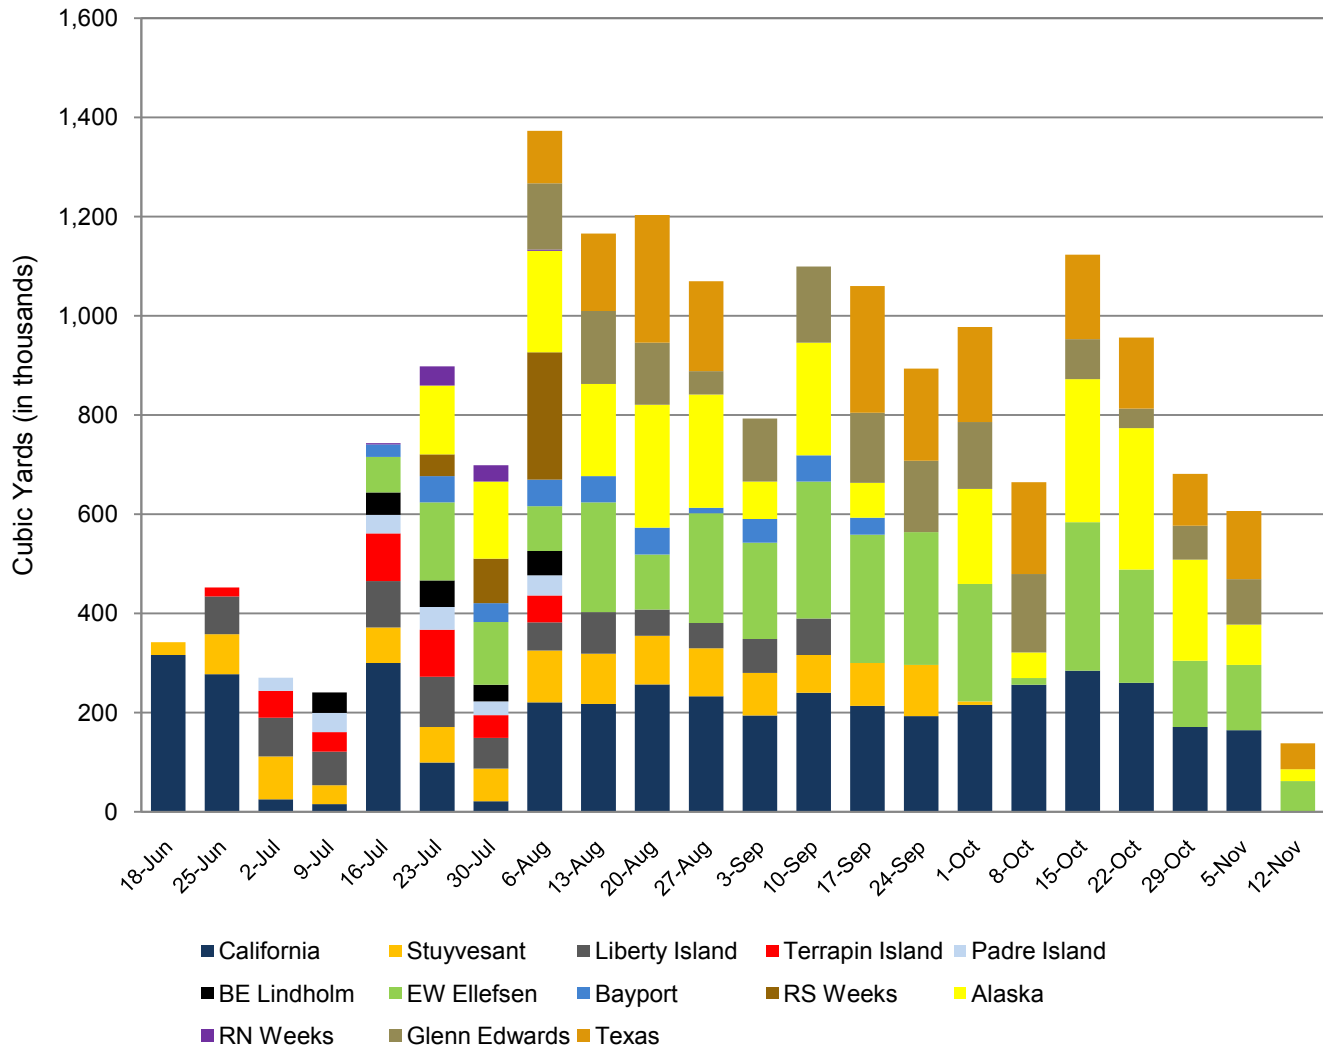

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

| Vessel | Handled - ITD (cy) | Hopper Loads - ITD |
|--------------------------|--------------------|--------------------|
| Cutter California* | 4,175,650 | |
| Cutter EW Ellefsen | 3,102,596 | |
| Cutter RS Weeks * | 391,350 | |
| Cutter Alaska | 2,658,918 | |
| Cutter Texas | 2,125,230 | |
| Hopper Stuyvesant * | 1,198,692 | 175 |
| Hopper Liberty Island * | 864,508 | 192 |
| Hopper Bayport * | 421,280 | 114 |
| Hopper Glenn Edwards* | 1,593,128 | 162 |
| Hopper Terrapin Island * | 403,823 | 119 |
| Hopper Padre Island * | 216,133 | 84 |
| Hopper BE Lindholm * | 222,527 | 76 |
| Hopper RN Weeks * | 77,010 | 29 |
| Total | 17,450,845 | 951 |

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

| Location | Actuals (CY) |
|-------------------|-------------------|
| E3 | 0 |
| E4 | 4,392,705 |
| W8 | 854,637 |
| W9 | 2,281,314 |
| W10 | 1,425,719 |
| W11 | 0 |
| Borrow Operations | 8,496,470 |
| Totals | 17,450,845 |

Progress by Berm (distance)

| Location | Under Construction (LF) |
|---------------|-------------------------|
| E3 | 0 |
| E4 | 26,186 |
| W8 | 5,939 |
| W9 | 12,449 |
| W10 | 10,830 |
| W11 | 0 |
| Totals | 55,404 |

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – November 7, 2010



W8 Berm – November 7, 2010
