



Barrier Berm Project – Daily Report

Day 181

Document: 139551-PMD-181-S

Date Prepared: November 29, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm – November 28, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 28 November

Vessel	Cubic Yards (CY) Handled
East	
Cutter Alaska	24,130
Subtotal East	24,130
Total	24,130


Today – 29 November

- Demobilization of West side operations to continue.
- E4 berm construction to continue.

Tomorrow – 30 November

- Today's operational activities to continue tomorrow.

All Dredges Weekly Volume

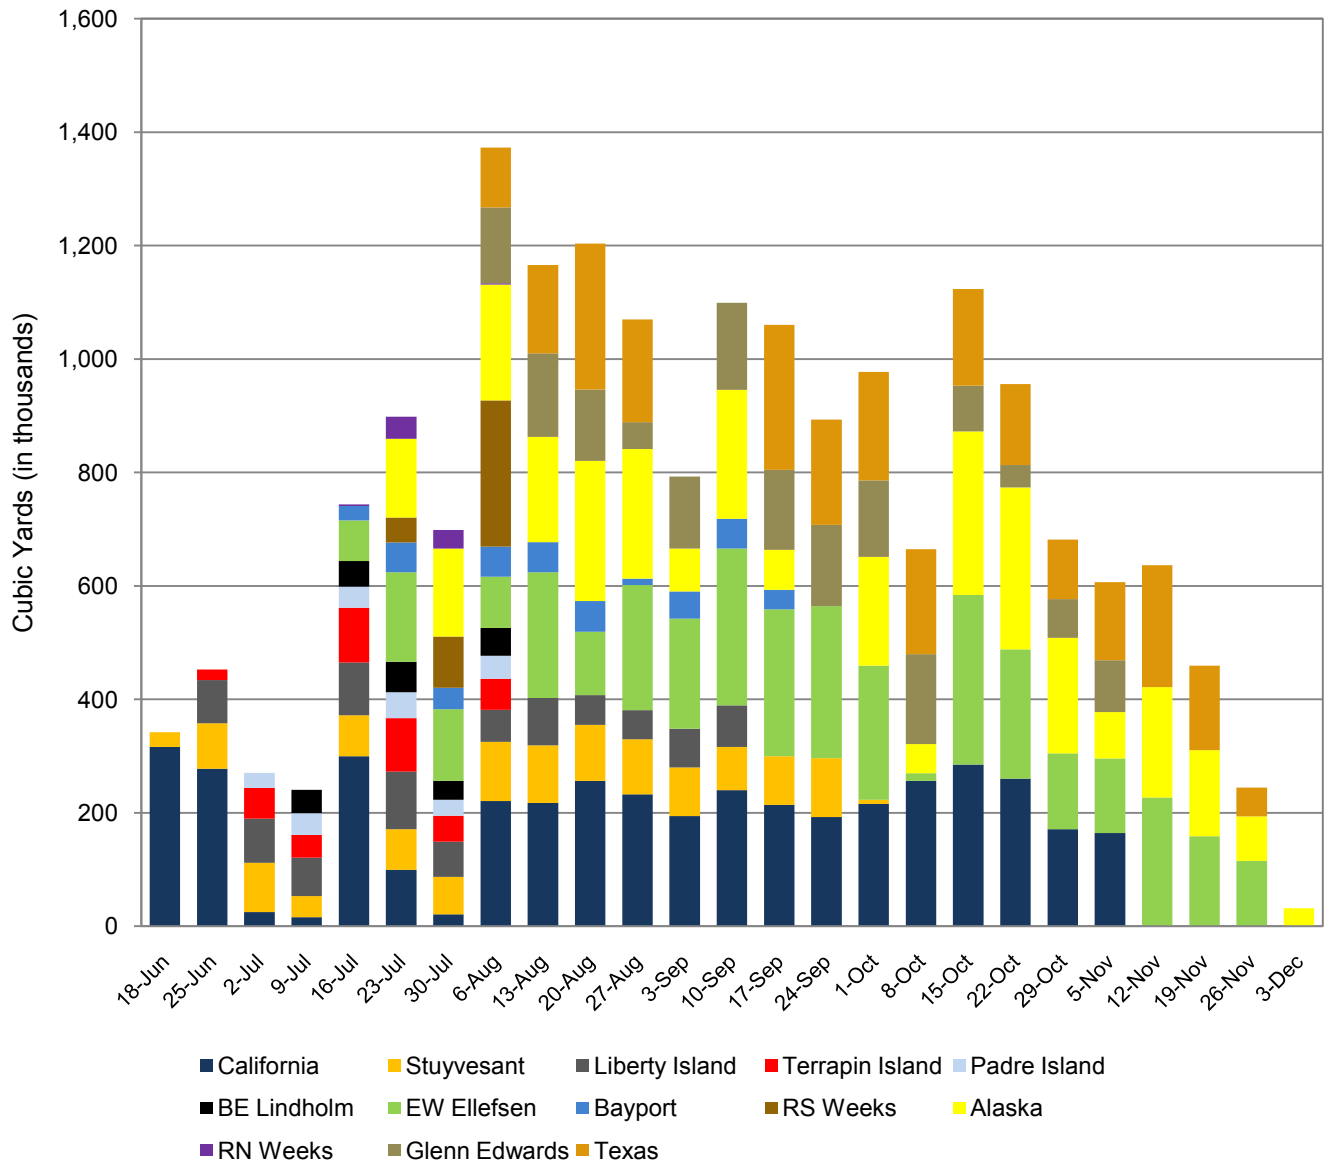

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California*	4,175,650	
Cutter EW Ellefsen*	3,542,049	
Cutter RS Weeks *	391,350	
Cutter Alaska	3,090,685	
Cutter Texas*	2,487,613	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards*	1,593,128	162
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	18,684,448	951

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,824,472
W8	1,294,090
W9	2,281,314
W10	1,788,102
W11	0
Borrow Operations	8,496,470
Totals	18,684,448

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	32,296
W8	8,289
W9	12,449
W10	14,230
W11	0
Totals	67,264

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W8 Berm – November 28, 2010



W10 Berm – November 28, 2010
