



Barrier Berm Project – Daily Report

Day 67

Document: 139551-PMD-067-S

Date Prepared: August 7, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm – August 5, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 6 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	22,868	
Cutter Texas	29,300	
Subtotal East	52,168	
West		
Cutter California	37,896	11 Scows
Cutter EW Ellefsen	22,556	
Cutter RS Weeks	0	
Hopper Stuyvesant	15,258	2
Hopper Liberty Island	0	0
Hopper Terrapin Island	7,106	2
Hopper Padre Island	5,341	2
Hopper BE Lindholm	8,881	3
Hopper Bayport	7,741	2
Hopper Glen Edwards	19,819	2
Subtotal West	124,598	13
Total	176,766	13

- Three hopper dredges demobilized at the end of the day per current project execution.

Today – 7 August

- Borrow operations to continue at Pass a Loutre and West, placement operations to continue at E4 North and W9.

Tomorrow – 8 August

- Today's operational activities expected to continue through tomorrow.


Near-Term Milestones

- Start E4 south berm construction forecast to begin 11 August.
- Start W10 berm construction forecast to begin 24 August.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Equipment rotation, uptime maximization and timely remaining operations.

All Dredges Weekly Volume

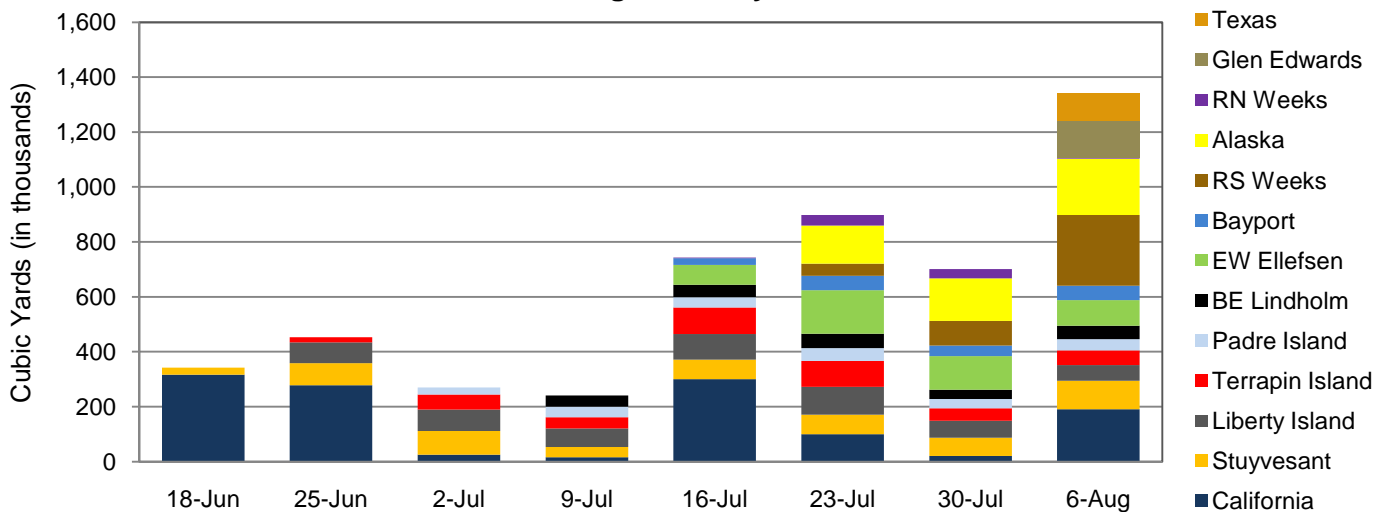

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,245,286	
Cutter EW Ellefsen	445,674	
Cutter RS Weeks	391,350	
Cutter Alaska	498,148	
Cutter Texas	100,758	
Hopper Stuyvesant	543,352	82
Hopper Liberty Island	535,190	122
Hopper Terrapin Island	403,843	119
Hopper Padre Island	221,494	84
Hopper BE Lindholm	222,527	76
Hopper Bayport	168,622	46
Hopper RN Weeks	77,010	28
Hopper Glen Edwards	133,735	14
Total	4,986,989	571

Progress by Berm and Borrow Operations

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	11-Aug-10	21-Oct-10	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	1-Nov-10	8,345,969	1,633,182	6,712,787	19.57%
W8	6-Sep-10	28-Nov-10	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	27-Aug-10	1,130,870	480,018	650,852	42.45%
W10	24-Aug-10	21-Sep-10	1,327,543	0	1,327,543	0.00%
W11	13-Oct-10	1-Nov-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	18-Oct-10	13,088,593	2,873,789	10,214,804	21.96%
Totals			31,081,372	4,986,989	26,094,383	16.04%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.



W9 Berm Construction – August 5, 2010



W9 Berm – August 5, 2010



E4 Berm – August 5, 2010



E4 Berm Construction – August 5, 2010
