



Barrier Berm Project – Daily Report

Day 72

Document: 139551-PMD-072-S

Date Prepared: August 12, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 Berm – August 10, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 11 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	0	
Cutter Texas	4,100	
Subtotal East	4,100	
West		
Cutter California	4,710	1 Scow
Cutter EW Ellefsen	16,533	
Hopper Stuyvesant	7,740	2
Hopper Liberty Island	9,974	2
Hopper Bayport	7,452	2
Hopper Glen Edwards	8,388	1
Subtotal West	54,797	7
Total	58,897	7

- Limited production due to tropical weather.

Today – 12 August

- Borrow operations at Pass a Loutre and West to resume.
- Cutter dredges to begin remobilization for berm placement operations pending weather.

Tomorrow – 13 August

- Berm placement operations to resume pending weather.


Near-Term Milestones

- Start of W10 berm construction forecast to begin 27 August.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Variations from current fleet configuration.
- Current weather system.

All Dredges Weekly Volume

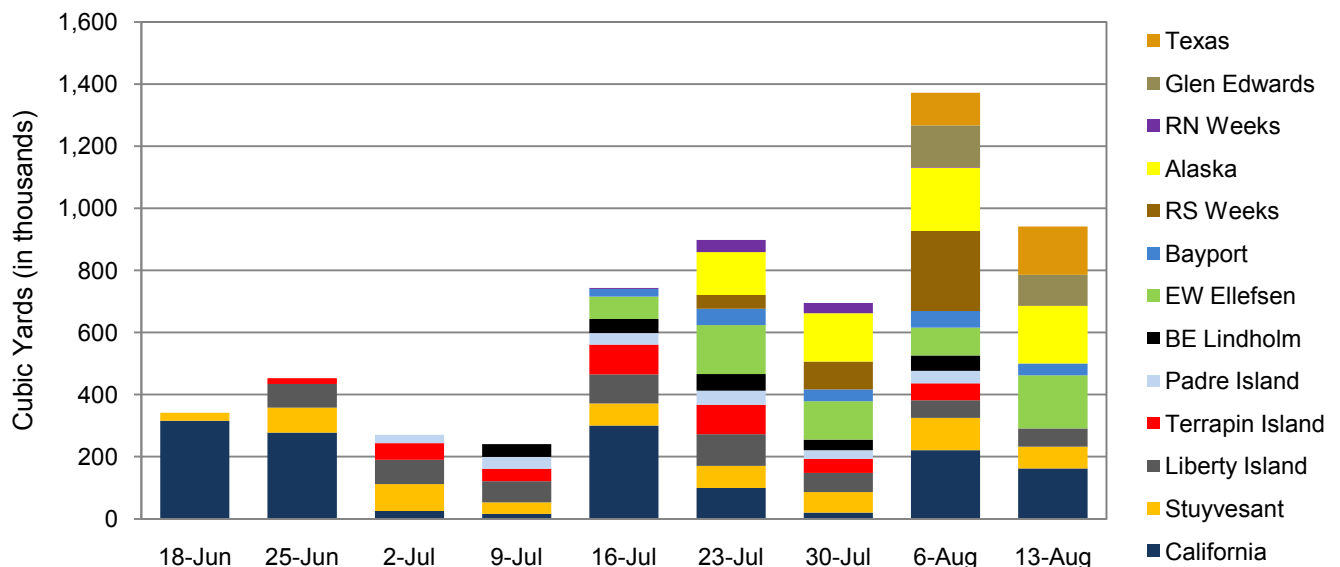

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,437,677	
Cutter EW Ellefsen	616,161	
Cutter RS Weeks *	391,350	
Cutter Alaska	683,863	
Cutter Texas	260,965	
Hopper Stuyvesant	612,841	92
Hopper Liberty Island	594,025	134
Hopper Bayport	206,580	56
Hopper Glen Edwards	233,034	24
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	28
Total	5,955,989	613

* Demobilized on or before August 6th.

Progress by Berm and Borrow Operations (cubic yards)

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	16-Aug-10	21-Oct-10	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	1-Nov-10	8,345,969	1,979,104	6,366,865	23.71%
W8	6-Sep-10	28-Nov-10	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	27-Aug-10	1,130,870	651,683	479,187	57.63%
W10	24-Aug-10	21-Sep-10	1,327,543	0	1,327,543	0.00%
W11	13-Oct-10	1-Nov-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	18-Oct-10	13,088,593	3,325,202	9,763,391	25.41%
Totals			31,081,372	5,955,989	25,125,383	19.16%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

Progress by Berm (linear feet)

Location	Forecast (LF)	Actual (LF)	To Go (LF)	Complete
E3	35,482	0	35,482	0.00%
E4	80,520	7,720	72,800	9.59%
W8	30,096	0	30,096	0.00%
W9	12,144	3,290	8,854	27.09%
W10	14,256	0	14,256	0.00%
W11	11,616	0	11,616	0.00%
Totals	184,114	11,010	173,104	5.98%

Note: Under normal field conditions, berm is advancing approximately 500 LF per reach per day.



E4 Berm Construction – August 10, 2010



W9 Berm – August 10, 2010
