



Barrier Berm Project – Daily Report

Day 75

Document: 139551-PMD-075-S

Date Prepared: August 15, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 Berm – August 10, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 14 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	0	
Cutter Texas	12,800	
Subtotal East	12,800	
West		
Cutter California	41,335	11 Scows
Cutter EW Ellefsen	25,736	
Hopper Stuyvesant	16,055	2
Hopper Liberty Island	9,816	2
Hopper Bayport	10,911	3
Hopper Glen Edwards	18,918	2
Subtotal West	122,771	9
Total	135,571	9

- Production began to ramp up in the East as the seas have subsided.

Today – 15 August

- Borrow operations at Pass a Loutre and West to continue.
- Alaska to resume berm placement operations on E4 North.
- Berm placement operations to continue on E4 South and W9.

Tomorrow – 16 August

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- Completion of W9 berm construction forecast for 30 August.
- Start of W10 berm construction forecast to begin 6 September.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Variations from current fleet configuration.

All Dredges Weekly Volume

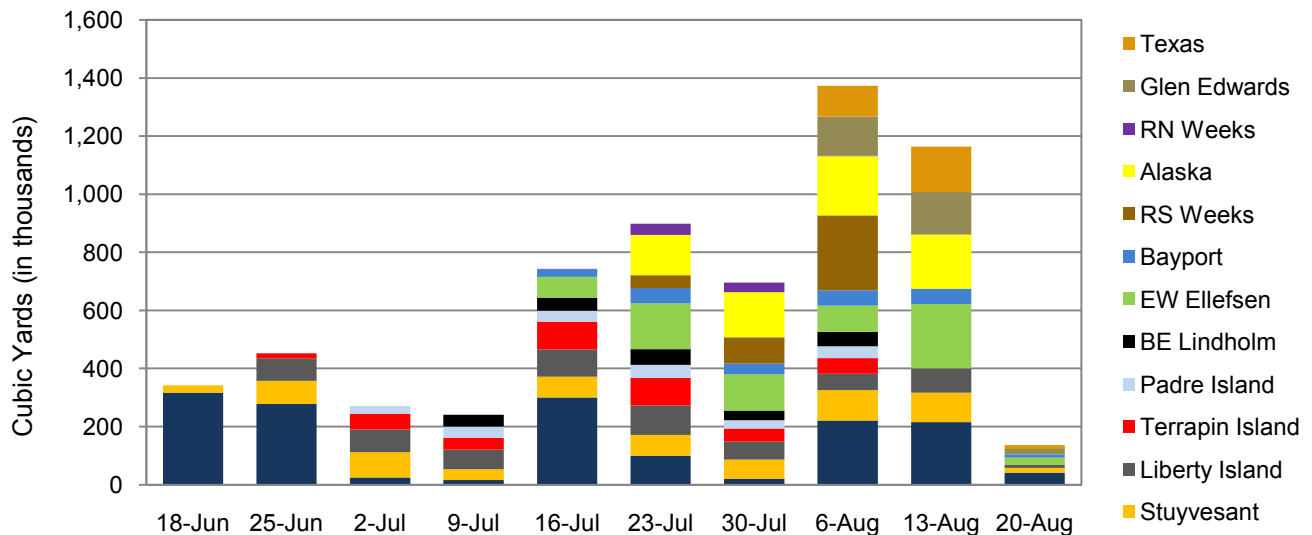

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,531,586	
Cutter EW Ellefsen	692,048	
Cutter RS Weeks *	391,350	
Cutter Alaska	683,863	
Cutter Texas	273,765	
Hopper Stuyvesant	660,985	96
Hopper Liberty Island	628,538	139
Hopper Bayport	232,395	60
Hopper Glen Edwards	299,916	29
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	28
Total	6,313,939	631

* Demobilized on or before August 6th.

Progress by Berm and Borrow Operations (cubic yards)

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	16-Aug-10	21-Oct-10	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	1-Nov-10	8,345,969	1,991,904	6,354,065	23.87%
W8	6-Sep-10	28-Nov-10	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	27-Aug-10	1,130,870	727,570	403,300	64.34%
W10	24-Aug-10	21-Sep-10	1,327,543	0	1,327,543	0.00%
W11	13-Oct-10	1-Nov-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	18-Oct-10	13,088,593	3,594,465	9,494,128	27.46%
Totals			31,081,372	6,313,939	24,767,433	20.31%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

Progress by Berm (linear feet)

Location	Forecast (LF)	Under Construction (LF)*	To Go (LF)	Complete
E3	35,482	0	35,482	0.00%
E4	80,520	9,330	72,800	9.59%
W8	30,096	0	30,096	0.00%
W9	12,144	3,700	8,854	27.09%
W10	14,256	0	14,256	0.00%
W11	11,616	0	11,616	0.00%
Totals	184,114	13,030	173,104	5.98%

Note: Under normal field conditions, berm is advancing approximately 500 LF per reach per day.

*Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 Berm Construction – August 14, 2010



W9 Berm – August 14, 2010
