



Barrier Berm Project – Daily Report

Day 85

Document: 139551-PMD-085-S

Date Prepared: August 25, 2010

Prepared by:
Shaw Environmental & Infrastructure Group



E4 North Berm – August 24, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 24 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	54,680	
Cutter Texas	15,658	
Subtotal East	70,338	
West		
Cutter California	35,016	10 Scows
Cutter EW Ellefsen	70,682	
Hopper Stuyvesant	15,153	2
Hopper Liberty Island	9,361	2
Hopper Bayport	0	0
Hopper Glenn Edwards	9,763	1
Subtotal West	139,975	5
Total	210,313	5

- Mechanical repairs continue on Hopper Bayport; anticipated return to service today.

Today – 25 August

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North and W9.
- Texas mobilizing to W10 for berm placement operations.

Tomorrow – 26 August

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- Completion of W9 berm construction forecast for 15 September.
- Start of W10 berm construction forecast to begin 8 September.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Variations from current fleet configuration.

All Dredges Weekly Volume

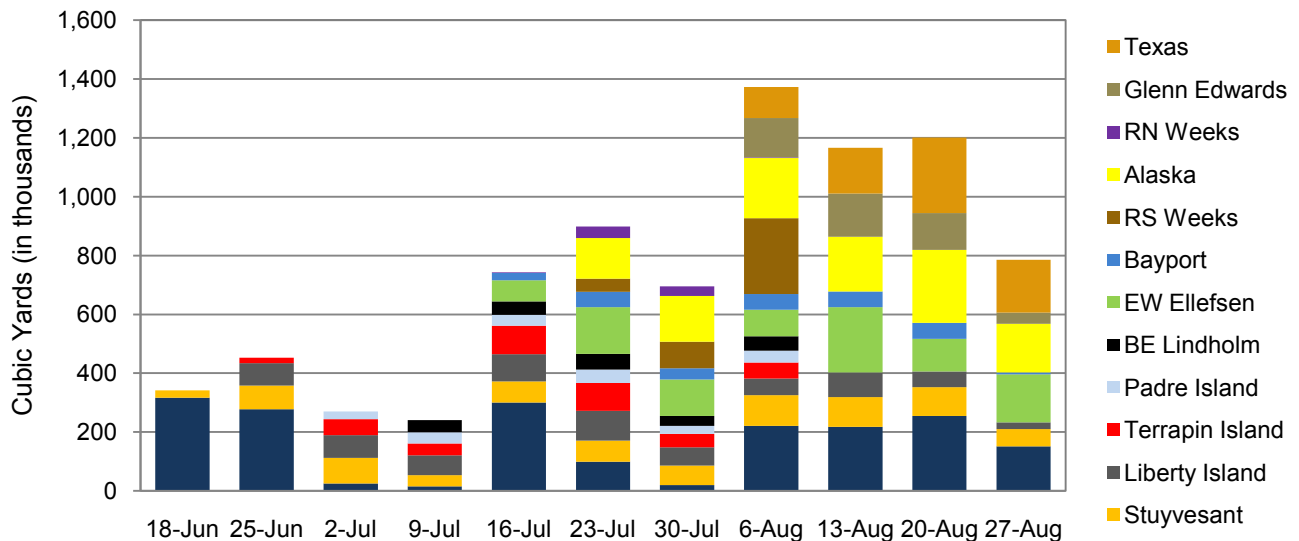

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,898,477	
Cutter EW Ellefsen	939,917	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,096,033	
Cutter Texas	698,291	
Hopper Stuyvesant	802,356	123
Hopper Liberty Island	694,802	155
Hopper Bayport	283,005	77
Hopper Glenn Edwards	444,410	46
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	8,168,134	709

* Demobilized on or before August 6th.

Progress by Berm and Borrow Operations (cubic yards)

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	6-Jan-11	10-Apr-11	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	11-Feb-11	8,345,969	2,828,600	5,517,369	33.89%
W8	5-Nov-10	25-Jan-11	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	15-Sep-10	1,130,870	975,439	155,431	86.26%
W10	8-Sep-10	14-Nov-10	1,327,543	0	1,327,543	0.00%
W11	20-Nov-10	21-Dec-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	7-Dec-10	13,088,593	4,364,095	8,724,498	33.34%
Totals			31,081,372	8,168,134	22,913,238	26.28%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

Progress by Berm (linear feet)

Location	Forecast (LF)	Under Construction (LF)*	To Go (LF)	Complete
E3	35,482	0	35,482	0.00%
E4	80,520	12,314	68,206	15.29%
W8	30,096	0	30,096	0.00%
W9	12,144	5,050	7,094	41.58%
W10	14,256	0	14,256	0.00%
W11	11,616	0	11,616	0.00%
Totals	184,114	17,364	166,750	9.43%

Note: Data subject to one day lag. Under normal field conditions, berm is advancing approximately 500 LF per reach per day.

*Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 South Berm – August 24, 2010



E4 North Berm Construction – August 24, 2010
