



Barrier Berm Project – Daily Report

Day 88

Document: 139551-PMD-088-S

Date Prepared: August 28, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W9 Berm – August 26, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 27 August

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	34,271	
Subtotal East	34,271	
West		
Cutter California	14,654	5 Scows
Cutter EW Ellefsen	3,111	
Cutter Texas	0	
Hopper Stuyvesant	7,528	1
Hopper Liberty Island	9,320	2
Hopper Bayport	3,726	1
Hopper Glenn Edwards	9,671	1
Subtotal West	48,010	5
Total	82,281	5

- Low production day due to the inclement weather.

Today – 28 August

- Borrow operations at Pass a Loutre and West to continue pending weather.
- Berm placement operations to continue on E4 North and W9 pending weather.

Tomorrow – 29 August

- Today's operational activities to continue through tomorrow.


Near-Term Milestones

- Completion of W9 berm construction forecast for 14 September.
- Start of W10 berm construction forecast to begin 5 September.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Variations from current fleet configuration.

All Dredges Weekly Volume

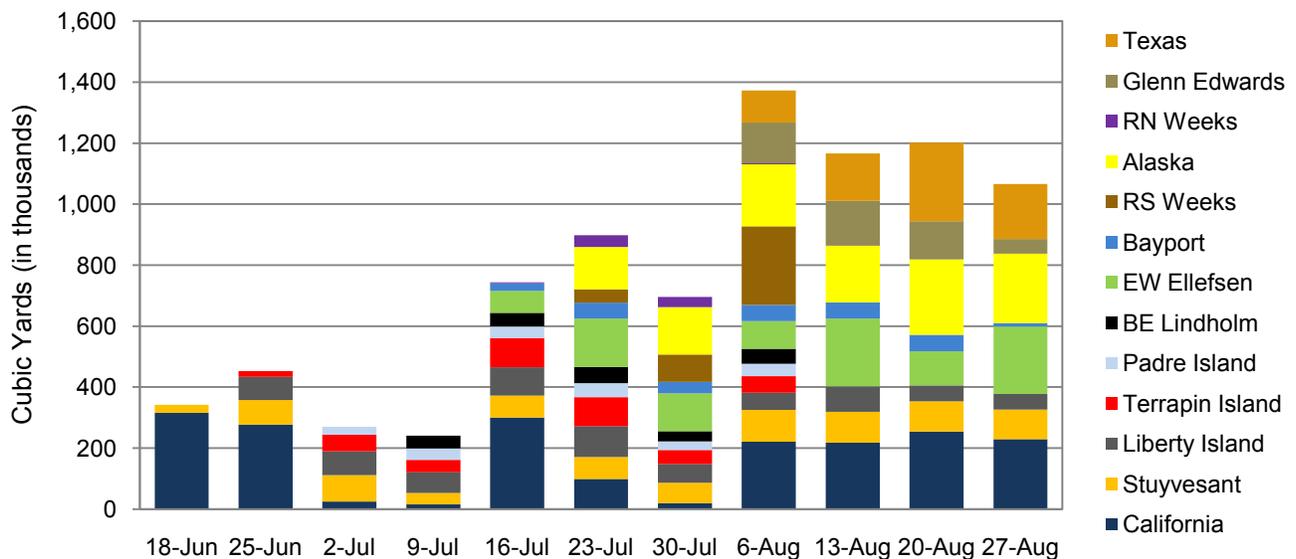

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	1,976,991	
Cutter EW Ellefsen	998,521	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,159,592	
Cutter Texas	698,291	
Hopper Stuyvesant	840,037	128
Hopper Liberty Island	722,822	161
Hopper Bayport	286,731	78
Hopper Glenn Edwards	454,081	47
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	8,447,909	722

* Demobilized on or before August 6th.

Progress by Berm and Borrow Operations (cubic yards)

Location	Start	End	Forecast (cy)	Actual (cy)	To Go (cy)	Complete
E3	6-Jan-11	10-Apr-11	3,304,107	0	3,304,107	0.00%
E4	14-Jun-10 A	11-Feb-11	8,345,969	2,892,159	5,453,810	34.65%
W8	5-Nov-10	25-Jan-11	2,802,588	0	2,802,588	0.00%
W9	18-Jul-10 A	15-Sep-10	1,130,870	1,034,043	96,827	91.44%
W10	8-Sep-10	14-Nov-10	1,327,543	0	1,327,543	0.00%
W11	20-Nov-10	21-Dec-10	1,081,702	0	1,081,702	0.00%
Borrow Operations	16-Jun-10 A	7-Dec-10	13,088,593	4,521,707	8,566,886	34.55%
Totals			31,081,372	8,447,909	22,633,463	27.18%

Note: Percent complete of material handled represents only 1 of 3 elements of percent complete for the overall project.

Progress by Berm (linear feet)

Location	Forecast (LF)	Under Construction (LF)*	To Go (LF)	Complete
E3	35,482	0	35,482	0.00%
E4	80,520	13,432	67,088	16.68%
W8	30,096	0	30,096	0.00%
W9	12,144	5,450	6,694	44.88%
W10	14,256	0	14,256	0.00%
W11	11,616	0	11,616	0.00%
Totals	184,114	18,882	165,232	10.26%

Note: Data subject to one day lag. Under normal field conditions, berm is advancing approximately 500 LF per reach per day.

*Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 South Berm – August 26, 2010



E4 North Berm Construction – August 26, 2010
