



# Barrier Berm Project – Daily Report

## Day 42

---

**Document:** 139551-PMD-042-S

**Date Prepared:** July 13, 2010

**Prepared by:** Shaw's Environmental & Infrastructure Group

---



*Spider barge – July 10, 2010*

# Barrier Berm Project 139551 – Project Summary

## Yesterday – 12 July

Vessel	Cubic Yards (CY) Handled	Hopper Loads
<b>East</b>		
Cutter California	63,000	n/a
Hopper Liberty Island	13,349	4
Hopper Terrapin Island	16,051	5
<b>Subtotal East</b>	<b>92,400</b>	<b>9</b>
<b>West</b>		
Cutter EW Ellefsen	21,227	n/a
Hopper Stuyvesant	11,268	2
Hopper Padre Island	5,021	2
Hopper BE Lindholm	8,844	3
<b>Subtotal West</b>	<b>46,360</b>	<b>7</b>
<b>Total</b>	<b>138,760</b>	<b>16</b>

## Today – 13 July

- Move of Stuyvesant to support East hopper operations planned to take place today.
- Kickoff for Hopper Bayport to take place today with operations commencing following meeting.

## Tomorrow – 14 July

- Hopper RN Weeks to commence operations after kickoff.


## Near-Term Milestones

- Forecast completion of first mile of berm approx. 26 July.
- Start of E4 South berm construction scheduled to begin 15 July.

## Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.
- Cost and schedule impacts due to weather and operational delays, trend book issuance by July 16, 2010.

**Fleet Mix**  
(total vessel count)

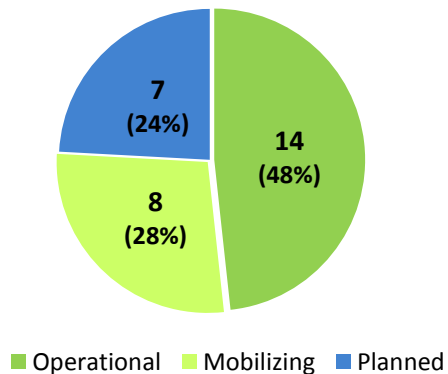

**All Dredges Weekly Volume**

