



Denison Rewind



Generator
Rewind

Denison
Powerhouse





Denison Rewind



Rewind Contract

- Awarded to Alstom May 2004
- \$4.56 million
- 526 calendar days



Denison Rewind



Original Schedule

- Start Unit #1 November 2004
- Complete Unit #1 May 2005

- Start Unit #2 September 2005
- Complete Unit #2 March 2006



Denison Rewind



Actual Activity Dates

- Start Unit #1 November 2004
- Complete Unit #1 November 2005

- Start Unit #2 December 2005
- Complete Unit #2 May 2006



Denison Rewind



Issues Unit 1

- Delivery Problems of Critical Materials
- Improper Installation of Stator core
- Winding Installation Problems



Denison Rewind





Denison Rewind





Unit 1





Unit 1






Unit 1





Unit 1

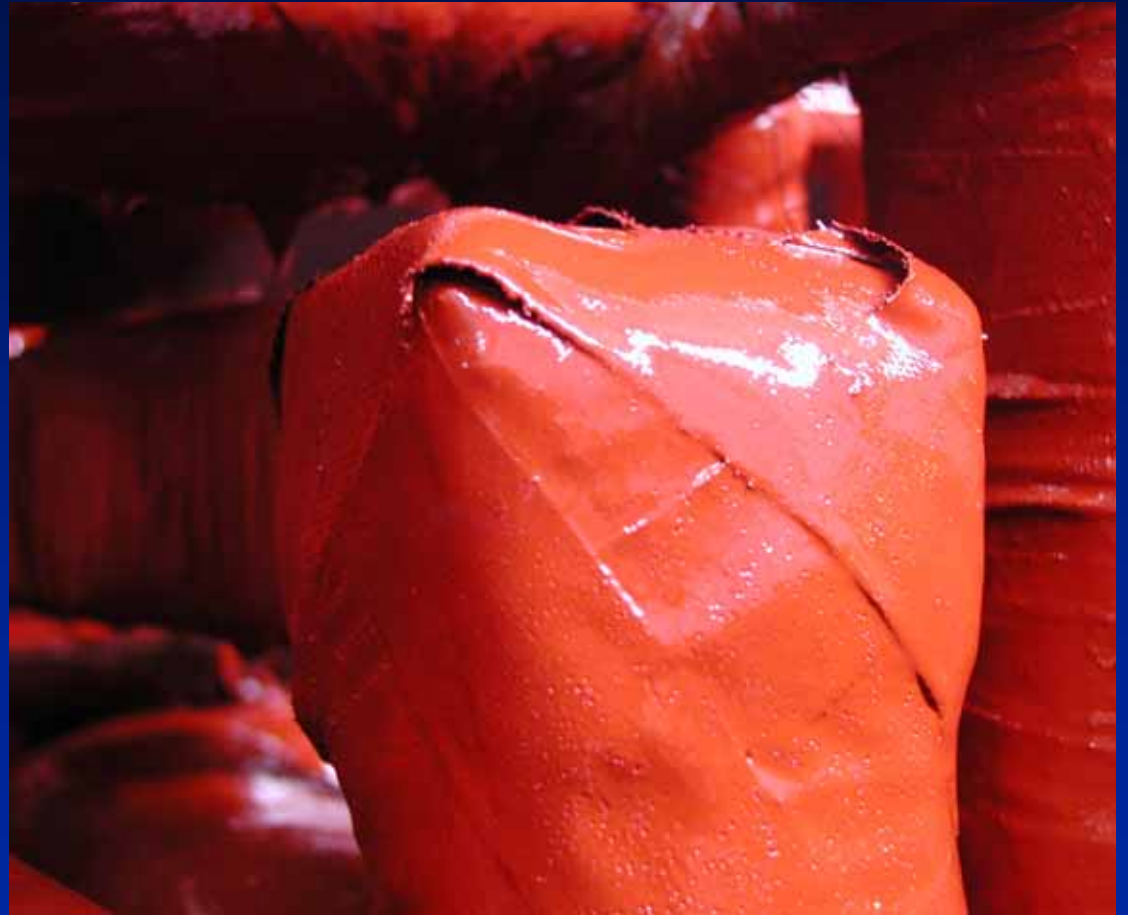



Unit 1





Unit 2





Unit 1





Unit 2





Denison Rewind



- ◆ Lessons Learned to make Unit 2 a Success
 - Qualified site manager
 - Empowered local site management
 - Consistent and Qualified QC management
 - Enforced workmanship standards



Unit 2

