

# **Barrier Berm Project – Daily Report**

**Day 132** 

**Document:** 139551-PMD-132-S

Date Prepared: October 11, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



E4 North Berm - October 7, 2010

## **Barrier Berm Project 139551 – Daily Information**

#### Yesterday – 10 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads		
East				
Cutter Alaska	25,547			
Subtotal East	25,547			
West				
Cutter California	42,262	14 Scows		
Cutter EW Ellefsen	54,617			
Cutter Texas	17,900			
Hopper Glenn Edwards	20,179	2		
Subtotal West	134,958	2		
Total	160,505	2		

· EW Ellefsen continued pad construction on W8.

#### Today – 11 October

- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.
- The Glenn Edwards will be shutting down for repairs and will be back Wednesday 10/13


#### Tomorrow - 12 October

Today's operational activities to continue through tomorrow.

#### **Potential Schedule Variability Items**

• Final permit requirements, third party agency requirements.

#### **All Dredges Weekly Volume**

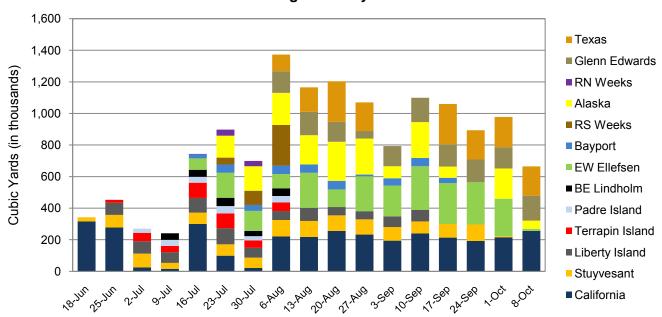

1

# **Barrier Berm Project 139551 – Cumulative Information**

## Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,365,119	
Cutter EW Ellefsen	2,315,985	
Cutter RS Weeks *	391,350	
Cutter Alaska	1,831,571	
Cutter Texas	1,567,433	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,352,641	136
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	14,228,072	925

<sup>\*</sup> Demobilized from Project.

## **Progress by Berm and Borrow Operations (volume)**

Location	Actuals (CY)
E3	0
E4	3,565,358
W8	68,026
W9	2,281,314
W10	867,922
W11	0
Borrow Operations	7,445,452
Totals	14,228,072

## Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	19,858
W8	0
W9	12,449
W10	5,050
W11	0
Totals	37,357

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W9 & W10 - October 7, 2010



W10 Berm Operations - October 7, 2010

