



HIGHWAY CONSTRUCTION PLAN

2005 – 2007 State Biennium (July 1, 2005 – June 30, 2007)

Table of Contents

ODOT Regions Programs and Estimated Expenditures Highway Construction Plan Layout Project Listings By County Baker Benton Clackamas Clatsop Columbia Coos
Highway Construction Plan Layout Project Listings By County Baker Benton Clackamas Clatsop Columbia
Highway Construction Plan Layout Project Listings By County Baker Benton Clackamas Clatsop Columbia
Baker Benton Clackamas Clatsop Columbia
Baker Benton Clackamas Clatsop Columbia
Benton Clackamas Clatsop Columbia
Clackamas Clatsop Columbia
Clatsop
Columbia
Crook
Curry
Deschutes
Douglas
Gilliam
Grant
Hood River
Jackson
Jefferson
Josephine
Klamath
Lake
Lane
Lincoln
Malheur
Marion
Morrow
Multnomah
Polk
Sherman
Tillamook
Umatilla
Union
Various
Wallowa
Wasco
Washington
Wheeler
Yamhill
Duoguam Cummanias
Program Summaries
STIP Project Lifecycle
Project Cost Profile Graphs
Pavement Preservation Project
Modernization Project
iviodomization i roject

Introduction

The Oregon Department of Transportation prepared the 2005-2007 Highway Construction Plan in accordance with ORS 184.654 to 184.666. The 2005-2007 Highway Construction Plan is a component of the department's budget for the 2005-2007 biennium.

The Highway Construction Plan describes specific projects the department will implement during the 2005-2007 biennium in five components of its Highway Program: Bridge, Highway Safety, Modernization, Operations and Pavement Preservation. Projects in the Highway Construction Plan were selected using the public involvement process of the Statewide Transportation Improvement Program (STIP), including consultation with local governments.

As the department implements its 2005-2007 biennial budget, the department will make status reports on implementation of the Plan to the Legislature after the end of each quarter. The quarterly status reports will also notify the Legislature of any projects that the department intends to implement that were not listed in this initial 2005-2007 Highway Construction Plan.

The Plan lists the projects that are located in each county. The entry for each project provides the project location, a brief description, its work type (Bridge, Highway Safety, Modernization, Operations and Pavement Preservation), and its current status. A project's status is:

- <u>Construction Complete:</u> Project is complete, but may still be pending final payment to the contractor.
- <u>Under Construction:</u> Construction work has started, or is scheduled to start, and a contractor has been awarded the construction contract.
- <u>Construction Funding Committed:</u> Project is either anticipated to go to contract within the biennium or pre-construction work is anticipated to begin during this time frame.
- <u>Under Development:</u> Project has received Oregon Transportation Commission approval to begin preliminary development work, but is not approved for construction funding.

Project names and work descriptions have been modified throughout the document in order to improve readability. Because of this, some projects may not appear consistently in prior department publications.


If you have questions, comments, or would like more information about this publication or the projects listed in it, please contact Victor Dodier, ODOT Government Relations Section, at 503-986-3422.

Oregon Department of Transportation Regional Boundaries

The five ODOT Region boundaries are outlined below:

- **<u>Region 1</u>**: Portland metro and surrounding areas, south to Wilsonville, east to Hood River.
- **Region 2:** Northwest Oregon including Astoria south to Florence, east including all of Lane County and north to the break between Marion and Clackamas Counties.
- **Region 3:** Southwest Oregon including Douglas County in the north, to the California border on the south, and east to the borders of Deschutes and Klamath Counties.
- **Region 4:** Central Oregon from the Washington border south to the California border, west including all of Jefferson, Deschutes, Wasco and Klamath Counties, and east including Gilliam, Wheeler, Crook and Lake Counties.
- **Region 5:** Eastern Oregon from the Washington border south to the California border, west including Grant and Morrow Counties and Harney County and east to the Idaho border.

State Highway Mileage & Population by ODOT Region

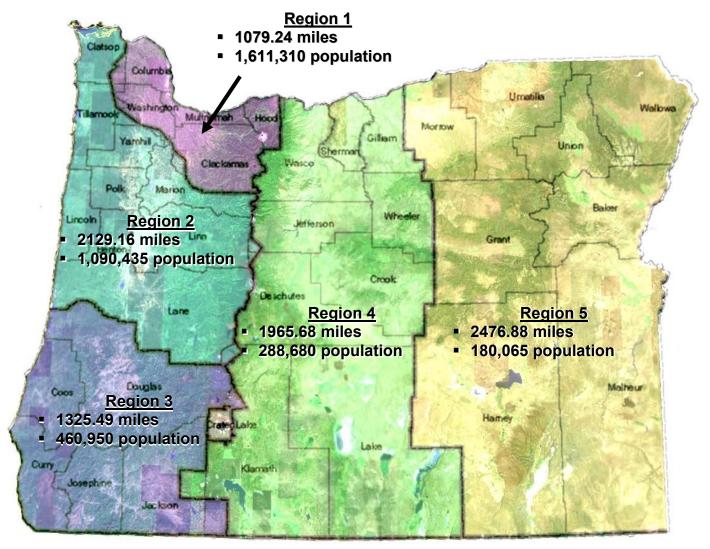

8976.45 total highway miles


3,631,440 total population

Programs and Estimated Expenditures (dollar amounts rounded)

(biennial)

	(bienniai)
Bridge Program - includes preservation of the bridges, tunnels and culverts on the state highway system.	\$533.6 M
Modernization Program - includes improvements that add capacity to highways, including but not limited to new or widened lanes and new bypasses.	\$453.8 M
Operations Program - includes improving the efficiency of existing highways through such means as traffic signaling systems, driver communication and ramp metering.	\$46 M
Pavement Preservation Program - includes paving, striping and reconstruction designed to add useful life to existing highways.	\$231.2 M
Safety Program - includes providing engineering solutions to accident problems on state and local highways.	\$54.5 M
Maintenance Program – includes keeping existing highways safe and usable for the traveling public through such means as repair, snow and ice removal, vegetation clearance, striping, signal repair and lighting. Includes Emergency Relief Program.	\$299.1 M
Special Programs - includes but is not limited to bicycle and pedestrian facility projects, environmental services and salmon and watershed projects.	\$175.3 M
Local Government - includes payments to cities, counties and metropolitan planning organizations.	\$214.9 M
Utility / Right of Way - includes issuing permits, inspection and review of work by utility companies on our right of way.	\$4.5 M

Highway Construction Plan Layout - Sample Project -

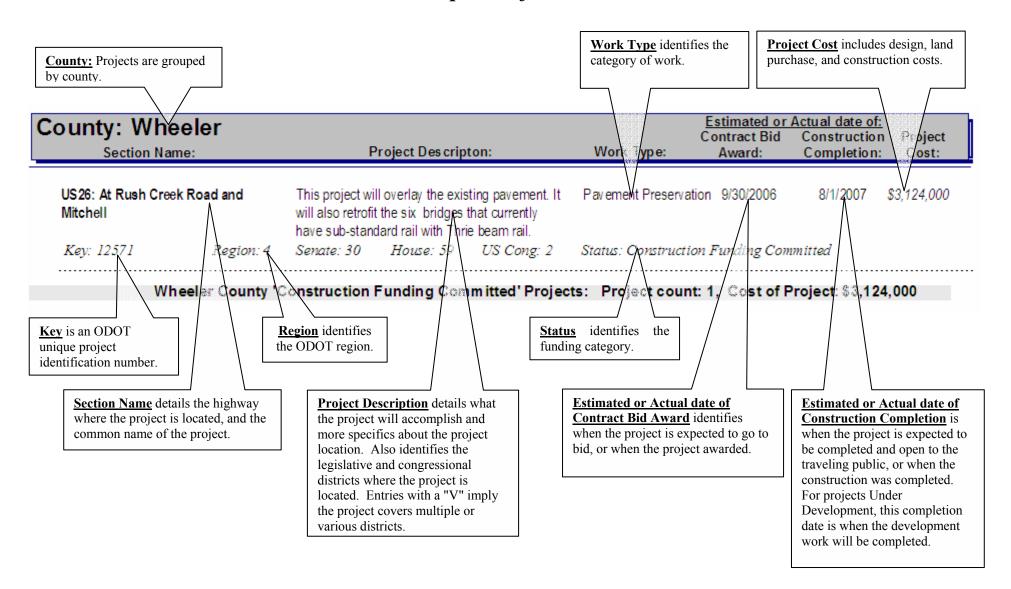

			Count	y: Baker	<u> </u>	stimated or a	Actual date of: Construction	
Section Name:		Pı	roject Descrip	ton:	Work Type:	Award:	Completion:	Cost:
OTIA III- I-84 Bridge Bund	lle 204		repair Bridge #s BE, 08423W, 079		Bridge	3/10/2005	9/21/2005	\$1,879,191
Key: 14026	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Constru	uction		
I-84 Pleasant Valley Intg. #8279E # 8279W	Bridges	and repave the interchange (#8		leasant Valley	Bridge	11/21/2002	10/31/2007	\$16,278,266
Key: 10473	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Constr	uction		
OR-7 Salisbury Jct Bak	er City	entire section to	place chipseal to preserve the extended to bridge rails on	disting pavement.	Pavement Preservation	1/13/2005	8/31/2005	\$294,734
Key: 11838	Region: 5	Senate: 30	House: 58	US Cong: 2	Status: Under Constru	uction		
OR86: Powder River Brid	ge	This project will	replace Bridge	# 02807.	Bridge	11/18/2004	4/30/2006	\$1,151,714
Key: 12796	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Constr	uction		
US26 Grant Co Line-Malh and ECL Burns	eur Co Line	This project will	provide paveme	ent preservation.	Pavement Preservation	3/31/2005	8/31/2006	\$3,071,561
Key: 14090	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Constr	uction		
	Bal	cer County 'Ui	nder Constru	uction' Project	s: Project count: 5,	Cost of Pr	ojects: \$22,67	75,465
OTIA III- I-84: Burnt River Interchange-Bundle 203	-Lime		replace bridge r 09354 and repail		Bridge	9/1/2006	8/1/2009	\$13,625,000
Key: 14116	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Construction	Funding Com	mitted	
OTIA III- I-84: Irrigon Jun Hilgard Interchange	ction-	bridges 00449A	replace bridge (, 08498W, 0849 / and 08931E (B		Bridge	5/11/2006	2/1/2009	\$9,990,000
Key: 14028	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Construction	Funding Com	mitted	
OR 7: Cambell Ave - I 84		Pavement prese	ervation		Pavement Preservation	2/23/2006	Not Available	\$81,000
Key: 12638	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Construction	Funding Com	mitted	
OR7: Campbell-I-84/Ceda Signal	r Street	traffic signal at t	reconstruct the the Cedar Street ent preservation.	signal and	Pavement Preservation	9/1/2006	12/1/2007	\$1,103,000
Key: 14196	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Construction	Funding Com	mitted	
OR 86: Richland City Sec	tion	This project will sidewalks, curb	rebase, pave, c s and storm sew		Modernization	4/27/2006	12/1/2007	\$3,227,000
				•				

Baker County 'Construction Funding Committed' Projects: Project count: 5, Cost of Projects: \$28,026,000

Total Project Count for Baker County: 10, Total Cost of Projects: \$50,701,465

Section Name:		Р	County: Bentor Project Descripton:			Estimated or Actual d Contract Bid Constr Award: Comp		
OTIA I/II- Alsea River (Ha Bridge	yden Rd.)	Project will rep	lace structure br.	#14538.	Bridge	9/30/2003	11/1/2003	\$721,000
Key: 12439	Region: 2	Senate: 12	House: 23	US Cong: 4	Status: Construction	Complete		
OTIA I/II- Flat Creek (Old Bridge	River Rd.)	Project will rep	lace structure br.	#14185.	Bridge	9/30/2004	11/1/2003	\$611,000
Key: 11975	Region: 2	Senate: 12	House: 23	US Cong: 4	Status: Construction	Complete		
OTIA I/II- OR-99W Elks D Blvd. (Corvallis)	rive - Circle		I travel lanes, into		Modernization	9/30/2003	7/9/2004	\$800,000
Key: 12920	Region: 2	Senate: 08	House: 16	US Cong: 5	Status: Construction	Complete		
	Benton	County 'Cons	struction Con	nplete' Project	ts: Project count: 3	, Cost of Pr	ojects: \$2,132	2,000
OTIA I/II- OR-99W Territo Improvements (Monroe)	rial Hwy	Project will wid inch pavement	en the shoulders overlay.	and provide a 4	Pavement Preservation	n 6/30/2004	9/14/2005	\$2,426,756
Key: 12378	Region: 2	Senate: 08	House: 16	US Cong: 5	Status: Under Constr	uction		
	Bei	nton County '	Under Const	ruction' Projec	cts: Project count:	1, Cost of P	roject: \$2,420	6,756
OR34: Willamette River (Avenue) bridge	Van Buren	This project wil	I paint bridge #02	2728	Bridge	8/2/2006	12/1/2007	\$1,440,000
Key: 12794	Region: 2	Senate: 08	House: 15	US Cong: 5	Status: Construction	Funding Com	mitted	
OR99W: Miller Creek Bri	dge	This project wil	I replace Bridge	#01588.	Bridge	12/14/2006	8/1/2008	\$2,185,000
Key: 12800	Region: 2	Senate: 12	House: 23	US Cong: 4	Status: Construction	Funding Com	mitted	
US20 @ Granger Rd and Independence Rd	@	This project wil	I improve interse	ctions.	Safety	4/12/2007	3/1/2008	\$246,000
Key: 12665	Region: 2	Senate: 08	House: 15	US Cong: 5	Status: Construction	Funding Com	mitted	
OTIA I/II- Philomath Cou	plet Unit 1	Project will con downtown Phil	struct Unit 1 of a omath.	couplet through	Modernization	6/30/2004	Not Available	\$3,011,000
Key: 11670	Region: 2	Senate: 08	House: 16	US Cong: 4	Status: Construction	Funding Com	mitted	
OTIA I/II- US20: Philomat	th Couplet		I construct couple TS shown, contri t work)		Modernization	12/31/2005	4/1/2008	\$8,944,000
Key: 13572	Region: 2	Senate: 08	House: 16	US Cong: 4	Status: Construction	Funding Com	mitted	
Benton	County 'Co	onstruction F	unding Comr	nitted' Project	ts: Project count: 5	, Cost of Pr	ojects: \$15,82	26,000
OR34 Van Buren St. Brid (Corvallis)	lge Replace.	Documents, ar	I produce the End ad construction w umber. Environm work	ill be under a	Modernization	4/14/2010		\$1,500,000
Key: 12827	Region: 2	Senate: 08	House: 15	US Cong: 5	Status: Under Develo	pment		
US20: Mary's river - mp 4	13.05	construction wi	I produce the Fin II be under a diffe ay old pavement	erent Key	Pavement Preservation	12/14/2006		\$53,000
Key: 12809	Region: 2	Senate: 12	House: 23	US Cong: 5	Status: Under Develo	opment		
US20: Clem Rd Old Blo	odgett hwy	construction w	I produce the Fin II be under a differ project will overlay	erent Key	Pavement Preservation	12/14/2006		\$310,000
Key: 12807		Senate: 05	House: 10	US Cong: 5				

Benton County 'Under Development' Projects: Project count: 3, Cost of Projects: \$1,863,000

Total Project Count for Benton County: 12, Total Cost of Projects: \$22,247,756

			Count	y: Clacka	mas	Estimated or a	Actual date of: Construction	
Section Name:		Р	roject Descrip	•	Work Type:	Award:	Construction:	
OTIA I/II- Arndt Road Imp (Clackamas County) Ph		Project will wide Knights Bridge	en and realign th Road	e intersection at	Modernization	3/31/2005	9/30/2003	\$1,200,000
Key: 13061	Region: 2	Senate: 14	House: 18	US Cong: 5	Status: Construction	Complete		
I-205 @ Sunnybrook Inte (Phase 1)	rchange		struct a split diar v structure over l	mond interchange -205 in East	Modernization	8/22/2002	12/15/2003	\$24,218,461
Key: 12522	Region: 1	Senate: 26	House: 51	US Cong: 3	Status: Construction	Complete		
(Clackamas	County 'Cons	truction Con	nplete' Projects	s: Project count: 2	, Cost of Pr	ojects: \$25,4°	18,461
OTIA I/II- Sunnyside Rd. 122nd-152nd Widening	(Phase 2)	Project will wide sidewalks and	en Sunnyside Ro bike lanes.	d. to 5 lanes with	Modernization	3/31/2005	Not Available	\$29,582,000
Key: 12399	Region: 1	Senate: 26	House: 51	US Cong: 3	Status: Under Const	ruction		
OTIA I/II- Hwy 211/Hwy 2 Intersection Improvemen			vide left-turn lane d northbound an	es on all d westbound right	Modernization	3/31/2004	Not Available	\$1,324,000
Key: 12912	Region: 1	Senate: 09	House: 18	US Cong: 5	Status: Under Const.	ruction		
OR-212 Rock Crk. Jct - F	Richey Rd.	Clackamas-Bo	ichey Road. The s, add guardrails	ween Rock Creek	Pavement Preservatio	n 9/26/2002	11/30/2004	\$6,571,337
Key: 10665	Region: 1	Senate: 26	House: 51	US Cong: 3	Status: Under Const	ruction		
OR-213 S. Liberal Way - Liberal/Molalla Rd.		intersection wit section of Mola approximately channelizations new Molalla Av	s between S. Libere. intersection. I Liberal Way turni	ouild a new ect Hwy 213 Build two left turn eral Way and the Improve the SB	Safety	2/26/2004	9/30/2005	\$3,208,574
Key: 04036	Region: 1	Senate: 09	House: 18	US Cong: 5	Status: Under Const	ruction		
OR 224: East Portland Fr Evelyn Street	eeway - SE		l add an eastbou E Evelyn on Hwy		Safety	5/18/2005	12/31/2005	\$3,313,780
Key: 12158	Region: 1	Senate: 20	House: V	US Cong: 3	Status: Under Const	ruction		
US-26 @ Kelso Road		and through mo	ovements from K nes. Includes sig	on, close left turn lelso Rd. and add gnalizing US 26 &	Safety	3/1/2004	10/31/2005	\$1,793,446
Key: 11928	Region: 1	Senate: 26	House: 52	US Cong: 3	Status: Under Const	ruction		
OTIA III- US-26 Zig Zag to Rhododendron (Phase 2)			en the Zig Zag R ing roadway to R		Modernization	7/24/2003	12/31/2004	\$10,103,600
Key: 12171	Region: 1	Senate: 26	House: 52	US Cong: 3	Status: Under Const.	ruction		
Multipor U-Xing to Timbe	erline Hwy	shortened and be updated to i	hway 26 passing design of interse mprove safety at the east end of C	cting roads will the intersection	Safety	3/25/2004	11/30/2005	\$2,443,532
	Region: 1	Senate: 28	House: 56	US Cong: 3		ruction		

Clackamas County 'Under Construction' Projects: Project count: 8, Cost of Projects: \$58,340,269

				ty: Clacka	illias (Contract Bid	Actual date of: Construction	
Section Name		Р	roject Descrip	oton:	Work Type:	Award:	Completion:	Cost:
OTIA I/II- Boeckman Re Connection	d Tooze Rd.	termination nea of 110th Avenu Tooze Road fro Ferry Road. Pro direction, left tu	e and Tooze Room 110th Avenu	o the intersection and. Construct e to Grahams travel lane in each sections and	Modernization	9/30/2005	10/1/2007	\$15,693,000
Key: 12400	Region: 1	Senate: 13	House: 26	US Cong: 5	Status: Construction	Funding Com	mitted	
I 205: Willamette River Br Pacific Hwy		This project will lanes between restripe.	l overlay hwy, a Stafford Road a	nd add auxilary nd I-5, and	Pavement Preservation	n 10/26/2006	4/1/2009	\$46,042,000
Key: 12874	Region: 1	Senate: 19	House: 37	US Cong: 5	Status: Construction	Funding Com	mitted	
1-5 Wilsonville Road - River	Willamette	rutting in this se upgrade the gu	I provide an ove ection of Intersta ardrail end secti to current stand	ons and other	Pavement Preservation	n 9/7/2006	4/1/2007	\$1,849,000
Key: 12837	Region: 1	Senate: 09	House: 18	US Cong: 5	Status: Construction	Funding Com	mitted	
OR212: Tong Rd Wy	East Rd.		l close existing ⁻ 'east, will also a	Fong Rd. and dd channelization.	Safety	2/22/2007	8/1/2008	\$3,393,000
Key: 12877	Region: 1	Senate: 10	House: 19	US Cong: 5	Status: Construction	Funding Com	mitted	
OR213: So. Conway Dr. Rd.	r So. Henrici	This project will lane.	l construct a cor	ntinuous left turn	Safety	11/16/2006	6/1/2008	\$5,740,000
Key: 12876	Region: 1	Senate: 20	House: 39	US Cong: 5	Status: Construction	Funding Com	mitted	
OR224: SE 17th - East	Portland Fwy	This project will	l overlay and str	ipe roadway.	Pavement Preservation	n 2/23/2006	5/1/2007	\$4,107,000
Key: 12872	Region: 1	Senate: 20	House: 60	US Cong: 3	Status: Construction	Funding Com	mitted	
OR99E: Kellogg Cr. Mi	9.19	Includes sidewa (possibly close reconfiguring th	I overlay roadwa alk infill, access existing drivewa ne 99E and Rive improved opera	management ays), includes	Pavement Preservation	n 1/25/2007	6/1/2008	\$5,731,000
Key: 12855	Region: 1	Senate: 21	House: 41	US Cong: 3	Status: Construction	Funding Com	mitted	
OR99E: Pacific Hwy Ea Territorial Rd.	ast @	crossing and a	I reconstruct inte		Safety	4/27/2006	9/1/2007	\$2,973,000
Key: 12904	Region: 1	Senate: 20	House: 39	US Cong: 5	Status: Construction	Funding Com	mitted	
Regoin 1 Rural Variabl Sign	e Message	This project will sign.	l install a new va	ariable message	Operations	8/24/2006	8/1/2007	\$300,000
Key: 13701	Region: 1	Senate: 26	House: 52	US Cong: 3	Status: Construction	Funding Com	mitted	

Clackamas County 'Construction Funding Committed' Projects: Project count: 9, Cost of Projects: \$85,828,000

Section Name	:	F	Count Project Descrip	ty: Clacka	Estimated or Contract Bid Award:	Actual date of: Construction Completion:	Project Cost:	
OR211: Meadowbrook	- Hult Rd.	construction w	Il produce the Fir ill be under a diffo project will overla	erent Key	Pavement Preserva	tion 9/17/2007	;	\$340,000
Key: 12871	Region: 1	Senate: 09	House: 18	US Cong: 5	Status: Under Dev			
US-26 West Ski Bowl - Camp Loop	Government	construction w	Il produce the Fir ill be under a diffo project will realigr d turn lane, signir	erent Key n intersections;	Safety	2/22/2007	\$	\$427,000
Key: 11967	Region: 1	Senate: 26	House: 52	US Cong: 3	Status: Under Dev	elopment		
US26: Wildwood - Wer	nme	construction w	Il produce the Fir ill be under a diffo project will constr	•	Safety	11/8/2007	\$	\$437,000
Key: 12840	Region: 1	Senate: 26	House: 52	US Cong: 3	Status: Under Dev	elopment		

Clackamas County 'Under Development' Projects: Project count: 3, Cost of Projects: \$1,204,000

Total Project Count for Clackamas County: 22, Total Cost of Projects: \$170,790,729

Castian Name				y: Clatso	P c	ontract Bid	Actual date of: Construction	Project
Section Name:			roject Descrip		Work Type:	Award:	Completion:	
Astoria Warning Signs		•	all warning signs		Safety	4/22/2004	9/30/2004	\$173,608
Key: 13574	Region: 2	Senate: 16	House: 31	US Cong: 1	Status: Construction	Complete		
OTIA I/II- 12th Avenue Bridges - Necanicum River			ace bridge # 073 urrent seismic st	309 with a 2-span tandards.	Bridge	10/4/2003	5/31/2004	\$1,388,000
Key: 13068	Region: 2	Senate:	House:	US Cong:	Status: Construction	Complete		
US-101 @ Cannon Beack Entrance	h North			nange at the north entrance to	Safety	11/15/2001	10/31/2003	\$10,361,23
Key: 09261	Region: 2	Senate: 16	House: 32	US Cong: 1	Status: Construction	Complete		
US-26 Mail Creek Culver	t	This project wil	replace culvert	(#08093A)	Bridge	7/30/2003	6/30/2004	\$1,433,411
Key: 12140	Region: 2	Senate: 16	House: 32	US Cong: 1	Status: Construction	Complete		
	Clatsop	County 'Cons	truction Con	nplete' Project	s: Project count: 4,	Cost of Pr	ojects: \$13,3	56,258
Astoria VMS Sign		·	l install a variable		Safety	1/27/2005	12/31/2005	
Key: 13575	Region: 2	Senate: 16	House: 31	US Cong: 1	Status: Under Constr		/0 // 2000	Ţ. 50,000
US 30 @ Columbia/Bond				d left-turn lane at	Operations	8/26/2004	10/31/2005	\$442,218
Key: 12668	Region: 2	Senate: 16	House: 32	US Cong: 1	Status: Under Constr	uction		
	Clats	op County 'U	nder Constru	uction' Project	s: Project count: 2,	Cost of Pr	oiects: \$632.	076
US26: Lindsley Creek-Lo Nehalem Road		This project is a	a safety and pres numbers 03095	servation project	Safety	4/14/2006	10/1/2007	\$2,239,000
Key: 14172	Region: 2	Senate: 16	House: 32	US Cong: 1	Status: Construction	Funding Com	mitted	
District 1 Traffic Signal Replacements & Upgrad	es		Upgrade or replation and Tillamoo	ace signals in	Operations	2/9/2006	12/1/2007	\$1,090,000
Key: 12671	Region: 2	Senate: 16		US Cong: 1	Status: Construction	Funding Com	mitted	
US-101 Youngs Bay Brid	lge	operator house	air the bridge girt & towers, and p de to bridge # 08	rovide an	Bridge	6/22/2006	4/1/2009	\$6,011,000
Key: 11792	Region: 2	Senate: 16	House: 32	US Cong: 1	Status: Construction	Funding Com	mitted	
US26: Jewell Jct Milita	ry Rd.	This project wil	overlay roadway	and restripe.	Pavement Preservation	1/26/2006	2/1/2007	\$3,244,000
Key: 12856	Region: 1	Senate: 16	House: 31	US Cong: 1	Status: Construction	Funding Com	mitted	
US30: John Day River B	ridge	This project wil (Bridge #01827	l replace bridge e	end panels.	Bridge	3/30/2007	12/1/2008	\$2,714,000
Key: 11798	Region: 2	Senate: 16	House: 31	US Cong: 1	Status: Construction	Funding Com	mitted	
US30: Knappa-Astoria D Striping	urable	of US30 in dura	complete the real able striping. The yed sections of U		Safety	9/21/2006	9/1/2007	\$321,000
Key: 14205	Region: 2	Senate: 16	House: 31	US Cong: 1	Status: Construction	Funding Com	mitted	
01-4	County 'Co	onstruction F	unding Comr	mitted' Project	s: Project count: 6,	Cost of Pr	ojects: \$15,6	19,000
Clatsop	-	This project wil	I produce the Fin	al Plans, and	Operations	7/6/2007		\$315,000
US-30 Astoria Signal and Upgrades	. 	number. This p cabinets, and in	roject will replace nterconnects. Re ungs Bay Bridge	place VMS and				

Clatsop County 'Under Development' Projects: Project count: 1, Cost of Project: \$315,000

Total Project Count for Clatsop County: 13, Total Cost of Projects: \$29,922,333

	Country Colum	ahia Est	imated or Actual da	te of:
Section Name:	County: Colun Project Descripton:	Con	tract Bid Constru	iction Project
		•		
OTIA I/II- Crown-Zellerbach Rd Project from Hwy 30-West Lane	Project will widen the local street.	Modernization 1	12/31/2004 12/30/2	2004 \$2,564,000
Key: 12397 Region	n: 1 Senate: 16 House: 31 US Cong: 1	Status: Construction Co	mplete	
Colu	mbia County 'Construction Complete' Proje	ects: Project count: 1,	Cost of Project: \$	2,564,000
US-30 Bennett Road to Laurel Av	e. This project will provide pavement preservation overlay project with bridge and safety improvements as needed.	Pavement Preservation 3	8/1/2004 9/15/2	004 \$2,502,441
Key: 11938 Region	n: 1 Senate: 16 House: 31 US Cong: 1	Status: Under Construct	tion	
OTIA I/II- US-30 @ Scappoose/Vernonia Rd. (Scapp	This project will realign intersection of US 30 and Scappoose/Vernonia Road. The project includes rebuilding the traffic signal and repaving one quarter mile of highway.		12/15/2	2004 \$2,275,260
Key: 10733 Region	n: 1 Senate: 16 House: 31 US Cong: 1	Status: Under Construct	tion	
Co	lumbia County 'Under Construction' Projec	ts: Project count: 2, C	Cost of Projects: \$	4,777,701
OR-202 Lyons Cr. Ford Cr. (Neha Hwy)	This project will replace structures Br. # 01975, 01974 and 03142	Bridge 1	11/25/2005 2/1/20	008 \$5,526,000
Key: 11950 Region	n: 1 Senate: 16 House: 32 US Cong: 1	Status: Construction Fu	nding Committed	
Columbia Cour	nty 'Construction Funding Committed' Proje	ects: Project count: 1,	Cost of Project: \$	5,526,000
US30: Columbia Co. Line - Swedetown Road	This project will produce the Final Plans, and construction will be under a different Key number. This project will overlay old pavement with new and add striping.	Pavement Preservation 2	2/22/2007	\$368,000
Key: 12870 Region	n: 1 Senate: 16 House: 31 US Cong: 1	Status: Under Developn	ient	
C	olumbia County 'Under Development' Proje	ects: Project count: 1,	Cost of Project: \$	368,000

Total Project Count for Columbia County: 5, Total Cost of Projects: \$13,235,701

			Count	ty: Coos			Actual date of:	
Section Name:		F	roject Descrip		Work Type:	Contract Bid Award:	Construction Completion:	Project Cost:
OTIA I/II- US-101 Isthmu Cemetery Road	s Street -	This project will make changes to improve the safety of left turns and make it easier for trucks to turn and improve sight distance.			Modernization	6/30/2003	9/30/2004	\$4,521,703
Key: 10876	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Construction	Complete		
	Coos	s County 'Cor	struction Co	omplete' Projec	ts: Project count:	1, Cost of P	roject: \$4,52°	1,703
OR42: Downtown Myrtle Repair	Point Slide	This project wi	I repair slide dar	mage.	Operations	3/10/2005	7/31/2005	\$583,734
Key: 13322	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Under Constr	uction		
US 101: Shinglehouse S Davis SI. Bridge	il. Road -		I overlay pavem Slough Road to t	ent from the Davis Slough	Pavement Preservation	n 11/18/2004	7/31/2005	\$2,601,477
Key: 12528	Region: 3	Senate: 05	House: 09	US Cong: 4	Status: Under Constr	uction		
	Co	os County 'U	nder Constr	uction' Projects	s: Project count: 2	, Cost of Pro	ojects: \$3,18	5,211
HWY 242: Powers slide	repair	This project wi	I repair slide dar	nage.	Operations	9/30/2004	1/1/2007	\$500,000
Key: 13643	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Construction	Funding Com	mitted	
Coos Bay/North Bend S Rebuilds	ignal	This project wi Hwy, US 101 (l rebuild signal c MP238.94)	on Cape Arago	Operations	9/7/2006	11/1/2007	\$595,000
Key: 12702	Region: 3	Senate: 05	House: 09	US Cong: 4	Status: Construction	Funding Com	mitted	
OR42: NF Coquille Road (Myrtle Point	I -Mill Cr. Rd.	This project wi signals and rep	l resurface pave pair sidewalks	ment, upgrade	Pavement Preservation	n 2/27/2006	4/1/2007	\$3,627,000
Key: 13456	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Construction	Funding Com	mitted	
OTIA I/II- US101: 13TH S Drive (Bandon)	t - Seabird	This project wi features.	I widen to 3 lane	es and add urban	Modernization	9/30/2008	8/1/2007	\$4,580,000
Key: 12732	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Construction	Funding Com	mitted	
US 101: McCullough Bri Bay) Rehab	dge (Coos	This project wi cathodic protect	I provide deck o	verlay and	Bridge	1/25/2007	5/1/2010	\$26,247,00
Key: 12692	Region: 3	Senate: 05	House: 09	US Cong: 4	Status: Construction	Funding Com	mitted	
US101: Bullards Bridge		Bullards Bridge	I provide improve to reduce poter ever height loads	ntial safety	Bridge	9/1/2006	10/1/2007	\$1,200,000
Key: 14220	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Construction	Funding Com	mitted	
Coos	s County 'C	onstruction F	unding Com	mitted' Projects	s: Project count: 6	, Cost of Pr	ojects: \$36,74	19,000
US-101: Isthmus Slough Bunker Hill Inters	Bridge &	Documents, ar different Key n	I produce the Er ad construction w umber. Environn and advance rig	vill be under a nental assessment	Pavement Preservation	n 12/2/2005		\$922,000
Key: 10844	Region: 3	Senate: 05	House: 09	US Cong: 4	Status: Under Develo	nmant		

Coos County 'Under Development' Projects: Project count: 1, Cost of Project: \$922,000

Total Project Count for Coos County: 10, Total Cost of Projects: \$45,377,914

Section Na	me:	P	Count	y: Crook	Work Type:	Estimated or Contract Bid Award:	Actual date of: Constructior Completion:	Project
OTIA I/II- OR-27 Crooked River Highway Preservation		Project will overlay 7 miles of roadway, including sidewalks along a portion of the highway within the City of Prineville.			Pavement Preserva	tion 12/24/2003	7/31/2004	\$1,716,441
Key: 12417	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Constructi	on Complete		
	Crool	County 'Cor	struction Co	mplete' Projec	ts: Project coun	t: 1, Cost of F	Project: \$1,71	6,441
US 26: Laughlin Ro (Prineville)	ad - Marks Creek		vide pavement p ion at Elephant F		Pavement Preserva	tion 6/1/2004	10/31/2005	\$3,429,234
Key: 12142	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Under Cor	struction		
	Cı	ook County '	Under Const	ruction' Projec	ts: Project coun	t: 1, Cost of F	Project: \$3,42	9,234
OR126: Crooked Ri at Harwood	ver Bridge-US26	bridge with a n problems at the Sidewalks will facilitate acces	e O'Neil Highway be installed on the s to the State Pa Il be installed at t	ge. It will correct y intersection. e bridge to	Bridge	9/22/2005	11/1/2007	\$4,869,000
Key: 14165	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Constructi	on Funding Com	mitted	
OTIA III- US26: Mari Creek-Bundle 505	ks Creek-Bridge	This project wil 07649.	I replace bridges	02553 and	Bridge	3/1/2007	9/1/2008	\$1,872,000
Key: 14236	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Constructi	E J: C	.,, 1	

Crook County 'Construction Funding Committed' Projects: Project count: 2, Cost of Projects: \$6,741,000

Total Project Count for Crook County: 4, Total Cost of Projects: \$11,886,675

Section Name:	County: Curry Project Descripton:	Estimated or Actual date of: Contract Bid Construction Project Work Type: Award: Completion: Cost:
US 101: Thomas Creek Bridge - Lone Ranch Beach	This project will grind/inlay & overlay (MP 347.87 - 357) Reconstruction of pavement (MP 357 - 357.87)	Pavement Preservation 3/25/2004 10/15/2004 \$2,929,085
Key: 13546 Region: 3	Senate: 01 House: 01 US Cong: 4	Status: Construction Complete
Curry	County 'Construction Complete' Project	ts: Project count: 1, Cost of Project: \$2,929,085
US-101 Rogue River (Gold Beach) Br.# 01172	This project will restore the historic bridge across the Rogue River at Gold Beach (#01172). Measures will be taken to protect the bridge's reinforcing steel from corrosion. This project was authorized in TEA-21 (#184).	Bridge 5/24/2001 9/30/2005 \$23,357,923
Key: 10910 Region: 3	Senate: 24 House: 48 US Cong: 4	Status: Under Construction
OTIA I/II- US 101: Lone Ranch Beach - Chetco River Bridge	This project will grind out old pavement and overlay/inlay with new at mile post 353.28 through 357.87. Install new sidewalks and illumination in downtown Brookings.	Pavement Preservation 3/31/2004 6/30/2006 \$5,671,550
Key: 13555 Region: 3	Senate: 01 House: 01 US Cong: 4	Status: Under Construction
US-101 Moore Street to Panorama Drive Resurfacing.	Project will overlay the existing pavement to preserve it.	Pavement Preservation 3/1/2004 9/15/2005 \$1,354,137
Key: 09849 Region: 3	Senate: 01 House: 01 US Cong: 4	Status: Under Construction
Cur	rry County 'Under Construction' Projects	s: Project count: 3, Cost of Projects: \$30,383,614
US 101: Rocky Creek Shoreline Protection	Project will repair slide damage on US 101 at Rocky Creek.	Operations 6/1/2004 7/1/2007 \$1,324,000
Key: 11567 Region: 3	Senate: 01 House: 01 US Cong: 4	Status: Construction Funding Committed
US101: Pistol River bridge rehab	Bridge Rehabilitation through Chloride extration process.	Bridge 2/23/2006 4/1/2008 \$4,421,000
Key: 12691 Region: 3	Senate: 01 House: 01 US Cong: 4	Status: Construction Funding Committed

Curry County 'Construction Funding Committed' Projects: Project count: 2, Cost of Projects: \$5,745,000

Total Project Count for Curry County: 6, Total Cost of Projects: \$39,057,699

			Count	y: Deschi		Estimated or a	Actual date of: Construction	Project
Section Name:		Pi	oject Descrip	ton:	Work Type:	Award:	Completion:	Cost:
OR-126 Sisters West & E Intersections	East End	Project will wide and west ends of devices.			Operations	10/9/2003	6/30/2004	\$851,652
Key: 09743	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Construction	Complete		
US 97: Wickiup Street - E	Bowery Lane	Project will millo millout inlay and 97 from Wickiup	l overlåy inner tr	avel lanes on US	Pavement Preservation	6/12/2003	10/15/2003	\$1,557,332
Key: 13097	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Construction	Complete		
US-97 South Bend Scale	Relocation	Project will reloc to the east side		end truck scales epoint 144.6	Operations	4/1/2003	4/30/2004	\$2,036,540
Key: 07206	Region: 4	Senate: 27	House: 54	US Cong: 2	Status: Construction	Complete		
US 97: Riley Bridge (Ben	d) #01679	Project will repla (Riley Bridge) o	ace bridge struc n US 97 near Be	ture #01679 end.	Bridge	6/1/2004	11/24/2004	\$240,124
Key: 11964	Region: 4	Senate: 27	House: 54	US Cong: 2	Status: Construction	Complete		
	Deschutes	County 'Cons	truction Con	nplete' Projects	s: Project count: 4,	Cost of Pr	ojects: \$4,68	5,648
OTIA I/II- OR126: Glacier couplet Phases 1 & 2	-Highland	This project will Widen HWY126 pedestrian acce	6. Add center tur		Modernization	9/30/2004	11/30/2006	\$13,784,632
Key: 13564	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Under Constr	ruction		
Bend and Sisters Preser	vation	This project will roadways.	provide preserv	ation of existing	Pavement Preservation	9/22/2005	10/31/2005	\$2,477,647
Key: 14262	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Under Constr	ruction		
US97: Reroute Phase 1 L (Redmond-Local sts)	Jnit 1A	This project will OR126 @ US97 US97.			Modernization	1/27/2005	6/30/2005	\$1,898,021
Key: 14141	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Under Constr	uction		
OTIA I/II- US-20 10th Stre Providence (Phase 1)	et -	Project will wide construct a raise and sidewalks.		o four lanes, install bike lanes	Modernization	9/30/2003	11/15/2003	\$7,539,734
Key: 12403	Region: 4	Senate: 27	House: 54	US Cong: 2	Status: Under Constr	ruction		

Deschutes County 'Under Construction' Projects: Project count: 4, Cost of Projects: \$25,700,033

			Count	y: Desch	utes	Estimated or Contract Bid	Actual date of: Construction	Project
Section Name	:	P	roject Descrip	ton:	Work Type:	Award:	Completion:	Cost:
OR126: Milepost 97-Ri Redmond	mrock Way-		I preserve the pa n at OR126 and I dewalks.		Pavement Preservati	on 3/3/2007	5/1/2008	\$5,405,000
Key: 14190	Region: 4	Senate: 27	House: 54	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US20: Suttle Lake - Sis	sters	This project wil	l add climbing an	nd passing lanes.	Modernization	8/25/2006	3/1/2008	\$2,853,000
Key: 11173	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US20: Hampton-Glass Torkelson Road	Butte and	pavement and	rvation project to upgrade a culver o US20 at Torkels	t. It will also	Pavement Preservati	on 5/30/2007	11/1/2008	\$6,898,000
Key: 14189	Region: 4	Senate: 27	House: 54	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US97: Village Way - Ba (Bend)	aker Road		I grind out and in tire section, and	lay travel lanes & thin treatment.	Pavement Preservati	on 6/30/2006	5/1/2008	\$1,032,000
Key: 12568	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US 97 @ South Centur (Sunriver)	y Drive	Project will pro	vide intersection	improvements.	Modernization	9/22/2005	11/1/2007	\$6,198,000
Key: 10637	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US97 at Vandervert		turn deceleration west off of the	I add a left turn la on for southboun highway. May po tury Drive projec	d traffic turning ossibly combine	Safety	9/1/2006	10/1/2007	\$651,000
Key: 12576	Region: 4	Senate: 27	House: 53	US Cong: 2	Status: Constructio	n Funding Com	mitted	

Deschutes County 'Construction Funding Committed' Projects: Project count: 6, Cost of Projects: \$23,037,000

Total Project Count for Deschutes County: 14, Total Cost of Projects: \$53,422,681

			Count	y: Dougla	16		Actual date of:	Dualant
Section Name:		Pr	oject Descript	•	Work Type:	ontract Bid Award:	Construction Completion:	Project Cost:
OTIA I/II- I-5 Vets Bridge - Creek	Myrtle		ace the Northbou will also inlay an		Bridge	6/30/2002	8/31/2004	\$13,457,941
Key: 12293	Region: 3	Senate: 01	House: 07	US Cong: 4	Status: Construction	Complete		
OTIA I/II- I-5 South Umpq (Fords) Bridge	ua River		ace the Fords Bri Ires; one northbo		Bridge	6/30/2002	7/31/2004	\$13,107,757
Key: 12297	Region: 3	Senate: 01	House: 07	US Cong: 4	Status: Construction	Complete		
Hancock Creek to Hayhu	rst Rd		repave about 9.5 ay from the Elk C		Pavement Preservation	1/22/2004	10/31/2004	\$3,678,765
Key: 10966	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Construction	Complete		
	Douglas (County 'Const	truction Com	plete' Project	s: Project count: 3,	Cost of Pro	ojects: \$30,24	14,463
OTIA I/II- Sutherlin-Rosek	ourg Project	07631A, 07627	replace Bridges AB, 07628AB and d widen OR 138	d 07629B,	Modernization	9/30/2006	4/30/2007	\$44,388,713
Key: 13467	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Under Constr	uction		
OTIA I/II- S. Umpqua Rive I-5 NB (Shady)	er & COPRR,	Project will replace 07713C)	ace the Shady Br	ridge (Bridge #	Bridge	9/25/2003	1/31/2008	\$31,803,432
Key: 12401	Region: 3	Senate: 01	House: 02	US Cong: 4	Status: Under Constr	uction		
I-5: Exit 125 & OR 138 Wi Signals-Roseburg	nchester		rebuild the entire den Valley Blvd. indard.		Safety	11/19/2004	7/15/2005	\$644,035
Key: 11728	Region: 3	Senate: 01	House: 02	US Cong: 4	Status: Under Constr	uction		
I-5 N/S-bound Cow Crk./G Bridges	Quines Crk	north-bound Co	ace four bridges: w Creek Bridges d Quines Creek b	and the south	Bridge	2/26/2004	9/15/2006	\$7,239,402
Key: 10764	Region: 3	Senate: 01	House: 02	US Cong: 4	Status: Under Constr	uction		
I-5 Canyonville - Azalea			repave about 10 n Canyonville an		Pavement Preservation	4/8/2004	7/31/2005	\$11,163,085
Key: 10832	Region: 3	Senate: 01	House: 02	US Cong: 4	Status: Under Constr	uction		
OR-42 Bear Creek - BLM (Rockfall)	Road		protection mattir ng, trim blasting, nt.		Operations	3/24/2005	9/15/2005	\$541,437
Key: 08867	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Under Constr	uction		

			Count	y: Dougla	s <u> </u>	stimated or A	Actual date of:	
Section Name:		P	roject Descript	_	Work Type:	ontract Bid Award:	Construction Completion:	Project Cost:
OTIA III- I-5: Exit 99 intrch Bridge Replacements	g Improv. &	lower under cro ramp. Bring Sc Bound on-ramp	s 08028N & 0802 ssing. Relocate buth Bound on-rai up to standard. round interchange	South Bound off- mp and North Improve access	Bridge	5/25/2005	4/1/2008	\$6,184,000
Key: 12707	Region: 3	Senate: 01	House: 02	US Cong: 4	Status: Construction I	Funding Com	nitted	
OTIA III- I-5: North Umpqua Bridges-Bundle 308	a River		replace bridge n vill repair bridge r		Bridge	8/23/2007	7/1/2011	\$59,383,000
Key: 14049	Region: 3	Senate: 04	House: 07	US Cong: 2	Status: Construction I	Funding Com	nitted	
OTIA III- OR38: Elk Creek- Hardscrabble Creek-Bund	le 401	This project will 01406, 01424 a	replace bridges and 01601.	01614, 01465,	Bridge	5/1/2006	8/1/2009	\$20,813,000
Key: 14221	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Construction I	Funding Comi	mitted	
OR-38 Elk Creek 2nd Xing		Retrofit the rail concrete deck of	and install a struc overlay	ctural microsilica	Bridge	4/27/2006	2/1/2007	\$417,000
Key: 11848	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Construction I	Funding Com	mitted	
OR38: Scottsburg to Scott Resurfacing	s Creek	This project will	grind and inlay/o	overlay pavement.	Pavement Preservation	10/12/2006	12/1/2007	\$2,927,000
Key: 12697	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Construction I	Funding Comi	mitted	
OR38: Mill Creek Bridge R	ehab	This project will overlay.	replace bridge ra	ail and deck	Bridge	11/9/2006	3/1/2008	\$1,347,000
Key: 12688	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Construction I	Funding Comi	mitted	
OR38: Truax Slide Repair		Slide repair, fur amendment #04	nds transfered fro 4-07-05.	m KN 12717	Operations	3/24/2006	6/1/2007	\$975,000
Key: 13571	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Construction I	Funding Comi	mitted	
OR42: Quiet Mnt Rd - Bend Resurfacing	edict Rd.	This project will	grind, inlay and	overlay roadway.	Pavement Preservation	9/1/2007	10/1/2008	\$2,161,000
Key: 12696	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Construction I	Funding Comi	mitted	
OTIA I/II- OR42: Glenhart - Lookingglass Rd (Winston		This project will add urban featu	widen roadway t ıres.	to 3 lanes and	Modernization	9/30/2007	8/1/2007	\$3,250,000
Key: 12731	Region: 3	Senate: 01	House: 01	US Cong: 4	Status: Construction I	Funding Comi	mitted	
OR-99 N. Umpqua River (C Winchester) Bridge	Old	Project will wide bridge floor bea	en the bridge and ims.	rehabilitate the	Bridge	8/10/2005	4/1/2010	\$9,379,000
Key: 11851	Region: 3	Senate: 01	House: 02	US Cong: 4	Status: Construction I	Funding Com	nitted	
Douglas C	ounty 'Cor	struction Fu	nding Commi	itted' Projects:	Project count: 10,	Cost of Pro	ojects: \$106,8	336,000
I5: Martin Creek - Anlauf R Repair	oadway	construction wil			Pavement Preservation	9/1/2006		\$200,000
Key: 12720	Region: 3	Senate: 04	House: 07	US Cong: 4	Status: Under Develo	pment		

Douglas County 'Under Development' Projects: Project count: 1, Cost of Project: \$200,000

Total Project Count for Douglas County: 20, Total Cost of Projects: \$233,060,567

			Count	ty: Gillian	า	Estimated or Contract Bid				
Section Nan	ne:	F	Project Descrip	ton:	Work Type:			•		
OTIA I/II- Rock Creek	Grade @ Olex	Project will improve grade and alignment for trucks.			Modernization	12/31/2005	11/11/2006	\$5,214,888		
Key: 11170	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Under Con	struction				

Gilliam County 'Under Construction' Projects: Project count: 1, Cost of Project: \$5,214,888

Total Project Count for Gilliam County: 1, Total Cost of Projects: \$5,214,888

Section Name:		P	Count	y: Grant	Work Type:	Estimated or A Contract Bid Award:	Actual date of: Construction Completion:	Project Cost:
US-395 Middle Fork Joh Br. #1922		Project will rep Fork John Day		cross the Middle ge is about 12	Bridge	1/24/2002		\$4,152,326
Key: 10471	Region: 5	Senate: 30	House: 59	US Cong: 2	Status: Constructio	n Complete		
	Grant	County 'Cor	struction Co	mplete' Projec	ts: Project count	: 1, Cost of P	roject: \$4,152	2,326
US-395 Fox to Beech (Creek	This project will pavement to pr	l add a chip seal eserve it.	to the existing	Pavement Preservati	on 2/24/2005	7/15/2005	\$447,586
Key: 10534	Region: 5	Senate: 30	House: 59	US Cong: 2	Status: Under Cons	struction		
	G	rant County '	Under Const	ruction' Projec	ts: Project count	: 1, Cost of P	roject: \$447, 	586
US 26 Dayville - Flat Cro	eek	This project is preserve it.	for repairing the p	pavement to	Pavement Preservati	on 11/16/2006	11/1/2008	\$2,616,000
Key: 12641	Region: 5	Senate: 30	House: 59	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US 395: Starr Ridge - C Creek	ottenwood	This project wil	I provide paveme	ent preservation.	Pavement Preservati	on 12/7/2006	12/1/2007	\$2,616,000
Key: 12634	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Constructio	n Funding Com	mitted	
Gran	nt County 'Co	nstruction F	unding Com	mitted' Project	s: Project count:	2, Cost of Pr	ojects: \$5,232	2,000
OR-19 North Fork John (Monument) Bridge	Day	Documents, an	I produce the End construction wumber. This project.	ill be under a	Bridge	11/9/2006		\$369,000
Key: 10475	Region: 5	Senate: 30	House: 59	US Cong: 2	Status: Under Deve	elopment		
OR-19 N. Fk. John Day (Kimberly) Bridge	River	Documents, an	I produce the End construction wurder. Project w		Bridge	12/7/2006		\$573,000
Key: 10465	Region: 5	Senate: 30	House: 59	US Cong: 2	Status: Under Deve	elopment		

Grant County 'Under Development' Projects: Project count: 2, Cost of Projects: \$942,000

			County	/: Hood F		Estimated or A		
Section Name:		Pr	oject Descript		Work Type:	Contract Bid Award:	Construction Completion:	
Hood River Hwy @ Pacif (Hood River)	fic Avenue		truct a signal at t er Hwy and Pacif		Safety	5/22/2003	10/15/2003	\$332,721
Key: 11915	Region: 1	Senate: 26	House: 52	US Cong: 2	Status: Construction	Complete		
I-84 Cascade Locks - Ho Interchange	ood River	necessary bridge	rface pavement, e repairs includin uctures. Replace an barrier.	g upgrading	Pavement Preservation	n 7/12/2001	11/30/2002	\$17,319,069
Key: 08291	Region: 1	Senate: 30	House: 56	US Cong: 2	Status: Construction	Complete		
I-84 Hood River - Mosier	Creek	the travel lane. Interchange. Instreatments and r	nent preservation Resurface the M stall current stand raise the guardra I height. Repair toles).	osier dard end il to meet the	Pavement Preservation	n 10/23/2003	9/15/2004	\$3,109,444
Key: 11910	Region: 4	Senate: 26	House: 52	US Cong: 2	Status: Construction	Complete		
	Hood River	County 'Const	ruction Com	plete' Projects	s: Project count: 3	, Cost of Pro	ojects: \$20,70	61,234
OR-35 Jct. Hood River H Creek	lwy - Polallie		of pavement pre ety work as need		Pavement Preservation	n 3/24/2005	10/31/2005	\$2,934,742
Key: 11939	Region: 1	Senate: 26	House: 52	US Cong: 2	Status: Under Consti	ruction		
OR-35 Neal Creek Road 91.5	- Milepoint	Project consists overlay and safe	of a pavement p		Pavement Preservation	n 2/24/2005	10/31/2005	\$1,160,923
Key: 11940	Region: 1	Senate: 26	House: 52	US Cong: 2	Status: Under Consti	ruction		
	Hood Riv	ver County 'Ur	nder Constru	ction' Projects	s: Project count: 2	, Cost of Pro	ojects: \$4,09	5,664
I-84: Rockfall at MP 61		This project will enlarge catchme	remove loose ma ent.	aterial and	Operations	10/14/2004	6/1/2006	\$1,528,508
Key: 13945	Region: 1	Senate: 28	House: 56	US Cong: 2	Status: Construction	Funding Com	nitted	
Hood Rive	er County 'C	Construction F	unding Com	mitted' Projec	ts: Project count:	1, Cost of P	roject: \$1,528	8,508
I-84: HCRH State Trail @) Viento	construction will number. This pro	produce the Fina be under a differ oject will construction olumbia Hwy Tra	ent Key ct a bike path	Modernization	11/8/2007		\$274,000
Key: 12842	Region: 1	Senate: 26	House: 52	US Cong: 2	Status: Under Develo	opment		
	Hood R	iver County 'U	Inder Develo	oment' Projec	ts: Project count:	1, Cost of P	roject: \$274,0	000

Total Project Count for Hood River County: 7, Total Cost of Projects: \$26,659,406

			Count	y: Jackso	on	Estimated or Contract Bid	Actual date of: Construction	Project
Section Na	me:	ı	Project Descrip	ton:	Work Type:	Award:	Completion:	Cost:
OTIA I/II- Pleasant A Bridges	Antelope Creek	Project will rep #29C198).	olace structures. (Br. #29C34 & Br.	Bridge	6/30/2004	7/1/2005	\$1,432,000
Key: 12444	Region: 3	Senate: 28	House: 55	US Cong: 2	Status: Constructio	n Complete		
OR-140 Butte Creek	RWIS/ICE Sign	wind/visibilty a	ill install remote o and ice detection r s of conditions.	perated monitoring station	Operations	8/12/2004	6/30/2005	\$159,028
Key: 11905	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Constructio	n Complete		
OTIA I/II- OR-234 Do	owntown Gold Hill		erlay the pavement Id Hill including sider Ir ramps.		Pavement Preservati	ion 12/31/2005	10/31/2004	\$2,537,351
Key: 12385	Region: 3	Senate: 02	House: 04	US Cong: 2	Status: Constructio	n Complete		
OR-234 Sams Valle Rd.	ey Hwy to Antioch	intersection of alternating flas intersection or	Il improve the turr Hwy 234 and An shing warning bea n the highway, up stent paved should tersection.	tioch Rd. install acons prior to the grade signs, and	Safety	2/13/2003	7/1/2003	\$237,000
Key: 10880	Region: 3	Senate: 02	House: 04	US Cong: 2	Status: Construction	n Complete		
OTIA I/II- Hwy 99 to Point	Haskell in Central		den West Pine St. Haskell St. to 5 lar ewalks.		Modernization	9/30/2005	2/3/2005	\$1,100,000
Key: 12381	Region: 3	Senate: 02	House: 04	US Cong: 2	Status: Constructio	n Complete		

Jackson County 'Construction Complete' Projects: Project count: 5, Cost of Projects: \$5,465,379

			Count	y: Jackso			Actual date of:	
Section Name:		Pi	roject Descript		Work Type:	ontract Bid Award:	Construction Completion:	•
OTIA I/II- Big Butte Cr. (Nethe	erlands	Project will repla	ace structure (Br	. #29C224).	Bridge	5/15/2004	Not Available	\$1,462,000
Key: 12447 Re ₂	gion: 3	Senate: 28	House: 55	US Cong: 2	Status: Under Constr	uction		
OTIA I/II- Little Butte Creek B	r.	Project will repla	ace stucture (Br.	#07001).	Bridge	9/30/2004	4/1/2006	\$2,245,000
Key: 10973 Reg	gion: 3	Senate: 02	House: V	US Cong: 2	Status: Under Constr	uction		
OTIA I/II- Rogue River Bridge (Depot Street)	#06970	Project will repla	ace existing brid	ge structure.	Bridge	6/30/2003	12/31/2005	\$15,157,880
Key: 08925 Reg	gion: 3	Senate: 02	House: 04	US Cong: 2	Status: Under Constr	uction		
I-5 North Ashland - 12th Stree	et	(inlay/overlay) a	grind and resurf a section of pave nd and Medford.		Pavement Preservation	11/18/2004	9/30/2005	\$12,581,376
Key: 11783 Reg	gion: 3	Senate: 03	House: V	US Cong: 2	Status: Under Constr	uction		
I-5 Central Point Southbound ramp improvements	l off-		ramp to improve	turn lanes on the signals	Operations	11/18/2004	6/30/2005	\$756,543
Key: 11727 Reg	gion: 3	Senate: 02	House: 04	US Cong: 2	Status: Under Constr	uction		
OR 140 @ Kershaw		This project will Beacon.	install advance l	hazard ID	Safety	3/25/2005	11/30/2005	\$713,716
Key: 12718 Reg	gion: 3	Senate: 28	House: 55	US Cong: 2	Status: Under Constr	uction		
Forest Service Boundry- mp 3 Diamond Lk.	3 West		d and inlay/overland and on highways 2	ay pavement the 2 and 233.	Pavement Preservation	11/18/2004	9/23/2005	\$3,539,200
Key: 10830 Reg	gion: 3	Senate: 28	House: 55	US Cong: 2	Status: Under Constr	uction		
OR 238: Long Gulch - Hanley	Paving	replace with ne	remove existing w, as well as pro and safety improv	vide some	Pavement Preservation	4/21/2005	9/15/2005	\$4,366,147
Key: 12685 Reg	gion: 3	Senate: 03	House: 05	US Cong: 2	Status: Under Constr	uction		
OR 238 @ Hanley Road (Bybe Corner)	ee	Project will impr	•	nt of OR 238 and	Modernization	2/24/2005	9/15/2006	\$2,711,532
Key: 12734 Reg	gion: 3	Senate: 03	House: 04	US Cong: 2	Status: Under Constr	uction		
I-5 N. Medford Interchange (O Corr. Solutions))R-62	interchange of I is the first phase	e of improvemen vas funded by TE	th Medford 62. This project ts in the Highway EA-21 as projects	Modernization	11/20/2003	10/31/2005	\$36,856,310
Key: 10838 Res	gion: 3	Senate: 03	House: 06	US Cong: 2	Status: Under Constr	uction		
OTIA I/II- OR 99; Colver Road Road (Talent)	- Rapp	•	bike lanes, sideve system, center		Modernization	12/31/2005	6/30/2006	\$7,769,000
Key: 12380 Reg	gion: 3	Senate: 03	House: 04	US Cong: 2	Status: Under Constr	uction		

Jackson County 'Under Construction' Projects: Project count: 11, Cost of Projects: \$88,158,704

			Coun	ty: Jacks	on	Estimated or .	Actual date of: Construction	Project
Section Na	me:	P	Project Descrip	oton:	Work Type:	Award:	Completion:	•
OTIA III- Stage 1a b Oaks	ridges - Seven	This project wil	Il repair/replace	stage 1a bridges	Bridge	6/30/2005	9/1/2008	\$18,747,000
Key: 13541	Region: 3	Senate: 04	House: 02	US Cong: 2	Status: Construction	Funding Com	mitted	
I-5: Bear Creek Brid	lges, NB and SB	, ,	ll replace both no ear Creek Bridge		Bridge	1/25/2006	8/1/2008	\$7,201,000
Key: 13000	Region: 3	Senate: 02	House: 04	US Cong: 2	Status: Construction	Funding Com	mitted	
I-5: Fern Valley Inte	rchange (Unit 2A)		Il widen and pos pad Interchange.	sibly re-align the	Modernization	1/22/2007	10/1/2009	\$11,685,000
Key: 12723	Region: 3	Senate: 03	House: 05	US Cong: 2	Status: Construction	Funding Com	mitted	
OTIA I/II- I-5 South Interchange (Medfo		This project will Interchange.	ll relocate and co	onstruct a new	Modernization	12/31/2006	1/1/2009	\$52,450,000
Key: 10964	Region: 3	Senate: 03	House: 06	US Cong: 2	Status: Construction	Funding Com	mitted	
I-5: Siskiyou Rest A	Area (Ashland)	Project will relo	ocate the I-5 Sisk	kiyou Rest Area.	Modernization	4/22/2004	12/1/2008	\$4,131,000
Key: 09436	Region: 3	Senate: 03	House: 05	US Cong: 2	Status: Construction	Funding Com	mitted	
OR-140 Brownsbor	o - Hanley Ranch		surface preserva		Pavement Preservation	n 1/17/2006	10/1/2007	\$3,374,000
Key: 11722	Region: 3	Senate: 02	House: 04	US Cong: 2	Status: Construction	Funding Com	mitted	
OR-99 Walker Ave.	- I-5 (Ashland)		ll repave 3.3 mile er Avenue and I-		Pavement Preservation	n 1/11/2007	1/1/2008	\$1,749,000
Key: 10829	Region: 3	Senate: 03	House: 05	US Cong: 2	Status: Construction	Funding Com	mitted	
Jacl	kson County 'Co	onstruction F	unding Com	mitted' Project	ts: Project count: 7	, Cost of Pr	ojects: \$99,33	37,000
Highway 62 Corrido	or Solutions EIS	construction winumber. Environment	Il produce the Fii ill be under a diff onmental impact dentify solutions	erent Key study will be	Modernization	9/30/2004		\$2,500,000
Key: 13226	Region: 3	Senate: 03	House: 06	US Cong: 2	Status: Under Devel	opment		

Jackson County 'Under Development' Projects: Project count: 1, Cost of Project: \$2,500,000

Total Project Count for Jackson County: 24, Total Cost of Projects: \$195,461,083

			Count	y: Jeffers	on	Estimated or Contract Bid	Actual date of: Construction	Project
Section Name:		Р	roject Descrip	ton:	Work Type:	Award:	Completion:	,
OTIA I/II- Trout Creek Bridg	ge (Gosner	Project will repl the bridge appr	ace bridge # 310 oaches.	C071 and repair	Bridge	6/1/2004	11/15/2004	\$1,124,000
Key: 10987	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Construction	n Complete		
US-26 Pelton Grade Curve	Correction	, ,	rove the existing accidents and i		Safety	3/25/2004	10/31/2004	\$1,391,988
Key: 11903	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Construction	n Complete		
•	Jefferson (County 'Cons	truction Con	nplete' Projects	: Project count:	2, Cost of Pr	ojects: \$2,51	5,988
OTIA I/II- US97/26 Willow C Depot Rd.	Creek br.		mprovement, pre Plum St-Willow (eservation on Hey Cr Br#00971A	Modernization	3/31/2004	10/31/2005	\$5,694,164
Key: 13573	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Under Cons	struction		
US-20 Lake Creek Bridge		Project will repl	ace bridge # 037	785A.	Bridge	3/1/2004	9/30/2006	\$2,161,129
Key: 12529	Region: 2	Senate: 30	House: 59	US Cong: 2	Status: Under Cons	struction		
	Jeffers	on County 'U	nder Constru	uction' Projects	: Project count:	2, Cost of Pr	ojects: \$7,85	5,293
US20 Hogg Rock and Johr Rockfall Mitigation	nny Cut		I construct Rockf R22 MP 79) & Jo	fall Mitigation. hnny cut (US20,	Operations	9/1/2007	10/1/2008	\$861,000
Key: 12579	Region: 2	Senate: 30	House: 59	US Cong: 4	Status: Construction	n Funding Com	mitted	
US97: S Madras NB & OR1 VMS Projects	38 Jct NB		l install VMS sigreather condition i	ns at two locations notification.	Operations	11/17/2005	1/1/2007	\$595,000
Key: 14112	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Construction	n Funding Com	mitted	
US97: Willowdale-Madras	Bridges	This project will replace bridge numbers 00813A, 00815A and 08600.			Bridge	9/1/2006	2/1/2009	\$6,551,000
Key: 14149 Region: 4 Senate: 30 House: 59 US Cong: 2			Status: Construction					

Total Project Count for Jefferson County: 7, Total Cost of Projects: \$18,378,280

			Count	y: Josepł	nine	Estimated or A		
Section Name:		Pr	oject Descript	_	Work Type:	Contract Bid Award:	Construction Completion:	Project Cost:
US199: Willow Ln Channelized Median (Grants Pass)		This project will safety improven	install channeliz	ed median as	Safety	9/30/2004	6/30/2004	\$370,000
Key: 13626 Reg	egion: 3	Senate: 25	House: 49	US Cong: 2	Status: Construction	Complete		
OR-238 Applegate River Br. #	#1985	This project will Applegate River	replace the bridg	ge across the	Bridge	1/23/2003	8/31/2005	\$4,720,958
Key: 02887 Reg	egion: 3	Senate: 02	House: 04	US Cong: 2	Status: Construction	Complete		
Jos	sephine C	ounty 'Const	truction Com	plete' Projects	s: Project count: 2	2, Cost of Pro	ojects: \$5,090),958
OTIA I/II- Grave Creek Bridge	e, I-5 SB	Project will repla (Bridge #06493)	ace the Graves C	Creek Bridge	Bridge	6/30/2003	11/13/2006	\$6,615,118
Key: 12365 Reg	egion: 3	Senate: 01	House: 02	US Cong: 2	Status: Under Const	truction		
I-5 Hugo - Glendale Road			place 2 variable Hugo and Glend		Operations	3/11/2004	12/15/2005	\$1,169,536
Key: 10855 Reg	egion: 3	Senate: 01	House: 02	US Cong: 2	Status: Under Const	truction		
OTIA III- US-199 E. & W. Fork River Bridge Rplcmnts	Illinois	Illinois River Brid	replace both the dge (Br. # 01077 er Bridge (Br. # 0	A) and the West	Bridge	3/24/2005	4/30/2008	\$18,013,631
Key: 11816 Reg	egion: 3	Senate: 02	House: 03	US Cong: 2	Status: Under Const	truction		
,	Josephin	e County 'Ur	nder Constru	iction' Projects	s: Project count: 3	B, Cost of Pro	ojects: \$25,79	8,285
Lower River Road Drainage (Pass)	(Grants	This project will	improve drainag	je.	Operations	6/6/2006	5/1/2007	\$399,000
Key: 12705 Reg	egion: 3	Senate: 02	House: 03	US Cong: 2	Status: Construction	Funding Com	mitted	
OTIA I/II- US 199: Rogue Rvr (6th&7th St.) Pk to Harbeck	Br.		udes pavement a lks, curbs, inters and signal work.		Bridge	12/31/2005	11/1/2006	\$5,831,000
Key: 13060 Reg	egion: 3	Senate: 02	House: 03	US Cong: 2	Status: Construction	Funding Com	mitted	
Us 199: Grants Pass parkway resurfacing	у		grind out old pavith new pavemer		Pavement Preservation	on 1/26/2006	5/1/2007	\$2,092,000
Key: 12693 Reg	egion: 3	Senate: 02	House: 04	US Cong: 2	Status: Construction	Funding Com	mitted	
US 199 @ Josephine county fairgrounds		This project will	improve function	n of intersection	Safety	1/22/2007	12/1/2007	\$334,000
Key: 12715 Reg	egion: 3	Senate: 02	House: 03	US Cong: 2	Status: Construction	Funding Com	mitted	
Allen Creek Road @ us 199 (GPass)	Grants	Extend Allen cre	eek north. Close	redwood avenue	Modernization	3/1/2007	6/1/2008	\$3,903,000
,		intersection.						
•	egion: 3	Senate: 02	House: 03	US Cong: 2	Status: Construction	Funding Com	mitted	
•		Senate: 02	House: 03 install left turn la		Status: Construction Operations	1/25/2007	<i>mitted</i> 4/1/2008	\$827,000

Josephine County 'Construction Funding Committed' Projects: Project count: 6, Cost of Projects: \$13,386,000

		nine	Estimated or Actual date of: Contract Bid Construction Pro					
Section Nam	ne:	F	Project Descrip	oton:	Work Type:	Award:	Completion:	Cost:
OR 238 @ Union & H Improvements	larbeck Signal	This project will produce the Final Plans, and construction will be under a different Key number. This project will rebuild the signal at OR 238 & Harbeck from a 6 phase to an 8 phase, and will include some median work.			Safety	1/27/2005		\$166,000
Key: 12727	Region: 3	Senate: 02	House: 03	US Cong: 2	Status: Under De	velopment		
OTIA I/II- US-199 Rog to Hwy 199 (6th/7th \$	•	This project will produce the Final Plans, and construction will be under a different Key number. Project will overlay the pavement, provide sidewalks, curbs, wheelchair ramps and other streetscape features.			Pavement Preserva	ation 11/19/2004	,	\$306,000
Key: 12383	Region: 3	Senate: 02	House: 03	US Cong: 2	Status: Under De	velopment		

Josephine County 'Under Development' Projects: Project count: 2, Cost of Projects: \$472,000

Total Project Count for Josephine County: 13, Total Cost of Projects: \$44,747,243

	County: Klamat				ath Estimated or Actual date of:			
Section Name:	Р	roject Descript		Work Type:	ontract Bid Award:	Construction Completion:	Project Cost:	
OTIA I/II- US97: Spring Cr Modoc Pt Unit 1	eek Hill-		7.6-257.83) N. Ch Hwy 422 (MP 0.0		Pavement Preservation	6/30/2004	10/15/2004	\$2,854,818
Key: 13266	Region: 4	Senate: 28	House: V	US Cong: 2	Status: Construction	Complete		
	Klamath	County 'Con	struction Co	mplete' Projec	ts: Project count:	1, Cost of F	Project: \$2,85	4,818
OTIA III- US97: Nevada Av Springs Drive.	e to Green	This project wil 09692.	l replace bridges	08346 and	Bridge	6/24/2004	11/11/2005	\$16,289,442
Key: 13213	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Under Constr	uction		
OTIA I/II- Washburn Way t	to US 97		rlay roadway surf houlders to main		Pavement Preservation	9/1/2003	6/30/2006	\$1,672,009
Key: 12413	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Under Constr	uction		
OTIA III- US97: Spring Cre Shady Pine Rd	eek Hill - N		I replace BR# 06 Widen sholders, a nt rehab.		Bridge	8/26/2004	11/30/2006	\$23,969,161
Key: 13585	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Under Constr	uction		
Doak Mtn.		This project co- construction. R		52 and 11810 for	Modernization	4/22/2004	9/30/2006	\$10,439,162
Key: 13302	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Under Constr	uction		
OR-140 @ OR 39 to Ritter Road.		Project will protreatment.	vide a thin, paven	nent preservation	Pavement Preservation	6/1/2004	6/30/2005	\$3,444,193
Key: 11879	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Under Constr	uction		
OR-66 Klamath River - Green Springs Interchange Project will install signal at i and OR 66. Make a "T" interest and southbound US 97 exit movements at the Clover C chevron signs to better delia 51.2.		ake a "T" intersed d US 97 exit ram the Clover Creek	ction with OR 66 p. Define turning Road, and use	Pavement Preservation	6/1/2004	12/31/2004	\$3,029,980	
Key: 12173	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Under Constr	uction		

			Count	y: Klamat	:h	Estimated or Contract Bid	Actual date of: Construction	
Section Name	e:	F	Project Descrip	ton:	Work Type:	Award:	Completion:	,
OR140: N Fork Little Butte Creek- Green Spring Hwy		This project will preserve pavement, upgrade the bridge guardrail, replace drain pipes and widen the shoulders.			Pavement Preservation 4/26/2007		10/1/2008	\$7,059,000
Key: 14211	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Constructio	n Funding Com	mitted	
OR140: Modoc Billy C Hole Creek	reek and Fish	and upgrade the areas that have thin treatment.	ne guardrail ends.	ase and provide a	Pavement Preservati	on 8/14/2007	9/1/2008	\$2,887,000
Key: 12573	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Constructio	n Funding Com	mitted	
OTIA I/II- OR-140 Beat	ty Curves	Project will install a guardrail and correct the roadway curve to improve safety.			Modernization	6/30/2005	3/1/2007	\$1,412,000
Key: 12402	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Constructio	n Funding Com	mitted	
OTIA I/II- OR-39 K Fall S. K Falls Hwy 424	s-Malin Hwy @	Project will insturn lanes.	tall a traffic signal	and build left	Modernization	1/22/2004	7/1/2006	\$901,269
Key: 12933	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Constructio	n Funding Com	mitted	
OR39: OCE Railroad C #02147 (Dairy)	O'xing Bridge	This project wi	Il replace a bridge	9.	Bridge	10/25/2007	7/1/2009	\$2,492,000
Key: 12740	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US97 Modoc Point - A Unit 1	Point - Algoma, Phase 2 This project will overlay pavement, widen shoulders, upgrade guardrail ends, possible minor realignment.			Modernization	5/3/2007	1/1/2009	\$6,017,000	
Key: 11532	Region: 4	Senate: 28	House: 56	US Cong: 2	Status: Constructio	n Funding Com	mitted	
US97: Southern Pacifi #07929 Chemult	ic RR Crossing	Widen or Repl	ace Bridge		Bridge	3/1/2007	6/1/2009	\$5,983,000
Key: 10716	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Constructio	n Funding Com	mitted	

Klamath County 'Construction Funding Committed' Projects: Project count: 7, Cost of Projects: \$26,751,269

Total Project Count for Klamath County: 14, Total Cost of Projects: \$88,450,033

Section Name	e:	F	Count Project Descrip	ty: Lake	Work Type:	Estimated or Contract Bid Award:	Actual date of: Construction Completion:	
OTIA I/II- OR-140 Greaser Canyon Preservation		aggregate to the condition. Proj	ne shoulders to in	m milepoint 40 to	Pavement Preservation 6/1/2002 6/1/2004		\$517,000	
Key: 12414	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Construction	Complete		
OTIA I/II- OR-140 Drak	se Creek - Adel	•	•	y surface and add rove the condition	Pavement Preservation	n 6/30/2003	6/1/2004	\$1,242,000
Key: 12410	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Construction	Complete		
	Lake	County 'Cons	struction Cor	mplete' Project	s: Project count: 2	., Cost of Pi	ojects: \$1,759	9,000
OR140: Doherty Slide		This project will produce the Final Plans, and construction will be under a different Key number. This project will develop plans for highway realignment.			Modernization			\$100,000
Key: 12554	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Under Devel	opment		

Lake County 'Under Development' Projects: Project count: 1, Cost of Project: \$100,000

Total Project Count for Lake County: 3, Total Cost of Projects: \$1,859,000

Section Name:		F	Count Project Descrip	y: Lane	Work Type:	Estimated or Contract Bid Award:	Actual date of: Construction Completion:	Project
OTIA III- I5: McKenzie-Willamette Brs (Detour/Temp repair)		This project will detour I5: McKenzie R. Bridge Southbound, do a temp repair to Northbound and detour Willamette R.			Bridge	10/23/2003	12/31/2004	\$34,815,310
Key: 13164	Region: 2	Senate: 06	House: 11	US Cong: 4	Status: Constructio	n Complete		
OR-126 Finn Rock - Lan Line	e County	Project will provide a pavement overlay and minor bridge work.			Pavement Preservati	ion 12/12/2002	11/30/2003	\$7,516,398
Key: 12517	Region: 2	Senate: 04	House: 07	US Cong: 4	Status: Constructio	n Complete		
OR-126 Siuslaw River - Chickahominy Creek		This project will overlay and upgrade guardrail, guardrail terminals, and bridge connections.			Pavement Preservati	ion 6/1/2004	6/30/2004	\$2,514,643
Key: 11885	Region: 2	Senate: 05	House: 10	US Cong: 4	Status: Construction	n Complete		
OR-58 Kitson Ridge to V Tunnel	V. Salt Cr.	This project will add two west bound passing lanes and one eastbound passing lane including pavement improvements along a 16 mile stretch of the Willamette Highway. Project will also install guard and bridge rails. Project is at Milepost 39.3 to Milepost 56.			Modernization	7/25/2002	8/31/2004	\$11,289,142
Key: 11522	Region: 2	Senate: 04	House: 07	US Cong: 4	Status: Constructio	on Complete		

Lane County 'Construction Complete' Projects: Project count: 4, Cost of Projects: \$56,135,493

Section Name:		D	Count	y: Lane		stimated or ontract Bid Award:	Actual date of: Construction Completion:	Project Cost:
			roject bescrip	tori.			•	
Territorial Hwy @ Mapleto City Hwy (OR36	on/Junction	Safety Project			Safety	9/1/2004	11/23/2005	\$258,605
Key: 13265	Region: 2	Senate: 07	House: 14	US Cong: 4	Status: Under Constru	ıction		
I-5: Cottage Grove Conne Crossing	ctor at Corp				Bridge	6/9/2005	9/15/2005	\$319,766
Key: 14288	Region: 2	Senate: 04	House: 07	US Cong: 4	Status: Under Constri	ıction		
I-105 Willamette River - Pacific Highway (Eugene)		reconstruct with structures and replace existin barrier. Build a Coburg Raod (I	n asphalt betwee repair joints at br g guardrail and o uxiliary lanes fro	concrete median om I-105 to om Delta Hwy to	Pavement Preservation	1/15/2004	11/30/2005	\$19,698,517
Key: 10349	Region: 2	Senate: 06	House: 12	US Cong: 4	Status: Under Constru	ıction		
OTIA I/II- Row River Bridg	e SB	Project will repl	ace bridge #078	29.	Bridge	6/30/2004	9/30/2006	\$9,041,011
Key: 12357	Region: 2	Senate: 04	House: 07	US Cong: 4	Status: Under Constru	ıction		
OTIA I/II- OR126: Badger I Pass Passing Lanes	Mt/Cougar	Project will exterpassing lanes.	end existion East	and West bound	Modernization	3/31/2006	10/30/2005	\$1,312,653
Key: 12922	Region: 2	Senate: 05	House: 10	US Cong: 4	Status: Under Constru	ıction		
OR-126 Willamette R. (Sp Bridges	oringfield)		repave the deck 3) over the Willan		Bridge	1/23/2003	11/30/2003	\$2,579,855
Key: 10606	Region: 2	Senate: 06	House: 12	US Cong: 4	Status: Under Constru	ıction		
OR-126 Jenkins Drive - Si	Iver Creek.	McKenzie High	repave about 33 way from Jenkin to Silver Creek.	s Drive in	Pavement Preservation	11/18/2004	8/31/2006	\$6,517,281
Key: 10808	Region: 2	Senate: 06	House: 07	US Cong: 4	Status: Under Constru	ıction		
OR-58 Salt Creek Tunnel			improve the Sal east of Oakridge		Bridge	6/1/2003	10/31/2005	\$2,461,309
Key: 09317	Region: 2	Senate: 04	House: 07	US Cong: 4	Status: Under Constru	ıction		
OR-58 Dexter Park to Kits Rd.	son Ridge		repave about 28 nway between Pl		Pavement Preservation	4/26/2002	8/31/2003	\$6,832,680
Key: 10781	Region: 2	Senate: 04	House: 07	US Cong: 4	Status: Under Constru	ıction		
US 101: Siuslaw River (Flo Bridge	orence)	Project will repl life span bridge		deck system and	Bridge	6/24/2004	6/1/2006	\$1,856,714
Key: 09309	Region: 2	Senate: 05	House: 09	US Cong: 4	Status: Under Constru	ıction		
US-101 Cape Creek Tunne Portal)	el (North		install a tunnel I of the Cape Cre		Bridge	7/25/2002	5/31/2005	\$7,281,769
Key: 11794	Region: 2	Senate: 05	House: 07	US Cong: 4	Status: Under Constri	ıction		

Lane County 'Under Construction' Projects: Project count: 11, Cost of Projects: \$58,160,162

Section Name:	County: Lane Project Descripton:	<u>Estimated or Actual date of:</u> Contract Bid Construction Project Work Type: Award: Completion: Cost:
OTIA I/II- I-5 Springfield/Creswell overcrossing	wy This project will replace I-5 over crossing at Springfield/Creswell hwy (#07739a), add bike and pedestrian facilities.	Bridge 4/30/2005 4/1/2008 \$8,064,000
Key: 13543 Regio.	2 Senate: 06 House: 11 US Cong: 4	Status: Construction Funding Committed
OTIA III- Stage 1A Bridges - Cott Grove/Pleasant Hill	e This project will repair/replace stage 1a bridges	Bridge 6/30/2005 Not Available \$3,002,000
Key: 13539 Regio.	2 Senate: V House: V US Cong: 4	Status: Construction Funding Committed
OTIA I/II- I-5 at Beltline Interchan (Eugene/Springfield)	This project will provide modernization of the interchange including fly-over bicycle and pedestrian bridge.	Bridge 12/30/2005 8/1/2009 \$68,500,000
Key: 14197 Regio	2 Senate: 07 House: 11 US Cong: 4	Status: Construction Funding Committed
OTIA III- I-5: McKenzie River Brid Bundle 215	This project will replace eight OTIA III structures on Interstate 5. The McKenzie River Bridge Bundle 215 includes bridges 06836A, 08870, 08178N, 08178S, 08175N 08175S, 08171N and 08171 S.	Bridge 12/1/2006 10/1/2009 \$57,377,000
Key: 14036 Regio.	2 Senate: 06 House: 11 US Cong: 4	Status: Construction Funding Committed
I-5: Dillard Access-Cattlepass Crossing	This project will install barrier rails at locations near mileposts 179 and 186.	Safety 9/1/2006 8/1/2007 \$387,000
Key: 14203 Regio.	2 Senate: 06 House: 12 US Cong: 5	Status: Construction Funding Committed
OTIA III- I-5: Coast Fork Willamet Martin Creek Bundle 310	 This project will replace bridge numbers 07861B, 07810B, 07810A, 07809A and 07809B. 	Bridge 4/26/2007 2/1/2010 \$11,410,000
Key: 14051 Regio	2 Senate: 04 House: 07 US Cong: 4	Status: Construction Funding Committed
I-5: Whiteaker Ave-London Road Bundle 311	This project will replace bridge numbers 07860, 07863A and 07863. It will repair bridges 07865A, 07864A and 07830.	Bridge 6/21/2007 7/1/2010 \$15,279,000
Key: 14255 Regio	2 Senate: V House: V US Cong: 4	Status: Construction Funding Committed
OR-126 W. 11th St. to Garfield (Eugene)	This project will build about 1.7 miles of new 4 lane roadway, the first part of improvements to the Florence-Eugene Highway, between W. 11th Street and Garfield Street in Eugene. This is the Unit 1, Part A project.	Modernization 9/1/2002 5/1/2009 \$17,737,000
Key: 07990 Regio.	2 Senate: 07 House: 14 US Cong: 4	Status: Construction Funding Committed
OR-126 Peterson Tunnel - Turne Creek	Project will construct a westbound passing lane.	Modernization 6/30/2005 4/1/2008 \$2,777,000
Key: 06494 Regio	2 Senate: 05 House: 10 US Cong: 4	Status: Construction Funding Committed
OR-126 N. Fork Suislaw River Br	ge Project will replace bridge #01183A (N. Fork Siuslaw River Bridge).	Bridge 4/27/2006 4/1/2010 \$14,700,000
Key: 11791 Regio	2 Senate: 05 House: 09 US Cong: 4	Status: Construction Funding Committed
OR222: Springfield ScI-Jasper B	This project will widen shoulders and remove objects from clear zone.	Safety 11/9/2006 1/1/2008 \$3,078,000
Key: 12581 Regio.	2 Senate: 06 House: 12 US Cong: 4	Status: Construction Funding Committed
OR36: Lingo Slough Bridge	Replace Bridge (#01755D)	Bridge 8/24/2006 9/1/2008 \$4,512,000
Key: 11797 Regio.	2 Senate: 05 House: 10 US Cong: 4	Status: Construction Funding Committed
OR58: Salt Creek Half Viaducts	This project will repair or replace bridges at mileposts 55.98, 56.23, 56.29 and 56.32.	Bridge 8/9/2007 10/1/2009 \$4,695,000
Key: 14145 Regio.	2 Senate: 04 House: 07 US Cong: 4	Status: Construction Funding Committed

Section Name:		Pı	County roject Descript	y: Lane		Estimated or A ontract Bid Award:	Actual date of: Construction Completion:	Project
OR99: Barger Ave- Washington/Jefferson St	(Eugene)	This project will	overlay roadway	· .	Pavement Preservation	9/1/2007	1/1/2009	\$2,667,000
Key: 14118	Region: 2	Senate: 07	House: 14	US Cong: 4	Status: Construction	Funding Comi	nitted	
US-101 Rock Creek Bridg	е	#01176 is to be	ge replacement preplaced in its cursture built to	urrent location	Bridge	2/23/2006	3/1/2008	\$3,846,000
Key: 12131	Region: 2	Senate: 05	House: 10	US Cong: 4	Status: Construction	Funding Comi	nitted	
US101: Tenmile Creek Br	idge		provide cathodic I and deck overla		Bridge	10/12/2006	11/1/2008	\$3,770,000
Key: 10617	Region: 2	Senate: 05	House: 09	US Cong: 4	Status: Construction	Funding Comi	nitted	
Lane C	County 'Co	nstruction Fur	nding Commi	tted' Projects:	Project count: 16,	Cost of Pro	ojects: \$221,8	801,000
OTIA I/II- I-5 Springfld/Cre Intch Bike/Ped	eswell Hwy	construction will number. The pr	produce the Fina I be under a differ oject will constuct across I-5 at exis	rent Key	Modernization	5/27/2004		\$185,000
Key: 12307	Region: 2	Senate: 06	House: 11	US Cong: 4	Status: Under Develo	pment		
OTIA III- Stage 1A Bridge Goshen/Gettings Creek	s -	construction wil	produce the Fina I be under a differ oject will repair/re	rent Key	Bridge			\$200,000
Key: 13538	Region: 2	Senate: V	House: V	US Cong: 4	Status: Under Develo	pment		
I-5 @ Beltline Study		construction will number. Project construction) we	produce the Final be under a differ t is for needed de ork to prepare for ject. This project t.	rent Key evelopment (pre- a future	Modernization			\$3,375,000
Key: 10377	Region: 2	Senate: 06	House: 12	US Cong: 4	Status: Under Develo	pment		
OR126: Poterf Creek - No Development	ti	Documents, and different Key nu only. It will deve vertical and hor roadway to a st	produce the Envidence of construction will imber. This project to indicate the project the Environmental and indicate the Environmental This project to indicate the Environmental This project the Environm	I be under a ct is for design mprove the s, widen d passing lanes	Modernization			\$500,000
Key: 12828	Region: 2	Senate: 05	House: 10	US Cong: 4	Status: Under Develo	pment		
OR58: Salt Creek Half Via	ducts	construction will number. This pr	produce the Fina be under a differ oject will replace 5, 56.23, 56.29 an	rent Key four bridges at	Bridge	9/1/2005		\$10,000
Key: 13143	Region: 2	Senate: 04	House: 07	US Cong: 4	Status: Under Develo	pment		
OR69: Beltline Hwy @ Co Interchange	berg Road	construction wil	produce the Fina I be under a differ oject will modern	rent Key	Modernization	1/24/2008		\$326,000
Key: 12836	Region: 2	Senate: 07	House: 12	US Cong: 4	Status: Under Develo	pment		

Lane County 'Under Development' Projects: Project count: 6, Cost of Projects: \$4,596,000

Total Project Count for Lane County: 37, Total Cost of Projects: \$340,692,655

		County: Lincoln				Estimated or Actual date of:		
Section Name	e:		Project Descrip		Work Type:	Contract Bid Award:	Construction Completion:	Project Cost:
US-101 Cooks Chasm	Bridge		place the Cooks (south of Yachats		Bridge	10/25/2001	5/23/2003	\$4,282,337
Key: 10615	Region: 2	Senate: 02	House: 04	US Cong: 5	Status: Construction	Complete		
	Lincolr	County 'Co	nstruction Co	omplete' Projec	ts: Project count:	1, Cost of P	roject: \$4,282	2,337
US101: Otis Jct - Boile	er Bay	This project w sidewalk impre	ill include paveme ovements.	ent overlay and	Pavement Preservatio	n 6/29/2005	11/30/2005	\$3,389,500
Key: 13657	Region: 2	Senate:	House:	US Cong:	Status: Under Const	ruction		
US101:Yaquina Bay B US20;US101-John Mo		This project is inlay/overlay.	pavement prese	rvation,	Pavement Preservatio	n 10/10/2004	10/15/2005	\$1,866,429
Key: 13589	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Under Const	ruction		
US-101 Yaquina Bay I (Newport)	Bridge Painting	This project w (#01820) in No	ill paint the Yaqui ewport.	ina Bay Bridge	Bridge	3/1/2004	9/30/2005	\$8,966,841
Key: 10605	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Under Const	ruction		
	Linc	oln County 'l	Jnder Constr	uction' Projects	s: Project count: 3	, Cost of Pr	ojects: \$14,22	22,770
US-101 Yaquina Bay I 123rd Street	Bridge - SE	Overlay paver WORK' area.)		to 145.3 is a 'NO	Pavement Preservatio	n 10/28/2004	Not Available	\$118,000
Key: 11874	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Construction	Funding Com	mitted	
US101 Newport signa	l upgrades	This project w	ill upgrade Traffic	signals.	Operations	5/5/2006	7/1/2007	\$876,000
Key: 12673	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Construction	Funding Com	mitted	
OTIA I/II- US-101 SE 1 St. (Lincoln Cty)	9th St./SE 32nd		den the existing to tion and pave the	wo-lane road to a e shoulder and	Modernization	6/30/2005	7/1/2007	\$5,076,000
Key: 12303	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Construction	Funding Com	mitted	
US-101 Spencer Crk ((#06510)	Crossing Bridge		place the bridge a	•	Bridge	6/30/2006	10/1/2008	\$8,358,000
Key: 10058	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Construction	Funding Com	mitted	
US101: WM Keady Wa Chasm	ayside-Cooks	This project w	ill provide overlay	<i>(</i> .	Pavement Preservatio	n 3/23/2006	4/1/2007	\$3,223,000
Key: 13569	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Construction	Funding Com	mitted	
US101" Millport Sloug		This project w	ill replace Bridge	#06579.	Bridge	12/14/2006	2/1/2009	\$4,900,000
Key: 12802	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Construction	Funding Com	mitted	
US20: Yaquina River	Bridge Painting	This project w Eddyville.	ill paint the Yaqui	ina River Bridge in	Bridge	9/1/2006	1/1/2007	\$247,000
Key: 14194	Region: 2	Senate: 05	House: 10	US Cong: 5	Status: Construction	Funding Com	mitted	

Lincoln County 'Construction Funding Committed' Projects: Project count: 7, Cost of Projects: \$22,798,000

Total Project Count for Lincoln County: 11, Total Cost of Projects: \$41,303,108

Section Name:		P	Count	y: Linn		Estimated or A Contract Bid Award:	Actual date of: Construction Completion:	
OTIA III- I-5 N. Jefferson Albany Intch (Phase 1)	Intch - N.		and Albany. It v	miles of freeway will repave the	Pavement Preservation	n 11/20/2003	6/30/2006	\$27,813,127
Key: 10352	Region: 2	Senate: V	House: 15	US Cong: 4	Status: Under Consti	ruction		
I-5 NB @ Lake Creek Var Message Sign	iable	This project will for NB motorist	l install a variable s.	e message sign	Operations	6/10/2004	3/31/2005	\$425,698
Key: 12940	Region: 2	Senate: 06	House: 11	US Cong: 4	Status: Under Consti	ruction		
OR-34 Corvallis - Newpo Peoria Rd.	rt Hwy to		l construct dual le signals and add r Wolcott Road.		Safety	3/24/2005	10/31/2005	\$1,580,898
Key: 11803	Region: 2	Senate: 08	House: 15	US Cong: 4	Status: Under Consti	ruction		
US-20 Wheeler St Mark (Lebanon)	et St.	to Market Stree	the signals from t, reconstruct the of the Wheeler-Mo	turning radii on	Safety	1/21/2005	11/1/2005	\$1,508,689
Key: 11799	Region: 2	Senate: 09	House: 17	US Cong: 4	Status: Under Consti	ruction		
OTIA I/II- US-20/OR 99 In Improvements (Albany)	terchange	Project will mod single point dia	dify the interchang	ge into a partial	Modernization	6/30/2004	11/30/2005	\$2,928,000
Key: 12302	Region: 2	Senate: 08	House: 15	US Cong: 4	Status: Under Consti	ruction		
OTIA III- I-5 Bridge Bund	le 213		l repair BR# 0825 2205B, 09413, 09		Bridge	4/14/2005	11/9/2005	\$2,052,931
Key: 14034	Region: 2	Senate: V	House: V	US Cong: 4	Status: Under Consti	ruction		
	Li	nn County 'U	nder Constru	ıction' Projects	s: Project count: 6	, Cost of Pr	ojects: \$36,30	09,343

			Count	ty: Linn		Estimated or Contract Bid	Actual date of: Construction	Project
Section Name:		F	Project Descrip	•	Work Type:	Award:	Construction:	•
OTIA III- Stage 1a bridge Albany interchange	es - North	This project wi	Il repair/replace s	stage 1 bridges.	Bridge	6/30/2005	4/1/2009	\$14,117,000
Key: 13542	Region: 2	Senate: 15	House: 08	US Cong: 4	Status: Construction	on Funding Com	mitted	
I-5: N Albany VMS & car	mera	Install a variab Albany.	le message sign	for I-5 at North	Operations	12/14/2006	1/1/2008	\$386,000
Key: 12941	Region: 2	Senate: 08	House: 16	US Cong: 4	Status: Construction	on Funding Com	mitted	
OTIA III- I-5: Sodom Dito River Bundle 216	ch-Calapooia	Interstate 5. B	ridge Bundle 216 6N, 08236S, 082	IA III structures on 6 includes bridge 235N, 08235S,	Bridge	2/22/2007	4/1/2010	\$18,700,000
Key: 14037	Region: 2	Senate: V	House: V	US Cong: 4	Status: Construction	on Funding Com	mitted	
OTIA III- I-5: Cox Creek- Access Bundle 214	McVay	and 08226S so		d bridges 08226N and the Cox Creek	Bridge	9/1/2006	5/1/2009	\$9,447,000
Key: 14035	Region: 2	Senate: 08	House: 15	US Cong: 4	Status: Construction	on Funding Com	mitted	
OTIA I/II- OR-99E (Halse	y) to I-5			y, provide a right ers, and improve	Pavement Preservat	ion 9/30/2005	10/1/2006	\$2,642,000
Key: 12312	Region: 2	Senate: 12	House: 23	US Cong: 4	Status: Construction	on Funding Com	mitted	
OTIA I/II- Tangent, SW H Lebanon Hwy/PED Impi			various improver on and Tangent.	ments in Sweet	Modernization	9/30/2006	9/1/2007	\$4,764,000
Key: 13095	Region: 2	Senate: 19	House: 37	US Cong: 4	Status: Construction	on Funding Com	mitted	
OR34 Roche Street-Wol	cott Road		ll construct fronta ment access con	age roads on N & atrol.	Safety	4/23/2009	9/1/2010	\$3,655,000
Key: 12580	Region: 2	Senate: 08	House: 15	US Cong: 4	Status: Construction	on Funding Com	mitted	
OR99E: Creek Bridge & Creak bridge	Big Muddy	This project wi (#00568)	ll replace Bridge	s (#00569) &	Bridge	11/17/2006	11/1/2008	\$3,817,000
Key: 14114	Region: 2	Senate: 19	House: 37	US Cong: 4	Status: Construction	on Funding Com	mitted	
US20: OR22 and Jack L Durable Striping	ake Road		Il replace the wa		Safety	3/9/2006	12/1/2007	\$1,078,000
Key: 14206	Region: 2	Senate: 09	House: 17	US Cong: 4	Status: Construction	on Funding Com	mitted	

Linn County 'Construction Funding Committed' Projects: Project count: 9, Cost of Projects: \$58,606,000

Total Project Count for Linn County: 15, Total Cost of Projects: \$94,915,343

			Count	ty: Malheu			Actual date of:	
Section Name:		P	roject Descrip		Work Type:	Contract Bid Award:	Construction Completion:	
SW 4th St SE 2nd Str	eet (Ontario)		d a new bridge a SW 18th Avenue		Modernization	2/22/2001	11/30/2002	\$6,494,699
Key: 10269	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Construction	Complete		
	Malheu	r County 'Cor	struction Co	omplete' Projec	ts: Project count:	1, Cost of P	roject: \$6,49	4,699
OR201: Jct US20/26 - N	1P12.53	Creek Highway Oregon Highway	r from the junction to the form the following to the following the follo		Pavement Preservation	n 7/22/2004	10/31/2005	\$4,040,394
Key: 10528	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Consti	ruction		
US-26 Snake River (Ny #01463A	rssa) Bridge	and reconstruc		dge and railing e existing bridge. led by Idaho DOT.	Bridge	7/25/2002	12/31/2003	\$6,920,635
Key: 10457	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Consti	ruction		
US-95 Jordan Valley Se	ection			ent preservation ntation. Add storm	Pavement Preservation	n 3/4/2004	10/31/2005	\$3,158,373
Key: 12492	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Consti	ruction		
	Malh	eur County 'U	nder Constr	uction' Projects	s: Project count: 3	, Cost of Pr	ojects: \$14,1	19,402
OTIA III- I-84: Stanton E River Bundle	Blvd-Snake		l replace bridge E, 08107W, 0797	07971 and repair 70, 08397E and	Bridge	6/8/2006	12/1/2009	\$30,343,000
Key: 14024	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Construction	Funding Com	mitted	
OTIA I/II- OR-201: N On Bridge	tario Intchg		struct a new ove R-201 alignment	erpass structure . (Br. #08635) MP	Modernization	12/31/2006	2/1/2009	\$11,743,000
Key: 11887	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Construction	Funding Com	mitted	
OR201: Airport Corner	- Cairo Jct.	Pavement pres	servation.		Pavement Preservation	n 11/23/2006	7/1/2007	\$779,000
Key: 12640	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Construction	Funding Com	mitted	
Malheu	ur County 'Co	onstruction F	unding Com	mitted' Projects	s: Project count: 3	, Cost of Pr	ojects: \$42,8	65,000
OR 201: Airport Corner Junction	r - Cairo	Documents, ar	I produce the End construction wumber. Access M	vill be under a	Operations	11/23/2006		\$314,000
Key: 12627	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Develo	opment		

Malheur County 'Under Development' Projects: Project count: 1, Cost of Project: \$314,000

Total Project Count for Malheur County: 8, Total Cost of Projects: \$63,793,101

			County	y: Marion		stimated or a	Actual date of: Construction	Project
Section Name:		Pi	roject Descript	on:	Work Type:	Award:	Completion:	Cost:
I-5: Mill Creek-Battle Creek	k	rebuild bridge a features, raise E	inlay/over lay ex pproaches, upgra Battle Cr Rd U-xii g structure shall	ng structure.	Pavement Preservation	9/30/2003	5/31/2005	\$4,573,838
Key: 13536	Region: 2	Senate: 10	House: 19	US Cong: 5	Status: Construction (Complete		
Chemawa Rd N Santiam Interchange	ı	locations on Mis	install medians a ssion St. Extend a Airport Rd. to N	3rd lane	Pavement Preservation	2/24/2004	5/31/2005	\$6,551,431
Key: 10807	Region: 2	Senate: 17	House: 33	US Cong: 5	Status: Construction C	Complete		
OR-214: I-5 - Evergreen Av (Woodburn)	ve.		reduce traffic co ound OR214, add eway on-ramp.	ngestion by ding dedicated rt-	Modernization	5/13/2004	9/30/2004	\$1,856,247
Key: 12519	Region: 2	Senate: 11	House: 22	US Cong: 5	Status: Construction C	Complete		
	Marion (County 'Cons	truction Com	plete' Projects	: Project count: 3,	Cost of Pr	ojects: \$12,98	31,516
OR99E: Howell Prairie Rd.	Waconda		nbines two projec and improve sign		Safety	12/23/2004	10/31/2005	\$2,448,913
Key: 13590	Region: 2	Senate: 11	House: 22	US Cong: 5	Status: Under Constru	ıction		
OTIA I/II- Arndt Rd. Improv (Marion County)	vements		rove Arndt Road anes on the Wils	in Marion County onville-Hubbard	Modernization	12/31/2004	Not Available	\$1,760,000
Key: 13033	Region: 2	Senate: 09	House: 18	US Cong: 5	Status: Under Constru	ıction		
OR213: Lone Pine Corner (Silverton)	-OR214	This project will between MP 24	inlay/over lay ex .74-MP 29.71.	isting pavement	Pavement Preservation	2/24/2005	9/30/2005	\$1,402,966
Key: 11860	Region: 2	Senate: 09	House: 18	US Cong: 5	Status: Under Constru	ıction		
OR22: N. Santiam Hwy Bri	idge	This project will	replace Bridges		Bridge	1/30/2004	12/15/2005	\$9,262,289
Replacements	•	07509, 12496,	10600, 12498 and	d 12529.				

				y: Marion	C	stimated or a	Actual date of: Construction	
Section Nam	e:	Р	roject Descrip	ton:	Work Type:	Award:	Completion:	Cost:
OR214 @ Evergreen oR211 @ Barlow Rd	(Woodburn)-		Evergreen, and	reconstruct curb, I reconstruct	Operations	9/26/2006	10/1/2007	\$671,000
Key: 13625	Region: 2	Senate: 11	House: 22	US Cong: 5	Status: Construction I	Funding Com	mitted	
OTIA III- I-5: N Santial (phase 3)	m - Kuebler	widening freew shall be replace repaired. One Sound wall and constructed. Exand off-ramps reconstructed.	ed. One structur box culvert shall	cility. Six bridges e shall be be extended. structure shall be h Hwy Intchg on d and r Intchg NB on-	Bridge	9/22/2005	8/1/2009	\$62,564,000
Key: 13284	Region: 2	Senate: 10	House: 19	US Cong: 5	Status: Construction I	Funding Com	mitted	
OR22: Fir Grove Lane	e - Gun Creek			ement with new 16.0 - MP 26 and	Pavement Preservation	11/29/2005	1/1/2007	\$3,768,000
Key: 12804	Region: 2	Senate: 09	House: 17	US Cong: 5	Status: Construction I	Funding Com	mitted	
OR99E at Checkerbo	ard Road	apply current a	ccess managem at the intersection		Safety	9/27/2007	12/1/2008	\$1,180,000
Key: 14204	Region: 2	Senate: 11	House: 22	US Cong: 4	Status: Construction I	Funding Com	mitted	
OR99E: Aurora-Salen Improvements	n Paving; Safety	on Jefferson-Ja	ames; signal imp	, raise the median rovements on eastle, Lincoln and	Pavement Preservation	7/26/2007	4/1/2009	\$7,545,000
Key: 13624	Region: 2	Senate: 17	House: 34	US Cong: 5	Status: Construction I	Funding Com	mitted	
Mar	ion County 'Co	nstruction F	unding Comr	nitted' Projects	s: Project count: 5,	Cost of Pr	ojects: \$75,72	28,000
I-5: Hayesville Itchg-E	Baldock rest area	construction wi	I produce the Fin II be under a differ roject will overlay	erent Key	Pavement Preservation	8/28/2006		\$114,000
Key: 12578	Region: 2	Senate: 11	House: 22	US Cong: 5	Status: Under Develo	pment		
OR22 at Sublimity Int 1	erchange Phase	construction wi number. This p interchange red Sublimity Interc	I produce the Fin Il be under a diffe roject is phase 1 construction on C change. It will pro	erent Key of the DR22 at the ovide free-flow	Modernization	2/7/2008		\$600,000
		traffic accelerates stream.	tion for safe mer	ge into traffic				

Marion County 'Under Development' Projects: Project count: 2, Cost of Projects: \$714,000

Total Project Count for Marion County: 14, Total Cost of Projects: \$104,297,684

Section Nam	ne:	P	Count	ty: Morrov	Work Type:	Estimated or Contract Bid Award:	Actual date of Construction Completion	Project
OR-74 Lexington - H	eppner		I provide pavement in stall bike/ped	ent preservation d lanes.	Pavement Preservation	on 11/18/2004	10/15/2005	\$1,977,139
Key: 11836	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Cons	truction		
	Мо	rrow County '	Under Const	ruction' Projec	ts: Project count	: 1, Cost of F	Project: \$1,97	7,139
OTIA III- East Beach Access (Port of Morr	•		l provide new rai umbia Ave from u	il access roads up Mainline to the	Modernization	9/1/2005	9/1/2007	\$5,850,000
Key: 13985	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Construction	n Funding Com	ımitted	

Morrow County 'Construction Funding Committed' Projects: Project count: 1, Cost of Project: \$5,850,000

Total Project Count for Morrow County: 2, Total Cost of Projects: \$7,827,139

			Count	y: Multno		Estimated or A	Actual date of: Construction	
Section Name:		Pi	roject Descript		Work Type:	Award:	Completion:	
OTIA I/II- Willamette River (Broadway) Br. (Phases 4		lower truss, rep	s lift span grating, placing the concre ewalks on bridge	ete bridge deck	Bridge	11/21/2002	11/15/2004	\$27,694,148
Key: 12493	Region: 1	Senate: V	House: V	US Cong: V	Status: Construction	Complete		
I-5 Iowa St. Slide Repair		Project to repair Highway in Port	r a slide area alor tland.	ng the Pacific	Operations	5/23/2002	11/15/2002	\$566,479
Key: 12010	Region: 1	Senate: 06	House: 36	US Cong: 1	Status: Construction	Complete		
I-5 Columbia River N & S Bridges (Portland)	3-Bound	on the north and Columbia River	Bridge Numbers	ridges across the	Bridge	4/24/2003	12/31/2004	\$14,433,857
Key: 10685	Region: 1	Senate: 22	House: 44	US Cong: 3	Status: Construction	Complete		
M	lultnomah (County 'Cons	truction Com	iplete' Projects	s: Project count: 3,	Cost of Pro	ojects: \$42,6\$	94,484
OTIA I/II- SW Champlain S			ace structure br,		Bridge	6/30/2004	Not Available	\$283,000
Key: 12431	Region: 1	Senate: 22	House: 44	US Cong: 1	Status: Under Constr	uction		
Region 1 Traffic Loop Rep & 13			epair Unit 12 & 13		Operations	1/27/2005	9/28/2005	\$270,150
Key: 13698	Region: 1	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
I-205 Columbia River - Wi River Bridges	illamette	Bridge to Harold interchange ram	ves 7.54 miles (C d Street) of NB ar nps and frontage rridges. Includes s	ind SB lanes and roads; structural	Pavement Preservation	n 1/27/2005	6/30/2006	\$18,735,275
Key: 11942	Region: 1	Senate: V	House: V	US Cong: 3	Status: Under Constr	uction		
I-5 Capitol Hwy to Marqua (Portland)	am Bridge	freeway betwee Highway and the will modify over clearance and a	ne Marquam Bridg rpasses to increas add needed safet	ge with the Capitol ge. The project use vertical ty improvements.	Pavement Preservation	1 3/1/2003	2/28/2005	\$25,360,479
Key: 09364	Region: 1	Senate: 18	House: 36	US Cong: 1	Status: Under Constr	uction		
US-26 Ross Island Bridge Ave (Portland)	e - SE 50th	Hood Highway I and SE 50th Av	I repave about 2.4 between the Ros venue. The proje letectors at traffic	ect will install bus	Pavement Preservation	1 7/22/2004	9/30/2005	\$3,759,501
Key: 10731	Region: 1	Senate: 21	House: 42	US Cong: 3	Status: Under Constr	uction		
US-30B St. Johns. Br. Pai Rehab. (Portland)	inting &	deck and repair safety improven	I repair bridge joir nt the St. John's E ments. Replace o ch ramps on west	Bridge, some drainage and	Bridge	8/22/2002	6/30/2005	\$43,080,297
Key: 09393	Region: 1	Senate: 17	House: 33	US Cong: 3	Status: Under Constr	uction		

Multnomah County 'Under Construction' Projects: Project count: 6, Cost of Projects: \$91,488,703

OTIA I/II- NE 33rd Ave Over Lombs St. & UPRR Key: 12448 Region I-84: 102nd Avenue Crossing-Bun 219 Key: 14257 Region OTIA I/II- Corbett Hill Road Viaduo	Senate: 22	ace bridge #0248 House: 43	34 in Portland.	Bridge	0/04/0005		
I-84: 102nd Avenue Crossing-Bun 219 Key: 14257 Region		House: 12		2	3/31/2005	1/1/2008	\$3,506,000
219 <i>Key: 14257 Region.</i>	e This project will	110use. 45	US Cong: 3	Status: Construction	Funding Comn	nitted	
		repair bridge nui	mber 13514E.	Bridge	9/1/2006	8/1/2008	\$3,282,000
OTIA I/II Corbott Hill Bood Viadua	Senate:	House:	US Cong:	Status: Construction	Funding Comn	nitted	
OTIA I/II- Corbett Hill Road Viaduc	Project will repla	ace bridge #51C	11 on Corbett Hill	Bridge	12/31/2005	9/1/2006	\$1,047,000
Key: 12442 Region	Senate: 26	House: 52	US Cong: 3	Status: Construction	Funding Comn	nitted	
OTIA I/II- Beaver Creek Bridge			22, located on the y near Troutdale.	Bridge	3/31/2005	9/1/2007	\$1,734,000
Key: 12441 Region	Senate: 26	House: 52	US Cong: 3	Status: Construction	Funding Comn	nitted	
Portland area variable message si	ns This project inst signs for Portlar	alls three new vand.	ariable message	Operations	8/24/2006	11/1/2007	\$900,000
Key: 13699 Region	Senate: V	House: V	US Cong: 1	Status: Construction	Funding Comn	nitted	
OTIA I/II- NE 33rd Ave. Over Columbia Slough	Project will repla	ace bridge #25T1	12 in Portland.	Bridge	6/30/2005	5/1/2007	\$1,456,000
Key: 12445 Region.	Senate: 22	House: 44	US Cong: 3	Status: Construction	Funding Comn	nitted	
East Portland Freeway at Glisan S & Park Place	This project will	expand ramp me	eter installation.	Operations	9/30/2004	12/1/2006	\$1,931,000
Key: 13464 Region.	Senate: V	House: V	US Cong: 3	Status: Construction	Funding Comn	nitted	
OR-99E Martin Luther K./Grand Viaducts (Portland)		replace the bridging Avenue acros #2115).		Bridge	11/10/2005	10/1/2009	\$42,134,000
Key: 09350 Region.	Senate: 21	House: 41	US Cong: 3	Status: Construction	Funding Comn	nitted	
OTIA I/II- Powell Blvd (174th to Burnside)	Project will cons 174th and Burns	struct a five lane side in Portland.	road between	Modernization	9/30/2005	3/1/2008	\$11,250,000
Key: 12911 Region	Senate: 25	House: 49	US Cong: 3	Status: Construction	Funding Comn	nitted	
OTIA I/II- US-30B E. Columbia Blvd Lombard St. Connector	 Project will cons and at-grade int 	struct a new, wide ersection.	er underpass	Modernization	9/30/2007	2/1/2008	\$30,742,000
Key: 08838 Region.	Senate: 22	House: 44	US Cong: 3	Status: Construction	Funding Comn	nitted	
OTIA I/II- US-30B Sandy Blvd. (NE 13th to NE 47th)	overlay with nev	ove excess pave v, build curb exte ts of the sidewalk	ensions, and	Pavement Preservation	n 1/19/2005	5/1/2007	\$8,205,000
Key: 12390 Region	-	House: V	US Cong: 3	Status: Construction	Funding Comn	nitted	
OTIA I/II- US-30B Sandy Blvd East 162nd to 207th		widen road to ac	dd shoulders, overlay pavement.	Pavement Preservation	n 4/5/2005	11/1/2006	\$1,346,000
Key: 12906 Region.	Senate: 25	House: 49	US Cong: 3	Status: Construction	Funding Comn	nitted	
Multnomah County	Construction Fur	nding Commi	itted' Projects:	Project count: 12	, Cost of Pro	jects: \$107,	533,000
I-405 Fremont Bridge - Marquam Bridge	construction will number. This is only to complete study to identify	e a design alterna possible options reeway while co	rent Key gineering project atives analysis s for resurfacing	Pavement Preservation	n 9/1/2005		\$250,000
Key: 13704 Region		House: 36	US Cong: 1	Status: Under Develo	pment		

Multnomah County 'Under Development' Projects: Project count: 1, Cost of Project: \$250,000

County: Mult	tnomah	Estimated or			
County. Mun	liioiiiaii	Contract Bid	Construction	Project	
Project Descripton:	Work Type:	Award:	Completion:	Cost:	

Total Project Count for Multnomah County: 22, Total Cost of Projects: \$241,966,187

Section Name:

	County: Polk	Estima	ated or Actual date of:
Section Name:	Project Descripton:	Contrac Work Type: Awa	
OTIA I/II- OR 22 - Rickreal Creek (Dallas)	Project will overlay, add curb ramps, ped crossings island near Uglow St.	Pavement Preservation 12/3	1/2004 9/30/2004 \$993,626
Key: 12524 Region: 2	Senate: 12 House: 23 US Cong: 5	Status: Construction Comp	lete
Polk	County 'Construction Complete' Project	ts: Project count: 1, Co	st of Project: \$993,626
OTIA I/II- OR22 @OR99W & OR233 Interchange (Rickreall)	This project will construct a grade separated interchange on a multi-lane highway.	Modernization 3/25	/2005 11/30/2006 \$18,263,857
Key: 14135 Region: 2	Senate: 08 House: 23 US Cong: 5	Status: Under Construction	
OTIA I/II- OR-223 Kings Valley Hwy @ Dallas-Rickreall Hwy	Project will realign and widen the intersection.	Modernization 3/31/	/2005 12/15/2005 \$3,554,377
Key: 12915 Region: 2	Senate: 12 House: 23 US Cong: 5	Status: Under Construction	
Po	olk County 'Under Construction' Projects	s: Project count: 2, Cos	t of Projects: \$21,818,234
OR-18 Fort Hill to Wallace Bridge (West of Salem)	This project will widen about 2.7 miles of highway between Fort Hill and Wallace Bridge. Includes adding a concrete median barrier and a local access road.	Modernization 2/10	/2004 Not Available \$348,000
Key: 10623 Region: 2	Senate: 12 House: 23 US Cong: 5	Status: Construction Funding	ng Committed
OR-18 @ Fort Hill Road	This project will realign Fort Hill Road & build a left turn refuge at the realigned intersection of OR-18 and Fort Hill Road near Valley Junction.	Safety 9/1/2	2003 Not Available \$620,000
Key: 09278 Region: 2	Senate: 12 House: 10 US Cong: 5	Status: Construction Fundi	ng Committed
Polk County 'Co	onstruction Funding Committed' Projects	s: Project count: 2, Cos	t of Projects: \$968,000
OR22 At Perrydale Road - Salt Creek	This project will produce the Final Plans, and construction will be under a different Key number. This project will realign the county road's intersection with the highway improving a driver's ability to safely manuver the intersection.	Safety 10/9	/2008 \$228,000
Key: 13778 Region: 2	Senate: 12 House: 23 US Cong: 5	Status: Under Development	:
F	Polk County 'Under Development' Projec	ts: Project count: 1, Co	st of Project: \$228,000

			Count	ty: Sherm	nan	Estimated or Contract Bid	Estimated or Actual date of: Contract Bid Construction	
Section Name:		Project Descripton:			Work Type:	Award:	Completion:	Project Cost:
US-97 Biggs-Wasco Correction	Field Curve	Project will pro	ovide pavement p on.	reservation and	Pavement Preserv	ation 3/1/2003	10/31/2004	\$5,569,641
Key: 12127	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Construct	ion Complete		

Sherman County 'Construction Complete' Projects: Project count: 1, Cost of Project: \$5,569,641

Total Project Count for Sherman County: 1, Total Cost of Projects: \$5,569,641

			Count	y: Tillamo	ook ,	Estimated or A	Actual date of: Construction	Project
Section Name:		Pro	oject Descrip		Work Type:	Award:	Completion:	Cost:
OTIA I/II- Earl Bridge		Project will remo			Bridge	6/30/2003	9/30/2003	\$142,000
Key: 12924	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Construction	Complete		
OTIA I/II- Blaser Bridge		Project will repla	ce the Blaser B	ridge.	Bridge	4/16/2003	12/31/2003	\$1,259,000
Key: 11976	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Construction	Complete		
OTIA I/II- Ocean St US	S 101	Project will overlapave the shoulded			Pavement Preservation	n 3/31/2003	10/31/2003	\$2,120,461
Key: 12308	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Construction	Complete		
	Tillamook	County 'Const	ruction Con	plete' Projects	s: Project count: 3	B, Cost of Pr	ojects: \$3,52°	1,461
US101-OR22: Blanchar US101-Castle Rk	d-Brooten &	This project will on and 11854.	overlay. Combir	ne Key #s 11855	Pavement Preservation	n 3/12/2004	6/30/2005	\$4,403,579
Key: 13466	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Under Const	ruction		
	Tillam	ook County 'U	nder Consti	ruction' Projec	ts: Project count:	1, Cost of P	roject: \$4,400	3,579
OR6 @ Wilson River Lo	oop Road	This project will o	construct interch	nange.	Modernization	3/1/2008	3/1/2010	\$8,550,000
Key: 12817	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Construction	Funding Com	mitted	
OTIA I/II- US101 @ Lon (Tillamook County)	g Prairie Road	Project will impro		and may include	Modernization	10/20/2006	10/1/2007	\$902,000
Key: 12913	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Construction	Funding Com	mitted	
US-101 Wilson River (7 Bridge #1499	Tillamook)	This project will in the Tillamook Brit Tillamook.			Bridge	11/20/2003	5/1/2006	\$324,000
Key: 10598	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Construction	Funding Com	mitted	
US101: Manzanita - who	eeler	Overlay old pave	ment with new.		Pavement Preservation	n 2/23/2006	2/1/2007	\$1,707,000
Key: 12852	Region: 2	Senate: 16	House: 32	US Cong: 1	Status: Construction	Funding Com	mitted	
US-101 Jetty Creek Rea	alignment	This project will on poor sight distan		vertical curve with lide.	Operations	3/11/2004	3/1/2010	\$1,221,000
Key: 10369	Region: 2	Senate: 16	House: 32	US Cong: 1	Status: Construction	Funding Com	mitted	
US-101 at Latimer Road	d	Project will instal and improve the and US 101.			Modernization	3/15/2007	5/1/2008	\$3,470,000
Key: 11667	Region: 2	Senate: 16	House: 32	US Cong: 5	Status: Construction	Funding Com	mitted	

Tillamook County 'Construction Funding Committed' Projects: Project count: 6, Cost of Projects: \$16,174,000

Total Project Count for Tillamook County: 10, Total Cost of Projects: \$24,099,040

			Coun	ty: Umatil	la		Actual date of:	
Section Nam	e:	ı	Project Descrip		Work Type:	Contract Bid Award:	Construction Completion:	
OR-11 Milton Freewa Improvements	ter Safety		regon - Washing	vements along 2.7 ton Highway in	Safety	2/28/2002	12/31/2004	\$1,102,529
Key: 10546	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Construction	n Complete		
	Umatilla	a County 'Co	nstruction Co	omplete' Projec	cts: Project count	: 1, Cost of F	Project: \$1,10	2,529
I-84: MP217 Mission 8 26.5 Madison VMS	MP217 Mission & OR207: MP This project will install Valadison VMS		ll install Variable	Message Signs.	Operations	6/30/2005	11/15/2005	\$412,917
Key: 14167	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Under Cons	truction		
OR 11: Weston Bridg	e	This project wi Bridge).	ll replace bridge	# 08929 (Weston	Bridge	6/1/2004	8/31/2005	\$4,117,226
Key: 12934	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Under Cons	truction		
OR-204 Tollgate Sec	tion	Project include and safety upo	eave about 10.1 res minor realignn grades. The proj grorthwest of El	ect is located	Pavement Preservation			\$16,476,310
Key: 10267	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Cons	truction		
Cold Springs Hwy - S (Pendleton)	SW Court Place		end SW Court p roject is a combi 153.		Modernization	9/25/2003	11/30/2005	\$10,595,151
Key: 13209	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Cons	truction		
US-395 Cape Horn St Rd.	ummit - Albee	between milep be excavated	as part of the pro project is located	41.96. Slopes will	Pavement Preservation	on 9/25/2003	11/30/2005	\$6,295,146
Key: 09522	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Under Cons	truction		
US-730 Jct. Hwy 333 State Line	Hwy 333 - Washington This project will provide pavement preservation with overlay. Correct safety deficiencies in guardrail sections to meet standards and minimum heights.		ficiencies in	Pavement Preservation	on 11/18/2004	9/30/2005	\$1,951,531	
Key: 11835	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Under Cons	truction		

			Count	y: Umatill	a E	stimated or A	Actual date of: Construction	Project	
Section Name:		Pı	roject Descript	ton:	Work Type:	Award:	Completion:	Cost:	
Greasewood Creek Bridg	je		replace the Great e #04792. The bath standards.		Bridge	6/1/2007	4/1/2008	\$375,000	
Key: 12795	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction Funding Committed				
OTIA I/II- I-84/US-395: Sta Interchange Improvemen		(OTIA III) and a	repair Bridge #0 ccess managem ② Pilot Truck Sto	ent	Bridge	9/30/2005	3/1/2009	\$19,750,000	
Key: 13429	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction I	Funding Comm	nitted		
OR 11: US 30 - Adams		This project is for preserve it.	or reparing the pa	avement to	Pavement Preservation	2/12/2007	11/1/2007	\$1,463,000	
Key: 12637	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction I	Funding Comm	nitted		
OR207 @ Hermiston Ave	(Hermiston)	This project will	improve intersec	ction.	Operations	8/24/2006	10/1/2007	\$690,000	
Key: 12593	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction I	Funding Comm	nitted		
OTIA I/II- OR207: Diagona	al Rd-I84			rojects for the preservation and	Pavement Preservation	3/31/2006	3/1/2008	\$5,400,000	
Key: 13768	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction I	Funding Comm	nitted		
US 395: Pendleton Interc Ramps	hange	Project will prov 84 interchange.		on of the OR-37/I-	Modernization	6/5/2007	10/1/2008	\$1,905,000	
Key: 12592	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction I	Funding Comm	nitted		
US-730 Columbia River F Guardrail Improvements	lwy -		ting bridge rails, nt and install gua	install a retaining ardrail.	Operations	11/18/2004	8/1/2006	\$344,000	
Key: 11834	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction I	Funding Comm	nitted		
Umatilla	County 'Co	onstruction Fเ	ınding Comn	nitted' Projects	: Project count: 7,	Cost of Pro	ojects: \$29,92	27,000	
184: Cabbage Hill Chain U Expansion	Jp	construction wil number. This pr area on Intersta lighting to enhal	produce the Final be under a differ oject will expand te 84 at Cabbag noe the saftey of and improve the v	rent Key I the chain up e Hill, including	Operations	4/10/2007		\$25,000	
Key: 13614	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Under Develop	pment			
OR207: Hermiston - Diag	onal Road	construction wil number. This pr	n, improving sigh	rent Key the existing six-	Modernization	11/10/2005		\$153,000	
Key: 12591	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Under Develop	pment			

Umatilla County 'Under Development' Projects: Project count: 2, Cost of Projects: \$178,000

Total Project Count for Umatilla County: 16, Total Cost of Projects: \$71,055,811

Section Name:		P	Count	y: Union	Work Type:	Estimated or A Contract Bid Award:	Actual date of: Construction Completion:	Project
I-84 Truck Safety Project		Burnt River Car	install truck warn nyon section, bric ach heating in La	dge deck and	Safety	9/30/2004	9/15/2005	\$1,821,085
Key: 13580	Region: 5	Senate:	House:	US Cong:	Status: Under Const	ruction		
OTIA I/II- I-84 EB over Gra River (Upper Perry)	nde Ronde	Project will repland	ace the Eastbour	nd Upper Perry	Bridge	9/30/2003	10/31/2006	\$9,657,341
Key: 12363	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Const	ruction		
Elgin City Section		•	the pavement b	ase, repave, add	Modernization	2/24/2005	11/30/2005	\$4,519,085
Key: 12033	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Const	ruction		
OR-82 La Grande Corrido Impr. (Island City)	r Trns.		s of a minor realig and expansion of		Modernization	10/9/2003	10/15/2005	\$4,337,275
Key: 11827	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Const	ruction		
OR82: Wallowa Lake Hwy Left Turn Lanes	Combined	improving the M	ovements are dire Market Lane and a providing a left	Alicel Lane	Safety	6/28/2004	6/30/2005	\$1,510,046
Key: 13238	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Const	ruction		
US 30 @ Willow Street (La	Grande)	This project will	install a traffic si	ignal.	Operations	11/4/2004	10/31/2005	\$790,755
Key: 12628	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Under Const	ruction		
	Uni	on County 'U	nder Constru	ıction' Projects	s: Project count: 6	6, Cost of Pr	ojects: \$22,6	35,587
I-84 Grande Ronde Under Upper Perry Arch	crossing	Project will repla	ace bridge (#006	26).	Bridge	2/10/2005	8/1/2008	\$1,849,000
Key: 11852	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Construction	Funding Com	mitted	
US30/OR203: WCL La Gra	nde - Union	Pavement pres	ervation and turn	channelization.	Pavement Preservation	n 1/26/2006	6/1/2007	\$5,298,000
Key: 14127	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Construction	Funding Com	mitted	
OR 82 @ Pierce Road (Un	ion County)	This project will	improve intersec	ctions.	Safety	1/25/2007	4/1/2008	\$807,000
Key: 12643	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Construction	Funding Com	mitted	
Union	County 'Co	nstruction Fu	unding Comn	nitted' Projects	s: Project count: 3	B, Cost of Pr	ojects: \$7,95	4,000
OR203: East City Limits L Union	a Grande -	construction will number. This preservation, re guardrail to con		erent Key e pavement grade existing	Pavement Preservation	n 1/12/2006		\$315,000
Key: 12636	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Devel	opment		
OR82: Riddle Road - Imbl Grande)	er (La	construction will number. This pr	produce the Final be under a differ roject provides particular d improved safet	erent Key avement	Pavement Preservation	n 1/25/2007		\$127,000
Key: 13601	Region: 5	Senate: 29	House: 57	US Cong: 2	Status: Under Devel	opment		
US-30 La Grande/Flying J lane	Right Turn	construction wil			Safety	1/12/2006		\$45,000
		0	ovo baloty.					

	County: Union		Estimated or	Actual date of:		
	County. Official		Contract Bid	Construction	Project	
Section Name:	Project Descripton:	Work Type:	Award:	Completion:	Cost:	

Total Project Count for Union County: 12, Total Cost of Projects: \$31,076,587

Section Na	me:	F	Count Project Descrip	ty: Various	S Work Type:	Estimated or Contract Bid Award:	Actual date of: Construction Completion:	
Region 1 ATMS Ra 6)	mp Meters (Phase	Install ramp metering at freeway entrance ramps Operations in Region 1.		3/25/2004	10/31/2004	\$1,252,734		
Key: 10695	Region: 1	Senate: V	Senate: V House: V US Cong: V			n Complete		
Automated Traffic	Recorder Sites	automatic traff	air or replace tra ic counter sites. litional automatio gion 2.	The project will	Operations	7/25/2002	5/31/2004	\$300,858
Key: 10429	Region: 2	Senate: V	House: V	US Cong: V	Status: Construction	n Complete		
SE 4th Street - I 84 Butter Creek	& Strawberry Rd-	Project will pro	vide pavement p	preservation.	Pavement Preservat	ion 2/26/2004	9/30/2004	\$4,348,745
Key: 13458	Region: 5	Senate: 29	House: 58	US Cong: 2	Status: Construction	n Complete		
US 97: Cottonwood Jct&Fremont Jct-L		97 from Cottor	vide pavement p wood to Fremon ion to the Lake C		Pavement Preservat	ion 6/1/2004	9/15/2004	\$4,315,715
Key: 12130	Region: 4	Senate: 28	House: 55	US Cong: 2	Status: Construction	n Complete		

Various County 'Construction Complete' Projects: Project count: 4, Cost of Projects: \$10,218,051

			Count	y: Variou		Estimated or a	Actual date of:	
Section Name:		Pr	oject Descript		Work Type:	Award:	Construction Completion:	•
Region 1 Traffic Signal Up (Unit 2)	ogrades	This project will Region 1.	upgrade various	s traffic signals in	Operations	4/22/2004	7/31/2005	\$1,821,770
Key: 10672	Region: 1	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
OTIA III- Mt. Hood to Cher (Combined)	nult	Design/Build brid stage 1.	dges from birdge	e option report	Bridge	3/31/2004	9/30/2006	\$36,948,000
Key: 13563	Region: 4	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
Area 1 Permanent Variabl Signs	e Message	This project will message signs to		nt variable	Safety	8/26/2004	3/31/2005	\$609,076
Key: 13183	Region: 2	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
ATMS Communications Infrastructure (Phase 6)		Project will insta fiber optic cable Management Op Region 1.	for the Transpo	rtation	Operations	11/25/2003	12/31/2004	\$2,166,069
Key: 10696	Region: 1	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
I-205 Columbia Rvr Bridg Willamette River	e to	This project will bound lanes (ab the Columbia Ri River.	out 6.66 miles)	of I-205 between	Pavement Preservation	1/23/2003	11/15/2004	\$18,483,756
Key: 10693	Region: 1	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
OTIA III- Clarks Branch to Race	Tunnel Mill	This project will 07745A, 07756A 07835A, 07839.	A, 07757AB, 078		Bridge	8/27/2004	5/18/2007	\$38,903,159
Key: 13711	Region: 2	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
I-5 Interstate Signing Proj	ect 2004	This project will interstate signing	•	r update	Pavement Preservation	3/16/2004	9/30/2005	\$1,943,221
Key: 12168	Region: 3	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
I-5: PCC Surface Repair		This project will Continuous reint 174.4 -188 and drainage issue a	forced concrete MP 253 - 260 ar	between MP	Pavement Preservation	9/30/2004	4/30/2005	\$1,075,244
Key: 13655	Region: 2	Senate: 10	House: 19	US Cong: 4	Status: Under Constr	uction		
US-101 Culverts		This project will 101.	repair various cu	ulverts on US-	Operations	3/24/2005	9/2/2005	\$801,910
Key: 11726	Region: 3	Senate: 16	House: 31	US Cong: 4	Status: Under Constr	uction		
OTIA III- US 20: Central O Bridges Project	regon Hwy	Project will repla Malheur Countie		Harney and	Bridge	2/26/2004	6/30/2006	\$30,382,045
Key: 13208	Region: 5	Senate: 30	House: 60	US Cong: 2	Status: Under Constr	uction		
District Operations and D Repair	rainage	Project will cons projects through		ainage repair	Operations	5/20/2004	9/30/2005	\$1,725,611
Key: 12366	Region: 2	Senate: V	House: V	US Cong: V	Status: Under Constr	uction		
Region 5 RWIS Cameras	(Phase 2)	Project will insta system cameras			Operations	10/14/2004	10/15/2005	\$367,609
Key: 11832	Region: 5	Senate: V	House: V	US Cong: 2	Status: Under Constr	uction		
Region 5 Overpass Scree	ning 2004	Project will insta on interstate brid		ening protection	Bridge	3/1/2004	6/30/2005	\$289,621
Key: 13135	Region: 5	Senate: V	House: V	US Cong: 2	Status: Under Constr	netion		

Various County 'Under Construction' Projects: Project count: 13, Cost of Projects: \$135,517,091

Section Name		Р	Coun'	ty: Variou		Estimated or contract Bid Award:	Actual date of: Constructior Completion:	Project
Region 1 Traffic Signal (Unit 4)	Upgrades	Upgrade variou	s traffic signals	in Region 1.	Operations	5/24/2007	8/1/2008	\$938,000
Key: 10874	Region: 1	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
Region 1 ATMS Comm Infrastructure	unications	data collections Management O	devices for the perations Centor is an Intelligent	np metering and Transportation er (TMOC) in Transportation	Operations	8/12/2005	2/1/2007	\$2,249,000
Key: 10870	Region: 1	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
Traffic Signal Upgrade	s (Unit 3)	Upgrade variou	s traffic signals	in Region 1.	Operations	9/21/2006	12/1/2007	\$901,000
Key: 10699	Region: 1	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
REGION 1 TRAFFIC LO UNIT 14	OOP REPAIR	Repair or replace	ce traffic detect	ors in Region 1.	Operations	3/1/2007	8/1/2013	\$886,000
Key: 10873	Region: 1	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
Region 2 Misc Operation	ons Project	Miscellaneous	operations proje	ects for Region 2.	Operations	1/26/2006	9/1/2007	\$802,000
Key: 13627	Region: 2	Senate: V		US Cong: V	Status: Construction		mitted	
Region 1 ATMS Hardw Software (Phase 8)	are and	This project will software in Reg		s, fiber optics and	Operations	9/1/2006	11/1/2007	\$1,009,000
Key: 12865	Region: 1	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
Region 2 sign rebuild 2	2006	Upgrade signs	to meet standar	ds.	Operations	10/27/2005	1/1/2007	\$324,000
Key: 12674	Region: 2	Senate: V			Status: Construction			,
OTIA III- I-5: Wilsonville Interchange	e-Hayesville	This project will 07794B. It will		s 07794A and 07855E and 09870.	Pavement Preservation	3/31/2006	4/1/2009	\$20,459,000
Key: 14033	Region: 2	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
OTIA III- I-84: Pendleto Powder Bundle 205	n - North	This project will includes repairs		07292B and te 84 bridge rail.	Bridge	3/9/2006	8/1/2008	\$6,128,000
Key: 14027	Region: 5	Senate: V	House: V	US Cong: 2	Status: Construction	Funding Com	mitted	
I-84: Sandy River - The (Fencing)	Dalles	Project will repa	air or reconstruc	ct fencing along I-	Pavement Preservation	n 4/27/2006	5/1/2008	\$1,697,000
Key: 12839	Region: 1	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
Region 2 OPS: Dallas S Loop Replacement	Signal & Var	This project will Main/Washington throughout Reg	on, replace vari	on OR223 @ ous signal loops	Operations	9/1/2007	10/1/2008	\$556,000
Key: 14155	Region: 2	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
US395: Deerlick Creek John Day River	-Middle Fork,	In addition to th	e pavement wo	ent preservation. rk, guardrail rought to current	Pavement Preservation	n 1/8/2007	8/1/2007	\$681,000
Key: 12639	Region: 5	Senate: V	House: V	US Cong: 2	Status: Construction	Funding Com	mitted	
OTIA III- I-5 and OR58: 217	Bridge Bundle	(bridge number	s 07732A and 0 ay 18, bridge n	II bridges on I-5 07732B) and on umbers. 07110, 25).	Bridge	11/10/2005	9/1/2007	\$2,608,000
Key: 14038	Region: 2	Senate: V	House: V	US Cong: V	Status: Construction	Funding Com	mitted	
Region 2 Bridge Painti	ng Project	Trask R Br (#56 Nehalem R (Mo Hwy, MP 17.7)			Bridge	9/21/2006	10/1/2007	\$603,000
		,,						

			Count	ty: Various	S	Estimated or Contract Bid	Actual date of: Construction	Project
Section Na	me:	F	Project Descrip		Work Type:	Award:	Completion:	Cost:
Region 2: Variable I	Message Signs	Signs that can Management (of delays, clos signs will be in 51, Highway 1	be programmed Center to notify the ures and possible stalled on Highw 26 at milepost 48 R69 at milepost	epost 7 and Interstate 5				\$1,451,000
Key: 14292	Region: 2	Senate: V	House: V	US Cong: V	Status: Construction	on Funding Com	mitted	
OTIA III- OR58: Willa Logging Road Bund		involving I-5/O	ll replace OTIA II R225 (bridge nur numbers 05287B	mber 08445) and	Bridge	12/14/2006 12/1/2009		\$12,864,000
Key: 14039	Region: 2	Senate: V	House: V	US Cong: V	Status: Construction	on Funding Com	mitted	
Region 2 Flasher Re	eplacements	This project wi	Il replace old flas	hing beacons.	Operations	2/20/2007	1/1/2008	\$175,000
Key: 13152	Region: 2	Senate: V	House: V	US Cong: V	Status: Construction	on Funding Com	mitted	
Vario	ous County 'Co	nstruction Fu	ınding Comm	nitted' Projects:	Project count:	17, Cost of Pr	ojects: \$54,3	31,000
Variable Message s 22, 126 and US20	igns-Highways	construction w number. This p messages sign	vest of the McKe	erent Key le variable 2, west of Idanha,	Operations	8/24/2006		\$50,000
Key: 13151	Region: 2	Senate: V	House: V	US Cong: V	Status: Under Dev	elopment		

Various County 'Under Development' Projects: Project count: 1, Cost of Project: \$50,000

Total Project Count for Various County: 35, Total Cost of Projects: \$200,116,142

Section Nan	ne:	F	Count	ty: Wasco	Estimated or Contract Bid Award:	Actual date of: Construction Completion:	Project	
US26: Badger Creek (Warm Springs)	-Sidwalter Rd	Project will cor	nstruct passing la	nes.	Modernization	10/23/2003	10/15/2004	\$1,626,127
Key: 13144	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Construction	on Complete		
	Wasco	County 'Cor	nstruction Co	mplete' Projec	ts: Project count	:: 1, Cost of P	Project: \$1,62	6,127
OTIA I/II- I-84 Over U Dalles	S030 at the	, ,	lace bridge # 087	766 due to cracks y.	Bridge	3/31/2005	10/15/2005	\$4,297,904
Key: 12930	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Under Cons	struction		

Wasco County 'Under Construction' Projects: Project count: 1, Cost of Project: \$4,297,904

Total Project Count for Wasco County: 2, Total Cost of Projects: \$5,924,031

Section Name:		Р	Count	ty: Washir		Estimated or Contract Bid Award:	Actual date of: Construction Completion:	Project
OTIA I/II- Tualatin River ((Rood Bridge Road)	Overflow	This project wil	l replace bridge	structure #671235.	Bridge	6/30/2003	12/30/2004	\$5,121,000
Key: 12907	Region: 1	Senate: 19	House: 26	US Cong: 1	Status: Construction	Complete		
I-5: Nyberg Rd Boone I section	Bridge	This project will cross-over acci		parrier to prevent	Safety	5/13/2004	10/15/2004	\$1,332,844
Key: 12863	Region: 1	Senate: 19	House: 37	US Cong: 1	Status: Construction	Complete		
OTIA I/II- Farmington Rd Preservation (Hwy 219-S	W209th)			widen roadway d lane, and make	Pavement Preservation	n 9/30/2003	3/31/2005	\$2,496,000
Key: 12392	Region: 1	Senate: 13	House: 26	US Cong: 1	Status: Construction	Complete		
OR-10 Beaverton/Tigard Mult./Wash. Cnty Line	Hwy -	miles of the Be	l grind down and averton-Hillsdale s safety improve		Pavement Preservation	n 4/25/2002	8/31/2004	\$4,305,072
Key: 10666	Region: 1	Senate: 17	House: 27	US Cong: 1	Status: Construction	Complete		
OR-47 Quince St. to Dist (Forest Grove)	. Boundary	Tualatin Valley in Forest Grove Gaston. The p	I repave about 8 Highway betwee and the District roject will include where they are r	en Quince Street Boundary in e safety	Pavement Preservation	n 2/26/2004	11/15/2004	\$3,102,307
Key: 10679	Region: 1	Senate: 13	House: 26	US Cong: 1	Status: Construction	Complete		
Minter Br. Rd. (Hillsboro) (Beaverton))- 117th Ave.	Valley Highway Beaverton and	ave 8.1 miles of between 117th Minter Bridge Ro safety improvem	Avenue in oad in Hillsboro	Pavement Preservation	n 4/25/2002	9/30/2003	\$7,354,600
Key: 10680	Region: 1	Senate: 17	House: 34	US Cong: 1	Status: Construction	Complete		
US 26: Strassel Rd - Neh	alem Hwy		left turn refuges ach of Nehalem	and realign Hwy with Sunset	Safety	12/18/2003	7/31/2004	\$1,015,505
Key: 13077	Region: 1	Senate: 16	House: 32	US Cong: 1	Status: Construction	Complete		
US-26 Camelot to Sylvan Interchange (Phase 2)	1	Highway betwee interchanges. To collector/distributhe Sylvan brid	en the Camelot he project builds	s east bound connections, and and phase of	Modernization	10/26/2000	6/30/2003	\$28,266,780
Key: 08009	Region: 1	Senate: 17	House: 34	US Cong: 1	Status: Construction	Complete		

Washington County 'Construction Complete' Projects: Project count: 8, Cost of Projects: \$52,994,107

Section Name:		P	County roject Descript	y: Washii ^{on:}		Estimated or Contract Bid Award:	Actual date of: Construction Completion:	Project
OTIA I/II- SW Nyberg Rd. (Tualatin)	@ I-5		en the structure a	S.	Modernization	12/31/2004	3/31/2005	\$4,402,255
Key: 11435	Region: 1	Senate: 13	House: 24	US Cong: 5	Status: Under Constr	uction		
OTIA I/II- US 26: OR-217 Interchange SEC	- Syvan	replace the Car widen the highv	instruct the Sunsityon Road Overc yay between Can Prchange by addii	rossing and nelot Court and	Modernization	6/30/2003	5/31/2005	\$24,100,478
Key: 13069	Region: 1	Senate: 17	House: 34	US Cong: 1	Status: Under Constr	uction		
OTIA I/II- Boones Ferry R Preservation	Rd.		ove excess pave nt of Boones Feri nt culvert.		Pavement Preservation	9/30/2003	12/31/2004	\$2,581,000
Key: 12388	Region: 1	Senate: 19	House: 37	US Cong: 1	Status: Under Constr	uction		
Vernonia NCL - Jct Suns	et Hwy		lvert repair will consfer \$260K to C		Pavement Preservation	10/9/2003	9/30/2004	\$4,507,026
Key: 13216	Region: 1	Senate: 16	House: 32	US Cong: 1	Status: Under Constr	uction		
OTIA I/II- Farmington Rd. SW 198th) Pres Safety	.(SW 209th-		overlay pavemented shoulder with provement.		Pavement Preservation	3/31/2004	Not Available	\$4,111,000
Key: 08850	Region: 1	Senate: 17	House: 30	US Cong: 1	Status: Under Constr	uction		
OR-10 Hwy 217 - SE Map	le Drive		en the road to cre d upgrade an off- ovement.		Pavement Preservation	n 6/1/2003	8/31/2005	\$1,249,720
Key: 12905	Region: 1	Senate: 17	House: 34	US Cong: 1	Status: Under Constr	uction		
OR-219 @ SE Walnut Str	eet	turn refuge at th	widen highway to be intersection of on Highway and	the	Safety	9/1/2003	9/30/2006	\$1,955,368
Key: 10867	Region: 1	Senate: 15	House: 29	US Cong: 1	Status: Under Constr	uction		
OR-219 Tongue Lane - G	rabel Road		build a left turn la ad to Tongue Lar		Safety	9/25/2003	9/30/2004	\$1,642,889
Key: 08006	Region: 1	Senate: 13	House: 26	US Cong: 1	Status: Under Constr	uction		
OR-6 S. Fork Rd. to Timb	er Rd.		1.2 miles of the \en the District bo		Pavement Preservation	n 6/23/2005	10/31/2005	\$4,378,944
Key: 11135	Region: 1	Senate: 16	House: 32	US Cong: 1	Status: Under Constr	uction		
OTIA I/II- US-26 Jackson Interchange	School Rd.	Project will build	d a new interchan	ge.	Modernization	6/30/2005	10/31/2005	\$13,834,535
Key: 12393	Region: 1	Senate: 15	House: 30	US Cong: 1	Status: Under Constr	uction		
OTIA I/II- US26: Cornell-Murray-OR217	Murray and		widen highway fi and add braided		Modernization	9/30/2004	6/30/2006	\$39,554,464
Key: 13459	Region: 1	Senate: 17	House: 33	US Cong: 1	Status: Under Constr	uction		
OTIA I/II- US-26 NW Corn Rd Interchange Improve		Project will build Road and add a	d new ramps,wide an interchange.	en Cornell Pass	Modernization	10/22/2003	2/1/2005	\$4,700,000
Key: 12909	Region: 1	Senate: 15	House: 26	US Cong: 1	Status: Under Constr	uction		

				y: Washin	igion _d	Contract Bid	Actual date of: Construction	Project
Section Name:		Pr	oject Descrip	ton:	Work Type:	Award:	Completion:	Cost:
US-26 @ Glencoe Road (Nort	th Plains)	This project will intersection of Gramp to the Sun	lencoe Road ar		Safety	1/27/2005	9/30/2005	\$270,792
Key: 10869 Re	egion: 1	Senate: 15	House: 30	US Cong: 1	Status: Under Consti	ruction		
Wa	ashingto	n County 'Und	der Construc	ction' Projects:	Project count: 13	, Cost of Pr	ojects: \$107,2	288,472
I-5: Capital Highway - Tualati	in River	This project will including joint re provide restripin	pair on the struc	•	Pavement Preservation	n 9/7/2006	4/1/2008	\$12,783,000
Key: 12858 Re	egion: 1	Senate: 18	House: 35	US Cong: 1	Status: Construction	Funding Com	mitted	
OR217: Sunset Hwy - SW 72r (Overlay)	nd	This project will barrier and restr	•	mm AC, replace	Pavement Preservation	n 5/31/2006	5/1/2008	\$10,468,000
Key: 12854 Re	egion: 1	Senate: 18	House: 35	US Cong: 1	Status: Construction	Funding Com	mitted	
OR- 219 Hilsboro - Silverton Unger Rd.	Hwy @	Construct left an Hillsboro-Silvert Unger Rd.			Safety	10/13/2005	1/1/2007	\$1,201,000
Key: 11943 Re	egion: 1	Senate: 13	House: 26	US Cong: 1	Status: Construction	Funding Com	mitted	
OR-219 @ Farmington Road		This project will on OR 219 and Campbells Bridg	Farmington Rd.	d right turn lanes and replace	Safety	10/28/2004	1/1/2008	\$3,542,000
Key: 11931 Re	egion: 1	Senate: 13	House: 26	US Cong: 1	Status: Construction	Funding Com	mitted	
OR219 @ Burkhalter/Simpso	n Rd	This project will	channelize left t	urns.	Safety	9/21/2006	1/1/2008	\$1,581,000
Key: 12861 Re	egion: 1	Senate: 13	House: 26	US Cong: 1	Status: Construction	Funding Com	mitted	
US-26 Hayward Rd - Chrysle	r Dr.	This project will (continuous left point.			Safety	1/26/2006	3/1/2007	\$2,400,000
Key: 05329 Re	egion: 1	Senate: 16	House: 32	US Cong: 1	Status: Construction	Funding Com	mitted	
US26: Sunset Highway Denn Edwards Tunnel	nis L	This project will and lighting on t (02552) on US2	he Dennis L Edv	wards Tunnel	Bridge	3/1/2007	9/1/2008	\$9,617,000
Key: 11948 Re	egion: 1	Senate: 16	House: 32	US Cong: 1	Status: Construction	Funding Com	mitted	
Washington Co	ounty 'Co	nstruction Fu	nding Comr	nitted' Projects	: Project count: 7	, Cost of Pr	ojects: \$41,59	92,000
OR217: US26 - TV Hwy		This project will construction will number. This pro structures. Com	be under a diffe oject will widen l	erent Key highway and	Modernization	3/8/2007		\$1,868,000
Key: 06025 Re	egion: 1	Senate: 14	House: 27	US Cong: 1	Status: Under Develo	opment		
US 26: Sunset Hwy @ Glence Ramp Impr.	oe Rd	This project will construction will number. Project of Sunset Highw	be under a diffe will relocate ran	erent Key nps on south side	Modernization	9/25/2007		\$522,000
Key: 12885 Re	egion: 1	Senate: 15	House: 30	US Cong: 1	Status: Under Develo	onment		

Washington County 'Under Development' Projects: Project count: 2, Cost of Projects: \$2,390,000

Total Project Count for Washington County: 30, Total Cost of Projects: \$204,264,579

			Count	y: Wheel	er	Estimated or Contract Bid	Actual date of Construction	
Section Name	Р	roject Descrip	ton:	Work Type:	Award:	Completion		
OTIA I/II- Kinzua Ln. (V	Wheeler County)	,	onstruct roadway and add/replace	, ,	Pavement Preserva	ion 9/30/2003	6/30/2004	\$1,172,000
Key: 12415	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Construction	on Complete		
	Wheeler	County 'Con	struction Co	mplete' Projec	cts: Project coun	t: 1, Cost of F	Project: \$1,17	2,000
US26: At Rush Creek Mitchell	Road and	will also retrofit	overlay the exis the six bridges ard rail with Thri	,	Pavement Preserva	ion 9/30/2006	8/1/2007	\$3,124,000
Key: 12571	Region: 4	Senate: 30	House: 59	US Cong: 2	Status: Construction	on Funding Con	ımitted	
Whee	eler County 'C	onstruction l	Funding Con	nmitted' Projec	cts: Project coun	t: 1, Cost of F	Project: \$3,12	4,000

Total Project Count for Wheeler County: 2, Total Cost of Projects: \$4,296,000

County: Yamhill					Estimated or Actual date of: Contract Bid Construction Pr						
Section Nar	me:	P	roject Descrip		Work Type:	Award:	Completion:	Project Cost:			
S Fork Yamhill river phase 2	bridge #08063 -	This project wil	I provide emerge	ency bridge repair	Bridge	5/13/2004	9/30/2004	\$1,089,080			
Key: 13556	Region: 2	Senate: 15	House: 38	US Cong: 5	Status: Under Con	struction					
	Yan	nhill County '	Under Const	ruction' Projec	ts: Project coun	t: 1, Cost of P	roject: \$1,089	9,080			
OR18 @ Red Prairie	Road	This project wil deceleration la	l change alignmenes.	ent and add	Safety	12/14/2006	2/1/2008	\$712,000			
Key: 13028	Region: 2	Senate: 12	House: 24	US Cong: 1	Status: Construction	on Funding Com	mitted				
OR-219 @ Wilsonvil	lle Road	to OR 219. Bu 219 and Spring conflict with the for the Newber and beacons n	ild new connection	ocation that avoids 19 interchange ss. Install signs ion of Hillsboro-	Safety	12/31/2002	12/1/2006	\$1,172,000			
Key: 09274	Region: 2	Senate: 13	House: 25	US Cong: 1	Status: Construction	on Funding Com	mitted				
OR99W: Dundee-Mo Improvements	Minnville Signal	Intersections: 9 99W/McDonald	•	e; 4th/Adams and	Operations	12/28/2006	3/1/2008	\$1,537,000			
Key: 12670	Region: 2	Senate: 12	House: 24	US Cong: 1	Status: Construction	on Funding Com	mitted				
Yar	nhill County 'Co	onstruction F	unding Comi	mitted' Projects	s: Project count	3, Cost of Pr	ojects: \$3,421	1,000			
OR99W: Parks Rd (Dundee)-Handley St (McMinnville)		construction wi	This project will produce the Final Plans, and construction will be under a different Key number. This project will overlay existing pavement.			tion 1/27/2006		\$300,000			
				US Cong: 1							

Yamhill County 'Under Development' Projects: Project count: 1, Cost of Project: \$300,000

Total Project Count for Yamhill County: 5, Total Cost of Projects: \$4,810,080

Grand Total for Report: 419 projects, Worth: \$2,531,262,352

Highway Construction Plan - Program Summary July 1, 2005 - June 30, 2007 (Based on Estimated Cost)


		Under		Funding		Under		Construction			
	D	evelopment		Committed		Construction		Complete		Totals:	
				Reg	ioi	n 1					
Bridge			\$	68,302,000	\$	43,363,297	\$	47,249,005	\$	158,914,302	
Modernization	\$	2,664,000	\$	57,685,000	\$	127,601,332	\$	55,049,240	\$	242,999,573	
Operations			\$	10,642,508	\$	4,257,989	\$	1,819,212	\$	16,719,709	
Preservation	\$	958,000	\$	95,472,000	\$	96,336,144	\$	34,577,047	\$	227,343,191	
Safety	\$	864,000	\$	20,830,000	\$	16,903,642	\$	2,681,070	\$	41,278,712	
Totals:	\$	4,486,000	\$	252,931,508	\$	288,462,403	\$	141,375,575	\$	687,255,486	
				Reg	ioi	n 2					
Bridge	\$	210,000	\$	346,054,000	\$	85,975,854	\$	44,652,058	\$	476,891,912	
Modernization	\$	6,486,000	\$	55,579,000	\$	27,818,888	\$	15,145,388	\$	105,029,276	
Operations	\$	365,000	\$	9,950,000	\$	2,593,527	\$	300,858	\$	13,209,385	
Preservation	\$	777,000	\$	42,129,000	\$	75,426,079	\$	24,270,398	\$	142,602,476	
Safety	\$	228,000	\$	14,688,000	\$	6,596,039	\$	10,534,847	\$	32,046,886	
Totals:	\$	8,066,000	\$	468,400,000	\$	198,410,387	\$	94,903,549	\$	769,779,936	
		.,,						- ,, -		, .,	
	Region 3										
Bridge			\$	161,170,000	\$	105,894,391	\$	32,718,655	\$	299,783,046	
Modernization	\$	2,500,000	\$	79,999,000	\$	91,725,555	\$	5,621,703	\$	179,846,258	
Operations			\$	4,620,000	\$	3,853,160			\$	8,473,160	
Preservation	\$	1,428,000	\$	15,930,000	\$	43,220,193	\$	9,145,201	\$	69,723,394	
Safety	\$	166,000	\$	334,000	\$	1,357,751	\$	607,000	\$	2,464,751	
Totals:	\$	4,094,000	\$	262,053,000	\$	246,051,049	\$	48,092,560	\$	560,290,609	
				Reg	ioi	n 4					
Bridge			\$	21,767,000	\$	81,504,507	\$	1,364,124	\$	104,635,631	
Modernization	\$	100,000	\$	17,381,269	\$	44,570,601	\$	1,626,127	\$	63,677,996	
Operations			\$	595,000			\$	3,047,220	\$	3,642,220	
Preservation			\$	26,405,000	\$	14,053,063	\$	22,054,391	\$	62,512,454	
Safety			\$	651,000			\$	1,391,988	\$	2,042,988	
Totals:	\$	100,000	\$	66,799,269	\$	140,128,170	\$	29,483,850	\$	236,511,289	
				Reg	ioi	n 5					
Bridge	\$	942,000	\$	82,060,000	\$	70,676,038	\$	4,152,326	\$	157,830,364	
Modernization	\$	153,000	\$	22,725,000	\$	19,451,511	\$	6,494,699	\$	48,824,210	
Operations	\$	339,000	\$	1,034,000	\$	1,571,282	*	-,,	\$	2,944,282	
Preservation	\$	442,000	\$	20,037,000	\$	37,712,773	\$	4,348,745	\$	62,540,518	
Safety	\$	45,000	\$	807,000	\$	3,331,131	\$	1,102,529	\$	5,285,660	
Totals:	\$	1,921,000	\$	126,663,000	\$	132,742,735	\$	16,098,298	\$	277,425,033	
Grand Totals:	\$	18,667,000	¢	1,176,846,776	¢	1,005,794,744	\$	329,953,832	\$	2,531,262,352	
Crana rotais.	Ψ	10,001,000	Ψ	.,	Ψ	.,000,134,144	Ψ	J20,000,032	Ψ	2,001,202,002	

Statewide Totals by Work Type and Status

TOTALS:		Under		Funding	Under		Construction			
TOTALO.	D	evelopment	Committed		Construction		Complete		Totals:	
Bridge	\$	1,152,000	\$	679,353,000	\$ 387,414,087	\$	130,136,168	\$	1,198,055,255	
Modernization	\$	11,903,000	\$	233,369,269	\$ 311,167,886	\$	83,937,158	\$	640,377,313	
Operations	\$	704,000	\$	26,841,508	\$ 12,275,957	\$	5,167,291	\$	44,988,756	
Preservation	\$	3,605,000	\$	199,973,000	\$ 266,748,251	\$	94,395,782	\$	564,722,033	
Safety	\$	1,303,000	\$	37,310,000	\$ 28,188,563	\$	16,317,433	\$	83,118,996	
Totals:	\$	18,667,000	\$	1,176,846,776	\$ 1,005,794,744	\$	329,953,832	\$	2,531,262,352	
# of Projects:		37		177	137		68		419	

STIP Project Lifecycle Calendar Year 1998 2000 2001 2002 2003 2005 2007 2009 2011 2012 2013 1999 2004 2006 2008 2010 Jan 1 - Dec 31 1999-2001 Biennium 2001-2003 Biennium 2003-2005 Biennium 2005-2007 Biennium 2007-2009 Biennium 2009-2011 Biennium 2011-2013 Biennium State of Oregon Fiscal Year July 1 - June 30 FY 20012 FY 1999 FY 2000 FY 2001 FY 2002 FY 2003 FY 2004 FY 2005 FY 2006 FY 2007 FY 2008 FY 2009 FY 2010 FY 2011 FY 20013 Federal Fiscal Year FY 20012 FY 1998 FY 1999 **FY 2000** FY 2001 FY 2002 FY 2003 FY 2004 FY 2005 FY 2006 **FY 2007 FY 2008** FY 2009 FY 2010 FY 2011 Oct 1 - Sept 30 1998-2001 STIP 2000-2003 STIP 2002-2005 STIP Statewide Transportation Improvement Program (STIP) 2004-2007 STIP 2006-2009 STIP 2008-2011 STIP PE 33% PE 33% PE 33% CP 15% CP 63% CP 22% **Large Modernization Project** PE 100% **CP 100%** Typical Preservation or Safety Project **Examples of STIP Projects Starting in** Different Years PE 33% PE 33% PE 33% CP 15% **CP 63% CP 22%** PE = Preliminary Engineering PE 33% PE 33% PE 33% CP 15% **CP 63%** CP 22% CP = Contract Payments PE 33% PE 33% PE 33% **CP 15% CP 63%** CP 22% The project lifecycle increases and decreases based on work type and complexity. PE 33% PE 33% PE 33% CP 15% CP 63% **CP 22%** PE 33% PE 33% PE 33% CP 15% **CP 63%** CP 22%

Sample Cost Profile of a \$3M Pavement Preservation Project

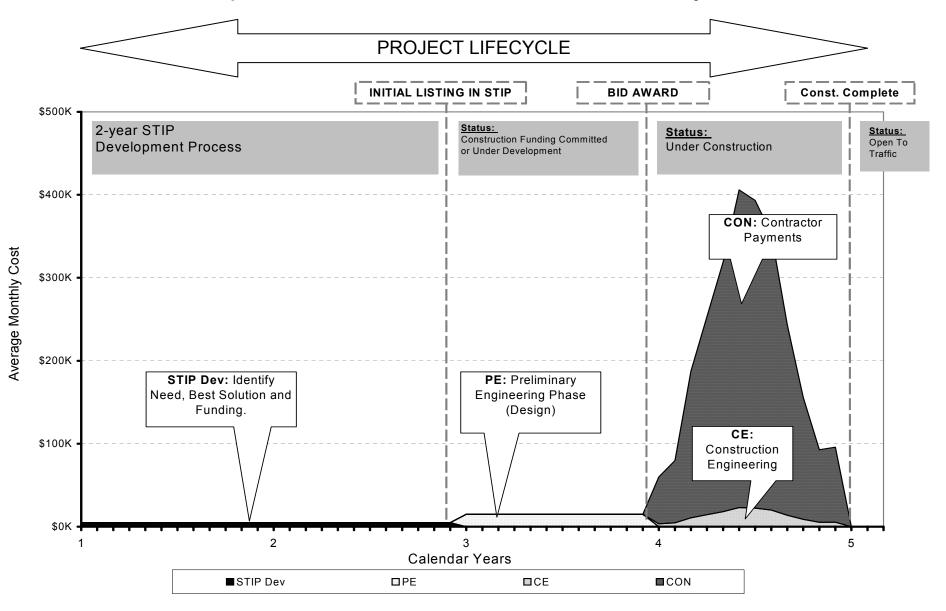

Sample Cost Profile of a \$30M Modernization Project PROJECT LIFECYCLE Const. Complete INITIAL LISTING IN STIP BID AWARD \$3,000K 2-year STIP Status: Status: Open Status: Development Process Construction Funding Committed or **Under Construction** Under Development Traffic \$2,500K Average Monthly Cost \$2,000K CON: Contractor Payments \$1,500K RW: Right of Way CE: Construction Purchases & Relocations Engineering \$1,000K STIP Dev: Identify PE: Preliminary Need, Best Solution Engineering Phase and Funding. (Design) \$500K \$0K -2 3 5 8 4 6

Calendar Years

□CE

■ CON

RW

■STIP Dev

□PE

■ Maint.

Oregon Department of Transportation Office of Project Delivery 680 Cottage St., NE Salem, OR 97301-2412

