

# Quarterly Operations Report



February 2018

### Quarterly Operations Report - February 2018

### Table of Contents

Operating Budget - FY2017 Budget-to-Actual	
Budget-to-Actual Section Divider	Page 3
Executive Summary	Page 4
University of North Texas	Page 8
UNT Health Science Center	Page 12
University of North Texas at Dallas	Page 16
UNT System Administration	Page 20
Investment Performance	
Investment Performance Section Divider	Page 24
Consolidated UNT System	Page 25
University of North Texas	Page 27
UNT Health Science Center	Page 29
University of North Texas at Dallas	Page 31
UNT System Administration	Page 33
Capital Improvement Plan Status	
Capital Improvement Plan Status Section Divider	Page 35
Project Budget Status	Page 36
Project Overview	Page 37
Capital Improvement Plan Summary	Page 38
Project Status Detail	Page 44
Information Technology Status Report	
Information Technology Project Status Report Section Divider	Page 68
Information Technology Project Status Report	Page 69

# **Budget to Actual**





### **University of North Texas**

	Q1 FYTD Estimate	Q1 FYTD Actual	Variance % (Q1 Est to Q1 Actual)	FY18 udget	-	FY18 earend orecast	Variance % (FY18 Fcst to FY18 Bud)	Overall Tracking
Total Revenues	\$ 477.3	\$ 509.0	6.2%	\$ 705.0	\$	704.7	0.0%	
Total Expenses	\$ 153.6	\$ 147.7	3.9%	\$ 581.2	\$	584.6	-0.6%	
Total Transfers	\$ (49.7)	\$ (56.8)	-14.2%	\$ (117.7)	\$	(117.5)	-0.2%	
Estimated Budgeted Impact on Fund Balances	4	\$ 304.4	11.1%	\$ 6.2	\$	2.7	-56.5%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

#### Revenue

- Overall, UNT revenues ended Q1 at \$31.6M 6.2% above Q1 budgeted estimates largely due to timing. Forecasts remain relatively flat to budget for year end.
- Net tuition and fees ended the first quarter above the Q1 revenue estimate by approximately \$8.2M, due primarily to increased SCH over FY17 Q1, and tuition and fee revenue that historically has posted in Q2 was recorded in Q1.
- Sales of Goods and Services ended Q1 \$24.3M or 57.3% above estimate due to movement of billing for housing and dining contracts from Q2 to Q1.
- Gift Income exceeds Q1 estimates due to continued success in donation and fundraising efforts by Advancement.

### Expense

- Overall, UNT expenses ended Q1 approximately 3.9% below Q1 budgeted estimates. Forecasts have been updated to reflect \$3.3M (0.6%) over budget by year end.
- Positive variances include personnel expenses at \$2.2M or 2.1% below estimates.
- M&O expenses ended Q1 \$3.4M above budget due primarily due Professional Fees and Services attributed to IT and production/design services, and Rentals and Leases for computing infrastructure and payments for PeopleSoft Grants and Contracts module.
- Capital Expenses were \$1.2M or 37.3% over budget because of increased capitalized books, reference material, and lab equipment purchases.
- Scholarship, exemptions, and financial aid expenses were under Q1 estimate by \$8.2M or 40.0% due to overestimating Q1 expenses and discounts and allowances. End of year forecasts are increased by \$8.6M or 12.1%, bringing FY18 in line with historical trends.

### **Impact to Fund Balances**

• UNT ended Q1 with an Impact to Fund Balance of \$304.4M, which is \$30.5M or 11.1% above Q1 estimates. Based on the impact of the adjustments mentioned above, UNT forecasts an increase to fund balance at year end of \$21.5M which is \$2.7M above the original budget estimate.



### **UNT Health Science Center**

	Q1 FYTD Estimate	Q1 FYTD Actual	Variance % (Q1 Est to Q1 Actual)	FY18 udget	Ye	Y18 arend ecast	Variance % (FY18 Fcst to FY18 Bud)	Overall Tracking
Total Revenues	\$ 147.4	\$ 158.1	6.8%	\$ 245.2	\$	240.0	-2.1%	
Total Expenses	\$ 52.0	\$ 52.3	-0.6%	\$ 210.6	\$	202.7	3.8%	
Total Transfers	\$ (11.5)	\$ (9.9)	13.9%	\$ (27.8)	\$	(27.4)	1.4%	
Estimated Budgeted Impact on Fund Balances		\$ 95.9	14.3%	\$ 6.8	\$	9.9	45.8%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

#### Revenue

- Overall, UNTHSC revenues ended Q1 \$10.7M or 6.8% above Q1 budgeted estimates due largely to timing. Year end forecasts have been updated to reflect being below budget by \$5.2M or 2.1% due to lower than estimated results for clinical activity at UNT Health.
- Net tuition and fees were over estimates by \$23.7M due to timing of entries which normally occur in Q2.
- Sales of Goods and Services also was above estimates by \$7.5M or 142.8% due to an accrual reversal for the Correctional Medicine Program not being recorded Q1 as planned and another accrual that was actually recorded as Gift Income.
- Negative variances include Grants and Contracts, Net Professional Fees, Gift Income and Investment Income.

### **Expenses**

- Overall, UNTHSC expenses ended Q1 in line with budget estimates. Forecasts have been updated to reflect \$7.9M or 3.8% under budget by year end.
- Personnel expenses were \$4.4M or 12.1% under budget due to UNT Health utilizing fewer employees paid from wages and timing of retiree benefit expense recording.
- M&O expenses were \$6.0M above budget due to Professional Fees and Services attributable to an accrual for Correctional Medicine not being reversed and expenses related to the Acclaim clinical partnership being delayed to FY18 that were intended to post in the prior Fiscal year.

### **Impact to Fund Balances**

• HSC ended Q1 with an Impact to Fund Balance of \$95.9M, which is \$12.0M or 14.3% above estimates. Based on the impact of the adjustments mentioned above, HSC is forecasting a \$9.9M increase to fund balance at year end, which is approximately \$3M above original budgeted estimate.



### **University of North Texas at Dallas**

	,	FYTD mate	Q1 FYTD Actual	Variance % (Q1 Est to Q1 Actual)	FY18 udget	FY18 earend orecast	Variance % (FY18 Fcst to FY18 Bud)	Overall Tracking
Total Revenues	\$	35.8	\$ 38.2	6.3%	\$ 58.4	\$ 60.2	3.1%	
Total Expenses	Ą	10.0	\$ 13.8	-38.9%	\$ 47.3	\$ 49.7	-5.1%	
Total Transfers	\$	(3.5)	\$ (1.1)	-67.8%	\$ (14.1)	\$ (13.8)	2.8%	
Estimated Budgeted								
Impact on Fund Balances	\$	22.4	\$ 23.3	4.2%	\$ (3.0)	\$ (3.3)	-8.1%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

#### Revenue

- Overall, UNT Dallas revenues ended Q1 \$2.4M or 6.3% above Q1 budgeted estimates. Year end forecasts have been updated to reflect being above budget by \$1.8M or 3.1%.
- Net Tuition and Fees revenues were in line with Q1 estimates and projected to end FY18 on budget.
- Positive variances include Sales of Goods and Services due to higher than anticipated revenue from the residence hall and parking and Grants and Contracts related to Federal Pell awards being higher than anticipated. It is expected that the Pell awards will come back in line with Q2 estimates. Gift Income is currently trending above Q1 estimates as well.

### **Expenses**

- Overall, UNT Dallas expenses ended Q1 \$3.8M or 38.9% over estimates, largely due to timing. Forecasts have been updated to reflect \$2.4M or 5.1% over budget by year end.
- Personnel expenses were \$1.4M or 23.7% over budget due to the quarterly estimate for Q1 being too low compared to other quarters. Forecasts have been updated to reflect \$1.2M over budget due to higher faculty salary expense related to increased enrollment.
- M&O expenses were \$0.4M under budget. Most M&O categories were well within estimates and projected to end the year on budget.

### Impact to Fund Balances

• UNT Dallas ended Q1 with an Impact to Fund Balance of \$23.3M, which is \$0.9M or 4.0% above estimates. Based on the impact of the adjustments mentioned above, UNTD is forecasting a \$3.3M decrease to fund balance at year end which is approximately \$.2M more than original budgeted estimate.



### **UNT System Administration**

	,	FYTD mate	(	Q1 FYTD Actual	Variance % (Q1 Est to Q1 Actual)	FY18 udget	Y	FY18 earend orecast	Variance % (FY18 Fcst to FY18 Bud)	Overall Tracking
Total Revenues	\$	1.8	\$	7.6	76.2%	\$ 6.3	\$	10.8	71.6%	
Total Expenses	\$	17.0	\$	16.3	3.7%	\$ 63.2	\$	63.8	-0.8%	
Total Transfers	\$	24.3	\$	17.8	-26.8%	\$ 57.7	\$	53.3	-7.7%	
Estimated Budgeted										
Impact on Fund Balances	\$	9.2	\$	9.0	1.4%	\$ 0.8	\$	0.3	-65.2%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

#### Revenue

- Overall, System Administration revenues ended Q1 \$5.8M or 76.2% above Q1 budgeted estimates due to categorization and timing. Forecasts have been updated to reflect being above budget by \$4.4M attributable to Tuition Revenue Bond (TRB) revenue categorization a corresponding reduction to Other legislative transfers is reflected in the year end forecast.
- State Appropriations ended Q1 with a large positive variance due to \$4.4M in TRB debt service reimbursements being recorded in in this line but budgeted in "Other Legislative Transfers". The remaining variance is due to State Appropriations being budgeted evenly across all quarters but the majority of the revenue is recognized in Q1. Forecast has been updated to reflect both of these issues for State Appropriations and Other Legislative Transfers.

### **Expenses**

- Overall, System Administration expenses ended Q1 \$0.6M or 3.7% under estimates. Forecasts have been updated to reflect \$0.5M or 0.8% over budget by year end.
- Personnel expenses ended Q1 very close to estimates.
- M&O expenses were under Q1 estimates due to large positive variances in Repairs and Maintenance attributable to IT related equipment repairs being less than anticipated and Communications and Utilities having a prior period adjusting entry that is causing a credit balance. This is expected to resolve in the Q2 report. Negative variances in Rentals and Leases are driven by software rental fees being greater than plan, forecast has been adjusted.

### Impact to Fund Balances

System Administration ended Q1 with an Impact to Fund Balance of \$9.0M, which is \$0.1M or 1.4% below estimates. Based on the impact of the adjustments mentioned above, System Administration is forecasting a \$0.3M increase to fund balance at year end – approximately \$.5M below original budgeted forecast.

# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



				ate iotai but							
		FY18 Q1 Estimate	FY18 Q1 Actuals	Variance	Variance % (Bud to Act)	Ref. No.	FY18 Budget	FY18 Year-End Forecast	Variance % (FY18 Fcst to FY18 Bud)	FY17 Preliminary Actuals	YOY Comparison (FY17 Act to FY18 Fcst)
REVENUES											
Net Tuition and Fees		\$ 268,192,262	\$ 276,367,086	\$ 8,174,824	3.0%	1	\$ 318,834,500	\$ 316,280,000	-0.8%	\$ 310,060,035	2.0%
Sales of Goods and Services		42,399,117	66,679,288	24,280,171	57.3%	2	98,899,496	98,899,496	0.0%	92,259,072	6.7%
Grants and Contracts		5,857,114	5,206,908	(650,206)	-11.1%		98,779,283	98,779,283	0.0%	102,695,036	-4.0%
State Appropriations		121,271,687	119,675,799	(1,595,888)	-1.3%		136,203,844	136,203,844	0.0%	133,222,566	
Capital Appropriations - HEF		37,562,056	37,562,081	25	0.0%		37,562,056		0.0%	37,562,056	
Net Professional Fees					0.0%		-	-	0.0%		0.0%
Gift Income		1,034,500	2,658,623	1,624,123	157.0%		9,780,214	12,000,000	22.7%	16,490,980	-37.4%
Investment Income		752,485	543,505	(208,980)	-27.8%		3,827,576		0.0%	5,371,214	-40.3%
Other Revenue		250,378	272,086	21,708	8.7%		1,132,356	1,132,356	0.0%	1,406,778	-24.2%
	al Revenues		\$ 508,965,376	\$ 31,645,777	6.2%		\$ 705,019,324		0.0%	\$ 699,067,736	0.8%
EXPENSES	ai nevellues	\$ 477,313,333	\$ 308,303,376	3 31,043,777	0.276		\$ 703,013,324	3 704,004,011	0.0%	\$ 055,007,730	0.876
Salaries - Faculty		\$ 42,056,639	\$ 40,999,042	\$ 1,057,597	2.5%		\$ 138,188,872	\$ 134,500,000	2.7%	\$ 127,651,323	5.1%
Salaries - Staff		35,067,255	33,186,292	1,880,963	5.4%		133,252,006		0.9%	129,232,377	2.1%
Wages and Other Compensation		7,778,787	7,069,190	709,597	9.1%		27,680,760		0.7%	31,251,600	-13.6%
Benefits and Other Payroll-Related Costs		16,619,244	18,101,429	(1,482,185)	-8.9%		77,684,635	76,500,000	1.5%	72,233,166	5.6%
Subtotal - Pers	onnel Costs	\$ 101,521,925			2.1%		\$ 376,806,273		1.7%	\$ 360,368,466	
Cost of Goods Sold		3,318,900	2,966,191	352,709	10.63%		12,300,640		26.8%	8,403,151	6.6%
Professional Fees and Services		2,798,200	3,893,847	(1,095,647)	-39.2%		12,826,585	14,000,000	-9.1%	14,197,638	-1.4%
Travel		2,738,200	2,025,983	258,895	11.3%	4	10,553,228		10.0%	9,530,434	-0.3%
					-12.9%			30,000,000	-10.5%	30,611,925	-2.0%
Materials and Supplies		5,539,688	6,255,418	(715,730)			27,152,904				
Communication and Utilities		1,919,077	2,454,324	(535,247)	-27.9%		10,114,835	12,600,000	-24.6%	12,598,872	0.0%
Repairs and Maintenance		3,810,404	4,527,567	(717,163)	-18.8%	_	19,183,305	18,000,000	6.2%	17,771,656	
Rentals and Leases		1,867,721	3,826,804	(1,959,083)	-104.9%		8,317,171		-20.2%	9,966,551	0.3%
Printing and Reproduction		390,702	912,520	(521,818)	-133.6%		2,019,274	1,300,000	35.6%	1,298,702	0.1%
Other Expenses		6,299,846	4,744,622	1,555,224	24.7%	6	18,243,571	17,500,000	4.1%	17,390,043	0.6%
Internal Income		-	-	· · · · · · · · · · · · · · · ·			-	-	0.0%	1,502,045	-100.0%
Subtotal - Maintenance & Oper	ration Costs	\$ 28,229,416	\$ 31,607,275	\$ (3,377,859)	-12.0%		\$ 120,711,513	\$ 121,900,000	-1.0%	\$ 123,271,017	-1.1%
Debt Service - Principal		-	-	-			-	-	0.0%	24,190,248	
Debt Service - Interest		-	-				-	-	0.0%	19,163,498	-100.0%
Capital Expenses		3,207,221	4,402,217	(1,194,996)	-37.3%	7	12,161,799	12,000,000	1.3%	14,450,010	-20.4%
Federal and State Pass-Through Expense		152,650	16,768	135,882	89.0%		152,650	152,650	0.0%	280,112	-83.5%
Scholarships, Exemptions and Financial Aid		20,512,626	12,308,815	8,203,811	40.0%	8	71,361,577	80,000,000	-12.1%	80,076,986	-0.1%
Tot	al Expenses	\$ 153,623,839	\$ 147,691,029	\$ 5,932,809	3.86%		\$ 581,193,812	\$ 584,552,650	-0.6%	\$ 621,800,338	-6.4%
TRANSFERS											
Intra-Campus Transfers Between Funds:											
Debt Service Transfer In/(Out)	:	\$ (11,088,339)	\$ (11,088,339)	\$ -	0.0%		\$ (44,353,357)	\$ (44,353,357)	0.0%	\$ -	-100.0%
Inter-Fund Transfers In/(Out)		(27,138,556)	(34,238,939)	(7,100,383)	-26.2%	9	(27,138,556)	\$ (27,000,000)	-0.5%	(20,560,819)	-23.8%
Transfers Between UNTS Components:		, , , ,	, , , ,	, , , ,							
Shared Services		(6,709,291)	(6,709,291)	-	0.0%		(26,837,165)	(26,837,165)	0.0%	(23,937,930)	-10.8%
Core Services		(4,832,195)	(4,832,195)	-	0.0%		(19,328,779)	(19,328,779)	0.0%	(14,847,244)	-23.2%
Other Inter-Unit Transfers In/(Out)		(11,471)	36,785	48,256	420.7%		(45,884)	36,785	-180.2%	(1,527,096)	4251.4%
Other Transfers:											
Transfer to other State Agencies In/(Out)		-	-	-	100.0%		-	-	0.0%	621,840	100.0%
Other Legislative Transfers In/(Out)		30,357	-	(30,357)	-100.0%		30,357	30,357	0.0%	6,536,781	-21433.0%
Lapsed Appropriations		-	-	-	0.0%		-	-	0.0%	(2,013,166)	100.0%
Tot	al Transfers	\$ (49,749,495)	\$ (56,831,980)	\$ (7,082,485)	-14.2%		\$ (117,673,384)	\$ (117,452,159)	-0.2%	\$ (55,727,634)	-52.6%
Estimated Budgeted Impact on Fund Balances		\$ 273,946,265	\$ 304,442,367	\$ 30,496,102	11.1%		\$ 6,152,128	\$ 2,679,802	56.4%	\$ 21,539,764	-703.8%

# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Variance Explanations




	REVENUES	
1	Net Tuition and Fees	Enrollment Headcount and SCH up versus FY17 by 0.3% and 0.4%, respectively. FY18 Q1 revenue showing collections that historically posted in Q2. Current YTD FY18 tuition and fee collections show flat to prior year.
2	Sales of Goods and Services	Revenue collections reflect change in housing and dining contracts billing moved up from Q2 to Q1.
	Grants and Contracts	
l	State Appropriations	
	Capital Appropriations - HEF	
	Net Professional Fees	
	110103310110111003	
3	Gift Income	Donation and fundraising efforts by Advancement has continued success from FY17 into the new fiscal year.
 	Investment Income	
	Other Revenue	
	EXPENSES	
	Salaries - Faculty	
	Salaries - Staff	
<u> </u>	Wages and Other Compensation	
	Benefits and Other Payroll-Related Costs	
	Cost of Goods Sold	
4	Professional Fees and Services	Variance driven by information technology services (\$0.68M) and production/ design services (\$0.65M).
	Travel	
	Materials and Supplies	
	Communication and Utilities	
	Repairs and Maintenance	
-		
5	Rentals and Leases	Variance driven by lease for computing storage and infrastructure (\$1.3M) and payments to Huron Consulting for Grants and Contracts Peoplesoft module (\$0.3M).
	Printing and Reproduction	
6	Other Expenses	Overallocated to Q1 estimate of other expenditures; positive variance in other expenses is offset by spending within other expenditure categories.
	Internal Income	
	Debt Service - Principal	
	Debt Service - Interest	
7	Capital Expenses	Variance driven by capital books/ reference material (\$2.1M) and capital lab equipment (\$1.1M).
	Federal and State Pass-Through Expense	
		Actual scholarship expense for Q1 is \$55.8M with (\$43.5M) discounts and allowances estimate, for net expense of \$12.3M. Budgeted estimate for Q1 was \$61.2M
8	Scholarships, Exemptions and Financial Aid	scholarship expense with (\$40.7M) discounts and allowances, for net budget of \$20.5M. Scholarship variance driven by negative variance for both scholarship expense
		and estimated discount and allowance.
	TRANSFERS	
	Intra-Campus Transfers Between Funds:	
	Debt Service Transfer In/(Out)	
9	Inter-Fund Transfers In/(Out)	Additional transfers to capital funds for Auxiliary funded projects (\$3.6M), HEF funded projects (\$2.4M)
	Transfers Between UNTS Components:	
	Shared Services	
	Core Services	
	Other Inter-Unit Transfers In/(Out)	
	Other Transfers:	
	Transfer to other State Agencies In/(Out)	
	Other Legislative Transfers In/(Out)	
	Lapsed Appropriations	


# **Key Expense Categories**


Q1 Actuals FY Actuals




In Millions





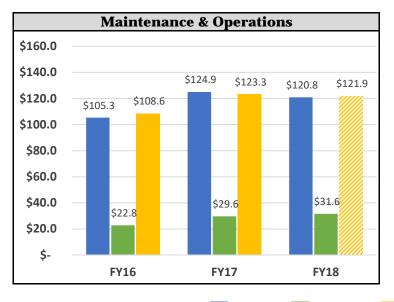

Budget





Projection


### **Key Revenue Categories**





In Millions

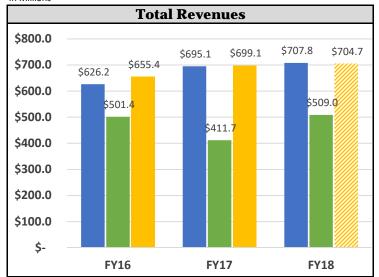









# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



P.   P.   P.   P.   P.   P.   P.   P.					ate rotal bud	.gerunu reu						LIENCE CENTER
Net Tuilon and Ferns Substance 1 1,200,000 0 5 2,8,813,30 5 11,891,330 9 74 8 1 5 13,120,000 1-10 5 5,940,902 1 3,945,000 1 3,			-		Variance			FY18 Budget		(FY18 Fcst to	-	(FY17 Act to
Sales of fronts and Services  5,20,000 12,72,200 7,92,200 12,25 0 135,000 39,225,000 0.0 0,0 6,000,00 13,0	REVENUES											
Grants and Contracts	Net Tuition and Fees		\$ 12,000,000	\$ 23,691,339	\$ 11,691,339	97.4%	1	\$ 31,750,280	\$ 31,200,000	-1.7%	\$ 30,149,923	3.4%
Stake Appropriations	Sales of Goods and Services		5,240,000	12,722,809	7,482,809	142.8%	2	39,225,000	39,225,000	0.0%	48,990,931	-24.9%
Capital Appropriations - IEF  1,7091,856	Grants and Contracts		8,980,000	1,349,417	(7,630,583)	-85.0%	3	35,900,000	32,300,000	-10.0%	43,810,626	-35.6%
Net Professional Feen	State Appropriations		98,720,583	99,313,264	592,681	0.6%		103,643,662	103,500,000	-0.1%	97,974,860	5.3%
Second   S	Capital Appropriations - HEF		17,091,856	17,091,856	-	0.0%		17,091,856	17,091,856	0.0%	17,091,856	0.0%
	Net Professional Fees		4,500,000	3,756,805	(743,195)	-16.5%	4	13,722,182	12,300,000	-10.4%	14,206,060	-15.5%
Other Neverwe	Gift Income		300,000	(324,419)	(624,419)	-208.1%	5	1,500,000	1,800,000	20.0%	2,321,129	-29.0%
Total Revenues   Staff, 242,498   \$158,129,266   \$1,0706,827   6.8%   \$245,192,980   \$240,016,856   7.1%   \$288,141,212   7.6%   \$286,141,212   7.6%   \$	Investment Income		560,000	436,959	(123,041)	-22.0%		2,240,000	2,240,000	0.0%	3,165,218	-41.3%
State   Stat	Other Revenue		30,000	91,236	61,236	204.1%		120,000	360,000	200.0%	430,609	-19.6%
Salaries Faculty Salari		Total Revenues	\$ 147,422,439	\$ 158,129,266	\$ 10,706,827	6.8%		\$ 245,192,980		-2.1%	\$ 258,141,212	-7.6%
Salaries - Staff	EXPENSES											
Mages and Other Compensation	Salaries - Faculty		\$ 11,535,000	\$ 10,960,598	\$ 574,402	5.0%		\$ 48,000,000	\$ 44,000,000	8.3%	\$ 45,728,366	-3.9%
Benefits and Other Payroll-Related Costs   8,258,000   5,814,805   2,443,195   29,6%   7   \$1,000,000   27,500,000   11,3%   27,917,918   1.5%   Cost of Goods Sold   5,000   3,076   (4,076)   48,5%   5,000   2,000,000   2,000,000   0.0%   8,015   29,3%   Professional Fees and Services   7,500,000   12,000,400   13,3%   2,000   2,000,000   0.0%   2,000,000   1,3%   37,183,097   -7,7%   Travel   414,000   131,830   95,599   23,1%   2,000,000   2,000,000   0.0%   3,000,000   0.0%   3,00	Salaries - Staff		14,773,000	14,031,091	741,909	5.0%		61,300,000	57,000,000	7.0%	56,507,248	0.9%
Subtotal - Personnel Costs (Scat of Goods Sold   \$36,431,000   \$32,037,855   \$4,393,145   \$12,155   \$147,800,000   \$133,400,000   \$9,405   \$136,861,150   \$2,605   \$136,661,150   \$136,861	Wages and Other Compensation		1,865,000	1,231,361	633,639	34.0%	6	7,000,000	4,900,000	30.0%	6,707,618	-36.9%
Cast of Goods Sold	Benefits and Other Payroll-Related Costs		8,258,000	5,814,805	2,443,195	29.6%	7	31,000,000	27,500,000	11.3%	27,917,918	-1.5%
Professional Fees and Services 7,350,000 12,208,464 (4,858,464) -66.18 8 30,500,000 34,500,000 -13.1% 37,163,097 -7.7% 173 (115,754) -13.8% 2,000,000 2,000,000 0,00% 2,208,004 -10.1% Advantarials and Supplies 1,56,000 1,777,74 (215,754) -13.8% 9,000,000 12,000,000 12,000,000 0,00% 2,208,004 -10.1% Advantarials and Utilities 497,000 533,021 (156,021) -11.3% 2,400,000 2,400,000 0,00% 2,109,900 12.1% Regains and Maintenance 1,005,000 7,877 2,371,272 23.6% 3,500,000 0,00% 0,00% 3,286,951 6.1% Regains and Maintenance 3,000 13,000,000 0,00% 1,266,576 -4.4% Printing and Reproduction 1330,000 47,542 85,458 64.3% 53,000 0,000 0,00% 1,566,576 -4.4% 133,000 47,542 85,458 64.3% 95,000 0,000 0,00% 1,566,576 -4.4% 10.1% 10.00%	Subtotal -	Personnel Costs	\$ 36,431,000	\$ 32,037,855	\$ 4,393,145	12.1%		\$ 147,300,000	\$ 133,400,000	9.4%	\$ 136,861,150	-2.6%
Trivel	Cost of Goods Sold		5,000	9,076	(4,076)	-81.51%		20,000	20,000	0.0%	8,015	59.9%
Trivel	Professional Fees and Services		7,350,000	12,208,464	(4,858,464)	-66.1%	8	30,500,000	34,500,000	-13.1%	37,163,097	-7.7%
Materials and Supplies	Travel		414,000	318,301		23.1%		2,000,000		0.0%		-10.1%
Communication and Utilities	Materials and Supplies		1,562,000	1,777,754	(215,754)	-13.8%		9,000,000		-33.3%		-4.4%
Repairs and Maintenance	'''											
Rentals and Leases 358,000 325,580 32,420 9.1% 1,500,000 1,500,000 0.0% 1,566,576 4.4% Printing and Reproduction 133,000 4,742 88,4858 64.3% 750,000 650,000 13.3% 887,943 3-36.5% 0.0% 1,500,000 7,000,000 7,000,000 7,000,000 7,000,000												
Printing and Reproduction  133,000	· ·											
Other Expenses Internal (Income)/Charges Subtotal - Maintenance & Operation Costs Subtotal - Maintenance & Operation Co												
Internal (Income)/Charges	,											
Subtotal - Maintenance & Operation Costs   12,388,000   18,387,173   (5,999,173)   -48.4%   55,170,000   563,570,000   -15.2%   56,241,800   -4.2%   -100.0%	· ·		-	2,573,555	(1,010,000)	120.070		-	,,000,000			
Debt Service - Principal Debt Service - Interest - Interes	, , ,	Operation Costs	\$ 12 388 000	\$ 18 387 173	\$ (5,999,173)	-48 4%		\$ 55,170,000	\$ 63.570.000			
Debt Service - Interest Capital Expenses		<b>-</b>	- 12,300,000	7 10,507,175	- (3,333,173)	40.470		- 33,170,000	Ç 03,370,000		- 00,241,000	
Capital Expenses	'		_	_	_			_			3 116 107	
Federal and State Pass-Through Expense Depreciation and Amortization Scholarships, Exemptions and Financial Aid Total Expenses  TRANSFERS Intra-Campus Transfers Between Funds: Debt Service Transfer In/(Out) Shared Services Core Services Core Services Core Services Transfers In/(Out) Corber Transfers In/(Out) Corpe Services Transfer In/(Out) Corpe Services Corpe Services Transfer In/(Out) Corpe Services Transfer In/(Out) Corpe Services Transfer In/(Out) Corpe Services Transfer In/(Out) Corpe Services Corpe Services Transfer In/(Out) Corpe Service			2 229 000	789 001	1 /20 000	64.6%	10	4 400 000	2 000 000			
Depreciation and Amortization Scholarships, Exemptions and Financial Aid 960,000 1,099,137 (139,137) -14.5% 3,000,000 3,000,000 0.0% 824,357 363.9% Total Expenses 5 52,008,000 \$ 52,323,765 \$ (315,765) -0.61% \$ 210,570,000 \$ 202,670,000 3.8% \$ 211,366,298 -4.3% TRANSFERS Intra-Campus Transfers Between Funds:  Debt Service Transfer In/(Out) \$ (3,970,000) \$ (2,500,558) \$ (1,469,442) 37.0% 11 \$ (15,891,925) \$ (15,491,925) -2.5% \$100.0% Inter-Fund Transfers In/(Out) \$ (270,000) \$ (133,019) \$ (136,981) \$ 50.7% \$ (2,600,000) \$ (2,600,000) \$ (2,600,000) \$ (12,548,514) \$ 382.6% Transfers Between UNTS Components:  Shared Services	' '		2,229,000									
Scholarships, Exemptions and Financial Aid   960,000   1,099,137   (139,137)   -14.5%   3,000,000   3,000,000   0.0%   824,357   363.9%	,		-	10,600	(10,600)	100.0%		700,000	700,000		907,544	
TRANSFERS Intra-Campus Transfers Between Funds: Debt Service Transfer In/(Out) Inter-Fund Transfers In/(Out) Signal Service Transfer In/(Out) Signal Service Signal Service Transfer In/(Out) Signal Service Signal Service Signal Service Transfer In/(Out) Signal Service Signa	l '		-	-	- 			-			-	
TRANSFERS  Intra-Campus Transfers Between Funds:  Debt Service Transfer In/(Out)  Service Transfer In/(Out)  (270,000)  Service Services  Core Services  Other Inter-Unit Transfers In/(Out)  Other Inter-Unit Transfers In/(Out)  Other Stared Services  Other Stared Services  Transfer to other State Agencies In/(Out)  Other Longistive Transfers In/(Out)  Transfers  Transfers  Transfers Setween Funds:  Other Longistive Transfers In/(Out)  Transfers  Transfers  Transfers  Services  Other Longistive Transfers In/(Out)  Other Longistive Transfers In/(Out)  Transfers  Transfer to other State Agencies In/(Out)  Transfers  Transfer to other State Agencies In/(Out)  Transfers  Total Transfers  Settimated Budgeted Impact on Fund Balances  Setti	Scholarships, Exemptions and Financial Aid		· · · · · ·									
Inter-Campus Transfers Between Funds:   Debt Service Transfer In/(Out)		Total Expenses	\$ 52,008,000	\$ 52,323,765	\$ (315,765)	-0.61%		\$ 210,570,000	\$ 202,670,000	3.8%	\$ 211,366,298	-4.3%
Debt Service Transfer In/(Out) \$ (3,970,000) \$ (2,500,558) \$ (1,469,442) 37.0% 11 \$ (15,891,925) \$ (15,491,925) \$ -2.5% \$ -100.0% Inter-Fund Transfers In/(Out) (270,000) (133,019) (136,981) 50.7% (2,600,000) \$ (2,600,000) 0.0% (12,548,514) 382.6% Transfers Between UNTS Components:  Shared Services	TRANSFERS											
Inter-Fund Transfers In/(Out)  Transfers Between UNTS Components: Shared Services  Core Services  Other Inter-Unit Transfers In/(Out)  Other Transfers In/(Out)  Other Transfers In/(Out)  Other Legislative Transfers In/(Out)  Other Legislative Transfers In/(Out)  Total Transfers  Total Transfers  Sa,884,458  \$ 95,881,942  \$ 11,997,484  14.3%  \$ 6,823,356  \$ 9,947,232  -45.8%  \$ 31,047,614  -212.1%	Intra-Campus Transfers Between Funds:											
Transfers Between UNTS Components: Shared Services Core Services Core Services Core Services Cother Inter-Unit Transfers In/(Out) Cother Inter-Unit Transfers In/(Out) Cother Transfers Transfer to other State Agencies In/(Out) Cother Legislative Transfers In/(Out) Cother Inter-Unit Transfers In/(Out) Cother Transfers Cother Inter-Unit Transfers Cother Transfer In/(Out) Cother Transfer In/(Out) Cother Inter-Unit Transfers In/(Out) Cother Transfer In/(Out) Cother Inter-Unit Transfers In/(Out) Cother Transfer In/(Out) Cother Inter-Unit Transfers In/(Out) Cother Transfers Cother Inter-Unit Transfers In/(Out) Cother Transfers Cother Inter-Unit	Debt Service Transfer In/(Out)								, , ,		•	-100.0%
Transfers between ON's Components: Shared Services  Core Services			(270,000)	(133,019)	(136,981)	50.7%		(2,600,000)		0.0%	(12,548,514)	382.6%
Core Services  Other Inter-Unit Transfers In/(Out)  Other Transfers:  Transfer to other State Agencies In/(Out)  Other Legislative Transfers In/(Out)  Total Transfers  Total Transfers  \$ 83,884,458 \$ 95,881,942 \$ 11,997,484 \$ 14.3% \$ 6,823,356 \$ 9,947,232 \$ -45.8% \$ 31,047,614 \$ -212.1%									0			2.51
Other Inter-Unit Transfers In/(Out) 0.0%			-	-	-			(0.04=5:-)	-			
Other Transfers:         Transfer to other State Agencies In/(Out)         -			-	-	-			(2,017,718)	(2,017,718)			
Transfer to other State Agencies In/(Out) Other Legislative Transfers In/(Out) Lapsed Appropriations  Total Transfers \$ (11,529,981) \$ (9,923,558) \$ 1,606,423			-	-	-	0.0%		-	-	0.0%	284,174	-100.0%
Lapsed Appropriations  Total Transfers \$ (11,529,981) \$ (9,923,558) \$ 1,606,423			-	-	-	0.0%		-	-	0.0%	12,149	-100.0%
Total Transfers \$ (11,529,981) \$ (9,923,558) \$ 1,606,423	Other Legislative Transfers In/(Out)		(7,289,981)	(7,289,981)	-	0.0%		(7,289,981)	(7,289,981)	0.0%	(588,947)	-1137.8%
Total Transfers \$ (11,529,981) \$ (9,923,558) \$ 1,606,423	Lapsed Appropriations		_					-		0.0%	(260,736)	-100.0%
Estimated Budgeted Impact on Fund Balances \$ 83,884,458 \$ 95,881,942 \$ 11,997,484 14.3% \$ 6,823,356 \$ 9,947,232 -45.8% \$ 31,047,614 -212.1%		Total Transfers	\$ (11,529,981)	\$ (9,923,558)	\$ 1,606,423	-13.9%		\$ (27,799,624)	\$ (27,399,624)	-1.4%	\$ (15,727,300)	-42.6%
Planned Use of Fund Balances \$ - \$ - \$ - \$ 5 -												
	Planned Use of Fund Balances		\$ -	\$ -	\$ -			\$ -			\$ -	

# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Variance Explanations




#### REVENUES


	REVENUES	
1	Net Tuition and Fees	The spring tuition, which is ordinarily recorded in the second quarter, was recorded earlier than anticipated.
2	Sales of Goods and Services	An accrual reversal for the Correctional Medicine Program was not recorded, and an accrual reversal for the TCU and UNTHSC School of Medicine was recorded under Gift Income.
3	Grants and Contracts	Due to the delay in getting the contract executed for the grants billing module, the go-live for the new module was pushed back to Dec 2017. As a result, revenue
3		for first quarter was lower than estimated.
	State Appropriations	
	Capital Appropriations - HEF	
4	Net Professional Fees	Clinical activity associated with UNT Health was lower than originally estimated.
5	Gift Income	An accrual reversal for the TCU and UNTHSC School of Medicine was recorded under Gift Income, when it should have been recorded under Sales of Goods and Services.
	Investment Income	
	Other Revenue	
	EXPENSES	
	Salaries - Faculty	
	Salaries - Staff	
6	Wages and Other Compensation	UNT Health utilized fewer employees paid from Wages.
7	Benefits and Other Payroll-Related Costs	There was a delay in the recording of retiree benefits.
	Cost of Goods Sold	
8	Professional Fees and Services	An accrual for the Correctional Medicine Program was not reversed.
	Travel Materials and Supplies	
	<b>(</b>	
	Communication and Utilities	
	Repairs and Maintenance	
	Rentals and Leases	
9	Printing and Reproduction Other Expenses	True seisele was set for a dream in a serie of a set in a fire was set in a fire was a
9	Other Expenses	Two reimbursements for educational services provided in the prior year by Acclaim were unexpectedly delayed until the current fiscal year.
	Internal (Income)/Charges	
	Debt Service - Principal	
	Debt Service - Interest	
10	Capital Expenses	Capital project expenditures were overestimated for the first quarter.
	Scholarships, Exemptions and Financial Aid	
	TRANSFERS	
	Intra-Campus Transfers Between Funds:	
11	Inter-Fund Transfers In/(Out)	The debt service payment for the first quarter was unintentionally overestimated. However, once the final debt service payment for the fiscal year is recorded, any significant differences between actuals and planned expenditures shall be eliminated.
	Transfers Between UNTS Components:	
	Shared Services	
	Core Services	
	Other Inter-Unit Transfers In/(Out)	
,	Other Transfers:	
	Transfer to other State Agencies In/(Out)	
	Other Legislative Transfers In/(Out)	


## **Key Expense Categories UN**




In Millions



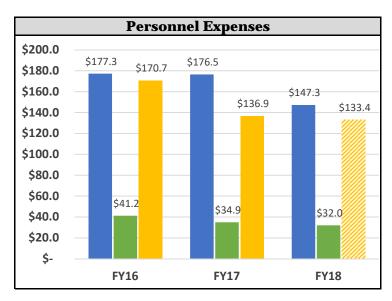

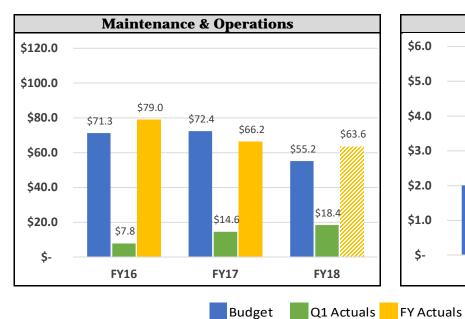





Projection


# **Key Revenue Categories UNT**





In Millions








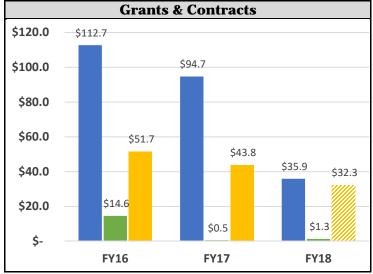





Projection

# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



								_	_								
			FY18 Q1 Estimate		FY18 Q1 Actuals	,	Variance	Variance % (Bud to Act)	Ref. No.	EV	/18 Budget	FY	18 Year-End Forecast	Variance % (FY18 Fcst to FY18 Bud)	Pi	FY17 reliminary Actuals	YOY Comparison (FY17 Act to FY18 Fcst)
REVENUES		-	Stillate		Actuals		variance	(Bud to Act)		-	10 Buuget		Forecast	FT16 Buu)		Actuals	FT16 FCSL)
Net Tuition and Fees		٠,	0 224 202	4	0.607.116	۲.	272 724	4.5%		Ś	10 250 028	,	10 250 028	0.00/	۲.	17 206 014	10.2%
Sales of Goods and Services		\$	8,324,382 205,625	Ş	8,697,116 516,338	Ş	372,734	151.1%	1	Ş	19,359,028	Ş	19,359,028	0.0% 48.6%	Ş	17,386,814 474,196	157.8%
Grants and Contracts		l i					310,713				822,500		1,222,500				
		l i	2,123,267		3,520,751		1,397,484	65.8%	2		9,651,215		10,651,215	10.4%		8,047,929	24.4%
State Appropriations		l i	22,889,402		22,982,200		92,798	0.4%			25,718,429		25,718,429	0.0%		17,565,488	31.7%
Capital Appropriations - HEF Net Professional Fees		i	2,113,004		2,113,004		-	0.0%			2,113,004		2,113,004	0.0%		2,113,004	0.0%
		i	125 000		205.002		240.002	102.00/			-		-	0.0%		400 111	0.0%
Gift Income		l i	125,000		365,963		240,963	192.8%			500,000		900,000	80.0%		480,111	46.7%
Investment Income		l i	54,000		49,479		(4,521)	-8.4%			216,000		216,000	0.0%		309,197	-43.1%
Other Revenue		_	5,000		274		(4,726)	100.0%			20,000	_	20,000	0.0%		23,702	-18.5%
EXPENSES	Total Revenues	\$	35,839,680	Ş	38,245,124	\$	2,405,444	6.3%		\$	58,400,176	Ş	60,200,176	3.1%	\$	46,400,440	22.9%
Salaries - Faculty		\$	1,998,264	ć	3,043,357	ć	(1,045,093)	-52.3%	3	Ś	9,991,320	ć	10,991,320	-10.0%	\$	9,069,946	17.5%
Salaries - Staff		٦		ڔ		ڔ		-3.5%	3	٦		ڔ		0.0%	ڔ		24.7%
		i	2,637,751		2,731,012		(93,261)				13,188,755		13,188,755			9,925,168	
Wages and Other Compensation		l i	192,991		290,903		(97,912)	-50.7%			964,956		984,255	-2.0%		1,194,625	-21.4%
Benefits and Other Payroll-Related Costs	D	_	1,122,014	_	1,294,791	_	(172,777)	-15.4%		_	5,610,068	_	5,722,269	-2.0%	_	5,175,251	9.6%
	Personnel Costs	\$	5,951,020	\$	7,360,063	Ş	(1,409,043)	-23.7%		\$	29,755,099	Ş	30,886,599	-3.8%	\$	25,364,990	17.9%
Cost of Goods Sold		l i			178		(178)							0.0%			0.0%
Professional Fees and Services		l i	262,189		462,348		(200,159)	-76.3%			1,048,755		1,248,755	-19.1%		1,430,830	-14.6%
Travel		l i	133,219		143,988		(10,769)	-8.1%			532,875		532,875	0.0%		392,295	26.4%
Materials and Supplies		l i	806,312		438,847		367,465	45.6%	4		3,225,246		3,025,246	6.2%		1,752,308	42.1%
Communication and Utilities		l i	186,857		96,645		90,212	48.3%			747,429		747,429	0.0%		336,498	55.0%
Repairs and Maintenance		l i	68,025		11,811		56,214	82.6%			272,098		272,098	0.0%		1,034,544	-280.2%
Rentals and Leases		l i	58,705		115,569		(56,864)	-96.9%			234,820		234,820	0.0%		655,324	-179.1%
Printing and Reproduction		l i	99,521		20,949		78,572	79.0%			398,082		398,082	0.0%		315,432	20.8%
Other Expenses		l i	339,264		224,389		114,875	33.9%			1,357,055		1,357,055	0.0%		1,153,839	15.0%
Internal Income			-				-	100.0%			-		-	0.0%		216,370	-100.0%
Subtotal - Maintenance &	Operation Costs	\$	1,954,092	\$	1,514,724	\$	439,368	22.5%		\$	7,816,360	\$	7,816,360	0.0%	\$	7,287,442	6.8%
Debt Service - Principal		l i	-		-		-				-		-	0.0%		7,163,050	-100.0%
Debt Service - Interest		l i	-		-		-				-		-	0.0%		1,431,044	-100.0%
Capital Expenses		l i	77,903		450,911		(373,008)	-478.8%	5		779,026		1,082,026	-38.9%		564,032	47.9%
Federal and State Pass-Through Expense		l i	-		-		-	0.0%			-		-	0.0%		-	0.0%
Depreciation and Amortization		l i	_				_	0.0%			_		_	0.0%		_	0.0%
Scholarships, Exemptions and Financial Aid		l i	1,969,267		4,498,976		(2,529,709)	-128.5%	6		8,951,215		9,951,215	-11.2%		7,420,464	25.4%
, , , , , , , , , , , , , , , , , , , ,	Total Expenses	Ś	9,952,280	Ś	13,824,674	Ś	(3,872,394)	-38.91%		Ś	47,301,700	Ś	49,736,200	-5.1%	\$	49,231,023	1.0%
TRANSFERS	•		-,,		-,- ,-	•	(-,- , ,			Ė	,,		.,,		•	, , , , , , , , , , , , , , , , , , , ,	
Intra-Campus Transfers Between Funds:		l i															
Debt Service Transfer In/(Out)		Ś	(2,245,640)	\$	(2,107,083)	\$	138,557	-100.00%		Ś	(8,982,558)	Ś	(8,982,558)	0.0%	\$	_	-100.0%
Inter-Fund Transfers In/(Out)		Ψ.	(2)2 .5)0 .0)	7	(2,107,003)	7	-	-100.00%		~	(0,302,330)	\$	(0,302,330)	0.0%	Y	(25,556)	100.0%
Transfers Between UNTS Components:		l i						100.0070				Ţ		0.070		(23,330)	100.070
Shared Services		l i	(650,310)		(650,310)		-	0.00%			(2,601,240)		(2,601,240)	0.0%		(2,388,246)	-8.2%
Core Services		l i	(317,356)		(295,481)		21,875	6.89%			(1,269,425)		(1,181,925)	-6.9%		(762,645)	-35.5%
Other Inter-Unit Transfers In/(Out)		l i	(322,180)		(194,561)		127,619	39.6%			(1,288,721)		(985,721)	-23.5%		(766,253)	-22.3%
Other Transfers:			. , ,		· //		,				, , -, -,		, - ,			,,	
Transfer to other State Agencies In/(Out)			-		-		-	0.00%			-		-	0.0%		-	0.0%
Other Legislative Transfers In/(Out)			-		-		-	0.00%			-		-	0.0%		9,095,463	-100.0%
Lapsed Appropriations					-			0.00%					-	0.0%		(597,887)	100.0%
	<b>Total Transfers</b>	\$	(3,535,486)	\$	(3,247,435)	\$	288,051	8.1%		\$	(14,141,944)	\$	(13,751,444)	-2.8%	\$	4,554,876	-133.1%
Estimated Budgeted Impact on Fund Balances		\$			21,210,361		·	-5.4%		\$	(3,043,468)		(3,287,468)	-8.0%	\$	1,724,294	-152.5%
Use of Fund Balances		\$	_	\$	-	\$	-			\$	(3,043,468)	\$	(3,287,468)		\$	-	
										_		_					

# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Variance Explanations




#### **REVENUES**


	Net Tuition and Fees	
1	Sales of Goods and Services	Residence Hall and Parking Permit revenues are exceeding budget projections. Year-End Forecast has been updated.
2	Grants and Contracts	Federal Financial Aid (Pell) revenue exceeded budget projections for Q1, variance should resolve in Q2.
	State Appropriations	
	Capital Appropriations - HEF	
	Net Professional Fees	
	Gift Income	
	Investment Income	
	Other Revenue	
	EXPENSES	
3	Salaries - Faculty	Budget estimate per quarter is too low, average is \$3M per quarters 1,2, and 3. Average for summer approximately \$1M for Q4. Year-End Forecast has been
3		updated to project increase in Faculty Salaries overall due to higher enrollment.
	Salaries - Staff	
	Wages and Other Compensation	
	Benefits and Other Payroll-Related Costs	
	Cost of Goods Sold	
	Professional Fees and Services	
	Travel	
4	Materials and Supplies	Budget reallocation from Materials and Supplies to Professional Fees and Services.
	Communication and Utilities	
	Repairs and Maintenance	
	Rentals and Leases	
	Printing and Reproduction	
	Other Expenses	
	Internal (Income)/Charges	
	Debt Service - Principal	
	Debt Service - Interest	
-	Control	ISA between UNT Dallas and UNT Library was recorded as a Capital Expense but was budgeted in Other Inter-Unit Transfers (\$303K). Year-End Forecasts have
5	Capital Expenses	been updated.
	Internal Charges	
6	Scholarships, Exemptions and Financial Aid	Federal Financial Aid (Pell) has exceeded budget projections for Q1 by \$1M; also D&A entry needs to be reviewed to reconcile institutionally funded
U	Scholarships, Exemptions and Financial Aid	scholarships. Expect variance to continue in upcoming quarters. Year-End Forecast has been updated to illustrate increase in Pell awards.
	TRANSFERS	
	Intra-Campus Transfers Between Funds:	
	Inter-Fund Transfers In/(Out)	
	Transfers Between UNTS Components:	
	Shared Services	
	Core Services	
	Other Inter-Unit Transfers In/(Out)	
	Other Transfers:	
	Transfer to other State Agencies In/(Out)	
	Other Legislative Transfers In/(Out)	


# **Key Expense Categories**






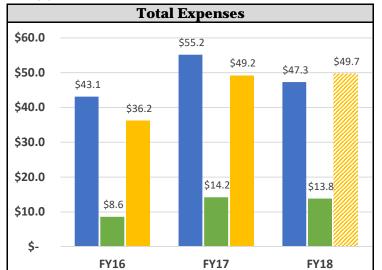



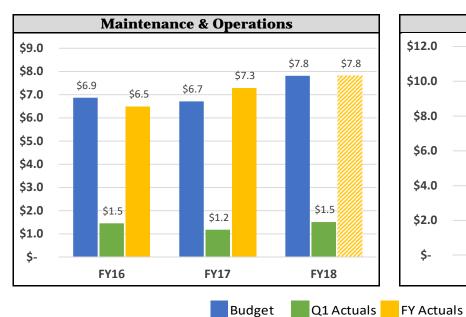





Projection


### **Key Revenue Categories**







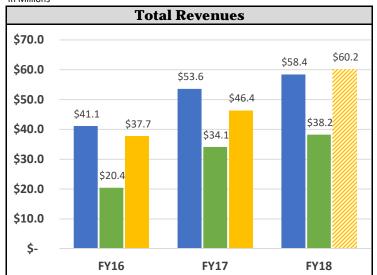

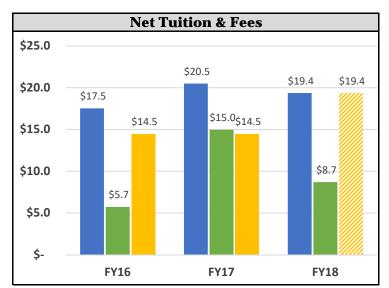

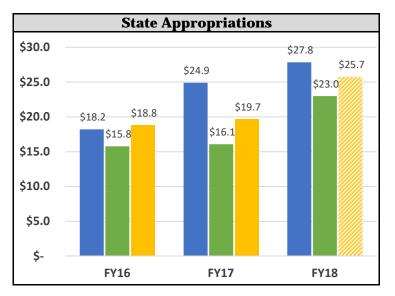



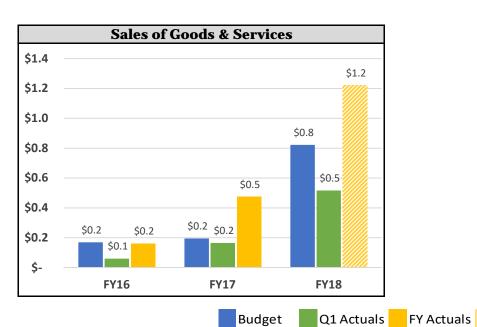

# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



Ī						•				
	FY18 Q1 Estimate	FY18 Q1 Actuals	Variance	Variance % (Bud to Act)	Ref. No.	FY18 Budget	FY18 Year-End Forecast	Variance % (FY18 Fcst to FY18 Bud)	FY17 Preliminary Actuals	YOY Comparison (FY17 Act to FY18 Fcst)
REVENUES	Estimate	rictuuis		(bud to Act)		1110 Dauget	1010005	1110 Daay	rictuuis	11101000
Net Tuition and Fees	Ś	- \$ 30	\$ 30			\$ -	\$ -	0.0%	\$ -	0.0%
Sales of Goods and Services	493,87			-1.2%		1,975,485	1,975,485	0.0%	2,017,740	-2.1%
Grants and Contracts	455,67		(3,303)	1.270		1,575,405	1,575,405	0.0%	2,017,740	0.0%
State Appropriations	1,257,889	7,007,261	5,749,372	457.1%	1	4,089,548	8,457,298	106.8%	8,987,972	
Capital Appropriations - HEF	1,237,00	7,007,201	3,743,372	457.170	1	4,005,540	0,437,230	0.0%	0,507,572	0.0%
Net Professional Fees						_		0.0%	_	0.0%
Gift Income								0.0%		0.0%
Investment Income	50,28	49,856	(429)	-0.9%		201,139	201,139	0.0%	280,974	-39.7%
Other Revenue	30,28.	- 30,414	, ,	100.0%		201,139	121,657	100.0%	235,273	-93.4%
Total Revenue	s \$ 1,802,04			76.2%		\$ 6,266,172		71.6%	\$ 11,521,960	-93.4% - <b>7.1</b> %
EXPENSES	\$ 1,802,04	5 7,575,467	\$ 5,773,422	70.2%		\$ 6,200,172	\$ 10,755,579	/1.0%	\$ 11,521,960	-7.1%
Salaries - Faculty	Ś	- \$ -	\$ -			\$ -		0.0%	\$ -	0.0%
Salaries - Staff	9,208,06		(81,645)	-0.9%		36,832,263	36,832,263	0.0%	36,892,078	-0.2%
Wages and Other Compensation	302,34			-42.7%		1,209,373	1,725,903	-42.7%	1,839,696	
Benefits and Other Payroll-Related Costs	2,443,35		, , ,	0.3%		9,773,428	9,773,428	0.0%	9,887,706	-1.2%
Subtotal - Personnel Cost				-1.7%		\$ 47,815,064		-1.1%	\$ 48,619,480	-0.6%
Cost of Goods Sold	3 7 11,933,700	- 12,137,939	Ç (204,173)	-1.770		\$ 47,813,004	\$ 40,331,334	0.0%	3 48,013,480	0.0%
Professional Fees and Services	908,14	923,843	(15,703)	-1.7%		3,632,559	3,632,559	0.0%	4,476,480	-23.2%
Travel	123,133		, , ,	47.1%		492,531	492,531	0.0%	4,470,480	8.4%
	210,29			-29.3%		841,165	841,165	0.0%	1,227,323	-45.9%
Materials and Supplies Communication and Utilities				-29.3% 148.8%	2	-		0.0%		-45.9% -157.5%
	201,58	, , ,				806,322	806,322 5,000,000		2,076,588	
Repairs and Maintenance	1,914,27			61.1%	3	5,254,369		4.8%	4,324,098	13.5%
Rentals and Leases	133,84		,	-462.9%	4	535,358	800,000	-49.4%	566,388	29.2% 93.0%
Printing and Reproduction	20,91			51.6%		83,658	83,658	0.0%	5,866	
Other Expenses	297,28	1 87,447	209,834	70.6%	1	1,189,125	1,189,125	0.0%	1,791,994	-50.7%
Internal (Income)/Charges	A 2 000 45		- 1 051 210	27.60/		42.025.007	Å 42.045.260	0.0%	(5,184,520)	-100.0%
Subtotal - Maintenance & Operation Cost	s \$ 3,809,45	4 \$ 2,758,105	\$ 1,051,349	27.6%	1	\$ 12,835,087	\$ 12,845,360	-0.1%	\$ 9,735,235	24.2%
Debt Service - Principal		-	-			-		0.0%	5,411,241	-100.0%
Debt Service - Interest	4 240 50	- 4 425 205	(24.4.720)	47.70/		2 502 004	2 502 004	0.0%	1,545,755	-100.0%
Capital Expenses	1,210,56	1,425,305	(214,739)	-17.7%	1	2,582,991	2,582,991	0.0%	568,127	354.6%
Federal and State Pass-Through Expense			-			-		0.0%	-	0.0%
Depreciation and Amortization			-			-		0.0%	-	0.0%
Scholarships, Exemptions and Financial Aid			-			-		0.0%	-	0.0%
Total Expense	s \$ 16,973,78	5 \$ 16,341,350	\$ 632,435	3.73%		\$ 63,233,142	\$ 63,759,945	-0.8%	\$ 65,879,838	-3.3%
TRANSFERS										
Intra-Campus Transfers Between Funds:										
Debt Service Transfer In/(Out)	\$ (1,953,994	) \$ (1,953,995)	\$ 1	0.00%		\$ (6,985,609)	\$ (6,985,609)	0.0%	\$ -	-100.0%
Inter-Fund Transfers In/(Out)		-	-			-	-	0.0%	417,020	-100.0%
Transfers Between UNTS Components:										
Shared Services	7,827,82		(468,223)	-5.98%			29,438,405	0.0%	27,683,339	6.0%
Core Services	6,487,79			-20.96%	6	22,615,922	22,528,422	-0.4%	16,878,153	
Other Inter-Unit Transfers In/(Out)	496,71	5 157,777	(338,938)	-68.2%	7	1,168,467	1,168,467	0.0%	2,009,175	-71.9%
Other Transfers: Transfer to other State Agencies In/(Out)	/4.44.633	,	444.000	400.000		(4.44.000)	-	400.00		0.000
· · · ·	(141,823		141,823	-100.00%		(141,823)	7.447.001	-100.0%	-	0.0%
Other Legislative Transfers In/(Out)	11,627,37	7,117,801	(4,509,573)	-38.78%	8	11,627,374	7,117,801	-38.8%	6,664,934	6.4%
Lapsed Appropriations		- 47.000.555	¢ (C F2F 225)	25.53		ć == =================================	- F0 007 400	0.0%	(551,391)	-100.0%
Total Transfer	, , ,			-26.8%	1	\$ 57,722,736		-7.7%	\$ 53,101,230	
Estimated Budgeted Impact on Fund Balances	\$ 9,172,14	8 \$ 9,042,977	\$ (129,171)	-1.4%		\$ 755,766	\$ 263,120	-65.2%	\$ (1,256,647)	577.6%
Planned Use of Fund Balances	\$	- \$ -	\$ -			\$ -	\$ -		\$ 1,256,647	

# FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Variance Explanations




#### **REVENUES**


	1120210020	
	Net Tuition and Fees	
	Sales of Goods and Services	
	Grants and Contracts	
		\$4.4m attributed to TRB debt service being budgeted in Other Legislative Transfers but recorded in State Appropriations. Remaining \$1.1m is due to State
1	State Appropriations	Appropriations being budgeted evenly throughout all four quarters but the entire amount was actually posted in Q1. This will be adjusted in future budgets
		and the forecast has been updated to reflect these variances.
	Capital Appropriations - HEF	
	Net Professional Fees	
	Gift Income	
	Investment Income	
	Other Revenue	
	EXPENSES	
	Salaries - Faculty	
	Salaries - Staff	
	Wages and Other Compensation	Wages scheduled to end over budget driven by termination payments. Forecast updated to reflect.
	Benefits and Other Payroll-Related Costs	
	Cost of Goods Sold	
	Professional Fees and Services	
	Travel	
	Materials and Supplies	
2	Communication and Utilities	Prior period adjustment causing credit balance. Expecting to come in line with budget by year end.
3	Repairs and Maintenance	IT related Repairs and Maintenance less than planned. Forecast has been adjusted to reflect.
4	Rentals and Leases	Driven mostly by software rental fees being greater than planned. Forecast has been adjusted to reflect.
	Printing and Reproduction	
	Other Expenses	
	Internal (Income)/Charges	
	Internal (income)/Charges	
	Debt Service - Principal	
	Debt Service - Interest	
	Capital Expenses	
	Scholarships, Exemptions and Financial Aid	
	TRANSFERS	
	Intra-Campus Transfers Between Funds:	
	Inter-Fund Transfers In/(Out)	
	Transfers Between UNTS Components:	
5	Shared Services	Timing of allocations not agreed upon until after budget submission.
6	Core Services	Timing of allocations not agreed upon until after budget submission.
7	Other Inter-Unit Transfers In/(Out)	Various transfers budgeted in Q1 now anticipated later in the year.
	Other Transfers:	
	Transfer to other State Agencies In/(Out)	
	Other Legislative Transfers In/(Out)	\$4.4m attributed to TRB debt service being budgeted in Other Legislative Transfers but recorded in State Appropriations. Remaining \$142k is due to
8		transfer to Texas A&M - Commerce being budgeted in "Transfers to Other State Agencies" but posted in Other Legislative Transfers. These variances will be
		adjusted in future budgets and the forecast has been updated to reflect.

## **Key Expense Categories**






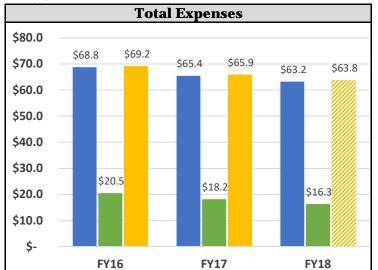



Projection

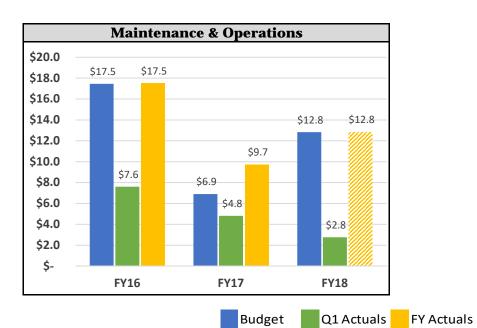



Page 22 of 69


## **Key Revenue Categories**





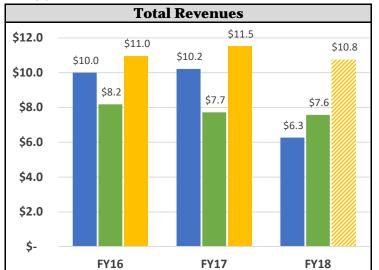





Projection

# **Investment Performance**



#### University of North Texas System Consolidated Investment Portfolio

For the Quarter Ending November 30, 2017	Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
-	Market Value	Market Value	Book Value	Interest	Yield*	Yield*
Short-Term Pool (STP) Investment Pool						
- Demand Deposit	\$ 13,511,398	\$ 10,130,490	\$ 10,130,490	\$ -	0.70%	0.70%
- Overnight Repurchase	7,665,644	1,820,441	1,820,441	-	0.08%	0.08%
- Demand Deposit Business Rate	14,882,914	17,178,469	17,178,469	-	1.12%	1.12%
- TexPool - Texas LGIP	10,258,799	972,933	972,933	-	1.03%	1.03%
- TexStar - Cash Reserve Fund	35,334,738	17,755,114	17,755,114	: -	1.05%	1.05%
- TexasTerm - TexasDaily	22,450,634	16,627,451	16,627,451	<u>-</u>	1.05%	1.05%
- TexasTerm - Term CP (matures 9/15/2017)	1,003,222	•		-	1.12%	1.12%
- TexasTerm - Term CP (matures 10/10/2017)	10,046,356		· :		1.20%	1.20%
- Morgan Stanley Prime MM Fund #8301	15,563,466	9,048,052	9,048,052	_	1.22%	1.22%
- Fidelity Prime MM Fund #2014	14,063,437	18,154,644	18,154,768	10,064	1.22%	1.22%
- Wells Fargo Heritage Select MM Fund #3801	14,065,561	9,347,803	9,347,803	,	1.25%	1.25%
- JPMorgan Prime MM Fund #3605	13,812,911	823,437	823,520		1.22%	1.22%
- Federated Prime MM Fund #58	13,306,031	7,584,821	7,588,497		1.28%	1.28%
- BlackRock Tmp Fund 24	13,300,031	98,720	98,720	3,679	1.21%	1.21%
- JPM Gov't Fund 3915	7,464,659	676,088	676,088	573	0.90%	0.90%
	252,352	070,000	070,000	3/3	0.87%	0.87%
- Legacy Texas Bank CD (matures 9/28/2017)  Total STP Investment Pool	\$ 193,682,121	\$ 110,218,463	\$ 110,222,345	\$ 14,316	1.10%	1.10%
Total 3 (P investment Pool	\$ 195,002,121	3 110,218,465	3 110,222,343	\$ 14,510	1.10%	1.10%
Intermediate Investment Pool (IIP)						
- Fannie Mae 1.25% Bond (matures 7/26/2019)	4,983,500	4,974,575	5,021,875	21,875	1.25%	1.25%
- Fannie Mae 1.125% Bond (matures 7/26/2019)	4,225,159	4,213,269	4,265,332	16,734	1.15%	1.15%
- Fed Farm Cr Bank 1.67% Bond (matures 6/22/2020)	5,012,754	4,985,979	5,034,534	36,879	1.69%	1.69%
- Vanguard S-T Corp. Bond Fund (VSTBX)	33,935,635	33,824,724	33,996,246	-	2.26%	2.26%
- Vanguard S-T Inv. Grade Bond Fund (VFSIX)	16,390,979	26,352,534	26,427,953	-	2.14%	2.14%
- Vanguard S-T Gov't. Bond Fund (VSBIX)	5,033,084	5,008,971	5,046,504	-	1.50%	1.50%
Total Intermediate Investment Pool	\$ 69,581,111	\$ 79,360,052	\$ 79,792,444	\$ 75,489	2.00%	2.00%
Debt Proceeds Investment Pool						
- TexasTerm - 2015A - TexasDaily	952,348	954,855	954,855	-	1.05%	1.05%
- TexasTerm - CP Proceeds - TexasDaily	805,209	807,330	807,330	-	1.05%	1.05%
- TexasTerm - CP Proceeds - Term CP (matures 12/26/2017)	10,805,788	10,838,754	10,838,754	88,754	1.23%	1.23%
- TexStar CP Proceeds- Cash Reserve Fund	3,497,924	3,507,106	3,507,106	•	1.05%	1.05%
- Fed Home LMC 1.45% Bond (matures 4/26/2019)	3,264,218	3,239,209	3,253,374	4,582	1.48%	1.48%
- Fed Home LMC 1.40% Bond (matures 4/26/2019)	5,019,255	4,980,156	5,005,691	6,806	1.42%	1.42%
- TexasTerm - 2017 A&B Bond Proceeds - Texas Daily	19,503,525	22,527,014	22,527,014	-	1.05%	1.05%
- TexasTerm - 2017 A&B Bond Proceeds - Term CP	183,638,848	147,726,516	147,726,516	726,516	1.29%	1.29%
Total Debt Proceeds Pool	227,487,114	194,580,939	194,620,639	826,657	1.26%	1.26%
Total Cash & Investment Pools	\$ 490,750,347	\$ 384,159,454	\$ 384,635,428	\$ 916,462	1.33%	1.33%
	Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
	Market Value	Market Value	Book Value	Interest	Return*	Return*
Long-Term Investments						
Long-Term Investment Pool	144,653,451	154,820,420	133,670,023	_	4.22%	4.22%
UNT and UNT Dallas Endowments	51,547,180	53,362,703	41,161,736	_	3.96%	3.96%
HSC Malpractice Fund	11,390,729	11,428,409	11,098,342	-	1.23%	1.23%
HSC Endowment Pool	2,356,259	4,515,763	4,252,907	-	4.17%	4.21%
HSC TEF Endowment Fund	28,047,520	28,721,761	24,287,402	· •	4.26%	4.21%
Total Long-Term Investments	237,995,139	252,849,056	214,470,410	-	4.03%	4.03%
						•
<u>Total UNTS Investments</u>	\$ 728,745,486	\$ 637,008,511	\$ 599,105,838	\$ 916,462	<u> </u>	.1

135,602,312

\$ 772,610,823

129,233,711

\$ 857,979,197

118,278,816

\$ 916,462

\$ 717,384,654

#### Other Investments


Foundation Investments - \*not assets of the System


**Total UNTS and Other Investments** 

3.99%

3.97%

### University of North Texas System Consolidated Investment Portfolio Market Values - 11/30/2017





Investment Type	Market Value	Allocation %	Policy Range %
STP	110,218,463	32.0%	10 - 20%
IIP	79,360,052	23.0%	20 - 60%
LTP	154,820,420	45.0%	25 - 60%
Total	344,398,936	100.0%	

<sup>\*</sup> The LTP Benchmarks are calculated using the revised Investment Policy as of May 2017



The attached report represents the investment portfolio of the University of North Texas for the period ending November 30, 2017, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.

Bo	b I	Вr	O'	W	'n
	_			-	

Digitally signed by Bob Brown DN: cn=8ob Brown, o=University of North Texas, ou=VP for Finance and Administration, email=bob.brown@unt.edu, c=US Date: 2018.02.06 11:36:37 -06'00'

Robert E. Brown, CPA Vice President for Finance and Administration, University of North Texas

Date

Digitally signed by James Mauldin James Mauldin

DN: cn=James Mauldin, o=UNT System, ou=Office
of the Vice Chancellor for Finance,
email=james.mauldin@untsystem.edu, c=US
Date: 2018.02.06 13:44:19 -06'00'

James Mauldin, CPA, CTP Associate Vice Chancellor for Treasury & Reporting, University of North Texas System

Date

1901 Main Street Dallas, TX 75201 (214) 752-8585 TEL (214) 752-8827 FAX

untsystem.unt.edu chancellor@unt.edu

#### University of North Texas Investment Portfolio

For the Quarter Ending November 30, 2017

#### Short-Term Pool (STP) Investment Pool

- Demand Deposit
- Overnight Repurchase
- Demand Deposit Business Rate
- TexPool Texas LGIP
- TexStar Cash Reserve Fund
- TexasTerm TexasDaily
- TexasTerm Term CP (matures 10/10/2017)
- Morgan Stanley Prime MM Fund #8301
- Fidelity Prime MM Fund #2014
- Wells Fargo Heritage Sel MM Fund #3801
- JPMorgan Prime MM Fund #3605
- Federated Inst MM Fund #58 <u>Total STP Investment Pool</u>

#### Intermediate Investment Pool (IIP)

- Fannie Mae 1.25% Bond (matures 7/26/2019)
- Fannie Mae 1.125% Bond (matures 7/26/2019)
- Vanguard S-T Corp. Bond Fund (VSTBX)
- Vanguard S-T Inv. Grade Bond Fund (VFSIX)
- Vanguard S-T Gov't. Bond Fund (VSBIX)

#### Total Intermediate Investment Pool

#### Debt Proceeds Pool

- TexasTerm 2015A TexasDaily
- TexasTerm CP Proceeds TexasDaily
- TexasTerm CP Proceeds Term CP (matures 12/26/2017)
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Texas Daily
- TexasTerm 2017 A&B Bond Proceeds Term CP

#### Total Debt Proceeds Pool

#### Long-Term Investment Accounts

UNT Long Term Investment Pool

**UNT Endowment** 

Total Long-Term Investments

#### **Total UNT Investments**

#### Other Investments for the Benefit of UNT


UNT Foundation Fund - \*not an asset of UNT

#### Total UNT and Other Investments

Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
Market Value	Market Value	Book Value	Interest	Yield*	Yield*
\$ 2,500,000	\$ 2,500,000	\$ 2,500,000	\$ -	** 1.00%	1.00%
6,812,155	312,485	312,485	-	0.08%	0.08%
14,882,914	17,178,469	17,178,469	-	1.12%	1.12%
8,936,358	193,738	193,738	-	1.03%	1.03%
15,106,756	619,840	619,840	-	1.05%	1.05%
2,388,252	2,708,784	2,708,784	-	1.05%	1.05%
10,046,356	-	- 1		1.20%	1.20%
15,563,466	9,048,052	9,048,052	2	1.22%	1.22%
14,063,437	8,144,580	8,144,704	2	1.22%	1.22%
14,065,561	9,347,803	9,347,803		1.25%	1.25%
13,812,911	823,437	823,520		1.22%	1.22%
13,306,031	7,584,821	7,588,497		1.28%	1.28%
\$ 131,484,197	\$ 58,462,009	\$ 58,465,891	\$ -	1.16%	1.16%
					4.050/
\$ 4,983,500	\$ 4,974,575	\$ 5,021,875	\$ 21,875	1.25%	1.25%
4,225,159	4,213,269	4,265,332	16,734	1.15%	1.15%
17,767,835	17,709,534	17,781,304	- 1	2.26%	2.26%
7,605,465	17,583,530	17,626,025	-	2.14%	2.14%
5,033,084	5,008,971	5,046,504	4 20 500	1.50%	1.50%
\$ 39,615,042	\$ 49,489,879	\$ 49,741,040	\$ 38,609	1.92%	1.92%
\$ 952,348	\$ 954,855	\$ 954,855	\$ -	1.05%	1.05%
288,462	289,222	289,222		1.05%	1.05%
4,020,758	4,033,025	4,033,025	33,025	1.23%	1.23%
872,883	866,165	869,983	1,225	1.48%	1.48%
1,342,196	1,331,694	1,338,569	1,820	1.42%	1.42%
5,467,776	8,479,747	8,479,747	-	1.05%	1.05%
52,439,853	42,334,261	42,334,261	206,670	1.29%	1.29%
\$ 65,384,277	\$ 58,288,968	\$ 58,299,662	\$ 242,739	1.26%	1.26%
Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
Market Value	Market Value	Book Value	Interest	Return*	Return*
\$ 98,377,029	\$ 106,939,796	\$ 91,500,000	\$ -	4.22%	4.22%
50,655,672	52,443,172	40,423,710		3.96%	3.96%
\$ 149,032,701	\$ 159,382,968	\$ 131,923,710	\$ -	4.14%	4.14%
		PH 191		712 170	
\$ 385,516,217	\$ 325,623,824	\$ 298,430,302	\$ 281,349		

<sup>\*</sup> Yield is reported as an annual figure, Return is reported for the current period

University of North Texas Investment Portfolio Market Values - 11/30/2017



\$ 500,337,302 \$ 445,698,058 \$ 403,794,517 \$ 281,349

<sup>\*\*</sup> Earnings Allowance Rate up to the amount of bank fees incurred during period



# UNT HEALTH SCIENCE CENTER

The attached report represents the investment portfolio of the University of North Texas Health Science Center for the period ending November 30, 2017, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.

Gregory R Anderson, CPA Executive VP for Finance and Chief Financial Officer, UNT Health Science Center
02 - 06 - 18 Date
James Mauldin  Digitally signed by James Mauldin  DN: cn=James Mauldin, o=UNT System, ou=Office of the Vice Chancellor for Finance, email=james.mauldingeutsystem.edu, c=US Date: 2018.02.06 08:19:17 -0600'
James Mauldin, CPA, CTP Associate Vice Chancellor for Treasury and Reporting, University of North Texas System
Date

1901 Main Street Dallas, TX 75201 (214) 752-8585 TEL (214) 752-8827 FAX untsystem.unt.edu chancellor@unt.edu University of North Texas Health Science Center Investment Portfolio

For the Quarter Ending November 30, 2017

#### Short-Term Pool (STP) Investment Pool

- Demand Deposit
- TexasTerm TexasDaily
- TexStar Cash Reserve Fund
- TexasTerm Term CP (matures 9/15/2017)
- JPM Govt MMF 3915
- BlackRock Temp MMF 24
- Fidelity Prime MMF 2014

#### Total STP Investment Pool

#### Intermediate Investment Pool (IIP)

- Vanguard S-T Corp. Bond Fund (VSTBX)
- Vanguard S-T Inv. Grade Bond Fund (VFSIX)
- Fed Farm Cr Bank 1.67% Bond (matures 6/22/2020)

#### Total Intermediate Investment Pool

#### Debt Proceeds

- TexasTerm CP Proceeds TexasDaily
- TexasTerm CP Proceeds Term CP (matures 12/26/2017)
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Texas Daily
- TexasTerm 2017 A&B Bond Proceeds Term CP

#### Total Debt Proceeds

#### Total STP, IIP & Debt Pools

#### Long-Term Investments

HSC Long Term Investment Pool HSC Malpractice Fund HSC Endowment Pool

HSC TEF Endowment Fund

Total Long-Term Investments

#### Total HSC Investment Portfolio

#### Other Investments

HSC Foundation - \* not an asset of HSC

#### Total HSC and Other Investments

Ν	larket Value	^	Narket Value		Book Value		1	nterest	Yield*	Yield*
,	0.463.904	\$	6,630,490	5	6,630,490	**	¢		0,50%	0.50%
\$	8,463,894	Þ	10,957,635	Ş	10,957,635		Ş		1.05%	1.05%
	19,918,021		13,250,347		13,250,347				1.05%	1.05%
	13,215,655		13,230,347		13,230,347				1.12%	1.12%
	1,003,222		676,088		676,088			573	0,90%	0.90%
	7,464,659		98,720		98,720			3,679	1.21%	1.21%
	-							10,064	1.22%	1.22%
\$	50,065,451	\$	10,010,064 41,623,344	\$	10,010,064		\$	14,316	1.01%	1.01%
-						Mari		1		
\$	16,167,800	\$	16,115,190	\$	16,214,942		\$		2.26%	2.26%
•	8,785,514		8,769,004		8,801,927			- 9	2.01%	2.02%
	5,012,754		4,985,979		5,034,534			36,879	1.69%	1.69%
\$	29,966,068	\$	29,870,173	\$	30,051,404		\$	36,879	2.09%	2,09%
	242,758	\$	243,398	\$	243,398		\$		1.05%	1.05%
\$	3,769,461	Ą	3,780,961	Ş	3,780,961		7	30,961	1.23%	1.23%
	909,336		902,444		906,316			1,276	1.48%	1.48%
	1,398,250		1,387,471		1,394,471			1,896	1.42%	1.42%
	3,837,203		614,999		614,999			1,030	1.05%	1.05%
	39,444,089		19,410,942		19,410,942			114,180	1,25%	1.25%
\$	49,601,098	\$	26,340,214	\$	26,351,086		\$	148,312	1,24%	1.24%
\$	129,632,617	\$	97,833,732	\$	98,025,834	16	\$	199,508	1.36%	1.36%
	Beginning		Ending	10	Ending			Accrued	QTR Approx.	YTD Approx.
Λ	farket Value	- 1	Market Value		Book Value			Interest	Return*	Return*
\$	34,476,555	\$	35,671,710	\$	31,400,000		\$		4.22%	4.22%
7	11,390,729	7	11,428,409	4	11,098,342		~		1.23%	1.23%
	2,356,259		4,515,763		4,252,907				4.17%	4.21%
	28,047,520		28,721,761		24,287,402				4.26%	4.21%
\$	76,271,063	\$	80,337,643	\$	71,038,651	A.	\$		3.80%	3.78%
						12.4			the second second second	

12,659,138

181,723,624

Ending

Accrued

QTR Approx.

4.11%

199,508

4.21%

YTD Approx.


Ending

Beginning

### University of North Texas HSC Investment Portfolio Market Values - 11/30/2017

13,756,261

219,659,941



15,272,615

193,443,989

<sup>\*</sup> Yield is reported as an annual figure, Return is reported for the current period

<sup>\*\*</sup> Earnings Allowance Rate up to the amount of bank fees incurred during period





The attached report represents the investment portfolio of the University of North Texas at Dallas for the period ending November 30, 2017, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.

X. A
D. : IEI I PLD
Daniel Edelman, PhD CFO & VP Finance and Administration, University of North Texas at Dallas
2/5/18
Date
Digitally signed by James Mauldin  DN: cn=James Mauldin, 0=UNT System, ou=Office of the Vice Chancellor for Finance, email=james.mauldin@untsystem.edu, c=US Date: 2018.02.02 14:02:14-06'00'
James Mauldin, CPA, CTP
Associate Vice Chancellor for Treasury & Reporting, University of North Texas System
Date

1901 Main Street Dallas, TX 75201 (214) 752-8585 TEL (214) 752-8827 FAX untsystem.unt.edu chancellor@unt.edu

#### University of North Texas at Dallas Investment Portfolio

For the Quarter Ending November 30, 2017

#### Short-Term Pool (STP) Investment Pool

- Demand Deposit
- Overnight Repurchase
- TexPool Texas LGIP
- TexStar Cash Reserve Fund
- Legacy Texas Bank CD (matured 9/28/2017)

#### Total STP Investment Pools

#### Debt Proceeds

- TexStar CP Proceeds- Cash Reserve Fund
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Daily Fund
- TexasTerm 2017 A&B Bond Proceeds Term CP

#### Total Debt Proceeds Pool

#### Total STP, IIP & Debt Pools

#### Long-Term Investments

UNTD Long Term Investment Pool UNTD Endowment

#### Total Long-Term Investments

#### Total UNT Dallas Investment Portfolio

#### Other Investments


Dallas Foundation Fund - \*not an asset of UNTD

#### Total UNT Dallas and Other Investments

	Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
٨	Market Value	Market Value	Book Value	Interest	Yield*	Yield*
\$	1,247,504	\$ 500,000	\$ 500,000	\$ -	1.00%	•• 1.00%
	- 4	65,014	65,014	# - H	0.08%	0.08%
	1,322,441	779,195	779,195	E - E	1.03%	1.03%
	1,400,835	1,608,178	1,608,178	: : I	1.05%	1.05%
	252,352	I - II	-	i - 1	0.87%	0.87%
\$	4,223,132	\$ 2,952,387	\$ 2,952,387	\$ -	1.02%	1.02%
	3,497,924	3,507,106	3,507,106	- 1	1.05%	1.05%
	785,391	779,354	782,782	1,102	1.48%	1.48%
	1,207,663	1,198,225	1,204,400	1,637	1.42%	1.42%
	6,166,999	9,887,211	9,887,211	- 1	1.05%	1.05%
	48,086,327	43,685,093	43,685,093	200,836	1.30%	1.30%
\$	59,744,304	\$ 59,056,990	\$ 59,066,592	\$ 203,576	1.26%	1.26%
\$	63,967,436	\$ 62,009,377	\$ 62,018,980	\$ 203,576	1.25%	1.25%
	Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
N	1arket Value	Market Value	Book Value	Interest	Return*	Return*
\$	5,998,571	\$ 6,206,515	\$ 5,496,792	\$ -	4.22%	4.22%
*	891,508	919,531	738,026	I . I	3.93%	3.93%
\$	6,890,079	\$ 7,126,045	\$ 6,234,818	\$ -	4.18%	4.18%
\$	70,857,515	\$ 69,135,423	\$ 68,253,798	\$ 203,576		
	656,366	255,463	255,463		0.00%	0.00%
\$	71,513,880	\$ 69,390,886	\$ 68,509,260	\$ 203,576	1.54%	1.54%

<sup>\*</sup> Yield is reported as an annual figure, Return is reported for the current period

### University of North Texas at Dallas Investment Portfolio Market Values - 11/30/2017 \* Excludes Debt Proceeds



<sup>\*\*</sup> Earnings Allowance Rate up to the amount of bank fees incurred during period





The attached report represents the investment portfolio of the University of North Texas System Administration for the period ending November 30, 2017, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.

James Mauldin Dictinally signed by James Mauldin DNt: cria James Mauldin, o-UNT System, ou=Office of the Vice Chancellor for Finance, email-james mauldin@untsystem.edu, c=US Date: 2018.02.05 103423-06000
James Mauldin, CPA, CTP Associate Vice Chancellor for Treasury and Reporting, University of North Texas System
Date
Bob Brown  Digitally signed by Bob Brown  DN: cn=Bob Brown, o=University of North Texas System, ou=Interim Vice Chancellor for Finance, email=bob.brown@unt.edu, c=US  Date: 2018.02.06 11:35:55 -06'00'
Robert E. Brown, CPA Interim Vice Chancellor for Finance, University of North Texas System
Date

1901 Main Street Dallas, TX 75201 (214) 752-8585 TEL (214) 752-8827 FAX untsystem.unt.edu chancellor@unt.edu

#### University of North Texas System Investment Portfolio

For the Quarter Ending November 30, 2017

#### Short-Term Pool (STP) Investment Pool

- Demand Deposit
- Overnight Repurchase
- TexStar Cash Reserve Fund
- TexasTerm TexasDaily

#### Total STP Investment Pool

#### **Debt Proceeds**

- TexasTerm CP Proceeds TexasDaily
- TexasTerm CP Proceeds Term CP (matures 12/26/2017)
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Texas Daily
- TexasTerm 2017 A&B Bond Proceeds Term CP

#### **Total Debt Proceeds**

#### Total STP and Debt Pools

#### Long-Term Investments

UNT Long Term Investment Pool

#### **Total Long-Term Investments**


#### **Total SYS Investments**

Beginning		Ending			Ending		Accrued		QTR Approx.	YTD Approx.	
Market Value		Market Value		В	Book Value		Interest		Yield*	Yield*	
									4.000/	4 000/	
\$	1,300,000.00	\$	500,000	\$	500,000	\$	7	••	1.00%	1.00%	
	853,489		1,442,942		1,442,942		-		0.08%	0.08%	
	5,611,493		2,276,749		2,276,749		-		1.05%	1.05%	
	144,361		2,961,032		2,961,032		-		1.05%	1.05%	
\$	7,909,343	\$	7,180,723	\$	7,180,723	\$			1.02%	1.02%	
\$	273,989	\$	274,710	\$	274,710	\$	<u> </u>		1.05%	1.05%	
	3,015,569		3,024,768		3,024,768		24,768		1.23%	1.23%	
	696,608		691,247		694,294		978		1.48%	1.48%	
	1,071,146		1,062,765		1,068,251		1,452		1.42%	1.42%	
	4,031,547		3,545,055		3,545,055		-		1.05%	1.05%	
	43,668,579		42,296,220		42,296,220		204,830		1.30%	1.30%	
\$	52,757,437	\$	50,894,766	\$	50,903,299	\$	232,029		1.28%	1.28%	
\$	60,666,780	\$	58,075,489	\$	58,084,022	\$	232,029		1.24%	1.24%	
_	Beginning		Ending		Ending				QTR Approx.	YTD Approx.	
١	Market Value	N	1arket Value	В	ook Value				Return*	Return*	
\$	5,801,294.75	\$	6,002,400	\$	5,273,231	\$	_		4.22%	4.22%	
\$	5,801,295	\$	6,002,400	\$	5,273,231	\$	-		4.22%	4.22%	
\$	66,468,074	\$	64,077,889	\$	63,357,253	\$	232,029				

<sup>\*</sup> Yield is reported as an annual figure, Return is reported for the current period

University of North Texas System Investment Portfolio Market Values - 11/30/2017

\* Excludes Debt Proceeds



<sup>\*\*</sup> Earnings Allowance Rate up to the amount of bank fees incurred during period

# Capital Improvement Plan Status



#### **UNT System FY 2018 Capital Improvement Plan Status**

February 2018 (Report as of December 20, 2017)



### **Project Budget Status**

Camp.	Project No.	Project Name	Аррі	roved Budget	Expensed	ı	Encumbered	Remaining Balance
UNT	2.20	Matthews Hall MEP*	\$	1,200,000	\$ 241,417	\$	69,000	\$ 889,583
	2.21	Wooten Hall MEP*	\$	3,450,000	\$ 1,012,747	\$	153,400	\$ 2,283,853
	2.33	Willis Library MEP*	\$	9,850,000	\$ 383,604	\$	89,420	\$ 9,376,976
	2.34	Hickory Hall MEP*	\$	3,000,000	\$ 2,756,322	\$	240,663	\$ 3,015
	16-1.20	College of Visual Arts and Design	\$	70,000,000	\$ 17,475,126	\$	41,778,490	\$ 10,746,384
	16-1.84a	New Residence Hall - Phase 1	\$	58,900,000	\$ 4,396,425	\$	48,711,311	\$ 5,792,264
	16-1.84b	New Residence Hall - Phase 2	\$	43,700,000	\$ -	\$	-	\$ 43,700,000
	16-2.25	General Academic Building MEP and Interior Renovation*	\$	10,350,000	\$ -	\$	623,041	\$ 9,726,959
	16-2.50	Life Science Lab Exhaust Upgrade*	\$	3,200,000	\$ -	\$	190,750	\$ 3,009,250
	16-2.55	Discovery Park MEP Upgrade*	\$	20,600,000	\$ -	\$	-	\$ 20,600,000
	16-2.65	Sycamore Hall 2nd Floor Renovation*	\$	3,950,000	\$ 3,363,513	\$	397,542	\$ 188,945
	16-2.66	Coliseum Concourse Renovation	\$	8,000,000	\$ 2,871,315	\$	4,616,403	\$ 512,282
	16-2.67	1500 I-35E Building	\$	12,500,000	\$ 630,759	\$	374,634	\$ 11,494,607
	16-2.77	Wooten Hall Code Upgrade*	\$	4,230,000	\$ 112,132	\$	23,855	\$ 4,094,013
	16-2.82	Track and Field Stadium	\$	13,590,000	\$ 1,750,086	\$	10,439,499	\$ 1,400,415
	16-2.85	Sage Hall Academic Success Center*	\$	1,850,000	\$ 824,509	\$	801,680	\$ 223,811
	17-01-0001	Terrill Hall MEP & Interior Renovation*	\$	7,300,000	\$ -	\$	-	\$ 7,300,000
	17-01-0002	Coliseum MEP Renovation*	\$	10,400,000	\$ -	\$	-	\$ 10,400,000
	17-01-0003	Kerr Hall MEP & Interior Renovation*	\$	5,790,000	\$ 2,780,240	\$	9,550	\$ 3,000,210
	17-01-0004	USB MEP Renovation*	\$	3,600,000	\$ -	\$	-	\$ 3,600,000
	17-01-0005	Discovery Park Bio-Medical Engineering Addition	\$	17,400,000	\$ 489,672	\$	835,961	\$ 16,074,367
	17-01-0006	Sage Hall Academic Success Center Phase II*	\$	2,920,000	\$ 35,582	\$	143,381	\$ 2,741,037
	17-01-0007	Life Science Building 4th Floor Laboratories Renovation*	\$	7,000,000	\$ -	\$	-	\$ 7,000,000
	17-01-0008	Coliseum Roof Replacement*	\$	2,430,000	\$ -	\$	-	\$ 2,430,000
	17-01-0009	Off-Site Campus #2*	\$	1,500,000	\$ -	\$	-	\$ 1,500,000
	17-01-0010	New Classroom Building	\$	25,100,000	\$ -	\$	-	\$ 25,100,000
	17-01-0011	Hickory Hall Renovation	\$	8,800,000	\$ -	\$	-	\$ 8,800,000
	17-01-0012	Eagle Point Parking Lot #80*	\$	2,200,000	\$ 78,786	\$	24,934	\$ 2,096,280
	18-01-0001	Maple Hall MEP & Renovation*	\$	4,380,000	\$ -	\$	-	\$ 4,380,000
	18-01-0002	Clark Hall Lobby Renovation*	\$	2,270,000	\$ -	\$	-	\$ 2,270,000
	18-01-0003	Sage Hall Academic Success Center Phase III*	\$	3,010,000	\$ -	\$	-	\$ 3,010,000
	18-01-0004	Art Building Roof Replacement	\$	1,350,000	\$ -	\$	30,630	\$ 1,319,370
	18-01-0005	Discovery Park Utility Capacity Upgrade*	\$	2,000,000	\$ -	\$	1,477,683	\$ 522,317
	18-01-0006	Music Building Courtyard Renovation*	\$	2,590,000	\$ -	\$	-	\$ 2,590,000
	18-01-0007	New Dining Hall	\$	25,470,000	\$ 195,376	\$	1,878,712	\$ 23,395,912
	18-01-0008	Fouts Field Demolition, Parking, and Bus Transfer Station	\$	14,000,000	\$ -	\$	890,106	\$ 13,109,894
	18-01-0009	New Athletics Indoor Practice Facility	\$	18,900,000	\$ -	\$	-	\$ 18,900,000
UNTD	16-1.01	Student Learning and Success Center	\$	63,000,000	\$ 6,655,173	\$	46,664,972	\$ 9,679,855
HSC	16-1.40	Interdisciplinary Research Building	\$	118,500,000	\$ 58,992,167	\$	46,386,046	\$ 13,121,787
	16-2.96	Research and Education (RES) Level 4	\$	4,500,000	\$ 3,600	\$	-	\$ 4,496,400
	17-03-0001	East Parking Garage Renovation*	\$	6,000,000	\$ -	\$	-	\$ 6,000,000
	17-03-0002	Medical Clinic	\$	4,200,000	\$ -	\$	-	\$ 4,200,000
	18-03-0001	Gross Anatomy Laboratory Renovation*	\$	2,470,000	\$ 	\$	-	\$ 2,470,000
	18-03-0002	1408 St. Louis Ave. Renovation*	\$	1,950,000	\$ 1,605,061	\$	313,009	\$
System	16-2.01	Renovate Dallas Municipal Building and Associated Law Buildings	\$	56,000,000	\$ 7,461,997	\$	36,340,179	\$ 12,197,824

February 2018 (Report as of December 20, 2017)



# **Project Overview**

Campus	Project No.	Project Name	Scope	Schedule	Budget
UNT	2.20	Matthews Hall MEP*			
	2.21	Wooten Hall MEP*			
	2.33	Willis Library MEP*			
	2.34	Hickory Hall MEP*			
	16-1.20	College of Visual Arts and Design			
	16-1.84a	New Residence Hall - Phase 1			
	16-1.84b	New Residence Hall - Phase 2			
	16-2.25	General Academic Building MEP and Interior Renovation*			
	16-2.50	Life Science Lab Exhaust Upgrade*			
	16-2.55	Discovery Park MEP Upgrade*			
	16-2.65	Sycamore Hall 2nd Floor Renovation*			
	16-2.66	Coliseum Concourse Renovation			
	16-2.67	1500 I-35E Building			
	16-2.77	Wooten Hall Code Upgrade*			
	16-2.82	Track and Field Stadium			
	16-2.85	Sage Hall Academic Success Center*			
	17-01-0001	Terrill Hall MEP & Interior Renovation*			
	17-01-0002	Coliseum MEP Renovation*			
	17-01-0003	Kerr Hall MEP & Interior Renovation*			
	17-01-0004	USB MEP Renovation*			
	17-01-0005	Discovery Park Bio-Medical Engineering Addition			
	17-01-0006	Sage Hall Academic Success Center Phase II*			
	17-01-0007	Life Science Building 4th Floor Laboratories Renovation*			
	17-01-0008	Coliseum Roof Replacement*			
	17-01-0009	Off-Site Campus #2*			
	17-01-0010	New Classroom Building			
	17-01-0011	Hickory Hall Renovation			
	17-01-0012	Eagle Point Parking Lot #80*			
	18-01-0001	Maple Hall MEP & Renovation*			
	18-01-0002	Clark Hall Lobby Renovation*			
	18-01-0003	Sage Hall Academic Success Center Phase III*			
	18-01-0004	Art Building Roof Replacement			
	18-01-0005	Discovery Park Utility Capacity Upgrade*			
	18-01-0006	Music Building Courtyard Renovation*			
	18-01-0007	New Dining Hall			
	18-01-0008	Fouts Field Demolition, Parking, and Bus Transfer Station			
	18-01-0009	New Athletics Indoor Practice Facility			
UNTD	16-1.01	Student Learning and Success Center			
HSC	16-1.40	Interdisciplinary Research Building			
	16-2.96	Research and Education (RES) Level 4			
	17-03-0001	East Parking Garage Renovation*			
	17-03-0002	Medical Clinic			
	18-03-0001	Gross Anatomy Laboratory Renovation*			
	18-03-0001	1408 St. Louis Ave. Renovation*			
System	16-2.01	Renovate Dallas Municipal Building and Associated Law Buildings			



Minor adjustment from previous project update

Substantial change from previous project update

Project On-Hold

# FY2018 SUMMARY (in \$Million)

		Funding	Prior Yrs						Total
Proj. No.	Project	Source	Budget	2018	2019	2020	2021	2022+	Project
University of	of North Texas								
18-01-0001	Maple Hall MEP & Renovation	AUX		4.38					4.38
18-01-0002	Clark Hall Lobby Renovation	AUX		0.17	2.10				2.27
18-01-0003	Sage Hall Academic Success Center Phase III	HEAF		0.26	2.75				3.0
18-01-0004	Art Building Roof Replacement	CP		1.35					1.3
18-01-0005	Discovery Park Utility Capacity Upgrade	HEAF		2.00					2.00
18-01-0006	Music Building Courtyard Renovation	HEAF	0.09	1.50					
		GIFT			1.00				2.59
18-01-0007	New Dining Hall	RFS	0.20	3.50	15.28	6.49			25.47
18-01-0008	Fouts Field Demolition, Parking, and Bus Transfer Station	RFS		2.00	12.00				14.00
18-01-0009	Athletic Indoor Practice Facility	RFS		1.50	9.90				
	,	GIFT			7.50				18.90
	University of No	rth Texas Total	0.29	16.66	50.53	6.49	-		73.97
University of	of North Texas Dallas								
	University of North Te	xas Dallas Total	-	-	-	-	-	-	-
University (	of North Texas Health Science Center								
18-03-0001	Gross Anatomy Laboratory Renovation	RFS		2.47					2.47
18-03-0002	1408 St. Louis Ave. Renovation	HEAF	0.30	1.65					1.95
	University of North Texas Health Scien	nce Center Total	0.30	4.12	-	-	-	-	4.42
University of	of North Texas System	_	_	_			·		
	University of North Tex	as System Total	-	-	-	-	-	-	-

	Funding	Prior Yrs						
	Source	Budget	2017	2018	2019	2020	2021+	Total
HEAF	HEAF	0.39	5.41	2.75	-	-	-	8.55
HEAF Reserve	HEAF Reserve	-	-	-		-	-	-
Tuition Revenue Bonds	TRB	-	-	-		-	-	-
Commercial Paper	CP	-	1.35	-		-	-	1.35
Private Placement	PP	-	-	-	-	-	-	
Revenue Bonds	RB	-	-	-		-	-	
Revenue Financing System Bonds	RFS	0.20	9.47	37.18	6.49	-	-	53.34
Auxiliary Reserves	AUX	-	4.55	2.10		-	-	6.65
Grants	GRNT	-	-	-		-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	8.50	-	-	-	8.50
Annual Budget, Operating and Capital	Local/Cash	-	-	-	-	-	-	•
	Total	0.59	20.78	50.53	6.49	-	-	78.39

# FY2018 Capital Improvement Plan UNIVERSITY of NORTH TEXAS SYSTEM

# UNIVERSITY OF NORTH TOPP

# FY2018 (in \$Million)

University	of North Texas		_		-				
Proj. No.	Project	Funding Source	Prior Yrs Budget	2018	2019	2020	2021	2022+	Total Project
	Approved Projects:	-							
2.20	Matthews Hall MEP (Amended)	HEAF	1.20						1.20
2.21	Wooten Hall MEP (Amended)	HEAF	3.45						3.45
2.33	Willis Library MEP (Amended)	HEAF	5.16	4.69					9.85
2.34	Hickory Hall MEP	HEAF	3.00						3.00
16-1.20	College of Visual Arts and Design	TRB	27.00	38.00	5.00				70.00
16-1.84	New Residence Hall								
16-1.84a	New Residence Hall - Phase 1 (Amended)	RFS	17.04	28.68	13.18				
16-1.84b	New Residence Hall - Phase 2	RFS	17.01	20.00	10.10	11.86	18.89	12.95	102.60
16-2.25	General Academic Building MEP & Interior Renovation		0.75			11.00	10.09	12.90	102.00
10-2.23	(Amended)	HEAF	0.75						
40.0.50		RFS			9.60				10.35
16-2.50	Life Science Lab Exhaust Upgrade	HEAF	3.20						3.20
16-2.55	Discovery Park MEP Upgrade (Amended)	HEAF		1.00	9.00	10.00	0.60		20.60
16-2.62a	Maple Common Area Renovation	AUX	1.65						1.65
16-2.65	Sycamore 2nd Floor Renovation (Amended)	HEAF	3.95						3.95
16-2.66	Coliseum Concourse Renovation	RFS	5.50	2.50					8.00
16-2.67	1500 I-35 Building (Amended)	RFS	10.50	2.00					12.50
16-2.77	Wooten Hall Code Upgrade (Amended)								
16-2.82	Track and Field Stadium (Amended)	HEAF	2.07	2.16					4.23
10-2.02	Track and Field Stadium (Amended)	RFS	4.00	5.90	2.00				
		AUX			1.69				13.59
16-2.85	Sage Hall Academic Success Center	HEAF Reserve	1.85						1.85
17-01-0001	Terrill Hall MEP & Interior Renovation (Amended)	HEAF	0.55	0.25	6.50				7.30
17-01-0002	Coliseum MEP Renovation (Amended)	RFS			0.90	9.50			10.40
17-01-0003	Kerr Hall MEP & Interior Renovation (Amended)	AUX	2.10	3.69					5.79
17-01-0004	USB MEP Renovation (Amended)	HEAF	0.30	3.30					3.60
	Discovery Park Bio-Medical Engineering Addition								
		RFS	2.00	15.40					17.40
17-01-0006	Sage Hall Academic Success Center Phase II (Amended)	HEAF Reserve	0.17						
17.01.0007	1.7.0 : D.17. 40 Et . 1	HEAF		2.75					2.92
17-01-0007	Life Science Building 4th Floor Laboratories Renovation (Amended)	RFS				0.70	6.30		7.00
17-01-0008	Coliseum Roof Replacement (Amended)	Local/Cash		2.43					2.43
17-01-0009	Off-Site Campus #2	Local/Cash	0.10	1.40					1.50
17-01-0010	New Classroom Building	RFS		2.20	22.90				25.10
17-01-0011	Hickory Hall Renovation	RFS		0.80	8.00				8.80
17-01-0012	Eagle Point Parking Lot #84	CP	2.20	0.00	0.00				2.20
	Previously Approv		97.74	117.15	78.77	32.06	25.79	12.95	364.46
New Project	ts for Approval:		<b>V</b>			<u> </u>			
	Maple Hall MEP & Renovation	AUX		4.38					4.38
	Clark Hall Lobby Renovation	AUX		0.17	2.10				2.27
	Sage Hall Academic Success Center Phase III	HEAF		0.26	2.75				3.01
18-01-0004	Art Building Roof Replacement	CP		1.35					1.35
	Discovery Park Utility Capacity Upgrade	HEAF		2.00					2.00
18-01-0006	Music Building Courtyard Renovation	HEAF	0.09	1.50					
10.01		GIFT			1.00				2.59
	New Dining Hall	RFS	0.20	3.50	15.28	6.49			25.47
	Fouts Field Demolition, Parking, and Bus Transfer Station	RFS		2.00	12.00 9.90				14.00
18-01-0009	Athletic Indoor Practice Facility	RFS GIFT		1.50	7.50				18.90
	New Project f	or Approval Total	0.29	16.66	50.53	6.49	-	_	73.97
Planned Pro	pjects with Identified Funding Sources:		5.20	10.00	55.55	5.75			, 5.57
01-0010	Administration Building Renovation	HEAF			1	1.70	7.20	10.00	18.90
01-0010	Curry Hall MEP	HEAF			0.52	5.25	7.20	10.00	5.77
01-0011	Underground Utility Repairs	HEAF			0.28	2.73			3.01
01-0013	PAC Foundation Repairs	HEAF				0.20	1.95		2.15
	Physical Education Building (PEB) MEP & Interior								
01-0014	Renovation	HEAF				1.75	17.35		19.10

# UNT

FY2018 (in \$Million)

	-		Prior Yrs						Total
Proj. No.	Project	Funding Source	Budget	2018	2019	2020	2021	2022+	Project
01-0015	Language Building MEP	HEAF			0.45	5.62	-		6.0
01-0016	Demo and Build New Business Svs Whse	AUX					1.25		1.2
01-0017	SRB MEP Renovation	HEAF				0.26	2.63		2.89
01-0018	RTFP MEP Renovation	HEAF			0.75	7.00			7.7
01-0019	Sage Hall Academic Success Center - Phase IV	HEAF			0.24	1.76			2.00
01-0020	Welch St Complex #2 Demolition	HEAF			1.50				1.50
01-0021	Chilton Classroom & Restrooms	HEAF			0.40	4.00			4.40
01-0022	Discovery Park Greenhouse Addition	RFS			3.00				3.00
01-0023	ESSC Envelope Upgrade	HEAF			7.80				7.80
01-0024	New Science & Tech Research Building	TRB				11.76	50.00	36.24	98.00
01-0025	Union Circle Drive Re-surface	AUX				2.00			2.00
01-0026	USB Interior Renovation	HEAF				0.25	2.50		2.75
	Planned Projects with Identified F	unding Sources Total	-	-	14.94	44.28	82.88	46.24	188.34
Planned La	and Acquisitions						·		
3.01	Land Acquisitions per Master Plan	HEAF		1.00	1.50	1.50	1.50	1.50	7.00
	Planned L	and Acquisition Total	-	1.00	1.50	1.50	1.50	1.50	7.00

Capital Improvement Plan Total \_

# Planned Project without Identified Funding Sources

New Construction:

New Athletics Indoor Practice Facility New Sports Arena Renovation:

134.81

98.03

Athletic Center Renovation and Expansion Music Building Renovations

84.33

110.17

60.69

633.77

145.74

**Summary by Funding Source** 

		Prior Yrs						
	Funding Source	Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	23.72	18.91	31.69	42.02	33.73	11.50	161.57
HEAF Reserve	HEAF Reserve	2.02	-		-	-	-	2.02
Tuition Revenue Bonds	TRB	27.00	38.00	5.00	11.76	50.00	36.24	168.00
Commercial Paper	СР	2.20	1.35	-	-	-	-	3.55
Private Placement	PP	-	-	-	-	-	-	-
Revenue Bonds	RB	-	-	-	-	-	-	-
Revenue Financing System Bonds	RFS	39.24	64.48	96.76	28.55	25.19	12.95	267.17
Auxiliary Reserves	AUX	3.75	8.24	3.79	2.00	1.25	-	19.03
Grants	GRNT	-	-	-	-	-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	8.50	-	-	-	8.50
Annual Budget, Operating and Capital	Local/Cash	0.10	3.83	-	-	-	-	3.93
	Total	98.03	134.81	145.74	84.33	110.17	60.69	633.7



73.15

# FY2018 (in \$Million)

**University of North Texas Dallas** 

			Prior Yrs						Total
Proj. No.	Project	Funding Source	Budget	2018	2019	2020	2021	2022+	Project
Previously	y Approved Projects:								
16-1.01	Student Learning and Success Center	TRB	16.00	33.40	13.60				63.00
16-1.04	Campus Infrastructure	HEAF	1.15						
		CP	0.50						1.65
1.03	Residence Hall (Amended)	RB	7.69						
		Local/Cash	0.81						8.50
	Previously	Approved Projects Total	26.15	33.40	13.60	-	-	-	73.15
New Proje	ects for Approval:								•
	New I	Project for Approval Total		-	-		-	-	-
Planned P	Projects with Identified Funding Sources:				•				
	Planned Projects with Identifie	ed Funding Sources Total	-	-	-	-	-	-	-
Planned L	and Acquisitions								•
									-
	Planne	ed Land Acquisition Total	-	-	-	-	-	-	-

Capital Improvement Plan Total 26.15

# Planned Project without Identified Funding Sources

New Construction:

Landmark Tower

Second Residence Hall
STEM Building
Business Technology Building
Event Center
Parking Garage

Renovation:

33.40

13.60

# **Summary by Funding Source**

		Prior Yrs						
	Funding Source	Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	1.15	-	-	-	-	-	1.15
HEAF Reserve	HEAF Reserve	-	-	-	-	-	-	
Tuition Revenue Bonds	TRB	16.00	33.40	13.60	-	-	-	63.00
Commercial Paper	СР	0.50	-	-	-	-	-	0.50
Private Placement	PP	-	-	=	-	-	-	-
Revenue Bonds	RB	7.69	-	-	-	-	-	7.69
Revenue Financing System Bonds	RFS	-	-	-	-	-	-	-
Auxiliary Reserves	AUX	-	-	-	-	-	-	-
Grants	GRNT	-	-	-	-	-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	-	-	-	-	-
Annual Budget, Operating and Capital	Local/Cash	0.81	-	-	-	-	-	0.81
	Total	26.15	33.40	13.60	-	-	-	73.15

Page 41 of 69

UNT HEALTH

# FY2018 (in \$Million)

			Prior Yrs						Total
Proj. No.	Project	Funding Source	Budget	2018	2019	2020	2021	2022+	Project
Previously	Approved Projects:								
16-1.40	Interdisciplinary Research Building	TRB	35.70	44.30					
		RFS	8.23	12.57	16.70				1
		GIFT			1.00				118.50
16-2.96	Research and Education (RES) Level 4	RFS	0.01		2.99	1.50			4.50
17-03-0001	East Parking Garage Renovation	RFS		0.40	5.60				6.00
17-03-0002	Medical Clinic (Amended)	RFS			1.00	3.20			4.20
	Previously A	Approved Projects Total	43.94	57.27	27.29	4.70	-	-	133.20
New Projec	cts for Approval:					·		•	
18-03-0001	Gross Anatomy Laboratory Renovation	RFS		2.47					2.47
18-03-0002	2 1408 St. Louis Ave. Renovation	HEAF	0.30	1.65					1.95
	New Pr	oject for Approval Total	0.30	4.12	-	-	-	-	4.42
Planned Pr	rojects with Identified Funding Sources:								
									ļ
	Planned Projects with Identified	Funding Sources Total	-	-	-	-		_	-
	and Acquisitions								
3.01	Property Acquisition	HEAF		1.00					1.00
	Planned	d Land Acquisition Total	-	1.00	-	-	-	-	1.00
	Canital	Improvement Plan Total	44.24	62.39	27.29	4.70	_	_	138.62

Planned Project without Identified Funding Sources

New Construction:

Parking Garage

Renovation:

Summary by Funding Source
---------------------------

		Prior Yrs						
	Funding Source	Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	0.30	2.65	-	-	-	-	2.95
HEAF Reserve	HEAF Reserve	-	-	-	-	-	-	-
Tuition Revenue Bonds	TRB	35.70	44.30	-	-	-	-	80.00
Commercial Paper	СР	-	-	-	-	-	-	-
Private Placement	PP	=	-	-	-	-	-	-
Revenue Bonds	RB	=	-	-	-	-	-	-
Revenue Financing System Bonds	RFS	8.24	15.44	26.29	4.70	-	-	54.67
Auxiliary Reserves	AUX	-	-	-	-	-	-	-
Grants	GRNT	-	-	-	-	-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	1.00	-	-	-	1.00
Annual Budget, Operating and Capital	Local/Cash	-	-	-	-	-	-	-
	Total	44.24	62.39	27.29	4.70	0.00	0.00	138.6



# FY2018 (in \$Million)

Proj. No.	· Project	Funding Source	Prior Yrs Budget	2018	2019	2020	2021	2022+	Total Project
Previous	ly Approved Projects:							2021 2022+	
16-2.01	Renovate Dallas Municipal Bldg and Assoc Law Bldgs	TRB	12.54	25.20	18.26				56.00
	Previously Approved	<u>l</u> l Projects Total	12.54	25.20	18.26	-	-	-	56.00
New Pro	jects for Approval:								
	New Project for	Approval Total	-	-	-	-	-	-	-
Planned	<b>Projects with Identified Funding Source</b>	s:							
04-0001	Renovation of the Municipal Building for Historical Exhibit	GIFT			3.50				3.50
	Diament Dunington with Identified Funding	Common Total			2.50				2.50
	Planned Projects with Identified Funding Land Acquisitions	Sources Total	-	-	3.50	-	-	-	3.50
									-
	Planned Land Ac	 :quisition Total	-	-	-	-	-	-	-
	Capital Improven	nent Plan Total	12.54	25.20	21.76	_	-	_	59.50

# **Planned Project without Identified Funding Sources**

New Construction:

# Renovation:

System Building 8th Floor System Building Floors 2-4 1900 Elm Street Lobby

**Summary by Funding Source** 

by I unumg Source	Funding Source	Prior Yrs Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	-	-	-	-	-	-	
HEAF Reserve	HEAF Reserve	-	-	-	-	-	-	
Tuition Revenue Bonds	TRB	12.54	25.20	18.26	-	-	-	56.00
Commercial Paper	CP	-	-	-	-	-	-	-
Private Placement	PP	-	-	-	-	-	-	-
Revenue Bonds	RB	-	-	-	-	-	-	
Revenue Financing System Bonds	RFS	-	-	-		-	-	-
Auxiliary Reserves	AUX	-	-	-	-	-	-	•
Grants	GRNT	-	-	-		-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	3.50	-	-	-	3.50
Annual Budget, Operating and Capital	Local/Cash	-	-	-	-	-	-	-
Tota		12.54	25.20	21.76	0.00	-	-	59.50

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# **Previously Approved Projects**

# 2.20 Matthews Hall MEP\*

#### **Current Project Status**

The re-design of the electrical portion of this project is anticipated to be complete February 2018 with the process to begin bidding via competative sealed proposal anticipated to begin in February 2018. It is anticipated that construction will begin in April 2018. The schedule is now adjusted based on when the Professional Services Amendment was processed.

Project Budget			
Approved Budget	\$ 1,200,000	Expensed	\$ 241,417
		Encumbered	\$ 69,000
		Remaining Balance	\$ 889,583

#### **Major Project Contract Information**

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Summit Consultants	14.00%
Contractor	CSP	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	70%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete		-	-	-	<u>-</u>
	Design Complete	Mar-15	-	Feb-18	-
<b>Construction Substantial Completion</b>		Apr-16	Sep-18	Dec-18	-
	Construction End	Apr-16	Oct-18	Jan-19	-

# 2.21 Wooten Hall MEP\*

#### **Current Project Status**

The coil replacement work for the mechanical system is scheduled to coordinate with the occupancy of the building, which affected the project completion date. The project is anticipated to be complete in February 2018.

Project Budget				
	\$ 3,450,000	Expensed	\$ 1,012,747	
		Encumbered	\$ 153,400	
		Remaining Balance	\$ 2,283,853	

	Solicitation/Type of	Solicitation/Type of				
	Contract	Selected Firm	HUB Participation			
Architect	RFQ	Campos Engineering	81.00%			
Contractor	State Contract	Entech	0.09%			
Contractor	-	-	-			
Contractor	-	-	-			

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	50%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete		-	-	-	-
	Design Complete	Aug-15	-	-	May-15
Con	struction Substantial Completion	Mar-17	Dec-18	Jan-19	-
	Construction End	Mar-17	Jan-19	Feb-19	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 2.33 Willis Library MEP\*

# **Current Project Status**

Due to the need to coordinate with another smaller construction project in the facility, which impacted the design of the electrical rooms of this project, design completion was delayed. Now that coordination has been resolved, the design can be finalized and is expected to be complete January 2018. Construction will be executed via Competitive Sealed Proposal (CSP), and is anticipated to begin April 2018. Projected completion dates have been updated based on estimates of when construction contracts could be awarded.

Project Budget				
Approved Budget	\$ 9,850,000	Expensed	\$ 383,604	
		Encumbered	\$ 89,420	
		Remaining Balance	\$ 9,376,976	

# **Major Project Contract Information**

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	RFQ	Yaggi Engineering	100.00%
Contractor	CSP	TBD	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	98%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete		-	-	-	May-15
	Design Complete	Nov-15	Oct-17	Jan-18	-
Const	ruction Substantial Completion	Mar-18	Jun-19	Aug-19	-
	Construction End	Mar-18	Jul-19	Sep-19	-

#### 2.34 Hickory Hall MEP\*

#### **Current Project Status**

The project was bid utilizing a competitive sealed proposal (CSP). Construction is currently underway and is anticipated to be complete January 2018. All four electrical shutdowns have been completed. Testing and Balancing is currently underway and is anticipated to be complete in January 2018. Any remaining punch list items are anticipated to be complete in February 2018.

Project Budget				
Approved Budget	\$ 3,000,000	Expensed \$	2,756,322	
		Encumbered \$	240,663	
		Remaining Balance \$	3,015	

	Solicitation/Type of	Solicitation/Type of			
	Contract	Selected Firm	HUB Participation		
Architect	RFQ	FAI Engineers	5.00%		
Contractor	CSP	DMI	28.00%		
Contractor	-	-	-		
Contractor	-	-	-		

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	92%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Pla	nning/Programming Complete	-	-	-	-
	Design Complete	Mar-15	-	-	Apr-15
Constr	uction Substantial Completion	Apr-16	Jan-18	Jan-18	-
	Construction End	Apr-16	Feb-18	Feb-18	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# **Approved FY 2016 CIP Projects**

# 16-1.20 College of Visual Arts and Design

#### **Current Project Status**

Construction activities continue. The concrete structure for the new facility is anticipated to be complete January 2018. Exterior building envelope, interior wall layout, and mechanical ductwork install have begun. Construction continues to be on schedule. Furniture, fixtures, and equipment items are in the bidding process with installation scheduled for June 2018. In preparation for summer 2018 moves, regular move coordination meetings have commenced.

Project Budget		
Approved Budget	\$ 70,000,000	<b>Expensed</b> \$ 17,475,126
		<b>Encumbered</b> \$ 41,778,490
		Remaining Balance \$ 10,746,384

# **Major Project Contract Information**

	Solicitation/Type of	of	
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Corgan	24.55%
Contractor	CMAR	<b>Hunt Construction Group</b>	2.17%
Contractor	-	-	-
Contractor	_	_	_

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	35%	Original CIP Schedule	<b>Previously Reported</b>	Current Projected	Actual
Р	lanning/Programming Complete	Dec-15	-	-	Jul-16
	Design Complete	Dec-16	Jun-17	-	Jun-17
Cons	truction Substantial Completion	Jun-18	Dec-18	Dec-18	-
	Construction End	Jul-18	Jan-19	Jan-19	-

#### 16-1.84a New Residence Hall - Phase 1

Burtan Caland I

#### **Current Project Status**

100% Construction Documents were issued August 2017. Notice to proceed (NTP) for construction was issued to the contractor on October 31, 2017. On-site construction activity started mid-November 2017.

Project Budget			
Approved Budget	\$ 58,900,000	Expensed	\$ 4,396,425
		Encumbered	\$ 48,711,311
		Remaining Balance	\$ 5,792,264

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Jacobs Engineering	13.09%
Contractor	CMAR	JT Vaughn	1.00%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	5%	Original CIP Schedule	<b>Previously Reported</b>	Current Projected	Actual
I	Planning/Programming Complete	May-16	-	-	Jan-17
	Design Complete	Feb-17	Sep-17	-	Sep-17
Con	struction Substantial Completion	May-18	Feb-19	Feb-19	-
	Construction End	Jun-18	Mar-19	Mar-19	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



#### 16-1.84b New Residence Hall - Phase 2

#### **Current Project Status**

With the completion of the housing master plan, it has been determined by campus administration that a second residence hall is not necessary at this time to fulfill demand. As a result, an amendment to the project budget is being requested for approval by the Board of Regents at the February 2018 meeting.

**Project Budget** 

**Approved Budget** \$ 43.700.000 Expensed \$

Encumbered \$ 43,700,000 Remaining Balance \$

**Major Project Contract Information** 

Solicitation/Type of

	Contract	Selected Firm	HUB Participation		
Architect	RFQ	TBD	-		
Contractor	CMAR	TBD	-		
Contractor	-	-	-		
Contractor	-	-	-		

**Project Schedule** 

**Project Phase: Planning** 

Phase % Co

Complete:	0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
	Planning/Programming Complete	Jun-16	Jun-20	Jun-20	-
	Design Complete	Jun-17	Jun-21	Jun-21	-
Co	onstruction Substantial Completion	May-19	May-22	May-22	-
	Construction End	Jun-19	Jun-22	Jun-22	-

#### 16-2.25 General Academic Building MEP and Interior Renovation\*

# **Current Project Status**

The execution of the Professional Service Agreement is underway. The delay in issuance of the Professional Service Agreement has affected the design start and the overall projected schedule. The design is tentatively scheduled to begin January 2018.

**Project Budget** 

**Approved Budget** 10,350,000

Expensed \$ Encumbered \$ 623,041

Remaining Balance \$ 9,726,959

Jun-20

**Major Project Contract Information** 

Solicitation/Type of

Construction End

	Solicitation, Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Baird Hampton Brown	=
Contractor	-	-	=
Contractor	-	-	-
Contractor	-	<u>-</u>	-

**Project Schedule** 

**Project Phase:** Design **Original CIP Schedule Previously Reported Current Projected** Phase % Complete: 0% Actual Planning/Programming Complete Dec-15 Dec-15 Design Complete Sep-16 Apr-18 Aug-18 **Construction Substantial Completion** Nov-17 Jan-20 May-20

Feb-20

Dec-17

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 16-2.50 Life Science Lab Exhaust Upgrade\*

#### **Current Project Status**

Estes McClure Associates has been awarded a professional service agreement utilizing an IDIQ contract and design is currently underway. A life safety study was completed on Life Science Building B, which is generating the need for an additional scope to this project. As a result, an amendment to the project budget is being requested for approval by the Board of Regents at the February 2018 meeting. The project schedule has been adjusted to accommodate the additional scope. Design has begun on the initial scope.

**Project Budget** 

Approved Budget \$ 3,200,000

Expensed \$

Encumbered \$ 190,750

Remaining Balance \$ 3,009,250

#### **Major Project Contract Information**

	Solicitation/Type o	f	
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	Estes McClure Associates	=
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

**Project Schedule** 

Project Phase: Design

Phase % Complete: 5%

t <b>e</b> : 5%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete	Dec-15	-	-	Jan-16
Design Complete	Sep-16	Jan-18	May-18	-
Construction Substantial Completion	Nov-17	Aug-18	Dec-19	-
Construction End	Dec-17	Nov-18	Jan-20	-

# 16-2.55 Discovery Park MEP Upgrade\*

#### **Current Project Status**

The Professional Service negotiations are complete with the execution of the contract anticipated by the end of January 2018. The facilities audit is anticipated to start Spring 2018 with projected design completion Winter 2018.

**Project Budget** 

Approved Budget \$ 20,600,000

Expensed \$
Encumbered \$

Remaining Balance \$ 20,600,000

**Major Project Contract Information** 

Solicitation/Type of

Design

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Siemens	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule Project Phase:

Phase % Complete:	0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
	Planning/Programming Complete	Dec-15	-	-	Dec-16
	Design Complete	Sep-16	Dec-18	Dec-18	-
Co	nstruction Substantial Completion	Jul-18	Nov-20	Nov-20	-
	Construction End	Aug-18	Dec-20	Dec-20	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 16-2.65 Sycamore Hall 2nd Floor Renovation\*

#### **Current Project Status**

Mayborn School of Journalism has relocated to Sycamore Hall and move-in was completed June 2017. Substantial completion of the remaining area is anticipated to be complete in December 2017. The Department of Sociology is scheduled to move into the space January 9, 2018, marking the completion of the project.

<b>Project Budget</b>				
Approved Budget	\$ 3,950,000	Expensed	\$ 3,363,513	
		Encumbered :	\$ 397,542	
		Remaining Balance	\$ 188,945	

# **Major Project Contract Information**

# Solicitation/Type of

	Contract	Selected Firm	HUB Participation		
Architect	IDIQ	FKP	15.00%		
Contractor	State Contract	JT Vaughn	39.00%		
Contractor	-	-	-		
Contractor	-	-	-		

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	90%	Original CIP Schedule	<b>Previously Reported</b>	Current Projected	Actual
	Planning/Programming Complete	Oct-15	-	<del>-</del>	Feb-16
	Design Complete	Aug-16	-	-	Aug-16
Co	nstruction Substantial Completion	Aug-17	Dec-17	-	Dec-17
	Construction End	Sep-17	Jan-18	Jan-18	-

#### 16-2.66 Coliseum Concourse Renovation

#### **Current Project Status**

Construction continues both in the interior concourse as well as the exterior additions. The next milestone will be the completion of the East addition. Once completed in March, the Coliseum staff and Basketball coaches and staff will be relocated to the addition. The remaining areas in the addition are anticipated to be substantially complete in May 2018, prior to commencement ceremonies.

Project Budget				
Approved Budget	\$ 8,000,000	Expensed	\$ 2,871,315	
		Encumbered	\$ 4,616,403	
		Remaining Balance	\$ 512,282	

olicitatio	n/Tvne	οf

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Elements of Architecture	74.00%
Contractor	CMAR	Construction Zone	19.00%
Contractor	-	-	-
Contractor	-	-	-

Proi	iect	Sch	iedu	le
	CCC	30.	ıcuu	

Project Phase:	Construction
Phase % Complete:	50%

% Complete:	50%	Original CIP Schedule	Previously Reported	Current Projected	Actual	
	Planning/Programming Complete	Dec-15	-	=	Dec-15	
	Design Complete	Oct-16	-	=	Apr-17	
Co	onstruction Substantial Completion	Aug-17	May-18	May-18	-	
	Construction End	Sen-17	lun-18	lun-18	_	

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



#### 16-2.67 1500 I-35E Building

#### **Current Project Status**

As of November 2017, the design of the project has resumed with different occupants identified for the facility. UNT System will be managing the design and construction of the building envelope, core necessities and required infrastructure to the facility, which is currently 60% complete. An early release package was issued in December 2017 for roof replacement and long lead mechanical items. The Guaranteed Maximum Price is expected in February 2018. Once a revised programming of space has been established, UNT facilities will manage the interior design, tenant finish out, parking lot upgrade and construction. Corgan will be contracted for the interior design utilizing the IDIQ Professional Services Agreement. In-house Programming has begun based on the identified tenants and will run concurrent to the interior design phase.

Pro		

 Approved Budget
 \$ 12,500,000
 Expensed
 \$ 630,759

 Encumbered
 \$ 374,634

 Remaining Balance
 \$ 11,494,607

#### **Major Project Contract Information**

Solicitation/Type o	f
---------------------	---

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	Sole Source	Corgan	14.00%
Contractor	CMAR	Pogue Construction	-
Contractor	-	-	-
Contractor	-	-	-

#### **Project Schedule**

Project Phase: Design

Phase % Complete: 60% **Original CIP Schedule Previously Reported Current Projected** Actual Planning/Programming Complete Feb-16 Oct-16 Design Complete Nov-16 TBD Jun-18 **Construction Substantial Completion** Aug-17 TRD Dec-18 Construction End Sep-17 **TBD** Jan-19

#### 16-2.77 Wooten Hall Code Upgrade\*

#### **Current Project Status**

Design was completed in November 2017. The Request for Proposal (RFP) package is anticipated to be posted soon, with the contract execution anticipated in April 2018. Construction is anticipated to begin May 2018 and substantial completion in December 2018. As a result, an amendment to the project budget is being requested for approval by the Board of Regents at the February 2018 meeting.

_		_	
Drni	iort	Ru	dget
	CCL	ьu	uget

 Approved Budget
 \$ 4,230,000
 Expensed
 \$ 112,132

 Encumbered
 \$ 23,855

Remaining Balance \$ 4,094,013

#### **Major Project Contract Information**

licitation	/Type	of
mulalion	/ I V DE	v.

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	HDR	-
Contractor	CSP	-	-
Contractor	-	-	-
Contractor	-	-	-

# **Project Schedule**

Project Phase: Design

Phase % Complete:	100%	Original CIP Schedule	Previously Reported	Current Projected	Actual	
	Planning/Programming Complete	Feb-16	=	=	Dec-16	Ī
	Design Complete	Aug-16	Oct-17	-	Nov-17	
Cor	nstruction Substantial Completion	Oct-17	Nov-18	Nov-18	-	
	Construction End	Nov-17	Dec-18	Dec-18	-	

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 16-2.82 Track and Field Stadium

# **Current Project Status**

Construction is underway. Underground utilities and electrical are being installed. Soil moisture conditioning for the track and soccer field is nearly complete. Piers and grade beams have been poured for the field house. The project is on schedule for substantial completion in July 2018.

<b>Project Budget</b>			
Approved Budget	\$ 13,590,000	Expensed \$	1,750,086
		Encumbered \$	10,439,499
		Remaining Balance \$	1,400,415

# **Major Project Contract Information**

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	BRW Architects	9.00%
Contractor	CSP	Pogue Construction	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	30%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Pla	nning/Programming Complete	-	-	-	-
	Design Complete	Sep-16	-	-	Jun-17
Constr	ruction Substantial Completion	Sep-17	Jul-18	Jul-18	-
	Construction End	Sep-17	Aug-18	Aug-18	-

#### 16-2.85 Sage Hall Academic Success Center\*

#### **Current Project Status**

The project construction is currently 65% complete. Changes to specifications for lighting fixtures and controls in support of campus -wide sustainability efforts have impacted the schedule. As a result, the selected fixtures and controls were long lead-time items affecting the completion of construction. Anticipated substantial completion is now March 2018.

<b>Project Budget</b>			
Approved Budget	\$ 1,850,000	Expensed	\$ 824,509
		Encumbered	\$ 801,680
		Remaining Balance	\$ 223,811

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Corgan	10.04%
Contractor	Co-Op	JT Vaughn	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	65%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Plan	nning/Programming Complete	-	-	-	-
	Design Complete	Mar-16	-		Apr-17
Constru	action Substantial Completion	Dec-17	Jan-18	Mar-18	-
	Construction End	Dec-17	Feb-18	Apr-18	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



Actual

# **Approved FY 2017 CIP Projects**

# 17-01-0001 Terrill Hall MEP & Interior Renovation\*

#### **Current Project Status**

Request for Qualification (RFQ) for the mechanical, electrical, and plumbing design services scope has been posted with qualifications to be received in February 2018. The delay in the posting of the RFQ has affected the design schedule.

**Project Budget** 

Approved Budget \$ 7,300,000 Expensed \$ Encumbered \$

Remaining Balance \$ 7,300,000

**Major Project Contract Information** 

Solicitation/Type of

	Contract	Selected Firm	<b>HUB Participation</b>	
Architect	RFQ	-	-	
Contractor	-	-	-	
Contractor	-	-	-	
Contractor	-	-	-	

**Project Schedule** 

Project Phase: Programming

Phase % Complete: 75% Original CIP Schedule Previously Reported Current Projected

 Planning/Programming Complete

# 17-01-0002 Coliseum MEP Renovation\*

# **Current Project Status**

The funding for this project was adjusted in August 2017 to begin in FY 19. However, the project schedule was not modified at that time. As a result, the schedule has now been aligned to reflect the adjusted funding.

**Project Budget** 

Approved Budget \$ 10,400,000 Expensed \$ Encumbered \$ -

Remaining Balance \$ 10,400,000

**Major Project Contract Information** 

Solicitation/Type of

_	Contract	Selected Firm	HUB Participation
Architect	RFQ	M.E. Group, Inc	-
Contractor	-	-	-
Contractor	-	=	-
Contractor	-	-	-

**Project Schedule** 

Project Phase: Design

Phase % Complete: 0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete	-	-	-	-
Design Complete	Sep-17	Jul-18	Nov-19	-
Construction Substantial Completion	May-19	Dec-19	Feb-21	-
Construction End	Jun-19	Jan-20	Mar-21	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 17-01-0003 Kerr Hall MEP & Interior Renovation\*

#### **Current Project Status**

The project to replace mechanical equipment is on-going. Current work underway includes replacement of air handler and domestic boilers. Work in progress during the winter break included: demolition and replacement of the basement air handler that services the first floor, boiler room air handler was hung and permanently piped in, and boiler room pipes were insulated and demolition began on the last remaining boiler. Phase II design work has been reevaluated. The second phase of the project will be replacing and updating equipment. SSR previously contracted through the IDIQ service, will not be utilized, and instead, the remaining MEP work to be contracted will utilize Co-op Purchasing Contracts. Proposals are being generated by the department to align with CIP approved scope and scheduling needs. Anticipated construction completion is currently on schedule.

#### **Project Budget**

Approved Budget \$ 5,790,000 Expensed \$

Encumbered \$ 9,550
Remaining Balance \$ 3,000,210

2,780,240

Jan-19

#### **Major Project Contract Information**

licitation	/Tvpe	of

**Construction End** 

	Solicitation, Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	SSR	-
Contractor	State Contract	Live Systems	-
Contractor	State Contract	Entech	-
Contractor	-	-	-

# **Project Schedule**

Project Phase:	Construction				
Phase % Complete:	47%	Original CIP Schedule	<b>Previously Reported</b>	Current Projected	Actual
	Planning/Programming Complete	-	-	-	-
	Design Complete	Dec-16	-	-	Dec-16
Co	onstruction Substantial Completion	Aug-18	Dec-18	Dec-18	-

Jan-19

Aug-18

# 17-01-0004 USB MEP Renovation\*

#### **Current Project Status**

The Request for Qualification (RFQ) was posted September 14, 2017, and the qualifications were opened on October 12, 2017. M.E. Group Inc. has been selected and contract negotiations are underway. It is anticipated that design will begin in February 2018 and complete August 2018. The project schedule has been altered to address previous delays in the issuing of the RFQ which has affected the execution of the design contract and issuance of a design services agreement.

n	:+	n		
rro	iect	вu	dget	

Approved Budget \$ 3,600,000 Expensed \$ Encumbered \$ -

Remaining Balance \$ 3,600,000

#### **Major Project Contract Information**

# Solicitation/Type of

	Jonatation, Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	M.E. Group, Inc	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

P	ro	ject	t Sc	hed	lule	

Project Phase:	Design				
Phase % Complete:	0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
	Planning/Programming Complete	-	-	-	=
	Design Complete	Aug-17	Mar-18	Aug-18	-
Cor	nstruction Substantial Completion	Dec-18	Mar-19	Oct-19	-
	Construction End	Dec-18	Apr-19	Nov-19	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 17-01-0005 Discovery Park Bio-Medical Engineering Addition

#### **Current Project Status**

Design Development is now complete. Construction Documentation is in progress and is anticipated to be completed in March 2018.

roject	Budg	et
--------	------	----

 Approved Budget
 \$ 17,400,000
 Expensed
 \$ 489,672

Encumbered \$ 835,961
Remaining Balance \$ 16,074,367

# **Major Project Contract Information**

#### Solicitation/Type of

	Contract	Selected Firm	HUB Participation	
Architect	RFQ	TreanorHL	7.00%	
Contractor	CMAR	Sundt Construction	-	
Contractor	-	-	-	
Contractor	-	-	-	

# **Project Schedule**

Project Phase: Design
Phase % Complete: 75%

ase % Complete:	75%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Mar-17	-	-	Jul-17
	Design Complete	May-18	May-18	Mar-18	-
Co	onstruction Substantial Completion	May-19	May-19	May-19	-
	Construction End	Jun-19	Jun-19	Jun-19	-

# 17-01-0006 Sage Hall Academic Success Center Phase II\*

#### **Current Project Status**

This project will renovate the third floor to facilitate the Student Academic Success Center. Design services were completed in November 2017 utilizing an IDIQ contract. The general contractor, JT Vaughn, has been selected utilizing a co-op contract to meet the project deadline. Procurement is underway and construction is anticipated to begin in March 2018 with substantial completion August 2018.

#### **Project Budget**

Approved Budget \$ 2,920,000

Expensed \$ 35,582
Encumbered \$ 143,381
Remaining Balance \$ 2,741,037

# **Major Project Contract Information**

# Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Corgan	-
Contractor	Co-Op	JT Vaughn	17.11%
Contractor	-	-	-
Contractor	-	-	-

#### **Project Schedule**

Project Phase: Design Phase % Complete: 100%

omplete:	100%	Original CIP Schedule	Previously Reported	<b>Current Projected</b>	Actual
	Planning/Programming Complete	Jul-17	-	-	Apr-17
	Design Complete	Dec-17	Nov-17	-	Nov-17
Co	onstruction Substantial Completion	Aug-18	Jul-18	Jul-18	-
	Construction End	Aug-18	Aug-18	Aug-18	_

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 17-01-0007 Life Science Building 4th Floor Laboratories Renovation\*

#### **Current Project Status**

The project schedule remains extended to allow for scope refinement & additional moves that will be necessary to complete the project.

**Project Budget** 

Approved Budget \$ 7,000,000 Expensed \$ Encumbered \$ -

Remaining Balance \$ 7,000,000

**Major Project Contract Information** 

.,,	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	-	-	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

**Project Schedule** 

Project Phase:	Planning				
Phase % Complete:	5%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Pla	nning/Programming Complete	Jan-17	Jan-20	Jan-20	-
	Design Complete	Sep-17	Jun-20	Jun-20	-
Constr	uction Substantial Completion	Jul-18	Jul-21	Jul-21	-
	Construction End	Aug-18	Aug-21	Aug-21	_

# 17-01-0008 Coliseum Roof Replacement\*

#### **Current Project Status**

This project will replace the Coliseum roof and metal parapet surrounding the facility. The project schedule was modified in November 2017 to consider the procurement method to be used which is currently being finalized. The project construction schedule will need to be reevaluated after the procurement method is finalized and building occupant schedules can be reviewed.

		_		
Pro	iect	Bu	d	get

Approved Budget \$ 2,430,000 Expensed \$ Encumbered \$ -

Remaining Balance \$ 2,430,000

Dec-18

# **Major Project Contract Information**

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	-	-	-
Contractor	-	-	-

Contractor - - - - - Contractor - - - - - -

**Construction End** 

Project Schedule	
------------------	--

Project Phase:	Design				
Phase % Complete	: 0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Jan-17	=	=	Jan-17
	Design Complete	Jul-17	Mar-18	Mar-18	-
(	Construction Substantial Completion	May-18	Dec-18	Dec-18	-

Dec-18

May-18

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



17-01-0009 Off-

Off-Site Campus #2\*

**Current Project Status** 

Consideration of sites and requirements are currently underway with UNT staff. This project has been placed on hold at the present time.

**Project Budget** 

Approved Budget \$ 1,500,000 Expensed \$

Encumbered \$ -

Remaining Balance \$ 1,500,000

**Major Project Contract Information** 

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	=	-	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

**Project Schedule** 

Project Phase: Planning

Phase % Complete: 0%

	9				
ete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Jan-17	TBD	TBD	-
	Design Complete	Aug-17	TBD	TBD	-
Co	nstruction Substantial Completion	Jul-18	TBD	TBD	-
	Construction End	Aug-18	TBD	TBD	-

# 17-01-0010 New Classroom Building

**Current Project Status** 

Response to the Request for Qualifications (RFQ) for programming and design services have been evaluated with TreanorHL selected as the most qualified candidate. Contract negotiations are underway with programming anticipated to begin in February 2018.

**Project Budget** 

Approved Budget \$ 25,100,000 Expensed \$ -

Encumbered \$ -

Remaining Balance \$ 25,100,000

**Major Project Contract Information** 

Solicitation/Type of

	Jonicitation, Type of	Solicitation, Type of		
	Contract	Selected Firm	<b>HUB Participation</b>	
Architect	RFQ	TreanorHL	-	
Contractor	-	-	-	
Contractor	-	-	-	
Contractor	-	<u>-</u>	-	

**Project Schedule** 

Project Phase: Planning

Phase % Complete: 0% **Original CIP Schedule Previously Reported Current Projected Actual** Planning/Programming Complete Apr-17 May-18 May-18 Design Complete Apr-18 May-19 May-19 **Construction Substantial Completion** Jul-19 Jul-20 Jul-20 **Construction End** Aug-19 Sep-20 Sep-20

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 17-01-0011 Hickory Hall Renovation

#### **Current Project Status**

Planning is currently underway with the campus. A portion of the space in Hickory Hall is occupied by the College of Visual Arts and Design (CVAD) and is expected to relocate into the new CVAD building. As a result, the construction phase cannot begin until the CVAD project is complete.

**Project Budget** 

Approved Budget \$ 8,800,000 Expensed \$

Encumbered \$ -

Remaining Balance \$ 8,800,000

# **Major Project Contract Information**

	Solicitation/Type of			
	Contract	Selected Firm	<b>HUB Participation</b>	
Architect	-	-	-	
Contractor	-	-	-	
Contractor	-	-	-	

**Project Schedule** 

Contractor

**Project Phase: Planning** Phase % Complete: 20% **Original CIP Schedule Previously Reported Current Projected** Actual Planning/Programming Complete Feb-17 May-18 May-18 Design Complete Jan-18 Mar-19 Mar-19 **Construction Substantial Completion** Jul-19 Mar-20 Mar-20 **Construction End** Aug-19 Apr-20 Apr-20

#### 17-01-0012 Eagle Point Parking Lot #80\*

# **Current Project Status**

Design was completed in October 2017. In order to maintain the required construction schedule, procurement was modified from competitive sealed proposal (CSP) to a co-op contract. The selected contractor, JT Vaughn, is now in the process of providing a proposal.

**Project Budget** 

 Approved Budget
 \$ 2,200,000
 Expensed
 \$ 78,786

 Encumbered
 \$ 24,934

Remaining Balance \$ 24,934 2,096,280

	Solicitation/Type of			
	Contract	Selected Firm	HUB Participation	
Architect	IDIQ	Smith GroupJJR	19.08%	
Contractor	Co-Op	JT Vaughn	=	
Contractor	-	-	=	
Contractor	-	-	-	

Project Schedule					
Project Phase:	Design				
Phase % Complete:	100%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
	Planning/Programming Complete	May-17	-	-	May-17
	Design Complete	Jul-17	Oct-17	-	Dec-17
Co	onstruction Substantial Completion	Dec-17	Aug-18	Aug-18	-
	Construction End	Dec-17	Sep-18	Sep-18	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# **Approved FY 2018 CIP Projects**

# 18-01-0001 Maple Hall MEP & Renovation\*

#### **Current Project Status**

UNT Campus in-house resources have completed the programming scope which includes installation of a fire suppression system, upgrades to the fire alarm, replacement of electrical switchgear, dining vestibule HVAC, cooling tower renovations, and enclosing the fire suppression equipment. The project initially was to be procured via Request for Competitive Sealed Proposal (RFCSP); however, due to the timeline of the project and the need to complete construction between the months of May and August of 2018, portions of this project will be procured utilizing a co-operative agreement. The fire suppression system will be addressed separately through design-build RFP that will be posted in late January 2018.

**Project Budget** 

 Approved Budget
 \$ 4,380,000
 Expensed
 \$ 

 Encumbered
 \$

Remaining Balance \$ 4,380,000

#### **Major Project Contract Information**

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	-	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	<del>-</del>	-

**Project Schedule** 

Project Phase: Design

Phase % Complete: 0%

te: 0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete	-	-	-	-
Design Complete	Dec-17	Mar-18	Mar-18	-
<b>Construction Substantial Completion</b>	Aug-18	Aug-18	Aug-18	-
Construction End	Sep-18	Sep-18	Sep-18	-
Construction End	Sep-18	Sep-18	Sep-18	-

# 18-01-0002 Clark Hall Lobby Renovation\*

#### **Current Project Status**

Initial in-house programming began September 2017 and is anticipated to be complete May 2018. TreanorHL has been selected to provide the design services via an IDIQ contract proposal and negotiations are underway.

**Project Budget** 

Approved Budget \$ 2,270,000 Expensed \$ Encumbered \$

Remaining Balance \$ 2,270,000

**Major Project Contract Information** 

Solicitation/Type of

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	TreanorHL	-
Contractor	-	-	-
Contractor	=	-	-
Contractor	-	-	-

**Project Schedule** 

Project Phase: Programming

Phase % Complete: 5% **Original CIP Schedule Previously Reported Current Projected** Actual Planning/Programming Complete Nov-17 May-18 May-18 **Design Complete** Mar-18 Aug-18 Aug-18 **Construction Substantial Completion** Aug-18 Aug-19 Aug-19 Construction End Sep-18 Sep-19 Sep-19

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 18-01-0003 Sage Hall Academic Success Center Phase III\*

#### **Current Project Status**

The scope of this project is the renovation of the second floor of Sage Hall in support of the Academic Success Center. Corgan has been selected via an IDIQ contract to provide design services. Construction completion has been delayed due to coordination of client schedules and dependency of construction completion of other Sage hall projects. Execution of the professional service agreement is currently underway.

Project Budget

Approved Budget \$ 3,010,000 Expensed \$

Encumbered \$ Remaining Balance \$ 3,010,000

**Major Project Contract Information** 

Solicitation/Type of

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	Corgan	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

**Project Schedule** 

Project Phase: Planning

Phase % Complete: 0%

ete: 0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete	Apr-18	Apr-18	Apr-18	-
Design Complete	Aug-18	Aug-18	Aug-18	-
<b>Construction Substantial Completion</b>	Jan-19	Jan-19	Apr-19	-
Construction End	Feb-19	Feb-19	May-19	-
			- / -	

# 18-01-0004 Art Building Roof Replacement

#### **Current Project Status**

Design is currently underway and is anticipated to be complete by January 2018. The construction will be coordinated with construction activity for the new College of Visual Arts & Design Building.

**Project Budget** 

Encumbered \$ 30,630 Remaining Balance \$ 1,319,370

Dec-18

**Major Project Contract Information** 

Solicitation/Type of

Construction End

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	Terracon	-
Contractor	=	-	-
Contractor	=	-	-
Contractor	-	-	-

**Project Schedule** 

**Project Phase:** Design Phase % Complete: 100% **Original CIP Schedule Previously Reported Current Projected** Actual Planning/Programming Complete Dec-17 Design Complete Sep-17 Jan-18 **Construction Substantial Completion** Aug-18 Nov-18 Nov-18

Dec-18

Sep-18

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 18-01-0005 Discovery Park Utility Capacity Upgrade\*

#### **Current Project Status**

Phase 1 includes purchasing and installing a new chiller in May 2018. Phase 2 includes design and contracting to provide minimum required electrical service to the location of new Biomedical Engineering Addition, as dictated by the Biomedical Addition Construction Schedule. Phase 3 includes additional electrical infrastructure upgrades at Discovery Park that have no energy savings impact and will be completed by May 2019. The planning process is complete, with Design now underway.

Proi		D4	~~+
PIU	ect	Duu	zei

Approved Budget \$ 2,000,000

Expensed \$

Encumbered \$

1,477,683

Remaining Balance \$

522,317

# **Major Project Contract Information**

Solicitation/Type o	f
---------------------	---

_	Contract	Selected Firm	<b>HUB Participation</b>
Architect	IDIQ	Campos Engineering	-
Contractor	Co-Op	Brandt Companies, LLC	-
Contractor	-	-	-
Contractor	-	-	-

#### **Project Schedule**

Project Phase: Design

Phase % Complete: 50%

ete:	50%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	-	Sep-17	-	Oct-17
	Design Complete	Feb-18	Dec-17	Jan-18	-
Co	nstruction Substantial Completion	May-19	May-19	May-19	-
	Construction End	Jun-19	Jun-19	Jun-19	-

# 18-01-0006 Music Building Courtyard Renovation\*

#### **Current Project Status**

Planning for this project has been completed along with conceptual renderings for fundraising purposes. Until donation funding is obtained or the scope of the project is reduced, this project will remain on hold.

# **Project Budget**

Approved Budget \$ 2,590,000

Expensed \$

Encumbered \$
Remaining Balance \$

2,590,000

# **Major Project Contract Information**

Soli	icita	atio	n/T	vne	οf

	Jonicitation, Type of	Solicitation, Type of		
	Contract	Selected Firm	<b>HUB Participation</b>	
Architect	IDIQ	GSBS Architects	=	
Contractor	-	-	=	
Contractor	-	-	-	
Contractor	<del>-</del>	<del>-</del>	<del>-</del>	

#### **Project Schedule**

Project	Phase:	Planning					
Phase %	Complete:	100%	Original CIP Schedule	<b>Previously Reported</b>	Current Projected	Actual	
	Pla	nning/Programming Complete	Jun-17	-	=	Jun-17	
		Design Complete	Dec-17	TBD	TBD	-	
	Const	ruction Substantial Completion	Jan-19	TBD	TBD	-	
		Construction End	Feb-19	TBD	TBD	-	

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 18-01-0007 New Dining Hall

#### **Current Project Status**

The dining Hall program was completed in November 2017. A contract for design services was executed with design beginning in November 2017. Construction Manager at Risk (CMAR) selection is underway with the anticipation of the execution of the contract occurring in January 2018.

Project Budget		
Approved Budget	\$ 25,470,000	Expensed \$

Encumbered \$ 1,878,712

Remaining Balance \$ 23,395,912

195,376

# **Major Project Contract Information**

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Kirksey Architects	25.80%
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	15%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
P	Planning/Programming Complete	Sep-17	Sep-18	-	Nov-17
	Design Complete	Oct-18	Oct-18	Oct-18	-
Cons	struction Substantial Completion	Dec-19	Dec-19	Dec-19	-
	Construction End	Jan-20	Jan-20	Jan-20	-

# 18-01-0008 Fouts Field Demolition, Parking, and Bus Transfer Station

#### **Current Project Status**

Huitt Zollars has been selected and a contract has been executed for design services. Design work has begun and is currently on track to be completed by August 2018. Once design is complete, a proposal for construction will be solicited via a competitive sealed proposal.

Project Budget			
Approved Budget	\$ 14,000,000	Expensed \$	-
		Encumbered \$	890,106
		Remaining Ralance S	13 109 894

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Huitt-Zollars	=
Contractor	CSP	TBD	-
Contractor	-	=	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	10%	Original CIP Schedule	<b>Previously Reported</b>	Current Projected	Actual
Planning/Programming Complete		=	-	-	-
	Design Complete	Aug-18	Aug-18	Aug-18	-
<b>Construction Substantial Completion</b>		Nov-18	Aug-19	Aug-19	-
	Construction End	Dec-18	Sep-19	Sep-19	-

University of North Texas Campus February 2018 (Reported as of December 20, 2017)



# 18-01-0009 New Athletics Indoor Practice Facility

#### **Current Project Status**

The Indoor Practice Facility programming phase was completed in October 2017. Design of the facility began in December 2017 and is anticipated to be complete June 2018. Once Design is complete, the project will be bid for construction via Competitive Sealed Proposal (CSP). It is anticipated that construction will begin August 2018.

Project Budget			
Approved Budget	\$ 18,900,000	Expensed	\$ -
		Encumbered	\$ -
		Remaining Balance	\$ 18,900,000

# **Major Project Contract Information**

	Solicitation/Type of	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>	
Architect	RFQ	Heery Architects	-	
Contractor	-	-	-	
Contractor	-	-	-	
Contractor	-	<del>-</del>	<del>-</del>	

Project Schedule					
Project Phase:	Design				
Phase % Complete:	0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
1	Planning/Programming Complete	Oct-17	-	-	Oct-17
	Design Complete	Jun-18	-	Jun-18	-
Con	struction Substantial Completion	Jun-19	-	Jul-19	-
	Construction End	Jul-19	-	Jul-19	-

# **Details of Other Minor Projects**

There are an additional \$8.68M allocated for minor projects including fire alarm upgrades within various facilities, energy management control upgrades within various facilities, elevator modernization within various facilities, energy efficiency upgrades to mechanical/ electrical equipment within various facilities, and academic space upgrades within various facilities. None of these projects will be executed with a single contract value in excess of \$1M or more.



University of North Texas Dallas Campus
February 2018
(Reported as of December 20, 2017)

# **Approved FY 2016 CIP Projects**

# 16-1.01 Student Learning and Success Center

# **Current Project Status**

The Guaranteed Maximum Price has been executed with the contractor. Construction is approximately 25% complete and is on schedule for completion in March 2019.

<b>Project Budget</b>			
<b>Approved Budget</b>	\$ 63,000,000	Expensed	\$ 6,655,173
		Encumbered	\$ 46,664,972
		Remaining Balance	\$ 9,679,855

Major Project Cor	ntract Information		
	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Moody Nolan	19.84%
Contractor	CMAR	<b>Austin Commercial</b>	1.70%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	25%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete		Jan-15	-	-	Jul-16
	Design Complete	Dec-16	-	-	Jun-17
Construction	<b>Substantial Completion</b>	Jun-19	Mar-19	Mar-19	-
	Construction End	Jul-19	May-19	May-19	-

<sup>\*</sup>Project managed and reported by the campus.



University of North Texas Health Science Center Campus February 2018 (Reported as of December 20, 2017)

# **Approved FY 2016 CIP Projects**

#### 16-1.40 **Interdisciplinary Research** Building

#### **Current Project Status**

Construction of the building is underway. The concrete superstructure is complete. Installation of precast panels is complete. Curtain wall and glazing are underway. Window chamber testing is in progress. Demolition of the existing chemical storage building is complete. Grading of the pedestrian spine from the Gibson D. Lewis Health Science Library to Clifton St. is in progress. Construction is on schedule for the building to be dried-in in January 2018. The tower crane is on schedule for removal in February 2018. The animal facility mechanical, electrical, and plumbing infrastructure is well underway. The project is on schedule to meet the substantial completion date of November 2018. Owner occupancy and final completion are scheduled for December 2018.

#### **Project Budget**

Expensed \$ **Approved Budget** \$ 118,500,000 58,992,167 Encumbered \$ 46,386,046 Remaining Balance \$ 13,121,787

#### **Major Project Contract Information**

Cal	licita	+:~~	/Type	. ~ £
30	IILILA	LIUII	/ I VDE	· UI

	• ••		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	TreanorHL	33.77%
Contractor	CMAR	JT Vaughn	9.59%
Contractor	=	-	=
Contractor	=	-	-

#### **Project Schedule**

Drainet Bhaca

Project Phase:	Construction					
Phase % Complete:	42%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual	
Planning/	Programming Complete	Jul-15	-	-	Oct-15	
	Design Complete	Aug-16	-	-	Oct-16	
Construction	<b>Substantial Completion</b>	Dec-18	Nov-18	Nov-18	-	
	Construction End	Dec-18	Dec-18	Dec-18	-	

#### Research and Education (RES) Level 4 16-2.96

# **Current Project Status**

This project is delayed until FY 19 until the IREB opens and departments are moved into the new building. This will allow the renovations to begin.

#### **Project Budget**

\$ **Approved Budget** 4,500,000 Expensed \$ 3,600 Encumbered \$

Remaining Balance \$ 4,496,400

# **Major Project Contract Information**

#### Solicitation/Type of

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	-	-	=
Contractor	-	-	=
Contractor	-	-	=
Contractor	-	-	-

# **Project Schedule**

Project Phase:						
Phase % Complete: 0%		Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual	
Planning/Programmi	ng Complete	Feb-16	Aug-18	TBD	-	
Desi	gn Complete	Apr-16	Mar-19	TBD	=	
Construction Substantia	l Completion	Dec-16	Nov-19	TBD	=	
Cons	struction End	Dec-16	Dec-19	TBD	=	
Cons	struction End	Dec-16	Dec-19	TBD	-	

<sup>\*</sup>Project managed and reported by the campus.



University of North Texas Health Science Center Campus
February 2018
(Reported as of December 20, 2017)

# **Approved FY 2017 CIP Projects**

# 17-03-0001 East Parking Garage Renovation\*

#### **Current Project Status**

Campus pre-planning discussions for this project are continuing. The UNT HSC Built Environment Council has been charged with the verification of the need for the additional parking structure on-campus. It has been determined that additional parking is required. The schedule has been adjusted to allow for the time that has been required for the verification process.

Project Budget			
<b>Approved Budget</b>	\$ 6,000,000	Expensed	\$ -
		Encumbered	\$ -

**Selected Firm** 

Jan-18

Remaining Balance \$ 6,000,000

Nov-18

**HUB Participation** 

Aug-18

# **Major Project Contract Information**

Solicitation/Type of
Contract

 Architect
 -

# **Project Schedule**

Project Phase: Planning				
Phase % Complete: 0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete	=	-	-	-
Design Complete	May-17	Dec-17	Apr-18	-
Construction Substantial Completion	Dec-17	Jul-18	Oct-18	-

# 17-03-0002 Medical Clinic

# **Current Project Status**

This project has been placed on hold at the present time.

Construction End

<b>Project Budget</b>			
<b>Approved Budget</b>	\$ 4,200,000	Expensed \$	-
		Encumbered \$	-
		Remaining Balance \$	4,200,000

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	-	=	-
Contractor	-	=	-
Contractor	-	=	-
Contractor	-	-	-

<b>Project Schedule</b>					
Project Phase:	Planning				
Phase % Complete:	0%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete		Dec-16	TBD	TBD	-
Design Complete		Aug-17	TBD	TBD	-
Construction Substantial Completion		May-18	TBD	TBD	-
	Construction End	Jul-18	TBD	TBD	-

<sup>\*</sup>Project managed and reported by the campus.



University of North Texas Health Science Center Campus
February 2018
(Reported as of December 20, 2017)

# **Approved FY 2018 CIP Projects**

# 18-03-0001 Gross Anatomy Laboratory Renovation\*

#### **Current Project Status**

The design of the mechanical, electrical and plumbing elements of the project will be executed utilizing Shaw Smith Associates under a proprietary justification due to previous RES experience and knowledge. The remaining design will be accomplished utilizing HSC staff.

**Project Budget** 

Approved Budget \$ 2,470,000 Expensed \$ Encumbered \$

Remaining Balance \$ 2,470,000

**Major Project Contract Information** 

Solicitation/Type of

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	Sole Source	Shaw Smith Associates	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

**Project Schedule** 

**Project Phase:** Design **Original CIP Schedule Current Projected** Phase % Complete: **Previously Reported** Actual Planning/Programming Complete **Design Complete** Mar-18 Mar-18 Mar-18 **Construction Substantial Completion** Jul-18 Jul-18 Jul-18 **Construction End** Aug-18 Aug-18 Aug-18

# 18-03-0002 1408 St. Louis Ave. Renovation\*

# **Current Project Status**

The construction of this project is underway with substantial completion anticipated in January 2018. There was a substantial delay due to the hurricane in Houston delaying Oncor installing power and AT&T delaying install of service.

<b>Project Budget</b>			
Approved Budget	\$ 1,950,000	Expensed	\$ 1,605,061
		Encumbered	\$ 313,009
		Remaining Balance	\$ 31,930

# **Major Project Contract Information**

Solicitation/Type of

	Contract	Selected Firm	<b>HUB Participation</b>
Architect	-	-	-
Contractor	State Contract	JT Vaughn	55.00%
Contractor	-	-	-
Contractor	-	-	-

_					
Pro	iect	Sci	าed	u	e

Project Phase: Construction

i roject i nase.	Construction					
Phase % Complete:	95%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual	
Planning/	Programming Complete	Apr-17	-	-	Apr-17	
	Design Complete	Jun-17	-	-	Jun-17	
Construction	Substantial Completion	Nov-17	Nov-17	Jan-18	-	
	Construction End	Dec-17	Dec-17	Jan-18	-	

<sup>\*</sup>Project managed and reported by the campus.

University of North Texas System February 2018 (Reported as of December 20, 2017)



# **Approved FY 2016 CIP Projects**

# 16-2.01 Renovate Dallas Municipal Building and Associated Law Buildings

#### **Current Project Status**

Structural demolition is ongoing, including the elevator extension excavation for new elevator pit. Installation of underground plumbing is in progress. Major mechanical equipment has been procurred. Project is on-schedule for Substantial Completion in December 2018 and Final Completion in January 2019.

<b>Project Budget</b>				
Approved Budget	\$ 56,000,000	Expensed	\$ 7,461,997	
		Encumbered	\$ 36,340,179	
		Remaining Balance	\$ 12,197,824	

	Solicitation/Type of		
	Contract	Selected Firm	<b>HUB Participation</b>
Architect	RFQ	Stantec	22.69%
Contractor	CMAR	<b>Turner Construction</b>	0.53%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	20%	Original CIP Schedule	<b>Previously Reported</b>	<b>Current Projected</b>	Actual
Planning/Programming Complete		Nov-15	-	-	Jun-16
	Design Complete	Dec-16	Mar-17	-	Apr-17
Construction Substantial Completion		Aug-19	Dec-18	Dec-18	-
	Construction End	Aug-19	Jan-19	Jan-19	-

<sup>\*</sup>Project managed and reported by the campus.

# Information Technology Project Status Report





Portfolio Review	Status	Progress	Start Date	Completion Date
Infrastructure	Status	Flogiess	Date	Date
Data Warehouse (Technical Implementation, Phase 2) COMPLETE		•	4/17/2017	12/22/2017
Data Warehousing Analytics/Dashboards		•	6/1/2015	1/20/2019
Enterprise Hybrid Cloud (EHC) UNT System v4.1 - Phase 2		Ō	8/1/2017	1/31/2019
Enterprise Applications Systems			0/4/2046	2/22/2242
Customer Relationship Management - Marketing Automation (Phase 2)		•	8/1/2016	2/28/2018
E-Forms		0	7/21/2017	3/28/2018
PeopleSoft Enterprise Learning Management 9.2 (ELM) COMPLETE			9/13/2016	11/13/2017
Finance and Administration Systems				
Time and Effort Phase III		•	1/27/2017	4/24/2018
Accounts Receivable & Billing COMPLETE		•	3/31/2017	12/4/2017
DigitalFuel IT Business Management		•	9/1/2017	4/13/2018
Concur Travel, Expense and P-Card		•	9/1/2017	TBD
Student Administration Systems				
Mobile Application Implementation - Phase 2		•	11/1/2016	3/1/2018
Intelligent Capture - Transcript Processing Improvement		•	11/16/2016	1/30/2018
Campus Solutions 9.2 Upgrade		•	12/1/2016	11/30/2018
Visual Schedule Builder Shopping Cart COMPLETE		•	7/15/2017	10/23/2017
Residential Management System		•	3/28/2017	1/31/2018
NetDragon SmartCampus	•	•	8/23/2017	4/6/2018
ServiceNow Applications				
IT Operations (ITOM) Tool Implementation		•	9/13/2017	2/5/2018
Business Services Customer Service Management		0	9/1/2017	TBD
