UNT | SYSTEM

Quarterly Operations Report



May 2018

Quarterly Operations Report - May 2018

Table of Contents

Operating Budget - FY2018 Budget-to-Actual	
Budget-to-Actual Section Divider	Page 3
Executive Summary	Page 4
University of North Texas	Page 8
UNT Health Science Center	Page 12
University of North Texas at Dallas	Page 16
UNT System Administration	Page 20
Investment Performance	_
Investment Performance Section Divider	Page 24
Consolidated UNT System	Page 25
University of North Texas	Page 27
UNT Health Science Center	Page 29
University of North Texas at Dallas	Page 31
UNT System Administration	Page 33
Capital Improvement Plan Status	_
Capital Improvement Plan Status Section Divider	Page 35
Project Budget Status (Revised 5/14/2018)	Page 36
Project Overview (Revised 5/14/2018)	Page 37
Capital Improvement Plan Summary (Revised 5/14/2018)	Page 38
Project Status Detail (Revised 5/14/2018)	Page 44
Information Technology Status Report	_
Information Technology Project Status Report Section Divider	Page 67
Information Technology Project Status Report	Page 68

Budget to Actual





In Millions

FY2018 Q2 Budget to Actuals Executive Summary

University of North Texas

	Q2 FYTD	Q	2 FYTD	Variance % (Q2 Est to		FY18		FY18 earend	Variance % (FY18 Fcst to	Overall
	Estimate	-	Actual	Q2 Actual)	В	udget	Fo	orecast	FY18 Bud)	Tracking
Total Revenues	\$ 584.9	\$	586.3	0.2%	\$	705.0	\$	700.3	-0.7%	
Total Expenses	\$ 339.2	\$	316.5	6.7%	\$	581.2	\$	579.9	0.2%	
Total Transfers	\$ (72.4)	\$	(87.2)	-20.4%	\$	(117.7)	\$	(117.6)	-0.1%	
Estimated Budgeted										
Impact on Fund Balances	\$ 173.3	\$	182.6	5.4%	\$	6.2	\$	2.8	-54.5%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

Revenue

- Overall, UNT revenues ended Q2 \$1.4M or 0.2% above Q2 budgeted estimates. Forecasts have been updated and remain relatively flat to budget for year end.
- Sales of Goods and Services ended Q2 under estimates by \$3.3M or 4.2% due to parking revenue coming in under expectations, as well as revenues for academic conferences, seminars, and other goods and services under by \$1.9M.
- State appropriations lagged behind Q2 estimates due to less than anticipated State benefit reimbursements.
- Investment income is above estimates due to higher than anticipated market gains.

Expense

- Overall, UNT expenses ended Q2 approximately 6.7% below Q2 budgeted estimates. Forecasts have been updated to reflect \$1.3M (0.2%) under budget by year end.
- Positive variances include personnel expenses which ended Q2 \$9.0M or 4.4% below estimates.
- M&O expenses ended Q2 \$4.2M above budget due primarily to Professional Fees and Services attributed to purchased services, data processing services, consulting fees, and temporary employment agency fees. Rentals and Leases attributed to software leases, computing equipment, and office equipment and furnishings. Printing and reproduction is above estimates due to a change in reporting display as Internal Income/Charges are now shown in their corresponding expense category. Printing and copy services at UNT are utilized across the campus and System. Materials and supplies are over due to higher than anticipated costs related to gasoline, uniforms, and office supplies.
- Scholarship, exemptions, and financial aid expenses were under Q2 estimate by \$18.5M or 27.2% due to overestimating discounts and allowances. End of year forecasts have



In Millions

been updated to reflect a \$8.7M or 12.2% over budget, which is in line with prior fiscal year trends.

Impact to Fund Balances

• UNT ended Q2 with an Impact to Fund Balance of \$182.6M, which is \$9.4M or 5.4% above estimates. UNT is forecasting a \$2.8M increase to fund balance at year end.

UNT Health Science Center

	,	FYTD mate		Q2 FYTD Actual	Variance % (Q2 Est to Q2 Actual)	FY18 udget	-	FY18 earend orecast	Variance % (FY18 Fcst to FY18 Bud)	Overall Tracking
Total Revenues	\$	197.0	\$	204.5	3.7%	245.2		255.2	4.1%	
Total Expenses	\$	103.4	\$	104.5	-1.1%	\$ 210.6	\$	218.6	-3.8%	
Total Transfers	\$	(18.0)	\$	(9.7)	46.1%	\$ (27.8)	\$	(27.8)	0.0%	
Estimated Budgeted		75.0		00.0	10.5%	6.0			20.50	
Impact on Fund Balances	Ş	75.3	Ş	90.2	19.5%	\$ 6.8	\$	8.8	28.6%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

Revenue

- Overall, UNTHSC revenues ended Q2 \$7.9M or 3.7% above Q2 budgeted estimates. Forecasts have been updated to reflect being above budget by \$10.0M or 4.1%.
- Net tuition and fees were under estimates by \$1.3M due to over estimating through the second quarter.
- Sales of Goods and Services also was above estimates by \$6.8M or 26.4% due to the contract to the federal prison system being unexpectedly reopened and allowing the Correctional Medicine program to continue providing medical services to incarcerated patients.
- Grants and Contracts were also above budget by \$5.4M or 29.4%.

Expenses

- Overall, UNTHSC expenses ended Q2 in line with budget estimates. Forecasts have been updated to reflect \$8.0M or 3.8% over budget by year end.
- Personnel expenses were \$9.3M or 6.3% under budget due to delays in filling vacant positions caused by the State-mandated hiring freeze. Also, transitioning the 1115 Waiver Program eliminated a number of positions.
- M&O expenses were \$8.2M above budget due to Professional Fees and Services attributable to the unexpected re-opening of the federal prison contract which provides medical services to incarcerated patients and the expenses were not budgeted for. Other negative variances were materials and supplies due to overestimation of the expenses



related to the Acclaim partnership; rentals and leases as a result of a large software purchase that was delayed until the current fiscal year; and other expenses due to reimbursements for educational expenses related to the Acclaim partnership being delayed until this fiscal year.

Impact to Fund Balances

• HSC ended Q2 with an Impact to Fund Balance of \$90.2M, which is \$14.9M or 19.8% above estimates. HSC is forecasting a \$8.8M increase to fund balance at year end.

University of North Texas at Dallas

	Q2 FYTD	(Q2 FYTD	Variance % (Q2 Est to	ı	Y18	FY18 Yearend	Variance % (FY18 Fcst to	Overall
	Estimate		Actual	Q2 Actual)	Bı	udget	Forecast	FY18 Bud)	Tracking
Total Revenues	\$ 50.0	\$	53.4	6.8%	\$	58.4	\$ 61.0	4.4%	
Total Expenses	ې 24.0	\$	27.6	-15.3%	\$	47.3	\$ 49.0	-4.9%	
Total Transfers	\$ (7.1)	\$	(3.8)	-46.7%	\$	(14.1)	\$ (13.6	3.8%	
Estimated Budgeted							•		
Impact on Fund Balances	\$ 19.0	\$	22.0	16.0%	\$	(3.0)	\$ (2.2) 27.4%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

Revenue

- Overall, UNT Dallas revenues ended Q2 \$3.4M or 6.4% above Q2 budgeted estimates. Forecasts have been updated to reflect being above budget by \$2.6M or 4.4%.
- Net Tuition and Fees revenue were \$1.5M or 9.1% above Q2 estimates and expected to end the year above budget by \$1.0M or 5.0%.
- Positive variances include Sales of Goods and Services due to higher than anticipated revenue from the residence hall, parking receipts, and revenue generated from the Caruth Police Institute.

Expenses

- Overall, UNT Dallas expenses ended Q2 \$3.7M or 15.3% over estimates. Forecasts have been updated to reflect \$2.3M or 4.9% over budget by year end.
- Personnel expenses were \$1.5M or 11.2% due primarily to increased faculty salaries as a result of increased enrollment driving higher faculty loads. Forecasts have been updated to reflect \$1.2M over budget due to higher faculty salary expense related to increased enrollment.
- M&O expenses were \$0.6M under budget. Most M&O categories were well within estimates and projected to end the year on budget.

In Millions



Impact to Fund Balances

 UNT Dallas ended Q2 with an Impact to Fund Balance of \$22.0M, which is \$3.0M or 13.8% above estimates.

UNT System Administration

	Q2 FYTD Estimate	(Q2 FYTD Actual	Variance % (Q2 Est to Q2 Actual)	_	Y18 Idget	FY18 Yearend Forecast	Variance % (FY18 Fcst to FY18 Bud)	Overall Tracking
Total Revenues	\$ 3.3	\$	9.1	178.0%	\$	6.3	\$ 10.9	73.3%	
Total Expenses	\$ 33.2	\$	31.8	4.3%	\$	63.2	\$ 63.7	-0.7%	
Total Transfers	\$ 37.8	\$	32.9	-12.9%	\$	57.7	\$ 53.3	-7.7%	
Estimated Budgeted Impact on Fund Balances		\$	10.3	-30.7%	\$	0.8	\$ 0.4	-42.9%	



Meets or exceeds target

Caution (varies from target by 1-3%)

Below target (varies from target by more than 3%)

In Millions

Revenue

- Overall, System Administration revenues ended Q2 \$5.9M or 178.0% above Q2 budgeted estimates. Forecasts have been updated to reflect being above budget by \$4.6M or 73.3%.
- State Appropriations ended Q2 with a large positive variance due to \$4.4M in TRB debt service reimbursements being recorded in this line but budgeted in "Other Legislative Transfers". The remaining variance is due to State Appropriations being budgeted evenly across all quarters but the majority of the revenue is recognized in Q1. Forecast has been updated to reflect both of these issues for State Appropriations and Other Legislative Transfers.

Expenses

- Overall, System Administration expenses ended Q2 \$1.4M or 4.3% under estimates. Forecasts have been updated to reflect \$0.5M or 0.7% over budget by year end.
- Personnel expenses ended Q2 very close to estimates.
- M&O expenses were under Q2 estimates due to large positive variances in Repairs and Maintenance attributable to IT related equipment repairs being less than anticipated.
- Negative variances include Rentals and Leases which were driven by software rental fees being greater than planned, forecast has been adjusted.

Impact to Fund Balances

• System Administration ended Q2 with an Impact to Fund Balance of \$10.3M, which is \$2.4M or 30.7% above estimates. System Administration is forecasting a \$0.4M increase to fund balance at year end.

FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



			riscai fear to									
		FY18 Q2 Estimate	FY18 Q2 Actuals	Variance	Variance % (Bud to Act)	Ref. No.		FY18 Budget	FY18 Year-End Forecast	Variance % (FY18 Fcst to FY18 Bud)	FY17 Actuals	Year-Over-Year Comparison (FY17 Act to FY18 Fcst)
REVENUES					· · ·			- V		•		,
Net Tuition and Fees		\$ 277,331,156	\$ 279,202,956	\$ 1,871,800	0.7%		\$	318,834,500	\$ 313,202,956	-1.8%	\$ 310,060,035	1.0%
Sales of Goods and Services		79,087,962	75,791,295	(3,296,667)	-4.2%	1	*	98,899,496	96,591,295	-2.3%	92,259,072	4.7%
Grants and Contracts		55,541,487	59,546,533	4,005,046	7.2%			98,779,283	102,546,533	3.8%	102,695,036	-0.1%
State Appropriations		127,155,752	124,447,676	(2,708,076)	-2.1%			136,203,844	133,447,676	-2.0%	133,222,566	0.2%
Capital Appropriations - HEF		37,562,056	37,562,056	(2),00,0,0,	0.0%	J		37,562,056	37,562,056	0.0%	37,562,056	0.0%
Net Professional Fees		37,302,030	57,502,050	_	0.0%			-	-	0.0%	-	0.0%
Gift Income		6,251,175	6,402,053	150,878	2.4%			9,780,214	12,000,000	22.7%	16,490,980	-27.2%
Investment Income		1,482,485	2,768,443	1,285,958	86.7%	4		3,827,576	3,827,576	0.0%	5,371,214	-28.7%
Other Revenue		491,091	569,250	78,159	15.9%	-		1,132,356	1,132,356	0.0%	1,406,778	-19.5%
	tal Revenues	\$ 584,903,163			0.2%		\$	705,019,324		-0.7%		0.2%
EXPENSES	tai Nevellues	3 364,303,103	3 380,290,203	3 1,367,033	0.276		Ą	705,015,324	\$ 700,310,449	-0.7 /6	\$ 055,007,730	0.2/6
Salaries - Faculty		\$ 84,676,161	\$ 82,046,561	\$ 2,629,600	3.1%	5	\$	138,188,872	\$ 132,046,561	4.4%	\$ 127,651,323	3.4%
Salaries - Staff		70,727,299	67,104,954	3,622,345	5.1%	6	*	133,252,006	129,604,954	2.7%	129,232,377	0.3%
Wages and Other Compensation		15,573,331	11,226,251	4,347,080	27.9%			27,680,760	23,226,251	16.1%	31,251,600	-25.7%
Benefits and Other Payroll-Related Costs		35,938,157	37,510,371	(1,572,214)	-4.4%	,		77,684,635	77,510,371	0.2%	72,233,166	7.3%
·	sonnel Costs	\$ 206,914,948			4.4%		\$	376,806,273		3.8%	\$ 360,368,466	0.6%
Cost of Goods Sold	30111161 60313	6,306,057	4,934,113	1,371,944	21.76%	8	7	12,300,640	9,934,113	19.2%	8,403,151	18.2%
Professional Fees and Services		6,054,421	8,290,022	(2,235,601)	-36.9%			12,826,585	14,290,022	-11.4%	14,197,638	0.7%
Travel		4,517,434	4,600,664	(83,230)	-1.8%	9		10,553,228	9,600,664	9.0%	9,530,434	0.7%
Materials and Supplies		11,689,298	13,150,677	(1,461,379)	-12.5%	10		27,152,904	28,650,677	-5.5%	30,611,925	-6.4%
Communication and Utilities												
		4,357,588	5,812,385	(1,454,797)	-33.4%	11		10,114,835	12,612,385	-24.7%	12,598,872	0.1% -1.0%
Repairs and Maintenance		8,347,708	7,592,392	755,316	9.0%	12		19,183,305	17,592,392	8.3%	17,771,656	-1.0% -3.0%
Rentals and Leases		3,951,999	5,369,973	(1,417,974)	-35.9%			8,317,171	9,669,973	-16.3%	9,966,551	
Printing and Reproduction		805,157	2,250,886	(1,445,729)	-179.6%			2,019,274	3,250,886	-61.0%	1,298,702	150.3%
Other Expenses		10,036,552	8,233,884	1,802,668	18.0%	14		18,243,571	17,433,884	4.4%	17,390,043	0.3%
Internal Income			- co 224 00F	- (4.450.704)	7.40/		_	- 420 744 542	ć 422.024.00F	0.0%	1,502,045	-100.0%
Subtotal - Maintenance & Ope	eration Costs	\$ 56,066,214	\$ 60,234,995	\$ (4,168,781)	-7.4%		\$	120,711,513	\$ 123,034,995	-1.9%		-0.2%
Debt Service - Principal		-	-	-				-	-	0.0%	24,190,248	-100.0%
Debt Service - Interest				-				-		0.0%	19,163,498	-100.0%
Capital Expenses		7,834,011	8,558,606	(724,595)	-9.2%			12,161,799	14,250,000	-17.2%	14,450,010	-1.4%
Federal and State Pass-Through Expense		152,650	55,580	97,070	63.6%			152,650	152,650	0.0%	280,112	-45.5%
Scholarships, Exemptions and Financial Aid		68,264,085	49,729,844	18,534,241	27.2%	15		71,361,577	80,100,000	-12.2%	80,076,986	0.0%
То	tal Expenses	\$ 339,231,908	\$ 316,467,161	\$ 22,764,747	6.71%		\$	581,193,812	\$ 579,925,781	0.2%	\$ 621,800,338	-6.7%
TRANSFERS												
Intra-Campus Transfers Between Funds:												
Debt Service Transfer In/(Out)		\$ (22,176,678)	\$ (22,176,678)	\$ (0)	0.0%		\$	(44,353,357)	\$ (44,353,357)	0.0%	\$ -	-100.0%
Inter-Fund Transfers In/(Out)		(27,138,556)	(41,990,271)	(14,851,715)	-54.7%	16		(27,138,556)	(27,138,556)	0.0%	(20,560,819)	-32.0%
Transfers Between UNTS Components:												
Shared Services		(13,418,582)	(13,418,582)	-	0.0%			(26,837,165)	(26,837,165)	0.0%	(23,937,930)	-12.1%
Core Services		(9,664,390)	(9,664,390)	-	0.0%			(19,328,779)	(19,328,779)	0.0%	(14,847,244)	-30.2%
Other Inter-Unit Transfers In/(Out)		(22,942)	42,554	65,496	285.5%			(45,884)	42,554	192.7%	(1,527,096)	102.8%
Other Transfers:												
Transfer to other State Agencies In/(Out)		-	-	-	100.0%			-	-	0.0%	621,840	-100.0%
Other Legislative Transfers In/(Out)		30,357	30,357	-	0.0%			30,357	30,357	0.0%	6,536,781	-99.5%
Lapsed Appropriations		-	-	-	-100.0%				-	0.0%	(2,013,166)	100.0%
То	tal Transfers	\$ (72,390,791)	\$ (87,177,010)	\$ (14,786,219)	-20.4%		\$	(117,673,384)	\$ (117,584,946)	0.1%	\$ (55,727,634)	-111.0%
Estimated Budgeted Impact on Fund Balances		\$ 173,280,464	\$ 182,646,091	\$ 9,365,627	5.4%		\$	6,152,128	\$ 2,799,721	-54.5%	\$ 21,539,764	-87.0%
Planned Use of Fund Balances		\$ -	\$ -	\$ -			\$	-	\$ -		\$ -	

FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Variance Explanations



REVENUES

Transfer to other State Agencies In/(Out)
Other Legislative Transfers In/(Out)


Lapsed Appropriations


	Net Tuition and Fees	
	INEL TUILIOITATIU FEES	
1	Sales of Goods and Services	Budgeted revenue for Parking under full year estimates by \$1.4M. Estimated revenue for Academic conferences, seminars, and other Goods & Services revenues under by \$1.9M.
2	Grants and Contracts	Trending ahead of quarterly estimates for Federal, State, and Other grants and contracts.
3	State Appropriations	Benefits reimbursement under quarterly estimates by \$2.7M.
	Capital Appropriations - HEF	
	Net Professional Fees	
	Gift Income	
4	Investment Income	Higher than budgeted market returns. Realized gains of \$1.0M and interest income of \$1.7M for FY18.
	Other Revenue	
	EXPENSES	
5	Salaries - Faculty	\$2.6M variance due to vacant and unfilled positions.
6	Salaries - Staff	\$3.6M variance due to vacant and unfilled positions.
		Underallocated Q2 estimate; wages under prior year year by \$3.7M due to change in reporting display to include Internal Income/ Charges with corresponding expense
7	Wages and Other Compensation	
	Benefits and Other Payroll-Related Costs	category.
8	Cost of Goods Sold	Overallocated Q2 estimate; positive variance in cost of goods sold is offset by spending within other expenditure categories.
9	Professional Fees and Services	Variance driven by Other Purchased Services (i.e. catering, meal plans, guest muscicians, instructional services, etc), IT and Data Processing Services, and General
		Business Services (i.e. business consulting fees and temp employment agencies).
	Travel	
10	Materials and Supplies	Variance driven by General Supplies expenses, primarily concentrated in Vehicle Gasoline, Uniforms, and Office Supplies.
11	Communication and Utilities	Utilities tracking over prior year Q2 by \$700K, primarily in Electricity. Telecom over prior year by \$500K due to change in reporting display to include Internal Income/
11	Communication and offitties	Charges with corresponding expense category.
	Repairs and Maintenance	
12	Rentals and Leases	Variance driven by Rental and Lease of software licences, computing equipment, and office furnishings/ equipment.
		Variance due to change in reporting display to include Internal Income/ Charges with corresponding expense category. The University's printing and copy services are
13	Printing and Reproduction	utilized throughout campus as internal income and charges.
14	Other Expenses	Current year tracking under prior year in insurance premium expense by \$1.0M.
	Internal Income	
	Debt Service - Principal	
	Debt Service - Interest	
	Capital Expenses	
	Federal and State Pass-Through Expense	
15	Scholarships, Exemptions and Financial Aid	Scholarship expense is up versus prior year Q2 by \$10.0M. Exemption expenses are up versus prior year Q2 by \$3.2M. Offset by overestimation of Discounts and
	TRANSFERS	Allowances of \$7.6M
	Intra-Campus Transfers Between Funds:	
	Debt Service Transfer In/(Out)	
16	Inter-Fund Transfers In/(Out)	Additional transfers to capital funds for Auxiliary funded projects (\$10.4M) and HEF funded projects (\$4.4M).
	Transfers Between UNTS Components:	
	Shared Services	
	Core Services	
	Other Inter-Unit Transfers In/(Out)	
	Other Transfers:	
I	1 -,	


Key Expense Categories






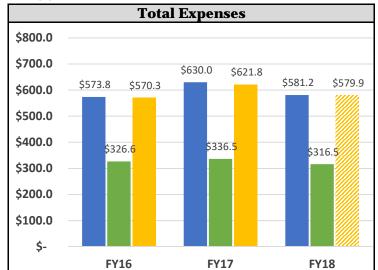

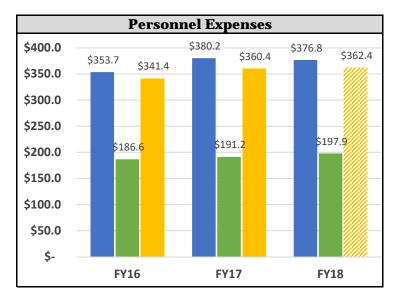

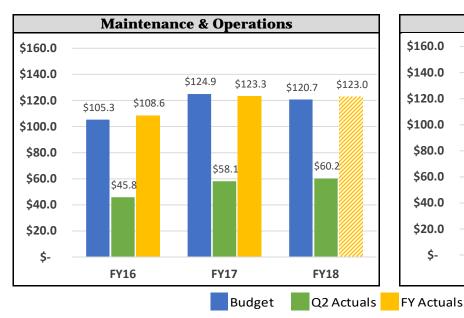





Projection


Key Revenue Categories





In Millions

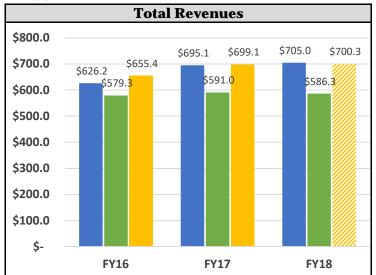



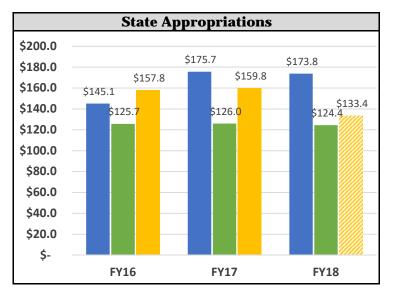

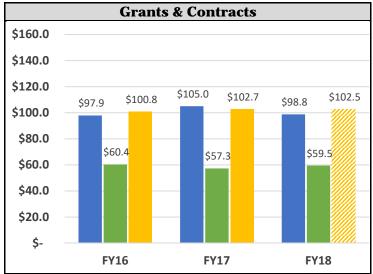

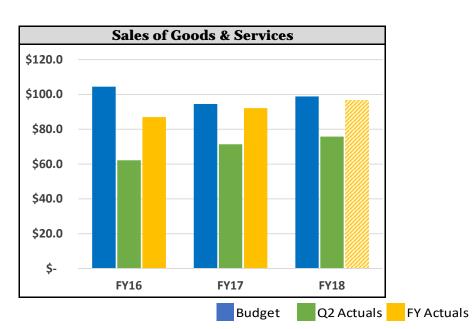

Projection

FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



			riscal fear to Date Total Budget and fear-End Forecast										2 0012	ENCE CENTER	
		FY18 Q2 Estimate		FY18 Q2 Actuals	Variance	Variance % (Bud to Act)	Ref. No.		FY18 Budget		18 Year-End Forecast	Variance % (FY18 Fcst to FY18 Bud)	FY17 Actuals	Year-Over-Year Comparison (FY17 Act to FY18 Fcst)	
REVENUES	ŀ					(= 0.0 10 1100)								(**************************************	
Net Tuition and Fees		\$ 26,020,000	Ś	24,690,147	\$ (1,329,853)	-5.1%	1	\$	31,750,280	Ś	31,200,000	-1.7%	\$ 30,149,923	3.5%	
Sales of Goods and Services		25,780,000		32,582,157	6,802,157	26.4%		~	39,225,000		48,225,000	22.9%	48,990,931	-1.6%	
Grants and Contracts		18,220,000		23,577,103	5,357,103	29.4%			35,900,000		38,000,000	5.8%	43,810,626	-13.3%	
State Appropriations		100,360,583		93,556,422	(6,804,161)	-6.8%			103,643,662		103,000,000	-0.6%	97,974,860	5.1%	
Capital Appropriations - HEF		17,091,856		17,091,856	(0,004,101)	0.0%	7		17,091,856		17,091,856	0.0%	17,091,856	0.0%	
Net Professional Fees		7,500,000		10,224,832	2,724,832	36.3%	5		13,722,182		13,300,000	-3.1%	14,206,060	-6.4%	
Gift Income		530,000		1,089,937	559,937	105.6%			1,500,000		1,800,000	20.0%	2,321,129	-22.5%	
Investment Income		1,120,000		1,520,709	400,709	35.8%			2,240,000		2,240,000	0.0%	3,165,218	-29.2%	
Other Revenue		60,000		201,419	141,419	235.7%			120,000		360,000	300.0%	430,609	-16.4%	
	anuas	\$ 196,682,439				3.8%		Ś	245,192,980		255,216,856	4.1%	\$ 258,141,212	-10.4%	
EXPENSES	ciiues	3 130,062,433	٠ ج	204,554,561	3 7,032,142	3.0/0		Ą	243,132,360	۶	255,210,850	4.1/0	3 230,141,212	-1.1/0	
Salaries - Faculty		\$ 23,207,000	Ś	22,330,291	\$ 876,709	3.8%		\$	48,000,000	Ś	45,000,000	6.3%	\$ 45,728,366	-1.6%	
Salaries - Staff		29,644,000		28,528,455	1,115,545	3.8%			61,300,000		59,000,000	3.8%	56,507,248	4.4%	
Wages and Other Compensation		3,556,000		2,056,867	1,499,133	42.2%			7,000,000		6,000,000	14.3%	6,707,618	-10.5%	
Benefits and Other Payroll-Related Costs		17,297,000		13,280,149	4,016,851	23.2%	9		31,000,000		28,000,000	9.7%	27,917,918	0.3%	
Subtotal - Personnel	Costs			66,195,762		10.2%		\$	147,300,000		138,000,000	6.3%	\$ 136,861,150	0.8%	
Cost of Goods Sold		9,000		10,338	(1,338)	-14.86%		7	20,000		20,000	0.0%	8,015	149.5%	
Professional Fees and Services		14,749,000		16,890,906	(2,141,906)	-14.5%			30,500,000		35,500,000	-16.4%	37,163,097	-4.5%	
Travel		727,000		707,915	19,085		10		2,000,000		2,000,000	0.0%	2,202,804	-9.2%	
Materials and Supplies		2,995,000		4,590,241	(1,595,241)	-53.3%	11		9,000,000		14,000,000	-55.6%	12,525,342	11.8%	
Communication and Utilities		1,016,000		1,473,731	(457,731)	-45.1%			2,400,000		2,400,000	0.0%	2,109,900	13.7%	
Repairs and Maintenance				1,473,731		-43.1%			3,500,000		3,500,000	0.0%	3,286,951	6.5%	
l ·		1,714,000 629,000			(211,767)	-12.4%	12				2,622,000			67.4%	
Rentals and Leases				1,670,911	(1,041,911)		12		1,500,000			-74.8%	1,566,576		
Printing and Reproduction		186,000		267,422	(81,422)	-43.8%	12		750,000		650,000	13.3%	887,943	-26.8%	
Other Expenses		2,380,000		5,105,337	(2,725,337)	-114.5%	13		5,500,000		10,000,000	-81.8%	6,399,939	56.3%	
Internal Income	<u></u>	ć 24.40F.000	Ś	- 22.642.566	- - -	22.00/		\$		ć	70.602.000	0.0%	91,234	-100.0% 6.7%	
Subtotal - Maintenance & Operation	Costs	\$ 24,405,000	Þ	32,642,566	\$ (8,237,566)	-33.8%		Þ	55,170,000	Þ	70,692,000	-28.1%	\$ 66,241,800		
Debt Service - Principal		-		-	-				-			0.0%	2 116 107	0.0%	
Debt Service - Interest		2 24 6 000		2 0 4 5 0 4 7	270.002	0.40/			4 400 000		c 000 000	0.0%	3,116,107	-100.0%	
Capital Expenses		3,216,000		2,945,917	270,083	8.4%			4,400,000		6,000,000	-36.4%	3,415,340	75.7%	
Federal and State Pass-Through Expense		-		279,364	(279,364)				700,000		700,000	0.0%	907,544	-22.9%	
Scholarships, Exemptions and Financial Aid		2,033,000	1	2,557,605	(524,605)	-25.8%	14		3,000,000		3,250,000	-8.3%	824,357	294.2%	
Total Exp	enses	\$ 103,358,000	\$	104,621,215	\$ (1,263,215)	-1.22%		\$	210,570,000	\$	218,642,000	-3.8%	\$ 211,366,298	3.4%	
TRANSFERS															
Intra-Campus Transfers Between Funds:															
Debt Service Transfer In/(Out)		\$ (7,950,000)	\$	(2,500,558)	\$ (5,449,442)	68.5%	15	\$	(15,891,925)	\$	(15,491,925)	-2.5%	\$ -	0.0%	
Inter-Fund Transfers In/(Out)		(730,000)		97,280	(827,280)	113.3%			(2,600,000)		(3,000,000)	15.4%	(12,548,514)	-76.1%	
Transfers Between UNTS Components: Shared Services		-		-	-				-		-	0.0%	-	0.0%	
Core Services		(2,017,718)		-	2,017,718	-100.0%	16		(2,017,718)		(2,017,718)	0.0%	(2,625,427)	-23.1%	
Other Inter-Unit Transfers In/(Out)		-		-	-				-		-	0.0%	284,174	-100.0%	
Other Transfers:											-				
Transfer to other State Agencies In/(Out)		-		-	-				-		-	0.0%	12,149	-100.0%	
Other Legislative Transfers In/(Out)		(7,289,981)		(7,289,981)	-	0.0%			(7,289,981)		(7,289,981)	0.0%	(588,947)	1137.8%	
Lapsed Appropriations		-							-			0.0%	(260,736)	-100.0%	
Total Trai	nsfers	\$ (17,987,699)	\$	(9,693,259)	\$ 8,294,440	-46.1%		\$	(27,799,624)	\$	(27,799,624)	0.0%	\$ (15,727,300)	76.8%	
Estimated Budgeted Impact on Fund Balances		\$ 75,336,740	\$	90,220,107	\$ 14,883,367	19.8%		\$	6,823,356	\$	8,775,232	-28.6%	\$ 31,047,614	63.3%	
Planned Use of Fund Balances		\$ -	\$		\$ -			\$		\$			\$ -		

FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter **Variance Explanations**



REVENUES

1	Not Tuitian and Food	Tuitien revenue was averagimated through the spend quarter
1	Net Tuition and Fees	Tuition revenue was overestimated through the second quarter.
2	Sales of Goods and Services	The federal prison contract to provide health care services was unexpectedly reopened, which has allowed UNTHSC's Correctional Medicine Program to continue
	Sales of Goods and Services	to provide medical services to incarcerated patients.
3	Grants and Contracts	Due to the implementation of the billing module within PeopleSoft, the frequency of billing vendors has increased which resulted in an underestimated budget.
4	State Appropriations	A change in the methodology to record State-paid benefits caused the budget estimate to be overstated.
	Capital Appropriations - HEF	
_	Net Professional Fees	The variance is primarily attributable to two items: Clinical activity associated with UNT Health was higher than originally estimated, and an Uncompensated Care
5	Net Professional Fees	reimbursement as part of the 1115 Waiver program was received sooner than expected.
6	Gift Income	An unexpected gift was donated to UNTHSC.
	Investment Income	
	Other Revenue	
	EXPENSES	

	Salaries - Faculty	
		The variance is primarily due to a longer-than-expected delay in filling vacant positions caused by the State-mandated hiring freeze, as well as the transitioning of
7	Salaries - Staff	the 1115 Waiver program, which shifted from an individual project-based model to an outcome-based patient model, thereby eliminating the majority of positions
		associated with the individual projects.
8	Wages and Other Compensation	The budget estimate inadvertently included one-time severance payouts for clinical faculty who transitioned from UNTHSC to Acclaim.
Λ	Panefits and Other Payrell Palated Costs	Filling the vacant positions caused by the State-mandated hiring freeze is taking longer than expected, along with the reduction in staff associated with the 1115
9	Benefits and Other Payroll-Related Costs	waiver program, which has resulted in lower-than-estimated payroll benefit costs.
	Cost of Goods Sold	
10	Professional Fees and Services	The federal prison contract to provide health care services was unexpectedly reopened, which has led UNTHSC's Correctional Medicine Program to continue to
10	Professional Fees and Services	provide medical services to incarcerated patients.
	Travel	
11	Materials and Supplies	The impact caused by the transition of UNT Health's medical services to Acclaim was overestimated, which caused the budget estimate to be understated.
	Communication and Utilities	
	Repairs and Maintenance	
12		A contract for the purchase of Axiom software was delayed until the current fiscal year, causing the budget to be underestimated.
	Printing and Reproduction	
13	Other Expenses	Reimbursements for educational services provided in the prior fiscal year by Acclaim were unexpectedly delayed until the current fiscal year.
	Internal Income	
	Debt Service - Principal	
	Debt Service - Interest	
	Capital Expenses	
14	Scholarships, Exemptions and Financial Aid	Scholarship expenses were underestimated through the second quarter.
	TRANSFERS	


TRANSFERS


	TIVATO ETO	
	Intra-Campus Transfers Between Funds:	
	Debt Service Transfer In/(Out)	
15	Inter-Fund Transfers In/(Out)	The debt service payment through the second quarter was inadvertently overestimated. However, once the final debt service payment for the fiscal year is
13	inter-rund transfers in/(Out)	recorded, any significant differences between actuals and planned expenditures shall be eliminated.
	Transfers Between UNTS Components:	
	Shared Services	
16	Core Services	Transfer of funds was delayed pending the final outcome of selected core services transitioning back to the UNT System components.
	Other Inter-Unit Transfers In/(Out)	
	Other Transfers:	
	Transfer to other State Agencies In/(Out)	
	Other Legislative Transfers In/(Out)	
	Lapsed Appropriations	


Key Expense Categories UN






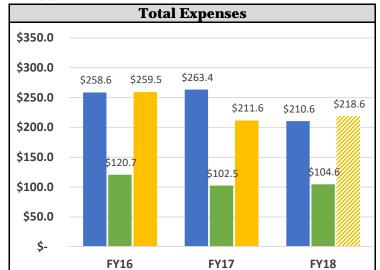










Key Revenue Categories UNT







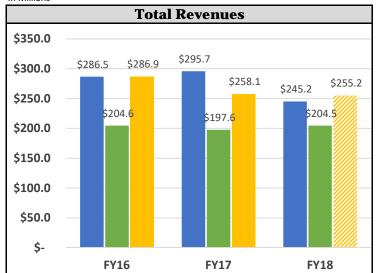


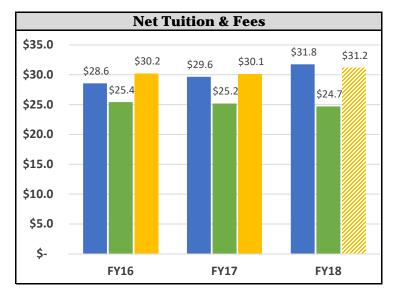









FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



		FY18 Q2		FY18 Q2			Variance %	Ref.		FY18	FY1	18 Year-End	Variance % (FY18 Fcst to		FY17	Year-Over-Year Comparison
		Estimate		Actuals	V	ariance	(Bud to Act)	No.		Budget		Forecast	FY18 Bud)		Actuals	(FY17 Act to FY18 Fcst)
REVENUES							(========									(
Net Tuition and Fees	Ś	16.455.174	Ś	17,944,859	Ś	1,489,685	9.1%	1	\$	19,359,028	Ś	20,326,979	5.0%	\$	17,386,814	16.9%
Sales of Goods and Services	,	411,250		973,603	7	562,353	136.7%	2	*	822,500	*	1,126,825	37.0%	7	474,196	137.6%
Grants and Contracts		6,755,851		7,937,236		1,181,385	17.5%	3		9,651,215		10,751,215	11.4%		8,047,929	33.6%
State Appropriations		23,918,139		23,849,744		(68,395)	-0.3%	J		25,718,429		25,718,429	0.0%		17,565,488	46.4%
Capital Appropriations - HEF		2,113,004		2,113,004		(00,333)	0.0%			2,113,004		2,113,004	0.0%		2,113,004	0.0%
Net Professional Fees		2,113,004		2,113,004		_	0.070			2,113,004		2,113,004	0.0%		2,113,004	0.0%
Gift Income		250,000		396,142		146,142	58.5%			500,000		646,142	29.2%		480,111	34.6%
Investment Income		108,000		183,104		75,104	69.5%			216,000		291,104	34.8%		309,197	-5.9%
Other Revenue		10,000		23,057		13,057	130.6%			20,000		23,500	17.5%		23,702	-0.9%
Total Revenu	es Ś	,	\$		Ś	3,399,333	6.8%		Ś	58,400,176	Ś	60,997,199	4.4%	\$	46,400,440	31.5%
EXPENSES			Ė	, . , .	•	.,,				, ,					.,,	
Salaries - Faculty	\$	4,496,094	\$	6,055,457	\$	(1,559,363)	-34.7%	4	\$	9,991,320	\$	10,616,320	-6.3%	\$	9,069,946	-17.0%
Salaries - Staff		5,934,940		5,593,237		341,703	5.8%			13,188,755		13,188,755	0.0%		9,925,168	-32.9%
Wages and Other Compensation		434,230		573,359		(139,129)	-32.0%			964,956		1,254,443	-30.0%		1,194,625	-5.0%
Benefits and Other Payroll-Related Costs		2,524,531		2,668,019		(143,488)	-5.7%			5,610,068		5,890,571	-5.0%		5,175,251	-13.8%
Subtotal - Personnel Co	its \$	13,389,795	\$	14,890,071	\$	(1,500,276)	-11.2%		\$	29,755,099	\$	30,950,089	-4.0%	\$	25,364,990	-22.0%
Cost of Goods Sold		-		-		-				-		-	0.0%		-	0.0%
Professional Fees and Services		524,378		897,103		(372,725)	-71.1%	5		1,048,755		1,421,480	-35.5%		1,430,830	0.7%
Travel		266,438		239,736		26,702	10.0%			532,875		532,875	0.0%		392,295	-35.8%
Materials and Supplies		1,612,623		818,665		793,958	49.2%	6		3,225,246		2,852,521	11.6%		1,752,308	-62.8%
Communication and Utilities		373,715		233,559		140,156	37.5%			747,429		747,429	0.0%		336,498	-122.1%
Repairs and Maintenance		136,049		249,102		(113,053)	-83.1%			272,098		272,098	0.0%		1,034,544	73.7%
Rentals and Leases		117,410		314,450		(197,040)	-167.8%			234,820		234,820	0.0%		655,324	64.2%
Printing and Reproduction		199,041		28,334		170,707	85.8%			398,082		398,082	0.0%		315,432	-26.2%
Other Expenses		678,528		569,169		109,359	16.1%			1,357,055		1,357,055	0.0%		1,153,839	-17.6%
Internal Income		-				-	100.0%			-		-	0.0%		216,370	100.0%
Subtotal - Maintenance & Operation Cos	its \$	3,908,182	\$	3,350,119	\$	558,063	14.3%		\$	7,816,360	\$	7,816,360	0.0%	\$	7,287,442	-7.3%
Debt Service - Principal		-		-		-				-		-	0.0%		7,163,050	100.0%
Debt Service - Interest		-		-		-				-		-	0.0%		1,431,044	100.0%
Capital Expenses		389,513		516,446		(126,933)	-32.6%			779,026		779,026	0.0%		564,032	-38.1%
Federal and State Pass-Through Expense		-		_		_	0.0%			_		_	0.0%		_	0.0%
Scholarships, Exemptions and Financial Aid		6,265,851		8,858,688		(2,592,837)	-41.4%	7		8,951,215		10,051,215	-12.3%		7,420,464	-35.5%
Total Expens	es Ś		Ś			(3,661,984)	-15.3%		Ś	47,301,700	Ś	49,596,690	-4.9%	\$	49,231,023	-0.7%
TRANSFERS	_				*	(-,,,				,,	<u> </u>	10,000,000			10,202,020	
Intra-Campus Transfers Between Funds:																
Debt Service Transfer In/(Out)	Ś	(4,491,279)	ς	(2,107,083)	\$	(2,384,196)	53.1%	8	\$	(8,982,558)	Ś	(8,982,558)	0.0%	\$	_	-100.0%
Inter-Fund Transfers In/(Out)		-	7	443,827	7	(443,827)	-100.0%	o	*	(=,==,===,	*	443,827	0.0%	7	(25,556)	1836.7%
Transfers Between UNTS Components:				5,527		(1.0,027)	200.070					. 10,027	0.070		(23,333)	20001770
Shared Services		(1,300,620)		(1,300,620)		-	0.0%			(2,601,240)		(2,601,240)	0.0%		(2,388,246)	-8.9%
Core Services		(634,713)		(590,962)		(43,751)	6.9%			(1,269,425)		(1,181,925)	-6.9%		(762,645)	-55.0%
Other Inter-Unit Transfers In/(Out)		(644,361)		(211,478)		432,883	67.2%			(1,288,721)		(1,288,721)	0.0%		(766,253)	-68.2%
Other Transfers:																
Transfer to other State Agencies In/(Out)		-		-		-	0.0%			-		-	0.0%		-	0.0%
Other Legislative Transfers In/(Out)		-		-		-	0.0%			-		-	0.0%		9,095,463	100.0%
Lapsed Appropriations		-				-	0.0%			-					(597,887)	100.0%
Total Transfe	rs \$	(7,070,972)	\$	(3,766,316)	\$	3,304,656	46.7%		\$	(14,141,944)	\$	(13,610,617)	-3.8%	\$	4,554,876	-398.8%
Estimated Budgeted Impact on Fund Balances	\$	18,997,106	\$	22,039,113	\$	3,042,006	16.0%		\$	(3,043,468)	\$	(2,210,108)	27.4%	\$	1,724,294	-228.2%
Planned Use of Fund Balances	\$	-	\$		\$	•			\$	3,155,236	\$	2,210,108		\$	-	

FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Variance Explanations




REVENUES


1	Net Tuition and Fees	Implemented new Academic & Career Advising Fee effective Spring 2018, revenue displayed in Q2 totals \$445K. The remaining variance is related to undergraduate SCH growth exceeding budget projections, additional non-resident students, and Discounts & Allowances below budget projections.
2	Sales of Goods and Services	Parking revenue exceeded budget projections due to increased enrollment and enforcement efforts. Also, Wisdom Hall occupancy rate exceeded conservative budget projections. Additionally, revenue generated by Caruth Police Institute exceeded expectations (\$140K).
3	Grants and Contracts	Federal Financial Aid awards came in higher than anticipated due to increased enrollment and eligibility (\$1M)
	State Appropriations	
	Capital Appropriations - HEF	
	Net Professional Fees	
	Gift Income	
	Investment Income	
	Other Revenue	
	EXPENSES	
_	Calarias Facultus	
4	Salaries - Faculty	Increased enrollment demanded more sections to be covered with faculty overloads and adjunct faculty than budgeted for Fall and Spring. Additionally, budget incorrectly spread the expense over the quarters. Majority of expenses should be captured thru Q2 with smaller amounts in Q3 and Q4.
	Salaries - Staff	incorrectly spread the expense over the quarters. Majority of expenses should be captured this Q2 with smaller amounts in Q3 and Q4.
	Wages and Other Compensation	
	Benefits and Other Payroll-Related Costs	
	Cost of Goods Sold	
5	Professional Fees and Services	Budget assumed expenses in Materials & Supplies, budget reallocations have taken place to match actual expenditures.
	Travel	
6	Materials and Supplies	Budget assumed expenses in Materials & Supplies, budget reallocations have taken place to match actual expenditures. Also, spending has taken place at a slower rate than anticipated.
	Communication and Utilities	
	Repairs and Maintenance	
	Rentals and Leases	
	Printing and Reproduction	
	Other Expenses	
	Internal Income	
	Debt Service - Principal	
	Debt Service - Interest	
	Capital Expenses	
	Federal and State Pass-Through Expense	
7	Scholarships, Exemptions and Financial Aid	Federal Financial Aid awards came in higher than anticipated due to increased enrollment and eligibility (\$1M)
	TRANSFERS	
	Intra-Campus Transfers Between Funds: Debt Service Transfer In/(Out)	
8	Inter-Fund Transfers In/(Out)	Additional transfers to capital funds for Auxiliary funded projects (\$10.4M) and HEF funded projects (\$4.4M).
	Transfers Between UNTS Components:	Additional transfers to capital ratios for Additional projects (\$25.40) and the rational projects (\$4.40).
	Shared Services	
	Core Services	
	Other Inter-Unit Transfers In/(Out)	
	Other Transfers:	
	Transfer to other State Agencies In/(Out)	
	Other Legislative Transfers In/(Out)	
	Lapsed Appropriations	


Key Expense Categories






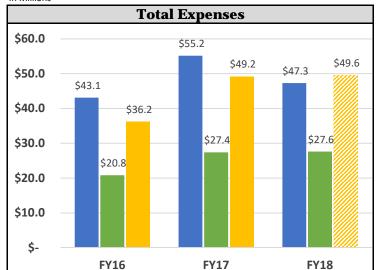

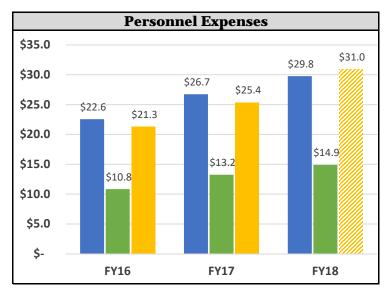

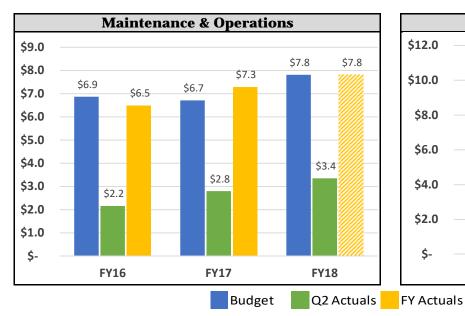


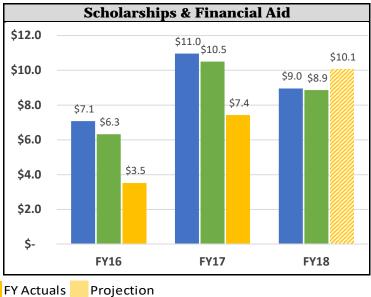



Key Revenue Categories







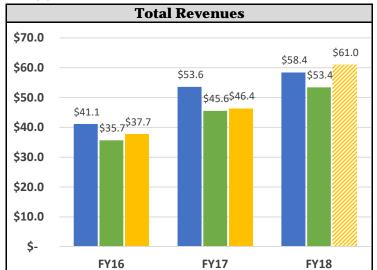

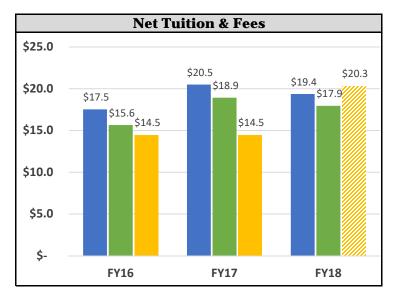

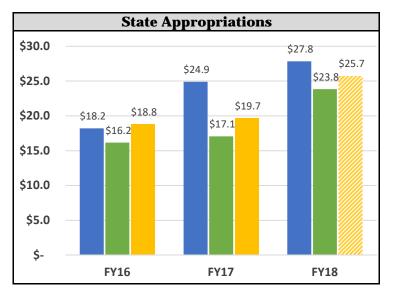

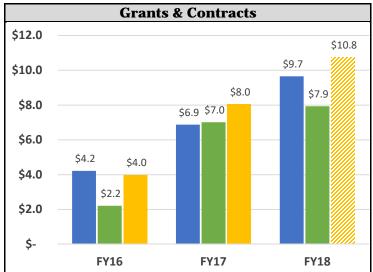

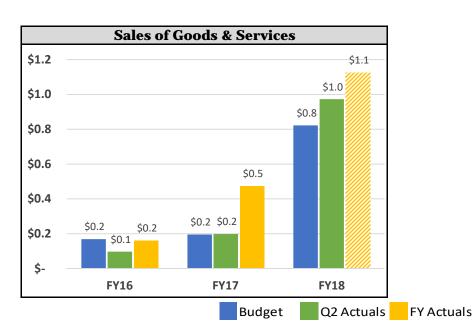

FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Fiscal Year to Date Total Budget and Year-End Forecast



						виадет and								
		FY18 Q2 Estimate	FY18 Actu		Variance	Variance % (Bud to Act)	Ref. No.		FY18 Budget	FY18 Yea		Variance % (FY18 Fcst to FY18 Bud)	FY17 Actuals	Year-Over-Year Comparison (FY17 Act to FY18 Fcst)
REVENUES						, ,								,
Net Tuition and Fees	\$	_	\$	-	\$	-		\$	-			0.0%	\$ -	0.0%
Sales of Goods and Services		987,743	. 6	60,490	(327,253) -33.19	1		1,975,485	1,	975,485	0.0%	2,017,740	-2.1%
Grants and Contracts		· -		· -	, ,	, -			-			0.0%	-	0.0%
State Appropriations		2,201,776	8.2	31,442	6,029,66	5 273.9%	2		4,089,548	8.	457,298	106.8%	8,987,972	
Capital Appropriations - HEF		-	-,	_	-,,	-			-	-,	,	0.0%	_	0.0%
Net Professional Fees		_		-		-			-			0.0%	-	0.0%
Gift Income		_		-		-			-			0.0%	-	0.0%
Investment Income		100,570	1	80,463	79,89	3 79.49			201,139		281,139	39.8%	280,974	
Other Revenue		· -		73,096	73,09				· -		146,192	100.0%	235,273	
Total Revenue	es \$	3,290,089		45,491				\$	6,266,172		860,114	73.3%		
EXPENSES					· · · · ·		1			. ,				
Salaries - Faculty	\$	-	\$	-	\$	-		\$	-			0.0%	\$ -	0.0%
Salaries - Staff		18,416,132	18,5	55,304	(139,172) -0.8%	S		36,832,263	35,	687,330	3.1%	36,892,078	3.3%
Wages and Other Compensation		604,687	(10	06,953)	711,64	117.79	3		1,209,373	1,	209,373	0.0%	1,839,696	34.3%
Benefits and Other Payroll-Related Costs		4,886,714	4,6	83,634	203,080	4.29	5		9,773,428	9,	367,269	4.2%	9,887,706	5.3%
Subtotal - Personnel Cos	ts \$	23,907,533	\$ 23,1	31,986	\$ 775,54	7 3.29	5	\$	47,815,064	\$ 46,	263,971	3.2%	\$ 48,619,480	4.8%
Cost of Goods Sold		-		-		-			-			0.0%	-	0.0%
Professional Fees and Services		1,816,280	2,3	06,982	(490,702) -27.0%	4		3,632,559	3,	800,000	-4.6%	4,476,480	15.1%
Travel		246,266	1	55,855	90,41	1 36.7%			492,531		492,531	0.0%	451,018	-9.2%
Materials and Supplies		420,583	4	54,795	(34,212	-8.19			841,165		876,165	-4.2%	1,227,323	28.6%
Communication and Utilities		403,161	5	33,062	(129,901) -32.2%			806,322		806,322	0.0%	2,076,588	61.2%
Repairs and Maintenance		3,539,198	1,7	74,924	1,764,27	49.89	5		5,254,369	5,	254,369	0.0%	4,324,098	-21.5%
Rentals and Leases		267,679		25,896	(658,217		6		535,358		851,793	-245.9%	566,388	
Printing and Reproduction		41,829		22,983	18,84				83,658		83,658	0.0%	5,866	-1326.1%
Other Expenses		594,563	8	42,267	(247,704) -41.7%	7		1,189,125	1,	684,535	-41.7%	1,791,994	6.0%
Internal Income						-						0.0%	(5,184,520)	100.0%
Subtotal - Maintenance & Operation Cos	ts \$	7,329,559	\$ 7,0	16,765	\$ 312,79	4.39	,	\$	12,835,087	\$ 14,	849,372	-15.7%		
Debt Service - Principal		-		-		-			-			0.0%	5,411,241	100.0%
Debt Service - Interest		-		-		-			-			0.0%	1,545,755	
Capital Expenses		1,963,241	1,6	20,025	343,21	5 17.5%	8		2,582,991	2,	582,991	0.0%	568,127	
Federal and State Pass-Through Expense		_				_						0.0%		0.0%
Scholarships, Exemptions and Financial Aid						_						0.0%		0.0%
Total Expense	s ¢	33,200,333	¢ 217	68,776	\$ 1,431,55	7 4.31%		Ś	63,233,142	¢ 62	696,335	-0.7%	\$ 65,879,838	
·	3 3	33,200,333	7 31,7	08,770	3 1,431,33	4.31/	1	,	03,233,142	y 03,	090,333	-0.770	3 03,873,838	3.3/0
TRANSFERS														
Intra-Campus Transfers Between Funds:	\$	(1,953,994)	ć /1.0F	-2 OOE)	٠.	0.0%		Ś	(6,985,609)	\$ 16.0	985,609)	0.0%	ć	-100.0%
Debt Service Transfer In/(Out) Inter-Fund Transfers In/(Out)	Ş	(1,555,554)	\$ (1,95	3,995)	\$	0.07	·	Ą	(0,963,009)	۶ (۵,۶	763,003)		\$ - 417,020	
Transfers Between UNTS Components:		-		-		-			-			0.0%	417,020	100.0%
Shared Services		15,031,351	14 7	19,202	(312,150) -2.19			29,438,405	29	438,405	0.0%	27,683,339	6.3%
Core Services		12,469,150		73,070	(196,080				22,615,922		528,422	-0.4%	, ,	
Other Inter-Unit Transfers In/(Out)		720,632		20,632	(===,===	- 0.0%			1,168,467		168,467	0.0%		
Other Transfers:		,		,					_,,				_,,,,,,,,	12.0/
Transfer to other State Agencies In/(Out)		(141,823)		-	141,82	3 -100.0%	5		(141,823)		-	-100.0%	-	0.0%
Other Legislative Transfers In/(Out)		11,627,374	7,1	17,801	(4,509,573				11,627,374	7,	117,801	-38.8%	6,664,934	6.8%
Lapsed Appropriations									-			0.0%	(551,391)	
Total Transfe	rs \$	37,752,690	\$ 32,8	76,710	\$ (4,875,980) -12.9%		\$	57,722,736	\$ 53,	267,486	-7.7%	\$ 53,101,230	0.3%
Estimated Budgeted Impact on Fund Balances	\$	7,842,446				30.7%		\$	755,766		431,265	42.9%		
Planned Use of Fund Balances	\$	-	\$	-	\$	-		\$		\$	-		\$ 1,256,647	

FY18 - Revenues, Expenses, and Transfers - Current Funds by Quarter Variance Explanations




REVENUES


	REVENUES	
	Net Tuition and Fees	
1	Sales of Goods and Services	1900 Elm Lofts rent posting two months behind due to receipt of information from real estate broker.
	Grants and Contracts	
		\$4.4M Fav - Tuition Revenue Bond debt service reimbursement budgeted in Other Legislative Transfers but posted as State Appropriations.
2	State Appropriations	\$923K Fav - State Benefits greater than planned.
		\$739K Fav - Appropriation budgeted to be received monthly. Received all at once
	Capital Appropriations - HEF	
	Net Professional Fees	
	146110163310114111663	
	Gift Income	
	Investment Income	
	Other Revenue	
	EXPENSES	
	Salaries - Faculty	
	Salaries - Staff	
3	Wages and Other Compensation	Includes \$1.25K internal income allocation.
	Benefits and Other Payroll-Related Costs	
	Cost of Goods Sold	
4	Professional Fees and Services	HR \$266K - over driven by ACA compliance license.
	Troicssionarrees and services	System Building \$150K - driven by real estate advisory service and security.
	Travel	
	Materials and Supplies	
	Communication and Utilities	
5	Repairs and Maintenance	ITSS repairs and maintenance less than planned (timing).
6	Rentals and Leases	Driven by various rental software (ITSS, Facilities, Internal Audit, HR).
	Printing and Reproduction	
7	Other Expenses	Various expenses greater than planned.
	Internal income	
	Debt Service - Principal	
	Debt Service - Interest	
8	Capital Expenses	Capital Expenditures less than planned.
	Scholarships, Exemptions and Financial Aid	
	TRANSFERS	l .
	Intra-Campus Transfers Between Funds:	
	Debt Service Transfer In/(Out)	
	Inter-Fund Transfers In/(Out)	
	Transfers Between UNTS Components:	
	Shared Services	
	Core Services	
	Other Inter-Unit Transfers In/(Out)	
	Other Transfers:	
	Transfer to other State Agencies In/(Out)	
9	Other Legislative Transfers In/(Out)	\$4.367K Unfav - Tuition Revenue Bond debt service reimbursement budgeted in Other Legislative Transfers but posted as State Appropriations.
9		\$141K Unfav - Texas A&M Commerce posted here but budgeted in Transfer to Other State Agencies.


Key Expense Categories





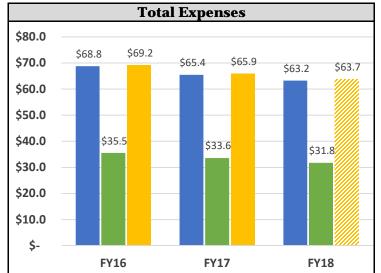

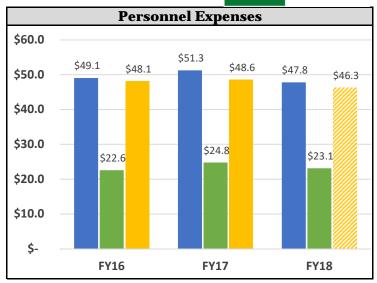

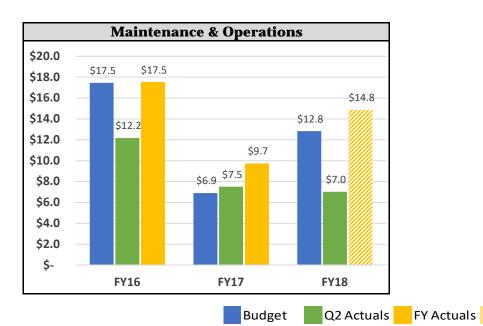



Projection


Key Revenue Categories









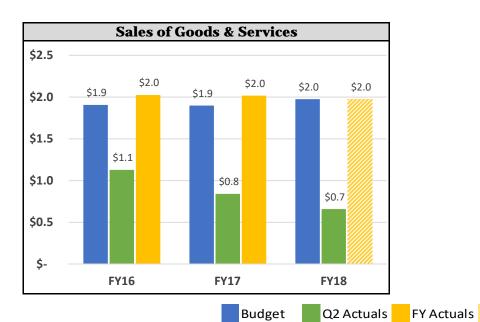

Projection


Investment Performance




University of North Texas System Consolidated Investment Portfolio

Investment Portfolio						
For the Quarter Ending February 28, 2018	Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
	Market Value	Market Value	Book Value	Interest	Yield*	Yield*
Short-Term Pool (STP) Investment Pool						
- Demand Deposit	\$ 10,130,490	\$ 8,455,457	\$ 8,455,457	\$ -	0.62%	0.65%
- Overnight Repurchase	1,820,441	1,331,746	1,331,746	-	0.09%	0.08%
- Demand Deposit Business Rate	17,178,469	7,704,947	7,704,947	-	1.21%	1.16%
- TexPool - Texas LGIP	972,933	6,948,289	6,948,289	-	1.27%	1.15%
- TexStar - Cash Reserve Fund	17,755,114	6,321,889	6,321,889	-	1.27%	1.16%
- TexasTerm - TexasDaily	16,627,451	6,916,639	6,916,639	-	1.31%	1.18%
- Invesco G&A Inst #9925	-	4,343,949	4,343,949	-	1.19%	1.19%
- Morgan Stanley Prime MM Fund #8301	9,048,052	14,407,395	14,407,395	-	1.46%	1.34%
- Fidelity Prime MM Fund #2014	18,154,644	28,227,370	28,227,370	12,641	1.45%	1.34%
- Wells Fargo Heritage Select MM Fund #3801	9,347,803	18,334,829	18,334,829		1.47%	1.36%
- JPMorgan Prime MM Fund #3605	823,437	3,963,419	3,963,419	-	1.42%	1.32%
- Federated Prime MM Fund #58	7,584,821	12,806,559	12,806,559	-	1.45%	1.36%
- Federated Prime MM Fund #10	-	14,715,749	14,715,749	15,749	1.44%	1.31%
- BlackRock Tmp Fund 24	98,720	10,206,806	10,206,806	12,525	1.49%	1.31%
- JPM Gov't Fund 3915	676,088	1,731,593	1,731,593	2,718	1.12%	1.01%
<u>Total STP Investment Pool</u>	\$ 110,218,462	\$ 146,416,635	\$ 146,416,635	\$ 43,633	1.27%	1.19%
Intermediate Investment Pool (IIP)						
- Fannie Mae 1.25% Bond (matures 7/26/2019)	4,974,575	4,930,450	5,006,250	6,250	1.25%	1.25%
- Fannie Mae 1.125% Bond (matures 7/26/2019)	4,213,269	4,185,081	4,253,591	4,781	1.15%	1.15%
- Fed Farm Cr Bank 1.67% Bond (matures 6/22/2020)	4,985,979	4,919,154	5,013,888	36,879	1.69%	1.69%
- Vanguard S-T Corp. Bond Fund (VSTBX)	33,824,724	33,599,290	34,193,748	-	2.68%	2.47%
- Vanguard S-T Inv. Grade Bond Fund (VFSIX)	26,352,534	26,185,876	26,583,751		2.62%	2.38%
- Vanguard S-T Gov't. Bond Fund (VSBIX)	5,008,971	4,990,529	5,063,755	-	1.98%	1.74%
Total Intermediate Investment Pool	\$ 79,360,053	\$ 78,810,381	\$ 80,114,984	\$ 47,910	2.38%	2.19%
Debt Proceeds Investment Pool						
- TexasTerm - 2015A - TexasDaily	954,855	957,956	957,956	-	1.31%	1.18%
- TexasTerm - CP Proceeds - TexasDaily	807,330	7,646,590	7,646,590	-	1.31%	1.18%
- TexasTerm - CP Proceeds - Term CP (matures 12/26/2017)	10,838,754	-	-	-	1.23%	1.23%
- TexStar CP Proceeds- Cash Reserve Fund	3,507,106	3,518,101	3,518,101	-	1.27%	1.16%
- Fed Home LMC 1.45% Bond (matures 4/26/2019)	3,239,209	3,241,143	3,265,426	16,363	1.48%	1.48%
- Fed Home LMC 1.40% Bond (matures 4/26/2019)	4,980,156	4,983,306	5,023,441	24,306	1.42%	1.42%
- TexasTerm - 2017 A&B Bond Proceeds - Texas Daily	22,527,014	47,351,649	47,351,649	-	1.32%	1.18%
- TexasTerm - 2017 A&B Bond Proceeds - Term CP	147,726,516	112,225,838	112,225,838	687,751	1.39%	1.34%
<u>Total Debt Proceeds Pool</u>	194,580,938	179,924,581	179,989,000	728,420	1.37%	1.29%
Total Cash & Investment Pools	\$ 384,159,453	\$ 405,151,598	\$ 406,520,619	\$ 819,963	1.53%	1.41%
	Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
	Market Value	Market Value	Book Value	Interest	Return*	Return*
Long-Term Investments	market value	THAT NOT TAILE	Doon Talue	c.csc	11000111	11000111
Long-Term Investment Pool	154,820,421	155,928,705	133,670,023		1.58%	5.80%
UNT and UNT Dallas Endowments	53,362,703	54,106,090	41,691,771	_	1.31%	5.27%
HSC Malpractice Fund	11,428,409	11,412,683	11,283,664	_	-0.13%	1.10%
HSC Endowment Pool	4,515,763	4,569,340	4,668,904	_	1.04%	5.38%
HSC TEF Endowment Fund	28,721,761	28,998,038	26,651,160	_	1.04%	5.30%
Total Long-Term Investments	252,849,057	255,014,855	217,965,522	-	1.37%	5.41%
				4	2.07,0	31.12/0
<u>Total UNTS Investments</u>	\$ 637,008,511	\$ 660,166,453	\$ 624,486,141	\$ 819,963		
Other Investments						
Foundation Investments - *not assets of the System	135,602,311	151,449,793	134,083,673	-	1.24%	5.29%
Total UNTS and Other Investments	\$ 772,610,822	\$ 811,616,247	\$ 758,569,814	\$ 819,963		

University of North Texas System Consolidated Investment Portfolio Market Values - 2/28/2018

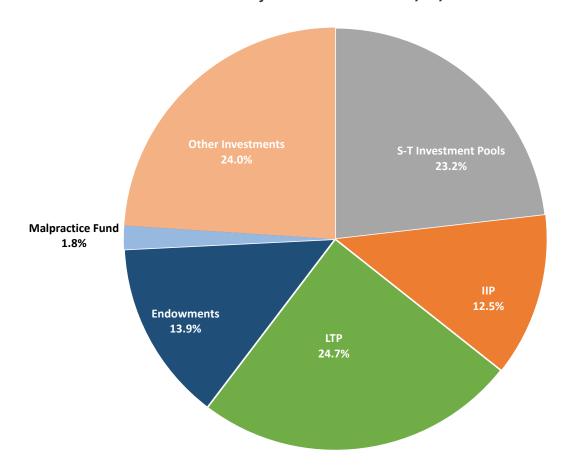



Investment			Policy
Туре	Market Value	Allocation %	Range %
STP	146,416,635	38.4%	10 - 20%
IIP	78,810,381	20.7%	20 - 60%
LTP	155,928,705	40.9%	25 - 60%
Total	381,155,722	100.0%	

^{*} The LTP Benchmarks are calculated using the revised Investment Policy as of May 2017



University of North Texas

University of North Texas Health Science Center

University of North Texas at Dallas

The attached report represents the investment portfolio of the University of North Texas for the period ending February 28, 2018, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.

Bob Brown
Robert E. Brown, CPA
Vice President for Finance and Administration, University of North Texas
5/5/18
Date
James Mauldin Digitally signed by James Mauldin, o=UNT System, ou=Office of the Vice Chancellor for Finance, email-james, mauldin@untsystem.edu, c=US Date: 2018/508/508140/9919-05'00'
James Mauldin, CPA, CTP
Associate Vice Chancellor for Treasury, University of North Texas System
Date

University of North Texas Investment Portfolio

For the Quarter Ending February 28, 2018

Short-Term Pool (STP) Investment Pool

- Demand Deposit
- Overnight Repurchase
- Demand Deposit Business Rate
- TexPool Texas LGIP
- TexStar Cash Reserve Fund
- TexasTerm TexasDaily
- Morgan Stanley Prime MM Fund #8301
- Fidelity Prime MM Fund #2014
- Wells Fargo Heritage Sel MM Fund #3801
- JPMorgan Prime MM Fund #3605
- Federated Inst MM Fund #58
- Invesco G&A Inst #9925

Total STP Investment Pool

Intermediate Investment Pool (IIP)

- Fannie Mae 1.25% Bond (matures 7/26/2019)
- Fannie Mae 1.125% Bond (matures 7/26/2019)
- Vanguard S-T Corp. Bond Fund (VSTBX)
- Vanguard S-T Inv. Grade Bond Fund (VFSIX)
- Vanguard S-T Gov't. Bond Fund (VSBIX)

Total Intermediate Investment Pool

Debt Proceeds Pool

- TexasTerm 2015A TexasDaily
- TexasTerm CP Proceeds TexasDaily
- TexasTerm CP Proceeds Term CP (matures 12/26/2017)
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Texas Daily
- TexasTerm 2017 A&B Bond Proceeds Term CP

Total Debt Proceeds Pool

Total STP, IIP and Debt Pools

Long-Term Investment Accounts

UNT Long Term Investment Pool UNT Endowment

Total Long-Term Investments

Total UNT Investments

Other Investments for the Benefit of UNT


UNT Foundation Fund - *not an asset of UNT

Total UNT and Other Investments

Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
Market Value	Market Value	Book Value	Interest	Yield*	Yield*
\$ 2,500,000	\$ 2,251,939	\$ 2,251,939	\$ -	1.00% **	1.00%
312,485			-	0.09%	0.08%
17,178,469	7,704,947	7,704,947	-	1.21%	1.16%
193,738	1,698,127	1,698,127	-	1.27%	1.15%
619,840	1,624,409	1,624,409	-	1.27%	1.16%
2,708,784	964,512	964,512	-	1.31%	1.18%
9,048,052	14,407,395	14,407,395	-	1.46%	1.34%
8,144,580	15,118,928	15,118,928	-	1.45%	1.34%
9,347,803	18,334,829	18,334,829	-	1.47%	1.36%
823,437	3,963,419	3,963,419	-	1.42%	1.32%
7,584,821	12,806,559	12,806,559	-	1.45%	1.36%
, , , <u>-</u> ,	4,343,949	4,343,949	-	1.19%	1.19%
\$ 58,462,009	\$ 83,219,014	\$ 83,219,014	\$ -	1.35%	1.25%
ć 4074 F7F	ć 4.020.4E0	ć F 000 350	ć C 250	1.250/	1.250/
\$ 4,974,575	\$ 4,930,450	\$ 5,006,250	\$ 6,250	1.25%	1.25%
4,213,269	4,185,081	4,253,591	4,781	1.15%	1.15%
17,709,534	17,591,273	17,884,476	-	2.68%	2.47% 2.38%
17,583,530 5,008,971	17,472,437 4,990,529	17,730,089	-	2.62% 1.98%	1.74%
\$ 49,489,879	\$ 49,169,770	5,063,755 \$ 49,938,161	\$ 11,031	2.31%	2.11%
\$ 43,403,073	\$ 49,109,770	\$ 49,938,101	\$ 11,031	2.31/0	2.11/0
\$ 954,855	\$ 957,956	\$ 957,956	\$ -	1.31%	1.18%
289,222	4,336,348	4,336,348	-	1.31%	1.18%
4,033,025	-	-	-	1.23%	1.23%
866,165	866,682	873,206	4,376	1.48%	1.48%
1,331,694	1,332,536	1,343,316	6,500	1.42%	1.42%
8,479,747	9,419,410	9,419,410	-	1.32%	1.18%
42,334,261	30,989,457	30,989,457	184,573	1.39%	1.34%
\$ 58,288,968	\$ 47,902,389	\$ 47,919,692	\$ 195,448	1.37%	1.26%
\$ 166,240,856	\$ 180,291,173	\$ 181,076,867	\$ 206,479	1.61%	1.43%
Beginning	Ending	Ending	Accrued	QTR Approx.	YTD Approx.
Market Value	Market Value	Book Value	Interest	Return*	Return*
\$ 106,939,796	\$ 107,705,337	\$ 91,500,000	\$ -	1.58%	5.80%
52,443,172	53,183,332	40,953,745	-	1.31%	5.27%
\$ 159,382,968	\$ 160,888,669	\$ 132,453,745	\$ -	1.49%	5.63%
\$ 325,623,824	\$ 341,179,842	\$ 313,530,612	\$ 206,479		
,	, .,		, , , , , ,		
400 0	404				
120,074,234	131,909,639	116,005,600	-	1.31%	5.27%

 $[\]ensuremath{^{*}}$ Yield is reported as an annual figure, Return is reported for the current period

University of North Texas Investment Portfolio Market Values - 2/28/2018
* Excludes Debt Proceeds



^{**} Earnings Allowance Rate up to the amount of bank fees incurred during period

University of North Texas

University of North Texas Health Science Center

University of North Texas at Dallas

The attached report represents the investment portfolio of the University of North Texas Health Science Center for the period ending February 28, 2018, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.

Therony R. A
Gregory R Anderson, CPA
Executive VP for Finance and Chief Financial Officer, UNT Health Science Center
May 8, 2018 Date
James Mauldin DN: cn=James Mauldin, 0=UNT System, ou=Office of the Vice Chancellor for Finance, email=james.mauldin@untsystem.edu, c=US Date: 2018.05.09 14:26:51-05'00'
James Mauldin, CPA, CTP
Associate Vice Chancellor for Treasury, University of North Texas System
Date

University of North Texas Health Science Center Investment Portfolio

For the Quarter Ending February 28, 2018

	Short-Term Pool	(STP) Investment Pool
--	-----------------	------	-------------------

- Demand Deposit
- TexasTerm TexasDaily
- TexStar Cash Reserve Fund
- JPM Govt MMF 3915
- BlackRock Temp MMF 24
- Federated Prime MMF 10
- Fidelity Prime MMF 2014

Total STP Investment Pool

Intermediate Investment Pool (IIP)

- Vanguard S-T Corp. Bond Fund (VSTBX)
- Vanguard S-T Inv. Grade Bond Fund (VFSIX)
- Fed Farm Cr Bank 1.67% Bond (matures 6/22/2020)

Total Intermediate Investment Pool

Debt Proceeds

- TexasTerm CP Proceeds TexasDaily
- TexasTerm CP Proceeds Term CP (matures 12/26/2017)
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Texas Daily
- TexasTerm 2017 A&B Bond Proceeds Term CP

Total Debt Proceeds

Total STP, IIP & Debt Pools

Long-Term Investments

HSC Long Term Investment Pool

HSC Malpractice Fund

HSC Endowment Pool

HSC TEF Endowment Fund

Total Long-Term Investments

Total HSC Investment Portfolio

Total HSC and Other Investments

Other Investments

HSC Foundation - * not an asset of HSC

QTR Approx. Beginning Ending Ending Accrued YTD Approx Market Value Market Value Book Value Interest Yield* Yield* 6,630,490 5,494,380 5,494,380 0.50% 0.50% 10,957,635 3,080,128 3,080,128 1.31% 1.18% 13,250,347 214.907 214,907 1.27% 1.16% 676,088 1,731,593 1,731,593 2,718 1.12% 1.01% 10,206,806 1.49% 1.31% 98,720 10,206,806 12,525 14,715,749 14,715,749 15,749 1.44% 1.31% 10,010,064 13,108,442 13,108,442 12,641 1.44% 1.35% 48,552,006 48,552,006 1.13% 1.08% 41,623,344 Ś 43,633 16,115,190 16,008,018 16,309,272 2.68% 2.47% \$ \$ \$ 8,769,004 2.38% 8,713,439 8,853,662 2.62% 36,879 4,985,979 4,919,154 5,013,888 1.69% 1.69% 29,870,173 29,640,611 \$ 30,176,822 \$ 36,879 2.50% 2.31% Ś 243,398 Ś 1.33% 1.19% 3,780,961 1.23% 1.23% 902,444 902,982 909,673 4,558 1.48% 1.48% 1,387,471 1,388,348 1,399,416 6,771 1.42% 1.42% 614,999 4,901,158 4,901,158 1.33% 1.14% 19,410,942 8,627,885 114.180 1.36% 1.29% 8,627,885 26,340,214 \$ 15,820,373 \$ 15,838,132 125,509 1.34% 1.27% 97,833,732 94,012,990 94,566,959 206,021 1.62% 1.48% Beginning Ending Ending Accrued QTR Approx. YTD Approx Market Value Book Value Market Value Return* Interest Return* 35,671,710 35,927,059 31,400,000 5.80% \$ 1.58% 11,428,409 11,412,683 11,283,664 -0.13% 1.10% 4,515,763 4,569,340 4,668,904 5.38% 1.04% 28,721,761 28,998,038 26,651,160 1.04% 5.30% 80,337,643 80,907,119 74,003,728 1.12% 4.93% 178,171,374 174,920,109 \$ 168,570,687 \$ 206,021 19,081,797 15,272,615 17,619,716 0.81% 4.92%


186,190,403

206,021

^{*} Yield is reported as an annual figure, Return is reported for the current period



193,443,989



194,001,907

^{**} Earnings Allowance Rate up to the amount of bank fees incurred during period

University of North Texas

University of North Texas Health Science Center

University of North Texas at Dallas

The attached report represents the investment portfolio of the University of North Texas at Dallas for the period ending February 28, 2018, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.



Digitally signed by April Barnes
DN: cn=April Barnes, o=UNT Dallas, ou=Finance &
Admin, email=April.Barnes@untdallas.edu, c=US
Date: 2018 05 04 11:01:59 -05:00'

April Barnes, CPA

Associate Vice President for Finance and Administration, University of North Texas at Dallas

May 4, 2018

Date

James Mauldin

Digitally signed by James Mauldin
DN: cn=James Mauldin, o=UNT System, ou=Office of the Vice
Chancellor for Finance, email=james.mauldin@untsystem.edu, c=US
Date: 2018.05.08 14:11:09 -05'00'

James Mauldin, CPA, CTP

Associate Vice Chancellor for Treasury, University of North Texas System

Date

University of North Texas at Dallas Investment Portfolio

For the Quarter Ending February 28, 2018

Short-Term Pool (STP) Investment Pool

- Demand Deposit
- Overnight Repurchase
- TexPool Texas LGIP
- TexStar Cash Reserve Fund

Total STP Investment Pools

Debt Proceeds

- TexStar CP Proceeds- Cash Reserve Fund
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Daily Fund
- TexasTerm 2017 A&B Bond Proceeds Term CP

Total Debt Proceeds Pool

Total STP, IIP & Debt Pools

Long-Term Investments

UNTD Long Term Investment Pool UNTD Endowment

Total Long-Term Investments

Total UNT Dallas Investment Portfolio


Other Investments

Dallas Foundation Fund - *not an asset of UNTD

Total UNT Dallas and Other Investments

	Yield* 1.00% **	Yield*
\$ 500,000 \$ 209,137 \$ 209,137 \$ -	1.00% **	
\$ 500,000 \$ 209,137 \$ 209,137 \$ -	1.00% **	
		1.00%
65,014	0.08%	0.08%
779,195 5,250,162 5,250,162 -	1.27%	1.15%
1,608,178 3,016,261 3,016,261 -	1.27%	1.16%
\$ 2,952,387 \$ 8,475,559 \$ 8,475,559 \$ -	1.24%	1.13%
3,507,106 3,518,101 3,518,101 -	1.27%	1.16%
	1.48%	1.48%
	1.42%	1.42%
	1.32%	1.42%
	1.40%	
1,111,111		1.35%
\$ 59,056,990 \$ 55,812,246 \$ 55,827,795 \$ 211,651	1.38%	1.32%
Ć C2 000 277 Ć C4 207 00F Ć C4 202 2FF Ć 244 CF4	1.270/	1.200/
\$ 62,009,377 \$ 64,287,805 \$ 64,303,355 \$ 211,651	1.37%	1.30%
		V== 4
	R Approx.	YTD Approx.
Market Value Market Value Book Value Interest R	Return*	Return*
1 3, 23, 2	1.58%	5.80%
	1.27%	5.20%
\$ 7,126,045 \$ 7,173,700 \$ 6,234,818 \$ -	1.54%	5.72%
\$ 69,135,423 \$71,461,506 \$70,538,173 \$211,651		
255,463 458,357 458,357 -		
\$ 69,390,886 \$ 71,919,862 \$ 70,996,530 \$ 211,651		

^{*} Yield is reported as an annual figure, Return is reported for the current period



 $[\]ensuremath{^{**}}$ Earnings Allowance Rate up to the amount of bank fees incurred during period



University of North Texas

University of North Texas Health Science Center

University of North Texas at Dallas

The attached report represents the investment portfolio of the University of North Texas System Administration for the period ending February 28, 2018, and is in compliance with Chapter 2256 of the Public Funds Investment Act and the Investment Strategy expressed in the UNT System's Investment Policy.



Digitally signed by James Mauldin DN: cn=James Mauldin, o=UNT System, email=james.mauldin@untsystem.edu, c=US Date: 2018.05.08 14:16:59 -05'00'

James Mauldin, CPA, CTP

Associate Vice Chancellor for Treasury, University of North Texas System

Gary Rahli	Digitally signed by Gary Rahlfs DN: cn=Gary Rahlfs, o=UNT System, ou=Vice Chancellor for Finance, email=gary.rahlfs@untsystem.edu, c=US Date: 2018.05.04 17:04:41 -05'00'
Gary Rahlfs Vice Chancellor for Finance,	University of North Texas System
Date	

For the Quarter Ending February 28, 2018

Short-Term Pool (STP) Investment Pool

- Demand Deposit
- Overnight Repurchase
- TexStar Cash Reserve Fund
- TexasTerm TexasDaily

Total STP Investment Pool

Debt Proceeds

- TexasTerm CP Proceeds TexasDaily
- TexasTerm CP Proceeds Term CP (matures 12/26/2017)
- Fed Home LMC 1.45% Bond (matures 4/26/2019)
- Fed Home LMC 1.40% Bond (matures 4/26/2019)
- TexasTerm 2017 A&B Bond Proceeds Texas Daily
- TexasTerm 2017 A&B Bond Proceeds Term CP

Total Debt Proceeds

Total STP and Debt Pools

Long-Term Investments

UNT Long Term Investment Pool

Total Long-Term Investments

Total SYS Investments

\$	500,000	\$	500,000	\$	500,000	\$	-	1.00%	**	1.00%
	1,442,942		1,331,746		1,331,746		-	0.09%		0.09%
	2,276,749		1,466,312		1,466,312		-	1.27%		1.16%
	2,961,032		2,871,999		2,871,999		-	1.31%		1.18%
\$	7,180,723	\$	6,170,057	\$	6,170,057	\$	-	1.24%		1.13%
\$	274,710	\$	3,310,242	\$	3,310,242	\$	_	1.31%		1.18%
	3,024,768		-		-		-	1.23%		1.23%
	691,247		691,660		696,866		3,492	1.48%		1.48%
	1,062,765		1,063,438		1,072,039		5,187	1.42%		1.42%
	3,545,055		17,064,885		17,064,885		-	1.33%		1.22%
	42,296,220		27,476,291		27,476,291		187,133	1.38%		1.34%
\$	50,894,766	\$	49,606,516	\$	49,620,323	\$	195,812	1.37%		1.33%
\$	58,075,489	\$	55,776,573	\$	55,790,380	\$	195,812	1.36%		1.30%
	Beginning		Ending		Ending			QTR Approx.		YTD Approx.
М	arket Value	V	arket Value		Book Value			Return*		Return*
\$	6,002,400	\$	6,045,367	\$	5,273,231	\$	-	1.58%		5.80%
\$	6,002,400	\$	6,045,367	\$	5,273,231	\$	-	1.58%		5.80%
\$	64,077,889	\$	61,821,940	\$	61,063,612	\$	195,812			

Ending

Book Value

Accrued

Interest

QTR Approx.

Yield*

YTD Approx.

Yield*

University of North Texas System Investment Portfolio Market Values - 2/28/2018


* Excludes Debt Proceeds

Beginning

Market Value

Ending

Market Value



 $[\]ensuremath{^{*}}$ Yield is reported as an annual figure, Return is reported for the current period

 $[\]ensuremath{^{**}}$ Earnings Allowance Rate up to the amount of bank fees incurred during period

Capital Improvement Plan Status



UNT System FY 2018 Capital Improvement Plan Status

May 2018 (Report as of April 6, 2018)

UNT | SYSTEM[®]

Project Budget Status

Revised 5/14/2018

											. 5/11/2010
Project Management											Remaining
Responsibility	Camp.	Project No.	Project Name		proved Budget		Expensed		ncumbered		Balance
OFPC	UNT	16-1.20	College of Visual Arts and Design	\$	70,000,000	\$	27,513,253	\$	35,359,293	\$	7,127,454
		16-1.84a	New Residence Hall - Phase 1	\$	58,900,000	\$	10,258,062	\$	43,041,070	\$	5,600,868
		16-2.66	Coliseum Concourse Renovation	\$	8,000,000	\$	5,372,848	\$	2,206,283	\$	420,868
		16-2.67	1500 I-35E Building	\$	12,500,000	\$	986,915	\$	4,249,192	\$	7,263,893
		16-2.82	Track and Field Stadium	\$	13,590,000	\$	3,692,766	\$	9,086,391	\$	810,843
		17-01-0005	Discovery Park Bio-Medical Engineering Addition	\$	17,400,000	\$	885,252	\$	528,988	\$	15,985,760
		17-01-0010	New Classroom Building	\$	25,100,000	\$	25,000	\$	-	\$	25,075,000
		17-01-0011	Hickory Hall Renovation	\$	8,800,000	\$	-	\$	-	\$	8,800,000
		18-01-0004	Art Building Roof Replacement	\$	1,350,000	\$	-	\$	30,630	\$	1,319,370
		18-01-0007	New Dining Hall	\$	25,470,000	\$	562,516	\$	1,755,790	\$	23,151,694
		18-01-0008	Fouts Field Demolition, Parking, and Bus Transfer Station	\$	14,000,000	\$	138,763	\$	793,881	\$	13,067,356
		18-01-0009	New Athletics Indoor Practice Facility	\$	18,900,000	\$	530,639	\$	576,816	\$	17,792,545
	UNTD	16-1.01	Student Learning and Success Center	\$	63,000,000	\$	12,817,062	\$	40,792,379	\$	9,390,558
	HSC	16-1.40	Interdisciplinary Research Building	\$	118,500,000	\$	73,226,383	\$	33,675,573	\$	11,598,044
		16-2.96	Research and Education (RES) Level 4	\$	4,500,000	\$	3,600	\$	-	\$	4,496,400
		17-03-0002	Medical Clinic	\$	4,200,000	\$	-	\$	-	\$	4,200,000
	System	16-2.01	Renovate Dallas Municipal Building and Associated Law Buildings	\$	56,000,000	\$	14,548,234	\$	29,773,359	\$	11,678,407
UNT Facilities	UNT	2.20	Matthews Hall MEP	\$	1,200,000	\$	241,417	\$	69,000	\$	889,583
		2.21	Wooten Hall MEP	\$	3,450,000	\$	1,020,196	\$	145,978	\$	2,283,826
		2.33	Willis Library MEP	\$	9,850,000	\$	473,024	\$	89,420	\$	9,287,556
		2.34	Hickory Hall MEP	\$	3,000,000	\$	2,911,825	\$	85,518	\$	2,657
		16-2.25	General Academic Building MEP and Interior Renovation	\$	10,350,000	\$	-	\$	623,041	\$	9,726,959
		16-2.50	Life Science Lab Exhaust Upgrade	\$	5,950,000	\$	-	\$	190,750	\$	3,009,250
		16-2.55	Discovery Park MEP Upgrade	\$	20,600,000	\$	-	\$	285,000	\$	20,315,000
		16-2.77	Wooten Hall Code Upgrade	\$	4,760,000	\$	138,370	\$	45,877	\$	4,045,753
		16-2.85	Sage Hall Academic Success Center	\$	1,850,000	\$	1,582,110	\$	120,642	\$	147,248
		17-01-0001	Terrill Hall MEP & Interior Renovation	\$	7,300,000	\$	-	\$	-	\$	7,300,000
		17-01-0002	Coliseum MEP Renovation	\$	10,400,000	\$		\$		\$	10,400,000
		17-01-0003	Kerr Hall MEP & Interior Renovation	Ś	5,790,000	Ś	2,780,240	Ś	9,550	Ś	3,000,210
		17-01-0004	USB MEP Renovation	\$	3,600,000	\$	_,,	\$	350,000	\$	3,250,000
		17-01-0006	Sage Hall Academic Success Center Phase	\$	2,920,000	\$	106,755	\$	2,094,526	\$	718,719
		17-01-0007	Life Science Building 4th Floor Laboratories Renovation	\$	7,000,000	\$	-	\$	-	\$	7,000,000
		17-01-0008	Coliseum Roof Replacement	\$	2,430,000	\$	-	\$	-	\$	2,430,000
		17-01-0009	Off-Site Campus #2	\$	1,500,000	\$	-	\$	-	\$	1,500,000
		17-01-0012	Eagle Point Parking Lot #80	\$	2,200,000	\$	84,114	\$	2,018,142	\$	97,744
		18-01-0001	Maple Hall MEP & Renovation	\$	4,380,000	\$	-	\$	-	\$	4,380,000
		18-01-0002	Clark Hall Lobby Renovation	\$	2,270,000	\$	-	\$	154,774	\$	2,115,226
		18-01-0003	Sage Hall Academic Success Center Phase	\$	3,010,000	\$	-	\$	239,000	\$	2,771,000
		18-01-0005	Discovery Park Utility Capacity Upgrade	\$	2,000,000	\$	61,750	\$	1,415,933	\$	522,317
		18-01-0006	Music Building Courtyard Renovation	\$	2,590,000	\$	87,503	\$	-	\$	2,502,497
HSC Facilities	HSC	17-03-0001	East Parking Garage Renovation	\$	6,000,000	\$	-	\$	-	\$	6,000,000
		18-03-0001	Gross Anatomy Laboratory Renovation	\$	2,470,000	\$	-	\$	-	\$	2,470,000
		18-03-0002	1408 St. Louis Ave. Renovation	\$	1,950,000	\$	1,948,050	\$	-	\$	1,950

May 2018 (Report as of April 6, 2018)

UNT | SYSTEM

Project Overview

Revised 5/14/2018

		<u> </u>		TC VISCO	3/14/2010
Project Management Responsibility	Project No.	Project Name	Scope	Schedule	Budget
OFPC	16-1.01	Student Learning and Success Center	Эсорс	Scrieduic	Dauget
0110	16-1.20	College of Visual Arts and Design			
	16-1.84a	New Residence Hall - Phase 1			
	16-1.40	Interdisciplinary Research Building			
	16-2.01	Renovate Dallas Municipal Building and Associated Law Buildings			
	16-2.66	Coliseum Concourse Renovation			
	16-2.67	1500 I-35E Building			
	16-2.82	Track and Field Stadium			
	16-2.96	Research and Education (RES) Level 4			
	17-01-0005	Discovery Park Bio-Medical Engineering Addition			
		New Classroom Building			
	17-01-0010	Hickory Hall Renovation			
		Medical Clinic			
	18-01-0004	Art Building Roof Replacement			
		New Dining Hall			
	18-01-0007	Fouts Field Demolition, Parking, and Bus Transfer Station			
	18-01-0009	New Athletics Indoor Practice Facility			
UNT Facilities	2.20	Matthews Hall MEP			
OIVI I acilities	2.21	Wooten Hall MEP			
	2.33	Willis Library MEP			
	2.34	Hickory Hall MEP			
	16-2.25	General Academic Building MEP and Interior Renovation			
	16-2.50	Life Science Lab Exhaust Upgrade			
	16-2.55	Discovery Park MEP Upgrade			
	16-2.77	Wooten Hall Code Upgrade			
	16-2.85	Sage Hall Academic Success Center			
	17-01-0001	Terrill Hall MEP & Interior Renovation			
		Coliseum MEP Renovation			
		Kerr Hall MEP & Interior Renovation			
		USB MEP Renovation			
		Sage Hall Academic Success Center Phase II			
	17-01-0007	Life Science Building 4th Floor Laboratories Renovation			
	17-01-0008	Coliseum Roof Replacement			
	17-01-0009	Off-Site Campus #2			
	18-01-0012	Maple Hall MEP & Renovation			
	18-01-0002	Clark Hall Lobby Renovation			
	18-01-0002	Sage Hall Academic Success Center Phase III			
	18-01-0005	Discovery Park Utility Capacity Upgrade			
	18-01-0006	Music Building Courtyard Renovation			
HSC Facilities	17-03-0001	East Parking Garage Renovation			
rise raciilles	18-03-0001	Gross Anatomy Laboratory Renovation			
	18-03-0001	1408 St. Louis Ave. Renovation			
	10-03-0002	1400 Jt. Louis Ave. Reliuvation			

- No change from previous project update
- Minor Adjustment from previous project update
- Substantial change from previous project update
- Project On-Hold / Cancelled

FY2018 SUMMARY (in \$Million)

UNT | SYSTEM

		Funding	Prior Yrs						Total
Proj. No. Projec	t	Source	Budget	2018	2019	2020	2021	2022+	Projec
Jniversity of North	Texas								
18-01-0001 Maple	Hall MEP & Renovation	AUX		4.38					4.3
18-01-0002 Clark H	Hall Lobby Renovation	AUX		0.17	2.10				2.2
18-01-0003 Sage H	Hall Academic Success Center Phase III	HEAF		0.26	2.75				3.0
18-01-0004 Art Bui	Iding Roof Replacement	CP		1.35					1.3
	ery Park Utility Capacity Upgrade	HEAF		2.00					2.0
18-01-0006 Music I	Building Courtyard Renovation	HEAF	0.09	1.50					
		GIFT			1.00				2.5
18-01-0007 New Di	ining Hall	RFS	0.20	3.50	15.28	6.49			25.4
8-01-0008 Fouts F	Field Demolition, Parking, and Bus Transfer Station	RFS		2.00	12.00				14.0
18-01-0009 Athletic	Indoor Practice Facility	RFS		1.50	9.90				
		GIFT			7.50				18.9
	University of No	rth Texas Total	0.29	16.66	50.53	6.49	-	•	73.9
Iniversity of North	Texas Dallas								
	University of North Tex	as Dallas Total	-	-	-	-	-	-	-
University of North	Texas Health Science Center								
18-03-0001 Gross	Anatomy Laboratory Renovation	RFS		2.47					2.4
18-03-0002 1408 S	t. Louis Ave. Renovation	HEAF	0.30	1.65					1.9
	University of North Texas Health Scien	ce Center Total	0.30	4.12	-	-	-	-	4.4
Iniversity of North	Texas System								
	University of North Texa	. 0 . 11 T. 111							1 -

y Funding Source								
	Funding	Prior Yrs						
	Source	Budget	2017	2018	2019	2020	2021+	Total
HEAF	HEAF	0.39	5.41	2.75	-	-	-	8.5
HEAF Reserve	HEAF Reserve	-		-	-	-	-	-
Tuition Revenue Bonds	TRB	-	-	-	-	-	-	-
Commercial Paper	CP	-	1.35	-	-	-	-	1.35
Private Placement	PP	-	-	-	-	-	-	-
Revenue Bonds	RB	-	-	-	-	-	-	-
Revenue Financing System Bonds	RFS	0.20	9.47	37.18	6.49	-	-	53.34
Auxiliary Reserves	AUX	-	4.55	2.10	-	-	-	6.65
Grants	GRNT	-	-	-	-	-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	8.50	-	-	-	8.50
Annual Budget, Operating and Capital	Local/Cash	-	-	-	-	-	-	-

Total

0.59

20.78

50.53

6.49

78.39

UNIVERSITY OF NORTH TOPP

FY18 (in \$Million)

University	of North Texas	,	,						
			Prior Yrs						Total
Proj. No.	•	Funding Source	Budget	2018	2019	2020	2021	2022+	Project
	Approved Projects:					1	ı		
2.20	Matthews Hall MEP (Amended)	HEAF	1.20						1.20
2.21	Wooten Hall MEP (Amended)	HEAF	3.45						3.45
2.33	Willis Library MEP (Amended)	HEAF	5.16	4.69					9.85
2.34	Hickory Hall MEP	HEAF	3.00						3.00
16-1.20	College of Visual Arts and Design	TRB	27.00	38.00	5.00				70.00
16-1.84	New Residence Hall								
16-1.84a	New Residence Hall - Phase 1 (Amended)	RFS	17.04	28.68	13.18				58.90
16-2.25	General Academic Building MEP & Interior Renovation	HEAF	0.75						
	(Amended)	RFS			9.60				10.35
16-2.50	Life Science Lab Exhaust Upgrade (Amended)	HEAF	3.20	2.75					5.95
16-2.55	Discovery Park MEP Upgrade (Amended)	HEAF		1.00	9.00	10.00	0.60		20.60
16-2.62a	Maple Common Area Renovation	AUX	1.65	1.00	3.00	10.00	0.00		
16-2.65	Sycamore 2nd Floor Renovation (Amended)	HEAF	1.65						1.65
16-2.66	Coliseum Concourse Renovation		3.95	0.50					3.95
		RFS	5.50	2.50					8.00
16-2.67	1500 I-35 Building (Amended)	RFS	10.50	2.00					12.50
16-2.77	Wooten Hall Code Upgrade (Amended)	HEAF	2.07	2.69					4.76
16-2.82	Track and Field Stadium (Amended)	RFS	4.00	5.90	2.00				
		AUX			1.69				13.59
16-2.85	Sage Hall Academic Success Center	HEAF Reserve	1.85						1.85
17-01-0001	Terrill Hall MEP & Interior Renovation (Amended)	HEAF	0.55	0.25	6.50				7.30
17-01-0002	Coliseum MEP Renovation (Amended)	RFS	0.00	0.20	0.90	9.50			10.40
17-01-0003	Kerr Hall MEP & Interior Renovation (Amended)	I G			0.30	9.50			10.40
01 0000	Tron train MET a micror tenovation (vincinaea)	AUX	2.10	3.69					5.79
17-01-0004	USB MEP Renovation (Amended)	HEAF							
	Discovery Park Bio-Medical Engineering Addition	1	0.30	3.30					3.60
	Sage Hall Academic Success Center Phase II (Amended)	RFS	2.00	15.40					17.40
17-01-0006	Sage Hall Academic Success Center Phase II (Amended)	HEAF Reserve	0.17						
47.04.0007		HEAF		2.75					2.92
17-01-0007	Life Science Building 4th Floor Laboratories Renovation	DEO				0.70	0.00		7.00
17-01-0008	(Amended) Coliseum Roof Replacement (Amended)	RFS		2.42		0.70	6.30		7.00
		Local/Cash		2.43					2.43
17-01-0009	Off-Site Campus #2	Local/Cash	0.10	1.40					1.50
17-01-0010	New Classroom Building	RFS		2.20	22.90				25.10
17-01-0011	Hickory Hall Renovation	RFS		0.80	8.00				8.80
17-01-0012	Eagle Point Parking Lot #84	CP	2.20						2.20
	Previously Approv	ed Projects Total	97.74	120.43	78.77	20.20	6.90	-	324.04
	ts for Approval:								
	Maple Hall MEP & Renovation	AUX		4.38					4.38
	Clark Hall Lobby Renovation	AUX		0.17	2.10				2.27
	Sage Hall Academic Success Center Phase III	HEAF		0.26	2.75				3.01
	Art Building Roof Replacement Discovery Park Utility Capacity Upgrade	CP HEAF		1.35 2.00					1.35 2.00
	Music Building Courtyard Renovation	HEAF	0.09	1.50					2.00
10-01-0000	Industryal distribution	GIFT	0.03	1.00	1.00				2.59
18-01-0007	New Dining Hall	RFS	0.20	3.50	15.28	6.49			25.47
	Fouts Field Demolition, Parking, and Bus Transfer Station	RFS		2.00	12.00				14.00
18-01-0009	Athletic Indoor Practice Facility	RFS		1.50	9.90				
		GIFT			7.50				18.90
		or Approval Total	0.29	16.66	50.53	6.49	-	-	73.97
	pjects with Identified Funding Sources:	1				. == 1			
01-0010	Administration Building Renovation	HEAF				1.70	7.20	10.00	18.90
01-0011	Curry Hall MEP	HEAF			0.52	5.25			5.77
01-0012 01-0013	Underground Utility Repairs PAC Foundation Repairs	HEAF HEAF			0.28	2.73 0.20	1.95		3.01 2.15
01-0013	Physical Education Building (PEB) MEP & Interior	LIEAF				0.20	1.93		2.15
01-0014	Renovation	HEAF				1.75	17.35		19.10
	· ···					0			

FY18 (in \$Million)

UNT

NEVERBLY OF NORTH TERRE

Proj. No.	Project	Funding Source	Prior Yrs Budget	2018	2019	2020	2021	2022+	Total Project
01-0015	Language Building MEP	HEAF		2010	0.45	5.62			6.07
01-0016	Demo and Build New Business Svs Whse	AUX			0.40	0.02	1.25		1.25
01-0017	SRB MEP Renovation	HEAF			†	0.26	2.63		2.89
01-0018	RTFP MEP Renovation	HEAF			0.75	7.00			7.75
01-0019	Sage Hall Academic Success Center - Phase IV	HEAF			0.24	1.76			2.00
01-0020	Welch St Complex #2 Demolition	HEAF			1.50				1.50
01-0021	Chilton Classroom & Restrooms	HEAF			0.40	4.00			4.40
01-0022	Discovery Park Greenhouse Addition	RFS			3.00				3.00
01-0023	ESSC Envelope Upgrade	HEAF			7.80				7.80
01-0024	New Science & Tech Research Building	TRB				11.76	50.00	36.24	98.00
01-0025	Union Circle Drive Re-surface	AUX				2.00			2.00
01-0026	USB Interior Renovation	HEAF				0.25	2.50		2.75
	Planned Projects with Identified Fo	Inding Sources Total	-	-	14.94	44.28	82.88	46.24	188.34
Planned La	and Acquisitions								
3.01	Land Acquisitions per Master Plan	HEAF		1.00	1.50	1.50	1.50	1.50	7.00
		and Acquisition Total	-	1.00	1.50	1.50	1.50	1.50	7.00
	Capital Im	provement Plan Total	98.03	138.09	145.74	72.47	91.28	47.74	593.35

Planned Project without Identified Funding Sources

New Construction:

New Athletics Indoor Practice Facility New Sports Arena

Renovation:

Athletic Center Renovation and Expansion Music Building Renovations

Summary by Funding Source

		Prior Yrs						
	Funding Source	Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	23.72	22.19	31.69	42.02	33.73	11.50	164.85
HEAF Reserve	HEAF Reserve	2.02	-		-	-	-	2.02
Tuition Revenue Bonds	TRB	27.00	38.00	5.00	11.76	50.00	36.24	168.00
Commercial Paper	СР	2.20	1.35	-	-	-	-	3.55
Private Placement	PP	-	-	-	-	-	-	-
Revenue Bonds	RB	-	-	-	-	-	-	-
Revenue Financing System Bonds	RFS	39.24	64.48	96.76	16.69	6.30	-	223.47
Auxiliary Reserves	AUX	3.75	8.24	3.79	2.00	1.25	-	19.03
Grants	GRNT		-	-	-	-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	8.50	-	-	-	8.50
Annual Budget, Operating and Capital	Local/Cash	0.10	3.83	-	-	-	-	3.93
	Total	98.03	138.09	145.74	72.47	91.28	47.74	593.3



FY2018 (in \$Million)

U	Ini	vers	sity	of	N	ort	h T	exas	Dal	las
---	-----	------	------	----	---	-----	-----	------	-----	-----

			Prior Yrs						Total
Proj. No.	Project	Funding Source	Budget	2018	2019	2020	2021	2022+	Project
Previously	y Approved Projects:								
16-1.01	Student Learning and Success Center	TRB	16.00	33.40	13.60				63.00
16-1.04	Campus Infrastructure	HEAF	1.15						
		CP	0.50						1.65
1.03	Residence Hall (Amended)	RB	7.69						
		Local/Cash	0.81						8.50
	Previously Ap	proved Projects Total	26.15	33.40	13.60	-	-	-	73.15
New Proje	ects for Approval:								
	New Pro	ject for Approval Total	-	-	-	-	-	-	-
Planned P	Projects with Identified Funding Sources:								
	Planned Projects with Identified I	Funding Sources Total	-	-	-	-	-	-	-
Planned L	and Acquisitions								
									-
	Planned I	Land Acquisition Total	-	-	-	-	-	-	-
	Capital In	nprovement Plan Total	26.15	33.40	13.60	_	_	_	73.15

Planned Project without Identified Funding Sources

New Construction:

Landmark Tower

W Construction:
Second Residence Hall
STEM Building
Business Technology Building
Event Center
Parking Garage

Renovation:

Summary by Funding Source

		Prior Yrs						
	Funding Source	Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	1.15	-	-	-	-	-	1.15
HEAF Reserve	HEAF Reserve	-	-	-	-	-	-	
Tuition Revenue Bonds	TRB	16.00	33.40	13.60	-	-	-	63.00
Commercial Paper	СР	0.50	-	-	-	-	-	0.50
Private Placement	PP	-	-	-	=	-	-	-
Revenue Bonds	RB	7.69	-	-	-	-	-	7.69
Revenue Financing System Bonds	RFS	-	-	-	-	-	-	-
Auxiliary Reserves	AUX	-	-	-	-	-	-	-
Grants	GRNT	-	-	-	=	-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	-	-	-	-	-
Annual Budget, Operating and Capital	Local/Cash	0.81	-	-	-	-	-	0.81
	Total	26.15	33.40	13.60	-	-	-	73.15

Page 41 of 68

UNT HEALTH

138.62

FY2018 (in \$Million)

			Prior Yrs						Total
Proj. No.	Project	Funding Source	Budget	2018	2019	2020	2021	2022+	Project
Previously	Approved Projects:								
16-1.40	Interdisciplinary Research Building	TRB	35.70	44.30					
		RFS	8.23	12.57	16.70				
		GIFT			1.00				118.50
16-2.96	Research and Education (RES) Level 4	RFS	0.01		2.99	1.50			4.50
17-03-0001	East Parking Garage Renovation	RFS		0.40	5.60				6.00
17-03-0002	Medical Clinic (Amended)	RFS			1.00	3.20			4.20
Previously Approved Projects Total				57.27	27.29	4.70	-	-	133.20
New Projec	cts for Approval:								
18-03-0001	Gross Anatomy Laboratory Renovation	RFS		2.47					2.47
18-03-0002	1408 St. Louis Ave. Renovation	HEAF	0.30	1.65					1.95
	New Pr	oject for Approval Total	0.30	4.12	-	-	-	•	4.42
Planned Pr	rojects with Identified Funding Sources:								
	Planned Projects with Identified	Funding Sources Total	-	-	-	-	-	-	-
Planned La	and Acquisitions								
3.01	Property Acquisition	HEAF		1.00					1.00
	Planned	Land Acquisition Total	_	1.00	_	_			1.00

Capital Improvement Plan Total

Planned Project without Identified Funding Sources

New Construction:

Parking Garage

Renovation:

62.39

27.29

4.70

44.24

Summary by Funding Source

		Prior Yrs						
	Funding Source	Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	0.30	2.65	-	-	-	-	2.95
HEAF Reserve	HEAF Reserve	-	-	-	-	-	-	-
Tuition Revenue Bonds	TRB	35.70	44.30	-	-	-	-	80.00
Commercial Paper	CP	-	-	-	-	-	-	-
Private Placement	PP	-	-	-	-	-	-	-
Revenue Bonds	RB	=	-	-	-	-	=	-
Revenue Financing System Bonds	RFS	8.24	15.44	26.29	4.70	-	=	54.67
Auxiliary Reserves	AUX	-	-	-	-	-	-	-
Grants	GRNT	-	_	_	-	-	-	-
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	1.00	-	-	-	1.00
Annual Budget, Operating and Capital	Local/Cash	-	-	-	-	-	-	-
	Γotal	44.24	62.39	27.29	4.70	0.00	0.00	138.62

UNT | SYSTEM

FY2018 (in \$Million)

Proj. No.	· Project	Funding Source	Prior Yrs Budget	2018	2019	2020	2021	2022+	Total Project
Previous	sly Approved Projects:								
16-2.01	Renovate Dallas Municipal Bldg and Assoc Law Bldgs	TRB	12.54	25.20	18.26				56.00
	Previously Approved	l Projects Total	12.54	25.20	18.26	-	-	-	56.00
New Pro	jects for Approval:								
	New Project for	Approval Total	-	-	-	-	-	-	-
Planned	Projects with Identified Funding Source	s:							
04-0001	Renovation of the Municipal Building for Historical Exhibit	GIFT			3.50				3.50
					2.52				0.50
	Planned Projects with Identified Funding Land Acquisitions	Sources Total	-	-	3.50	<u>-</u>	-	-	3.50
									-
	Planned Land Ac	 :quisition Total	-	-	-	-	-	-	-
-	Capital Improven	nent Plan Total	12.54	25.20	21.76	_	_	_	59.50

Planned Project without Identified Funding Sources

New Construction:


Renovation:

System Building 8th Floor System Building Floors 2-4 1900 Elm Street Lobby

Summary	bу	Funding	Source

	Funding Source	Prior Yrs Budget	2018	2019	2020	2021	2022+	Total
HEAF	HEAF	-	-	-	-	-	-	-
HEAF Reserve	HEAF Reserve	-	-	-	-	ı	-	
Tuition Revenue Bonds	TRB	12.54	25.20	18.26	-	1	-	56.00
Commercial Paper	CP	-	-	-	-	-	-	-
Private Placement	PP	-	-	-	-	ı	-	-
Revenue Bonds	RB	-	-	-	-	ı	-	
Revenue Financing System Bonds	RFS	-	-	-	-	ı	-	•
Auxiliary Reserves	AUX	-	-	-	-	ı	-	
Grants	GRNT	-	-	-	-	•	-	
Student Fees	SF	-	-	-	-	-	-	-
Housing Revenue	HR	-	-	-	-	-	-	-
Gift/Donations	GIFT	-	-	3.50	-	ı	-	3.50
Annual Budget, Operating and Capital	Local/Cash	-	-	-	-	•	-	-
Tota	ıl .	12.54	25.20	21.76	0.00	-	-	59.50

University of North Texas System Facilities Planning Construction
May 2018
(Reported as of April 6, 2018)



Revised 5/14/2018

The planning, programming, design, and construction of the following (18) projects are managed by the UNT System Office of Facilities Planning and Construction (OFPC). All update information is provided by OFPC.

University of North Texas Campus

16-1.20 College of Visual Arts and Design

Current Project Status

Construction activities continue. Building enclosure is on track for completion at the end of April 2018. Permanent power is on and elevator installation is ahead of schedule. Interior Framing and MEP rough-in are nearing completion. Site Paving has begun. Owner furniture and equipment move-in are on track to begin June 1, 2018. The project is on schedule for substantial Completion in July 2018 with the renovation of the existing facility beginning in July 2018.

Project Budget				
Approved Budget	\$ 70,000,000	Expensed \$	27,513,253	
		Encumbered \$	35,359,293	
		Remaining Balance \$	7,127,454	

Major Project Contract Information

50	licitation	/Typo	٥f
20	licitation	/ IVNP	OT

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Corgan	27.54%
Contractor	CMAR	Hunt Construction Group	5.90%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	60%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning,	Programming Complete	Dec-15	-	-	Jul-16
	Design Complete	Dec-16	-	-	Jun-17
Construction	n Substantial Completion	Jun-18	Dec-18	Dec-18	-
	Construction End	Jul-18	Jan-19	Jan-19	-

16-1.84a New Residence Hall - Phase 1

Current Project Status

Construction is on-going for both the Residence Hall and Tour Center with structural construction currently underway for both buildings. Residence Hall is on schedule to meet substantial completion date of February 2019. The Tour Center is on schedule to meet the substantial completion date of December 2018.


Project Budget				
Approved Budget	\$ 58,900,000	Expensed	\$ 10,258,062	
		Encumbered	\$ 43,041,070	
		Remaining Balance	\$ 5,600,868	

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Jacobs Engineering	14.88%
Contractor	CMAR	JT Vaughn	2.35%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	17%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning	Programming Complete	May-16	-	-	Jan-17
	Design Complete	Feb-17	-	-	Sep-17
Construction	n Substantial Completion	May-18	Feb-19	Feb-19	-
	Construction End	lun-18	Mar-19	Mar-19	_



University of North Texas System Facilities Planning Construction

May 2018
(Reported as of April 6, 2018)

16-1.84b New Residence Hall - Phase 2

Current Project Status

With the completion of the housing master plan, it has been determined by campus administration that a second residence hall is not necessary at this time to fulfill demand. As a result, an amendment to the reduce the overall project budget was approved by the Board of Regents at the February 2018 meeting to cancel the second phase.

Project Budget				
Approved Budget	\$ -	Expensed \$	-	
		Encumbered \$	-	
		Remaining Balance \$	-	

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	TBD	-
Contractor	CMAR	TBD	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Planning				
Phase % Complete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning,	Programming Complete	Jun-16	Jun-20	-	=
	Design Complete	Jun-17	Jun-21	-	-
Construction	Substantial Completion	May-19	May-22	-	-
	Construction End	Jun-19	Jun-22	-	-

16-2.66 Coliseum Concourse Renovation

Current Project Status

Construction continues both in the interior concourse as well as the exterior additions. Basketball coaching staff have been relocated to their new offices in the East addition and their old offices are being demolished on the interior concourse. The remaining areas in the addition are anticipated to be substantially complete in May 2018, prior to commencement ceremonies. Terrazzo polishing is underway on the interior concourse and punch list items are being scheduled in efforts to complete by commencement ceremonies in May.

Project Budget			
Approved Budget	\$ 8,000,000	Expensed	\$ 5,372,848
		Encumbered	\$ 2,206,283
		Remaining Balance	\$ 420,868

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Elements of Architecture	100.00%
Contractor	CMAR	Construction Zone	100.00%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	80%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning	Programming Complete	Dec-15	-	-	Dec-15
	Design Complete	Oct-16	-	-	Apr-17
Construction	n Substantial Completion	Aug-17	May-18	May-18	-
	Construction End	Sep-17	Jun-18	Jun-18	-



University of North Texas System Facilities Planning Construction

May 2018
(Reported as of April 6, 2018)

16-2.67 1500 I-35E Building

Current Project Status

The management of the design and construction of this project is split between UNT System Facilities and UNT Facilities. UNT System Facilities is responsible for the building envelope, core necessities and required infrastructure of the facility. Design for this portion of work is 100% complete and construction is now underway. This portion of the project is on schedule to be complete in September 2018. UNT Facilities is responsible for the programming, design, and construction of the interior of the building and other necessary improvements to the parking lot. Corgan has been selected as the consultant for the interior design utilizing the IDIQ professional services agreement. The contractor selection will utilize the Texas State Group & Cooperative purchasing. The anticipated move-in date is January 2019. Interior Programming is 80% complete.

Project Budget

 Approved Budget
 \$ 12,500,000
 Expensed
 \$ 986,915

 Encumbered
 \$ 4,249,192

 Remaining Balance
 \$ 7,263,893

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	Sole Source	Corgan	14.00%
Contractor	CMAR	Pogue Construction	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase (UNT): Programming
Phase % Complete: 80%
Project Phase (OFPC): Construction

Phase % Complete: 10%

6 Complete: 10%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete	Feb-16	-	-	Oct-16
Design Complete	Nov-16	Jun-18	Jun-18	-
Construction Substantial Completion	Aug-17	Dec-18	Dec-18	-
Construction End	Sep-17	Jan-19	Jan-19	-

16-2.82 Track and Field Stadium

Current Project Status

Construction continues. The concrete pour for the north parking lot expansion is complete. Construction of the throwing field area events is nearing completion. Structural steel top out is complete on the field house. LED stadium lights and conduits have been installed around the track.

Proj	ect	Buc	lget
------	-----	-----	------

 Approved Budget
 \$ 13,590,000
 Expensed
 \$ 3,692,766

 Encumbered
 \$ 9,086,391

 Remaining Balance
 \$ 810,843

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	BRW Architects	25.80%
Contractor	CSP	Pogue Construction	7.74%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Construction

Phase % Complete: 50%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete	-	-	-	-
Design Complete	Sep-16	-	-	Jun-17
Construction Substantial Completion	Sep-17	Jul-18	Jul-18	-
Construction End	Sep-17	Aug-18	Aug-18	-



University of North Texas System Facilities Planning Construction

May 2018
(Reported as of April 6, 2018)

17-01-0005 Discovery Park Bio-Medical Engineering Addition

Current Project Status

100% construction documentation is now complete. A Guaranteed Maximum Price was submitted March 30, 2018. The expected construction start date is May 1, 2018.

prove	ed Budget	\$ 17,400,000	Expensed	\$ 885,252
			Encumbered	\$ 528,988
			Remaining Balance	\$ 15,985,760

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	TreanorHL	12.08%
Contractor	CMAR	Sundt Construction	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule Project Phase: Design Phase % Complete: 100% **Original CIP Schedule Previously Reported Current Projected** Actual Planning/Programming Complete Mar-17 Jul-17 Design Complete May-18 Mar-18 Mar-18 **Construction Substantial Completion** May-19 May-19 May-19 Construction End Jun-19 Jun-19 Jun-19

17-01-0010 New Classroom Building

Current Project Status

UNT Campus administration has directed this project has been placed on hold at the present time.

Project Budget				
Approved Budget	\$ 25,100,000	Expensed	\$ 25,00	00
		Encumbered	\$ -	
		Remaining Balance	\$ 25,075,00	00

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	TreanorHL	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

lanning				
%	Original CIP Schedule	Previously Reported	Current Projected	Actual
gramming Complete	Apr-17	May-18	TBD	-
Design Complete	Apr-18	May-19	TBD	-
bstantial Completion	Jul-19	Jul-20	TBD	-
Construction End	Aug-19	Sep-20	TBD	-
	bstantial Completion	% Original CIP Schedule begramming Complete Apr-17 Design Complete Apr-18 bstantial Completion Jul-19	%Original CIP SchedulePreviously Reportedogramming CompleteApr-17May-18Design CompleteApr-18May-19obstantial CompletionJul-19Jul-20	Original CIP Schedule Previously Reported Current Projected ogramming Complete Apr-17 May-18 TBD Design Complete Apr-18 May-19 TBD obstantial Completion Jul-19 Jul-20 TBD



University of North Texas System Facilities Planning Construction
May 2018
(Reported as of April 6, 2018)

17-01-0011 Hickory Hall Renovation

Current Project Status

Planning is currently underway with the campus. A portion of the space in Hickory Hall is occupied by the College of Visual Arts and Design (CVAD) and is expected to relocate into the new CVAD building. As a result, the construction phase cannot begin until the CVAD project is complete. At campus direction, this project has been placed on hold pending on-going planning review by UNT Administration.

Project Budget			
Approved Budget	\$ 8,800,000	Expensed	\$ -
		Encumbered	\$ -
		Remaining Balance	\$ 8,800,000

Major Project Conf	tract Information		
	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Planning				
Phase % Complete:	20%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete		Feb-17	May-18	TBD	-
	Design Complete	Jan-18	Mar-19	TBD	-
Construction Substantial Completion		Jul-19	Mar-20	TBD	-
	Construction End	Aug-19	Apr-20	TBD	-

18-01-0004 Art Building Roof Replacement

Contractor

Current Project Status

The construction will be coordinated with construction activity for the new College of Visual Arts & Design Building. Design has been completed and the project is currently bidding, with cost due by mid- April 2018.

Project Budget			
Approved Budget	\$ 1,350,000	Expensed	\$ -
		Encumbered	\$ 30,630
		Remaining Balance	\$ 1,319,370

Solicitation/Type of		
Contract	Selected Firm	HUB Participation
IDIQ	Terracon	-
CSP	Hunt Construction Group	-
-	-	-
-	-	-
	Contract IDIQ CSP	Contract Selected Firm IDIQ Terracon CSP Hunt Construction Group -

Project Schedule					
Project Phase:	Design				
Phase % Complete:	100%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete		-	-	-	-
	Design Complete	Sep-17	Jan-18	-	Feb-18
Construction	n Substantial Completion	Aug-18	Nov-18	Nov-18	-
	Construction End	Sep-18	Dec-18	Dec-18	-

UNT SYSTEM

University of North Texas System Facilities Planning Construction

May 2018
(Reported as of April 6, 2018)

18-01-0007 New Dining Hall

Current Project Status

100% Schematic Design documents were issued in March 2018. Roger-O'Brien Construction has been selected as the construction manager at risk and is now under contract to provide pre/construction services. The design team and CMAR are in the process of reconciling the schematic design drawing to the project scope and budget.

Project Budget				
Approved Budget	\$ 25,470,000	Expensed	\$ 562,516	
		Encumbered	\$ 1,755,790	
		Remaining Balance	\$ 23,151,694	

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Kirksey Architects	25.80%
Contractor	CMAR	Rogers-O'Brien Construction	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	20%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete		Sep-17	-	-	Nov-17
	Design Complete	Oct-18	Oct-18	Oct-18	-
Construction Substantial Completion		Dec-19	Dec-19	Dec-19	-
	Construction End	Jan-20	Jan-20	Jan-20	-

18-01-0008 Fouts Field Demolition, Parking, and Bus Transfer Station

Current Project Status

Huitt Zollars has been selected and a contract has been executed for design services. Design work continues and is currently on track to be completed by August 2018. Once design is complete, a proposal for construction will be solicited via a competitive sealed proposal.

Project Budget				
Approved Budget	\$ 14,000,000	Expensed	\$ 138,763	
		Encumbered	\$ 793,881	
		Remaining Balance	\$ 13,067,356	

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Huitt-Zollars	-
Contractor	CSP	TBD	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	50%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/	Programming Complete	-	-	-	-
	Design Complete	Aug-18	Aug-18	Aug-18	-
Construction	Substantial Completion	Nov-18	Aug-19	Aug-19	-
	Construction End	Dec-18	Sep-19	Sep-19	-



University of North Texas System Facilities Planning Construction

May 2018
(Reported as of April 6, 2018)

18-01-0009 New Athletics Indoor Practice Facility

Current Project Status

Design of the facility began in December 2017 and is anticipated to be complete June 2018. Once Design is complete, the project will be bid for construction via Competitive Sealed Proposal (CSP). It is anticipated that construction will begin August 2018.

Proje	ect I	Bud	get

 Approved Budget
 \$ 18,900,000
 Expensed
 \$ 530,639

 Encumbered
 \$ 576,816

Remaining Balance \$ 17,792,545

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Heery Architects	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Design

Phase % Complete: **Original CIP Schedule Previously Reported** 60% **Current Projected** Actual Planning/Programming Complete Oct-17 Oct-17 Design Complete Jun-18 Jun-18 Jun-18 **Construction Substantial Completion** Jun-19 Jul-19 Jul-19 Construction End Jul-19 Jul-19 Jul-19

University of North Texas Dallas Campus

16-1.01 Student Learning and Success Center

Current Project Status

Construction is on-going and approximately 33% complete and is on schedule for completion in March 2019.

Project Budget

 Approved Budget
 \$ 63,000,000
 Expensed
 \$ 12,817,062

 Encumbered
 \$ 40,792,379

Remaining Balance \$ 9,390,559

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Moody Nolan	20.04%
Contractor	CMAR	Austin Commercial	3.05%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Construction

Phase % Complete: 33%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete	Jan-15	-	-	Jul-16
Design Complete	Dec-16	-	-	Jun-17
Construction Substantial Completion	Jun-19	Mar-19	Mar-19	-
Construction End	Jul-19	May-19	May-19	-



University of North Texas System Facilities Planning Construction

May 2018
(Reported as of April 6, 2018)

University of North Texas Health Science Center Campus

16-1.40 Interdisciplinary Research Building

Current Project Status

Construction of the building is underway. The concrete superstructure is complete. Installation of precast panels is complete. Curtain wall and glazing are complete. The building is dried in and the building air has been turned on. Drywall has been installed on levels 1-4 and is in progress on level 5. Window chamber testing is in progress. Demolition of the existing chemical storage building is complete. There is potential for an early substantial completion, currently tracking September 2018.

PIO	nect	Bud	ıget

 Approved Budget
 \$ 118,500,000
 Expensed
 \$ 73,226,383

 Encumbered
 \$ 33,675,573

 Remaining Balance
 \$ 11,598,044

Major Project Contract Information

Solicitation/Type of Contract Selected Firm

 Architect
 RFQ
 TreanorHL
 35.06%

 Contractor
 CMAR
 JT Vaughn
 13.62%

 Contractor

 Contractor

Project Schedule

Project Phase: Construction Phase % Complete: 78% **Original CIP Schedule Previously Reported Current Projected** Actual Planning/Programming Complete Jul-15 Oct-15 **Design Complete** Aug-16 Oct-16 **Construction Substantial Completion** Dec-18 Nov-18 Nov-18 Construction End Dec-18 Dec-18 Dec-18

HUB Participation

16-2.96 Research and Education (RES) Level 4

Current Project Status

UNTHSC has requested to delay this project until FY 19 until the IREB opens and departments are moved into the new building. This will allow the renovations to begin.

Project Budget

 Approved Budget
 \$ 4,500,000
 Expensed
 \$ 3,600

 Encumbered
 \$


 Remaining Balance
 \$ 4,496,400

Major Project Contract Information

	Solicitation/Type of				
	Contract	Selected Firm	HUB Participation		
Architect	-	-	-		
Contractor	-	-	-		
Contractor	-	-	-		
Contractor	-	-	-		

Project Schedule Project Phase:

Phase % Complete: 0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete	Feb-16	TBD	TBD	-
Design Complete	Apr-16	TBD	TBD	-
Construction Substantial Completion	Dec-16	TBD	TBD	-
Construction End	Dec-16	TBD	TBD	-



University of North Texas System Facilities Planning Construction

May 2018
(Reported as of April 6, 2018)

17-03-0002 Medical Clinic

Current Project Status

UNTHSC has requested that this project project be placed on hold at the present time.

Project Budget			
Approved Budget	\$ 4,200,000	Expensed	\$ -
		Encumbered	\$ -
		Remaining Balance	\$ 4,200,000

Major Project Contract Information

	Solicitati	ion/	Type	of
--	------------	------	------	----

	Contract	Selected Firm	HUB Participation
Architect	-	-	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project	Sched	lule
---------	-------	------

Project Phase:	Planning
DI 0/0 I.	00/

Phase % Complete: 0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete	Dec-16	TBD	TBD	-
Design Complete	Aug-17	TBD	TBD	-
Construction Substantial Completion	May-18	TBD	TBD	-
Construction End	Jul-18	TBD	TBD	-

University of North Texas System

16-2.01 Renovate Dallas Municipal Building and Associated Law Buildings

Current Project Status

Most of the demolition is complete. Installation of framing is in process on levels one and two. Mechanical/Electrical /Plumbing are in process on all floors. Air Handling Units have been installed on the roof and sub-basement mechanical rooms. One of the two new stairways is being installed. The excavation of the elevator extension to the sub-basement has revealed unforeseen conditions that have caused some delay in that area of work. The impact of that delay is being reviewed, but a substantial completion date of February 9, 2019 should be acheivable.

Project Budget			
Approved Budget	\$ 56,000,000	Expensed \$ 14,548,234	
		Encumbered \$ 29,773,359	
		Remaining Balance \$ 11,678,407	

Solicitation/Type	of
-------------------	----

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Stantec	23.43%
Contractor	CMAR	Turner Construction	2.41%
Contractor	-	-	-
Contractor	-	-	-

Project	Schedul	le
---------	---------	----

Project Phase:	Construction

Phase % Complete: 35%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete	Nov-15	-	-	Jun-16
Design Complete	Dec-16	-	-	Apr-17
Construction Substantial Completion	Aug-19	Dec-18	Feb-19	-
Construction End	Aug-19	Jan-19	Mar-19	-

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



The planning, programming, design, and construction of the following (23) projects are managed by UNT Facilities. All update information is provided by UNT Facilities.

UNT Facilities Projects

2.20 Matthews Hall MEP

Current Project Status

The re-design of the electrical portion of this project is anticipated to be complete April 2018 with the process to begin bidding via competitive sealed proposal anticipated to begin in April 2018. Additional design review time impacted projected schedule by a month. It is anticipated that construction will begin in June 2018.

Project Budget			
Approved Budget	\$ 1,200,000	Expensed	\$ 241,417
		Encumbered	\$ 69,000
		Remaining Balance	\$ 889,583

Major Project Contract Information

	Solicitation/Type of	Solicitation/Type of			
	Contract	Selected Firm	HUB Participation		
Architect	RFQ	Summit Consultants	14.00%		
Contractor	CSP	TBD	-		
Contractor	-	-	-		
Contractor	-	-	-		

Project Schedule					
Project Phase:	Design				
Phase % Complete:	95%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Plar	nning/Programming Complete	=	-	-	-
	Design Complete	Mar-15	Feb-18	Apr-18	-
Constru	uction Substantial Completion	Apr-16	Dec-18	Jan-19	-
	Construction End	Apr-16	Jan-19	Feb-19	-

2.21 Wooten Hall MEP

Current Project Status

Construction Phase has started, fan and coil replacement for air handler was completed in January 2018. A Professional Services Amendment had to be written to Campos Engineering to redesign portions of the project to reduce construction cost and meet the approved budget. The redesign splits the MEP project into smaller parts to correct areas severely needing upgrade and replacement. The Construction schedule is adjusted based on estimated lead time for procuring new Construction services based on the adjusted scope.

Project Budget				
	\$ 3,450,000	Expensed	\$ 1,020,196	
		Encumbered	\$ 145,978	
		Remaining Balance	\$ 2,283,826	

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	RFQ	Campos Engineering	100.00%
Contractor	State Contract	Entech	0.09%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	50%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Plan	ning/Programming Complete	-	-	-	=
	Design Complete	Aug-15	-	-	May-15
Constru	ction Substantial Completion	Mar-17	Jan-19	Feb-19	-
	Construction End	Mar-17	Feb-19	Mar-19	-

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



2.33 Willis Library MEP

Current Project Status

The design is expected to be complete in May 2018. The schedule was extended due to coordination with other remodeling projects in the building that impacted the electrical room panels on each floor. Construction delivery will be via Request for Competitive Sealed Proposal (RFCSP) and is expected to begin in Aug 2018. Projected schedule is adjusted based on estimated design completion and procurement lead time.

Project Budget			
Approved Budget	\$ 9,850,000	Expensed \$	473,024
		Encumbered \$	89,420
		Remaining Balance \$	9,287,556

Major Project Contract Information

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	RFQ	Yaggi Engineering	100.00%
Contractor	CSP	TBD	-
Contractor	-	-	-
Contractor	-	-	-

esign				
9% 	Original CIP Schedule	Previously Reported	Current Projected	Actual
ogramming Complete	=	-	-	May-15
Design Complete	Nov-15	Jan-18	May-18	-
ubstantial Completion	Mar-18	Aug-19	Jan-20	-
Construction End	Mar-18	Sep-19	Feb-20	-
	ubstantial Completion	Original CIP Schedule ogramming Complete Design Complete Ubstantial Completion Design Completion Design Completion Mar-18	Original CIP Schedule Previously Reported Ogramming Complete Design Complete Ubstantial Completion Design Completion Design Completion Mar-18 Design Completion Mar-18 Design Completion	Original CIP Schedule Previously Reported Current Projected ogramming Complete Design Complete Ubstantial Completion Design Completion Des

2.34 Hickory Hall MEP

Current Project Status

As of February 28, 2018, construction was complete.

Project Budget				
Approved Budget	\$ 3,000,000	Expensed	\$ 2,911,825	
		Encumbered	\$ 85,518	
		Remaining Balance	\$ 2,657	

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	RFQ	FAI Engineers	5.00%
Contractor	CSP	DMI	28.00%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Complete				
Phase % Complete	: 100%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	=	-	-	-
	Design Complete	Mar-15	-	-	Apr-15
(Construction Substantial Completion	Apr-16	Jan-18	-	Jan-18
	Construction End	Apr-16	Feb-18	-	Feb-18

University of North Texas Facilities
May 2018
(Reported as of April 6, 2018)



16-2.25 General Academic Building MEP and Interior Renovation

Current Project Status

The Professional Service Agreement was executed on February 16, 2018. The project design is currently underway. Revised schedule dates reflect the contract execution time.

Project Budget

Approved Budget \$ 10,350,000 Expensed \$ -

Encumbered \$ 623,041 Remaining Balance \$ 9,726,959

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	RFQ	Baird Hampton Brown	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Design
Phase % Complete: 5% Original CIP Schedule Previously

Current Projected **Previously Reported** Actual Planning/Programming Complete Dec-15 Dec-15 **Design Complete** Nov-18 Sep-16 Aug-18 **Construction Substantial Completion** Nov-17 May-20 Aug-20 **Construction End** Dec-17 Jun-20 Sep-20

16-2.50 Life Science Lab Exhaust Upgrade

Current Project Status

Estes McClure Associates was awarded a Professional Service Agreement utilizing an IDIQ contract. The completed life safety study on Life Science Building B, generated the need for additional scope; which, increased the budget by \$2.75M at the February 2018 Board of Regents meeting. The Professional Services Agreement and Hub Subcontracting Plan are being revised to accommodate the expanded design. The new scope requires two design packages and two Request for Competitive Sealed Proposal bids. The preliminary completion schedule for the first design package is June 2018. The Construction contract is scheduled to be awarded October 2018, and Substantial Completion in August 2019. The second design package will be the commissioning of the entire facility, and Final Completion of the project is expected to complete January 2020.

Project Budget

Approved Budget \$ 5,950,000 Expensed \$ Encumbered \$ 190,

Encumbered \$ 190,750 Remaining Balance \$ 5,759,250

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Estes McClure Associates	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Design

Phase % Complete: 5% **Original CIP Schedule Previously Reported Current Projected Actual** Planning/Programming Complete Dec-15 Jan-16 Design Complete Sep-16 May-18 **Construction Substantial Completion** Nov-17 Dec-19 Dec-19 Construction End Dec-17 Jan-20 Jan-20

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



16-2.55 Discovery Park MEP Upgrade

Current Project Status

The facilities audit is underway and is anticipated to complete by June 2018, with projected design completion Winter 2018. A 3rd party review of the Audit is required by the SECO, and will be accomplished via IDIQ provider, to be completed by July 2018.

Project Budget			
Approved Budget	\$ 20,600,000	Expensed \$	-
		Encumbered \$	285,000
		Remaining Balance \$	20,315,000

Major Project Contract Information

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	RFQ	Siemens	-
Contractor	-	=	-
Contractor	-	=	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	2%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Dec-15	-	-	Dec-16
	Design Complete	Sep-16	Dec-18	Dec-18	-
Cor	nstruction Substantial Completion	Jul-18	Nov-20	Nov-20	-
	Construction End	Aug-18	Dec-20	Dec-20	-

16-2.77 Wooten Hall Code Upgrade

Current Project Status

Project Design completed November 2017. The Request for Proposal (RFP) Evaluation completed March 26, 2018. Contractor selection has occurred, and Construction Contract Execution anticipated prior to scheduled construction start of May 2018. Construction contract completion contingent on executed Construction Contract Agreement.

Project Budget			
Approved Budget	\$ 4,760,000	Expensed	138,370
		Encumbered	45,877
		Remaining Balance	4,575,753

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	IDIQ	HDR	0.00%
Contractor	CSP	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Construction				
Phase % Complete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete		Feb-16	=	=	Dec-16
	Design Complete	Aug-16	=		Nov-17
Construction Substantial Completion		Oct-17	Nov-18	Dec-18	-
Construction End		Nov-17	Dec-18	Jan-19	-

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



16-2.85 Sage Hall Academic Success Center

Current Project Status

The project construction is currently 95% complete. The final project pieces are the installation of the storefront, and client moves. Client moves are scheduled to complete the week of May 14, 2018, marking the project end.

Project Budget			
Approved Budget	\$ 1,850,000	Expensed \$	1,582,110
		Encumbered \$	120,642
		Remaining Balance \$	147,248

Major Project Contract Information

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Corgan	10.04%
Contractor	Co-Op	JT Vaughn	-
Contractor	-	=	-
Contractor	-	-	-

Project Schedule				
Project Phase: Construction				
Phase % Complete: 95%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Compl	ete -	=	=	-
Design Compl	ete Mar-16	-	-	Apr-17
Construction Substantial Complet	ion Dec-17	Mar-18	-	Apr-18
Construction E	End Dec-17	Apr-18	May-18	-

17-01-0001 Terrill Hall MEP & Interior Renovation

Current Project Status

Request for Qualifications received February 2018. TLC Architecture is recommended as the Design Consultant. Design fee negotiations begin April 2018, with an agreement expected June 2018.

Project Budget				
Approved Budget	\$ 7,300,000	Expensed	\$ -	
		Encumbered	\$ -	
		Remaining Balance	\$ 7,300,00	0

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	RFQ	-	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
P	Planning/Programming Complete	-	-	-	-
	Design Complete	Jul-17	Oct-18	Jan-19	-
Construction Substantial Completion		Aug-18	May-20	May-20	-
	Construction End	Aug-18	Jun-20	Jun-20	-

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



17-01-0002 **Coliseum MEP Renovation**

Current Project Status

The funding for the project was adjusted in August 2017 to begin University fiscal year 2019. The planned project schedule is in alignment with the funding as approved by the Board of Regents.

)roi	inct	Bud	mnt.
-10	CLL	buu	gei

Approved Budget 10,400,000 Expensed \$

Encumbered \$

Remaining Balance \$ 10,400,000

Major Project Contract Information

Sol	icitation	/Type of
		I VDE UI

	Contract	Selected Firm	HUB Participation
Architect	RFQ	M.E. Group, Inc	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Design

Outstand CID Cales dula Phase % Complete:

ete:	U%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	=	-	-	-
	Design Complete	Sep-17	Nov-19	Nov-19	-
C	onstruction Substantial Completion	May-19	Feb-21	Aug-21	-
	Construction End	Jun-19	Mar-21	Sep-21	-

17-01-0003 **Kerr Hall MEP & Interior Renovation**

Current Project Status

The project to replace mechanical equipment is on-going. Completed upgrades include B- Tower AHU's, basement air handler, two heating boilers, two domestic boilers and one steam boiler. Work schedule during summer shut down comprises 24 air handlers in the A-Tower, and during winter shut down two air handlers in dining will be upgraded. The remaining MEP work will utilize Co-op purchasing contracts. Proposals are being negotiated by the department and contractor to align with CIP approved scope and scheduling needs. Anticipated construction completion is currently on schedule.

Project Budget

Approved Budget \$ 5,790,000 Expensed \$ 2,780,240

Encumbered \$ 9,550 Remaining Balance \$ 3,000,210

Jan-19

Major Project Contract Information

Solicitation/Type of

Construction End

	Contract	Selected Firm	HUB Participation
Architect	IDIQ	SSR	-
Contractor	State Contract	Live Systems	-
Contractor	State Contract	Entech	-
Contractor	-	-	-

Project Schedule

Project Phase:	Construction

Phase % Complete: 50% **Original CIP Schedule Previously Reported Current Projected Actual** Planning/Programming Complete Design Complete Dec-16 Dec-16 **Construction Substantial Completion** Aug-18 Dec-18 Dec-18

Jan-19

Aug-18

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



17-01-0004 USB MEP Renovation

Current Project Status

The Professional Design Service was previously reported to start February 2018 and complete August 2018. The design firm Professional Service Agreement was finalized March 2, 2018, resulting in a delay to the commencement of design.

_				_					
D	roi	Δ	ct	R	•	М	a	0	H

Approved Budget \$ 3,600,000

Expensed \$
Encumbered \$

Remaining Balance \$

350,000 3,250,000

Major Project Contract Information

	Solicitation/Type of	Solicitation/Type of			
	Contract	Selected Firm	HUB Participation		
Architect	RFQ	M.E. Group, Inc	-		
Contractor	-	-	-		
Contractor	-	-	-		
Contractor	-	-	<u>-</u>		

Project Schedule

Project Phase: Design

Phase % Complete: 5%

Phase % Complete:	5%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	-	-	-	-
	Design Complete	Aug-17	Aug-18	Oct-18	-
Co	onstruction Substantial Completion	Dec-18	Oct-19	Oct-19	-
	Construction End	Dec-18	Nov-19	Nov-19	_

17-01-0006 Sage Hall Academic Success Center Phase II

Current Project Status

Demolition and abatement of the Student Academic Success Center Phase II Renovation are underway. The Construction administration is on track to meet the Current Projected Completion schedule.

Project	Budget
---------	--------

> Encumbered \$ 2,094,526 Remaining Balance \$ 718,719

Major Project Contract Information

So	licitation	/Type of

	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Corgan	-
Contractor	Co-Op	JT Vaughn	17.11%
Contractor	-	-	-
Contractor	-	_	-

Project Schedule

Project Phase: Construction

Phase % Complete:	10%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Jul-17	-	-	Apr-17
	Design Complete	Dec-17	-	-	Nov-17
Co	nstruction Substantial Completion	Aug-18	Jul-18	Jul-18	-
	Construction End	Aug-18	Aug-18	Aug-18	-

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



17-01-0007 Life Science Building 4th Floor Laboratories Renovation

Current Project Status

The project administration is on hold, under consideration of UNT Leadership.

Project Budget

Approved Budget 7,000,000 Expensed \$

Encumbered \$

Remaining Balance \$ 7,000,000

Major Project Contract Information

Solicitation/	Type of
---------------	---------

	Contract	Selected Firm	HUB Participation	
Architect	-	-	-	
Contractor	-	-	-	
Contractor	-	-	-	
Contractor	-	-	-	

Project Schedule

Project Phase:	Planning
Phase % Complete:	50%

,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,					
ase % Complete:	50%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Jan-17	Jan-20	TBD	=
	Design Complete	Sep-17	Jun-20	TBD	-
Co	onstruction Substantial Completion	Jul-18	Jul-21	TBD	-
	Construction End	Aug-18	Aug-21	TBD	-

Coliseum Roof Replacement 17-01-0008

Current Project Status

This project will replace the Coliseum roof and metal parapet surrounding the facility. Planning completed in January 2017. It was subsequently determined that a more economical roofing system could reduce the overall project budget. The Board of Regents approved the reduction of the project budget in August 2017. The Co-operative purchasing method was accepted, based on the proposed reduced design. Proposals are being negotiated by the department and contractor.

Project Budget

Approved Budget 2,430,000 Expensed \$

Encumbered \$ Remaining Balance \$ 2,430,000

Major Project Contract Information

Solicitation/Type of

Construction End

	Contract	Selected Firm	HUB Participation
Architect	-	-	-
Contractor	-	=	-
Contractor	-	=	-
Contractor	-	-	-

Project Schedule

Project Phase: Design Phase % Complete: 25%

Original CIP Schedule Current Projected Previously Reported Actual Planning/Programming Complete Jan-17 Jan-17 Design Complete Jul-17 Mar-18 Mar-18 **Construction Substantial Completion** May-18 Dec-18 Dec-18

Dec-18

May-18

Dec-18

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



Actual

17-01-0009 Off-Site Campus #2

Current Project Status

Consideration of sites and requirements are currently underway with UNT staff. This project has been placed on hold at the present time.

	Proj	ect	Bud	lget
--	------	-----	-----	------

Approved Budget \$ 1,500,000 Expensed \$ -

Encumbered \$ Remaining Balance \$ 1,500,000

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation		
Architect	-	-	-		
Contractor	-	-	-		
Contractor	-	-	-		
Contractor	-	-	-		

Project Schedule

Project Phase: Planning

Phase % Complete: 0% Original CIP Schedule Previously Reported Current Projected

Planning/Programming Complete Jan-17 TBD TBD **Design Complete** Aug-17 TBD TBD **Construction Substantial Completion** Jul-18 TBD TBD Construction End Aug-18 TBD TBD

17-01-0012 Eagle Point Parking Lot #80

Current Project Status

The selected contractor, JT Vaughn, has received their executed agreement. Construction Administration has begun with construction planned to start mid - April with August 1st substantial completion of the parking lot.

Project Budget

 Approved Budget
 \$ 2,200,000
 Expensed
 \$ 84,114

 Encumbered
 \$ 2,018,142

Remaining Balance \$ 2,018,142

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Smith GroupJJR	19.08%
Contractor	Co-Op	JT Vaughn	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Construction

Phase % Complete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	May-17	=	-	May-17
	Design Complete	Jul-17	=	-	Dec-17
Co	nstruction Substantial Completion	Dec-17	Aug-18	Aug-18	-
	Construction End	Dec-17	Sep-18	Sep-18	-

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



18-01-0001 Maple Hall MEP & Renovation

Current Project Status

UNT Campus In-house resources have completed the programming scope. The project initially was to be procured via Request for Competitive Sealed Proposal (RFCSP); however, due to the timeline of the project and the need to complete construction between the months of May and August of 2018, mechanical portions of this project will be procured utilizing a co-operative purchasing agreement. The mechanical scope of work is in the procurement stage. Work is scheduled to begin May 14, to upgrade all 14 air handling units and two heating boilers along with upgrading existing switchgear and related distribution panels, wiring, conduit, and devices. The fire suppression system will be addressed separately through design-build RFP.

Project Budget

Approved Budget 4,380,000 Expensed \$

> Encumbered \$ Remaining Balance \$ 4,380,000

Major Project Contract Information

Solicitation/Type of

	Contract	Selected Firm	HUB Participation	
Architect	IDIQ	-	-	
Contractor	-	-	-	
Contractor	-	-	-	
Contractor	-	-	-	

Project Schedule

Project Phase: Construction

Phase % Com

mplete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	=	-	=	-
	Design Complete	Dec-17	Mar-18	-	Mar-18
C	onstruction Substantial Completion	Aug-18	Aug-18	Aug-18	-
	Construction End	Sep-18	Sep-18	Sep-18	-

18-01-0002 **Clark Hall Lobby Renovation**

Current Project Status

Initial in-house programming began September 2017. TreanorHL has been selected to complete the Programming and provide the design services via an IDIQ contract proposal. TreanorHL received the Executed Professional Service Agreement March 23rd, and is scheduled to begin programming week of April 2nd, 2018. The programming phase is expected to complete in June 2018, and design completion is planned for November 2018.

Project Budget

Approved Budget \$ 2,270,000

Expensed \$ Encumbered \$

Remaining Balance \$ 2,115,226

154,774

Major Project Contract Information

Solicitation/Type of

	Solicitation, Type of		
	Contract	Selected Firm	HUB Participation
Architect	IDIQ	TreanorHL	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	_	<u>-</u>	_

Project Schedule

Project Phase:	Programming				
Phase % Complete:	7%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Nov-17	May-18	Jun-18	-
	Design Complete	Mar-18	Aug-18	Nov-18	-
Cor	nstruction Substantial Completion	Aug-18	Aug-19	Aug-19	-
	Construction End	Sep-18	Sep-19	Sep-19	-

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



18-01-0003 Sage Hall Academic Success Center Phase III

Current Project Status

The professional service agreement was executed March 26 thus delaying the programming completion. UNT Campus administration of Professional Service Contract underway.

)roi	inct	Bud	mnt.
-10	CLL	buu	gei

Approved Budget \$ 3,010,000

Expensed \$ Encumbered \$ 239,000

Remaining Balance \$ 2,771,000

Major Project Contract Information

_			-	•
<u>د</u> م	licita	tion	/Tvpe	Λŧ

	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Corgan	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase: Planning Phase % Complete: 2%

ete:	2%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning	/Programming Complete	Apr-18	Apr-18	Apr-18	-
	Design Complete	Aug-18	Aug-18	Aug-18	-
Constructio	n Substantial Completion	Jan-19	Apr-19	Apr-19	-
	Construction End	Feb-19	May-19	May-19	-

18-01-0005 Discovery Park Utility Capacity Upgrade

Current Project Status

Phase 1 includes purchasing and installing a new chiller in May 2018. Phase 2 provides design and contracting to provide minimum required electrical service to the location of new Biomedical Engineering Addition, as dictated by the Biomedical Addition Construction Schedule. Phase 3 includes additional electrical infrastructure upgrades at Discovery Park and will be completed by May 2019. The planning process is complete, and Phase 2 design is underway. Planned Electrical Power Shutdowns for the entire building to Support Phase 1 construction scheduled for May 2018, and August 2018. Phase 1 construction completion anticipated June 2018. Phase 2 Electrical power for new Biomedical Engineering Addition will be available no later than September 2018. Phase 3 construction to begin after September 2018.

Project Budget

 Approved Budget
 \$ 2,000,000
 Expensed
 \$ 61,750

 Encumbered
 \$ 1.415.933

Encumbered \$ 1,415,933 Remaining Balance \$ 522,317

Major Project Contract Information

Solicitation/Type of

_	Contract	Selected Firm	HUB Participation
Architect	IDIQ	Campos Engineering	-
Contractor	Co-Op	Brandt Companies, LLC	-
Contractor	-	-	-
Contractor	-	-	-

Project Schedule

Project Phase:	Construction					
Phase % Complete	2%	Original CIP Schedule	Previously Reported	Current Projected	Actual	
	Planning/Programming Complete	-	-	-	Oct-17	
	Design Complete	Feb-18	Jan-18	-	Jan-18	
(Construction Substantial Completion	May-19	May-19	May-19	-	
	Construction End	Jun-19	Jun-19	Jun-19	-	

University of North Texas Facilities May 2018 (Reported as of April 6, 2018)



18-01-0006 Music Building Courtyard Renovation

Current Project Status

A feasibility and planning study by GSBS Architects was completed in 2017. Music Department obtained donation funding, and the project scope modified to allow the project to move forward. SmithGroup JJR Architects has been selected via an IDIQ contract to provide design and construction documents. Their proposal has been received and is under review. The project is scheduled to begin the design phase in June of 2018

Project Budget			
Approved Budget	\$ 2,590,000	Expensed	\$ 87,503
		Encumbered	\$ -
		Remaining Balance	\$ 2,502,497

Major Project Contract Information					
	Solicitation/Type of				
	Contract	Selected Firm	HUB Participation		
Architect	IDIQ	GSBS Architects	-		
Contractor	-	-	-		
Contractor	-	-	-		
Contractor	-	-	-		

Project Schedule					
Project Phase:	Design				
Phase % Complete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
	Planning/Programming Complete	Jun-17	-	-	Jun-17
	Design Complete	Dec-17	TBD	Nov-18	-
Co	enstruction Substantial Completion	Jan-19	TBD	Sep-19	-
	Construction End	Feb-19	TBD	Oct-19	-

Details of Other Minor Projects

There are an additional \$8.68M allocated for minor projects including fire alarm upgrades within various facilities, energy management control upgrades within various facilities, elevator modernization within various facilities, energy efficiency upgrades to mechanical/ electrical equipment within various facilities, and academic space upgrades within various facilities. None of these projects will be executed with a single contract value in excess of \$1M or more.



University of North Texas Health Science Center Campus May 2018 (Reported as of April 6, 2018)

The planning, programming, design, and construction of the following (3) projects are managed by UNTHSC Facilities. All update information is

provided by UNTHSC Facilities. **UNTHSC Facilities Projects**

17-03-0001 East Parking Garage Renovation

Current Project Status

Campus pre-planning discussions for this project are continuing. The UNT HSC Built Environment Council has been charged with the verification of the need for the additional parking structure on-campus. It has been determined that additional parking is required. The schedule has been adjusted to allow for the time that has been required for the verification process.

Project Budget				
Approved Budget	\$ 6,000,000	Expensed	\$	-
		Encumbered	\$	-
		Remaining Balance	\$ 6,000	0,000

M	ajor	Project	Contract	Information

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	-	-	-
Contractor	-	-	-
Contractor	-	-	-
Contractor	-	-	-

Planning				
0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete		-	-	-
Design Complete	May-17	Apr-18	Aug-18	-
Substantial Completion	Dec-17	Oct-18	Jan-19	-
Construction End	Jan-18	Nov-18	Feb-19	-
	0% /Programming Complete Design Complete s Substantial Completion	0% Original CIP Schedule /Programming Complete Design Complete substantial Completion Dec-17	0% Original CIP Schedule Previously Reported Programming Complete Design Complete Substantial Completion Dec-17 Oct-18	0% Original CIP Schedule Previously Reported Current Projected Programming Complete Design Complete Substantial Completion Dec-17 Oct-18 Design Complete Dec-17 Oct-18 Dec-19

18-03-0001 Gross Anatomy Laboratory Renovation

Current Project Status

The design of the mechanical, electrical and plumbing elements of the project will be executed utilizing Shaw Smith Associates under a proprietary justification due to previous RES experience and knowledge. The remaining design will be accomplished utilizing HSC staff.

Project Budget			
Approved Budget	\$ 2,470,000	Expensed \$	-
		Encumbered \$	-
		Remaining Balance \$	2,470,000

Approved Budget	Ş	2,470,000	Expensed S	5	-	
			Encumbered S	\$	-	
			Remaining Balance	\$	2,470,000	
Major Project Contra	act Inforn	nation				

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	Sole Source	Shaw Smith Associates	-
Contractor	-	=	=
Contractor	-	=	=
Contractor	-	-	-

Project Schedule					
Project Phase:	Design				
Phase % Complete:	0%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete		-	=	-	=
	Design Complete	Mar-18	Mar-18	Feb-18	-
Construction	Substantial Completion	Jul-18	Jul-18	Jun-18	-
	Construction End	Aug-18	Aug-18	Jul-18	-



University of North Texas Health Science Center Campus
May 2018
(Reported as of April 6, 2018)

18-03-0002 1408 St. Louis Ave. Renovation

Current Project Status

This project was finished in January 2018 and the building is now occupied.

Project Budget				
Approved Budget	\$ 1,950,000	Expensed \$	1,948,050	
		Encumbered \$	-	
		Remaining Balance	1,950	

	Solicitation/Type of		
	Contract	Selected Firm	HUB Participation
Architect	-	-	-
Contractor	State Contract	JT Vaughn	55.00%
Contractor	-	-	-
Contractor	-	-	-

Project Schedule					
Project Phase:	Complete				
Phase % Complete:	100%	Original CIP Schedule	Previously Reported	Current Projected	Actual
Planning/Programming Complete		Apr-17	-	-	Apr-17
Design Complete		Jun-17	-	-	Jun-17
Construction Substantial Completion		Nov-17	Jan-18	=	Jan-18
	Construction End	Dec-17	Jan-18	-	Jan-18

Information Technology Project Status Report





Portfolio Review	Status	Progress	Start Date	Completion Date
Infrastructure				
Data Warehouse (Technical Implementation, Phase 2) COMPLETE		•	4/17/2017	12/22/2017
Data Warehousing Analytics/Dashboards		•	6/1/2015	1/20/2019
Enterprise Hybrid Cloud (EHC) UNT System v4.1 - Phase 2		•	8/1/2017	1/31/2019
Enterprise Applications Systems				
Customer Relationship Management - Marketing Automation (Phase 2)		•	8/1/2016	2/28/2018
E-Forms			7/21/2017	3/28/2018
PeopleSoft Enterprise Learning Management 9.2 (ELM) COMPLETE		•	9/13/2016	11/13/2017
Finance and Administration Systems				
Time and Effort Phase III		•	1/27/2017	4/24/2018
Accounts Receivable & Billing COMPLETE		•	3/31/2017	12/4/2017
DigitalFuel IT Business Management		•	9/1/2017	4/13/2018
Concur Travel, Expense and P-Card	•	O	9/1/2017	TBD
Student Administration Systems				
Mobile Application Implementation - Phase 2		•	11/1/2016	3/1/2018
Intelligent Capture - Transcript Processing Improvement		•	11/16/2016	1/30/2018
Campus Solutions 9.2 Upgrade		•	12/1/2016	11/30/2018
Visual Schedule Builder Shopping Cart COMPLETE		•	7/15/2017	10/23/2017
Residential Management System		•	3/28/2017	1/31/2018
NetDragon SmartCampus		•	8/23/2017	4/6/2018
ServiceNow Applications				
IT Operations (ITOM) Tool Implementation		•	9/13/2017	2/5/2018
Business Services Customer Service Management		•	9/1/2017	TBD
