



# HUNTERS POINT SHIPYARD NAVY MONTHLY PROGRESS REPORT

**BRAC**  
PMO WEST



JUNE 28, 2007

<http://www.bracpmo.navy.mil/bracbases/california/hps>

USS Vicksburg

This monthly progress report (MPR) summarizes environmental restoration activities conducted by the U.S. Department of the Navy (Navy) at Hunters Point Shipyard (HPS) during May 2007. This MPR is prepared in accordance with the HPS Federal Facility Agreement, Section 6.6. The MPR is presented in three sections. Section 1.0, Parcel Updates, summarizes key activities at each parcel completed during the past month and planned for the upcoming 2 months. Section 2.0, Special Recognition, recognizes members of the Navy, regulatory agencies, and community who work together on projects for HPS. Section 3.0, Schedule, identifies submittals, meetings, and field activities completed during the past month and planned for the upcoming 2 months.

## 1.0 PARCEL UPDATES

This section summarizes key activities at each parcel completed during the past month and activities planned for the upcoming two months.

### 1.1 PARCEL B


The activities completed during May 2007 and planned for the upcoming 2 months at Parcel B are summarized below.

#### *May 2007 Activities at Parcel B*

- Continue the radiological removal action with active dust control, air monitoring, and implementation of the storm water pollution prevention plan.

#### *June to July 2007 Future Activities at Parcel B*

- Continue groundwater sampling in accordance with the Remedial Action Monitoring Plan for groundwater monitoring. Continue to develop and submit quarterly groundwater monitoring reports.
- Prepare and submit the Draft Final TMSRA.
- Prepare and submit the Draft Radiological Addenda for the TMSRA.
- Prepare and submit the Final Finding of Suitability to Lease (FOSL), Buildings 104, 115, 116, 117, 120, 125, and 606, Open Spaces 1 and 2 (Parcel B and E)
- For the radiological removal action, complete excavation activities in June and complete swale construction for runoff control in July. Construction activities are conducted with active dust control, air monitoring, and implementation of the storm water pollution prevention plan.

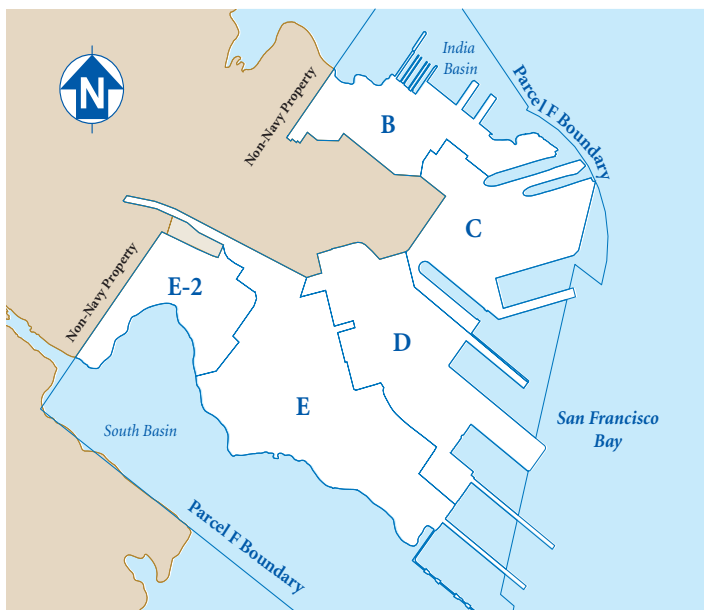

Hunters Point Shipyard

**1.2 PARCEL C**

The activities completed during May 2007 and planned for the upcoming 2 months at Parcel C are summarized below.

**May 2007 Activities at Parcel C**

- Continued to develop and submit quarterly groundwater monitoring reports.
- Continued preparation of the Draft Feasibility Study (FS) Report.

**June to July 2007 Future Activities at Parcel C**

- Continue groundwater sampling in accordance with the Sampling and Analysis Plan (SAP) for basewide groundwater monitoring. Continue to develop and submit quarterly groundwater monitoring reports.
- Continue preparation of the Draft FS Report.

**1.3 PARCEL D**

The activities completed during May 2007 and planned for the upcoming two months at Parcel D are summarized below.

**May 2007 Activities at Parcel D**

- Continued to develop and submit quarterly groundwater monitoring reports.
- Continued preparation of the Draft Final Revised FS Report.

**June to July 2007 Future Activities at Parcel D**

- Continue groundwater sampling in accordance with the SAP for basewide groundwater monitoring. Continue to develop and submit quarterly groundwater monitoring reports.
- Prepare and submit the Draft Final Revised FS Report.
- Conduct pre-construction activities for the radiological removal action. Complete construction of the Radiological Screening Yard 2. Begin pipe removal actions with active dust control, air monitoring, and implementation of the storm water pollution prevention plan.
- Prepare and submit the Final Treatability Study Work Plan.



Concrete Encased Pipe



Portal Monitors at Parcel D



**1.4 PARCEL E**

The activities completed during May 2007 and planned for the upcoming two months at Parcel E are summarized below.

**May 2007 Activities at Parcel E**

- Continued to develop and submit quarterly groundwater monitoring reports.
- Continued preparation of the Draft Remedial Investigation (RI) Report.

**June to July 2007 Future Activities at Parcel E**

- Continue groundwater sampling in accordance with the SAP for basewide groundwater monitoring. Continue to develop and submit quarterly groundwater monitoring reports.
- Prepare and submit the Shoreline Tech Memo Response to Comments (RTCs).
- Prepare and submit the Draft Metal Debris Reef/Metal Slag Area Removal Action Completion Report (Parcel E and E-2).
- Prepare and submit the Draft RI Report.

**1.5 PARCEL E-2**

The activities completed during May 2007 and planned for the upcoming months at Parcel E-2 are summarized below.

**May 2007 Activities at Parcel E-2**

- Continued monthly gas monitoring at the landfill. Continued to develop and submit quarterly landfill gas monitoring reports.

**June and July 2007 Future Activities at Parcel E-2**

- Continue monthly gas monitoring at the landfill. Continue to develop and submit quarterly landfill gas monitoring reports.
- Prepare and submit the Draft July 2006 - June 2007 Landfill Cap Operation and Maintenance (O&M) Report.
- Prepare and submit the Draft 2006-2007 Annual Storm Water Report.

**1.6 PARCEL F**

The activities completed during May 2007 and planned for the upcoming 2 months at Parcel F are summarized below.

**May 2007 Activities at Parcel F**

- Continued preparation of the Draft FS Report.

**June to July 2007 Future Activities at Parcel F**

- Prepare and submit the Feasibility Study Data Gaps Investigation Technical Memorandum with RTCs.

**1.7 BASEWIDE**

The Basewide activities completed during May 2007 and planned for the upcoming 2 months are summarized below.

**May 2007 Basewide Activities**

- Prepare and submit the Draft Basewide Storm Water Annual Report (2006-2007).

**June to July 2007 Basewide Activities**

- Prepare and submit the Final Basewide Storm Drain and Sanitary Sewer Removal Work Plan, Revision 1.
- Prepare and submit the Revised Basewide Radiological Work Plan.
- Prepare and submit the Community Notification Plan, 2007 Update.
- Final Basewide Stormwater Annual Report (2006-2007).
- Final Project Work Plan for Transportation and Removal of Contaminated Soil.

**2.0 SPECIAL RECOGNITION**

The Navy is recognizing Doug Bielskis, Engineering/Remediation Resources Group (ERRG) for his execution of the Draft Remedial Investigation (RI)/Feasibility Study (FS) for Parcel E-2. Mr. Bielskis is the Project Manager of work being done at Parcel E-2 by the Navy. Mr. Bielskis graduated from University of California, Berkeley with a Bachelor and Masters in Science in Civil and Environmental Engineering. Mr. Bielskis hobbies include jogging, listening to music and watching the San Francisco Giants. The Navy would like to thank Mr. Bielskis for his continued support on the HPS project.



**Doug Bielskis**  
Engineering Remediation Resources Group

**3.0 SCHEDULE**

This section presents meetings conducted and planned and deliverables submitted and planned during this reporting period.

**May 2007 Meetings:**

- ▶ Base Realignment and Closure (BRAC) Cleanup Team (BCT) Meeting – May 22, 2007
- ▶ Restoration Advisory Board (RAB) Meeting - May 24, 2007

**May 2007 Deliverables:**

- ▶ Revised Draft FS Report (Parcel F)
- ▶ Draft Basewide Storm Water Annual Report (2006-2007)

**June and July 2007 Meetings:**

- ▶ BCT Meeting – June 26, 2007
- ▶ RAB Meeting – June 28, 2007
- ▶ BCT Meeting – July 24, 2007
- ▶ RAB Meeting – July 26, 2007

**June and July 2007 Deliverables**

**Basewide**

- ▶ Revised Basewide Radiological Work Plan
- ▶ Revised Basewide Storm Drain and Sanitary Sewer Removal Work Plan
- ▶ Community Notification Plan, 2007 Update
- ▶ Final Basewide Stormwater Annual Report (2006-2007)
- ▶ Final Project Work Plan for Transportation and Removal of Contaminated Soil

**Parcel B**

- ▶ Final July to September 2006 Groundwater Monitoring Report
- ▶ Draft October to December 2006 Groundwater Monitoring Report
- ▶ Draft Final TMSRA
- ▶ Draft January to March 2007 Groundwater Monitoring Report
- ▶ Draft Radiological Addenda for the TMSRA
- ▶ FOSL Buildings 103, 104, 115, 116, 117, 120, 125, and 606, Open Spaces 1 and 2 (Parcel B and E)

**Parcel C**

- ▶ Final July to September 2006 Groundwater Monitoring Report (Parcels C, D, E)
- ▶ Draft October to December 2006 Groundwater Monitoring Report (Parcels C, D, E)
- ▶ Draft January to March 2007 Groundwater Monitoring Report (Parcels C, D, E)

**Parcels D**

- ▶ Draft Final Revised FS Report
- ▶ Parcel D groundwater data will be included in the basewide monitoring reports listed for Parcel C Final Treatability Study Work Plan

**Parcel E**

- ▶ Shoreline Technical Memorandum RTCs
- ▶ Parcel E groundwater data will be included in the basewide monitoring reports listed for Parcel C
- ▶ Draft Metal Debris Reef/Metal Slag Area Removal Action Completion Report (Parcels E and E-2)
- ▶ Draft Remedial Investigation Report

**Parcels E-2**

- ▶ Draft July 2006 - June 2007 Landfill Cap O&M Report
- ▶ Final January through March 2007 Landfill Gas Monitoring Report
- ▶ Draft 2006-2007 Annual Storm Water Report

**Parcel F**

- ▶ Feasibility Study Data Gaps Investigation Technical Memorandum with RTCs
