

35EXPRESS

TxDOT PROJECT TRACKER

DALLASDISTRICT



"Work with others to provide safe and reliable transportation solutions for Texas."

OVERVIEW

Interstate 35E (I-35E) serves the rapidly growing areas of southern and central Denton County, as well as the major Dallas suburbs immediately north of I-635. This corridor functions as a major artery for hundreds of thousands of commuters, as well as a primary link to major universities in the city of Denton, including the fourth-largest university in the state, the University of North Texas (UNT). In addition, I-35E is an important truck corridor and accommodates more than 12,000 trucks daily. The interstate also handles almost 200,000 total vehicles daily near I-635, and 128,000 vehicles a day across Lewisville Lake. Furthermore, due to the lack of continuous frontage roads across Lewisville Lake, there are no viable north-south commuting alternatives to I-35E at this crossing. Therefore, it is imperative to provide motorists reliable alternatives with a combination of continuous frontage roads and managed lanes. The \$4.8 billion project, proposed to be constructed in phases, would rebuild the entire 30-mile corridor and provide managed lanes that feature dynamic pricing to keep traffic moving at 50 mph. Approximately \$1.4 billion in funding has been identified for Phase 1 of this project, which includes SH 121 regional toll revenue (RTR) funds dedicated to Denton County. Phase 2 of the project will occur when the additional funding becomes available.

PROJECT HISTORY

- I-35E constructed: 1950s and 1960s
- Major Investment Study for future expansion: Began 1998
- Express Lane Demonstration Program approval by Federal Highway Administration: Sept. 30, 2009
- The Senate Bill (SB) 1420 Committee determined in March 2012 that Phase 1 of the project should be delivered as a design-build project with public financing and utilizing the Regional Transportation Council managed lane policy.
- Request for Qualifications (RFQs) issued 1/23/12; received 3/23/12
- Request for Proposals (RFPs) issued July 13, 2012; received Nov. 12, 2012
- AGL Constructors, comprised of Archer Western, Granite and LANE Constructors, were selected and awarded the contract on Dec. 13, 2012
- Contract Executed: May 17, 2013
- TxDOT issued Notice to Proceed (NTP) 1 to AGL to begin design in May 2013 and NTP 2 for construction in Sept. 2013
- Construction began in late October 2013

ENVIRONMENTAL REVIEW STATUS

- Environmental Assessment public meetings: 2008
- Environmental Assessment process: 2003-2012 (complete)
- Finding of No Significant Impact by FHWA: Dec. 28, 2011-south segment; Jan. 28, 2011 - middle segment Jan. 31, 2012 - north segment
- All public hearings have been completed
- Phase 1 FHWA environmental concurrence: Feb. 15, 2013 - south segment; April 18, 2013 - middle segment; March 11, 2013 - north segment

PROJECT FACTS

- South segment (I-635 to Pres. George Bush Turnpike - PGBT): 7.5 miles
- Middle segment (Pres. George Bush TP to FM 2181): 12.1 miles
- North segment (FM 2181 to US 380): 10.5 miles
- Additional general purpose lane in each direction: N of SH 121 to US 380



Pictured above is the column construction for the new southbound Lewisville Lake Bridge.

AGL photo archives


- Two reversible managed toll lanes from I-635 to Turbeville/Hundley
- New southbound bridge over Lewisville Lake
- Belt Line Road intersection reconstruction
- Intersection improvements at Dickerson, FM 407, Garden Ridge, S. Denton/Oak, Turbeville/Hundley, Corinth, Post Oak, North Texas Blvd.
- Substantial completion: Mid 2017

PROJECT PROGRESS

- Demolition of existing southbound I-35E bridge over Belt Line Rd completed, southbound I-35E traffic shifted to the middle. Construction of new I-35E bridge and temporary southbound frontage continue.
- Southbound frontage road traffic from Garden Ridge Blvd to FM 407/Justin Rd on new permanent pavement. Construction continues to prepare for 2015-Q1 demolition of FM 407 bridge over I-35E and to elevate I-35E over an widened FM 407.
- Work continues on new Lewisville Lake bridge. Bridge column construction continues to accelerate.
- Work has started on new trail at Copperas Branch Park on east side of I-35E.
- Bridge widening continues on northbound I-35E over US 77/Dallas Dr entrance ramp to southbound I-35E. Northbound I-35E traffic shifted to the middle on temporary pavement as widening progresses.
- Traffic barriers placed on mainlanes near Corinth Blvd and Post Oak Dr for mainlane traffic shift for 2015-Q1 demolition of Corinth Blvd bridge over I-35E; I-35E to be reconstructed to go over an widened Corinth Blvd.
- I-35E bridge widening continue over Valley View Ln, Valwood Pkwy, Crosby Rd, Sandy Lake Rd/Whitlock Ln, Timber Creek, Mayhill Rd and Loop 288.

FUNDING

- Base scope and seven additional options = \$1.4 billion for Phase 1
- Federal - \$460 million; State - \$979 million (includes \$534 million in RTR funds, and \$285 million in RTR backstop funds for options, totaling \$819 million from RTR funds). Pending Transportation Infrastructure Finance and Innovation Act (TIFIA) loan approval, the Federal amount will increase and the State amount will decrease; Local - \$14 million

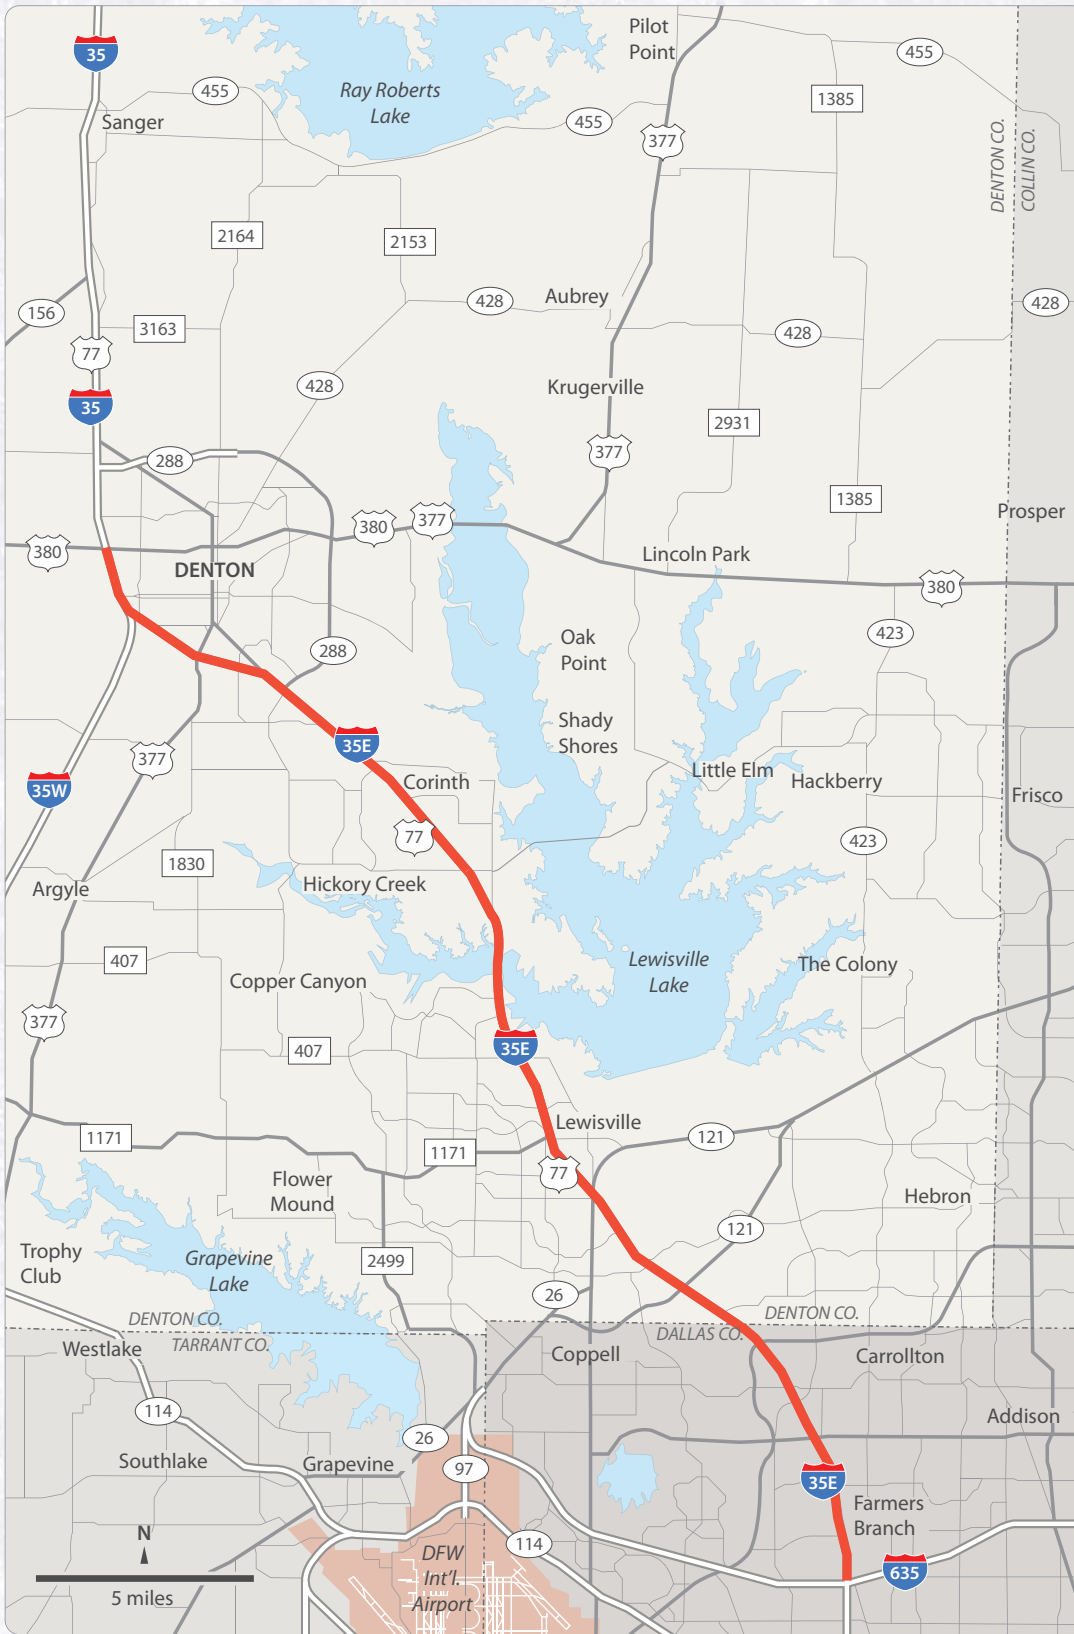

NOTE: Highlighted areas are not to scale.

Roadway and Limits	Existing frontage road lanes (Each dir.)	Existing main lanes (Each dir.)	Existing HOV lanes (Each dir.)	Interim** frontage road lanes (Each dir., 2016)	Interim** general purpose lanes (Each dir., 2016)	Interim** reversible managed lanes (2016)	Proposed frontage road lanes (Each dir., 2030)	Proposed general purpose lanes (Each dir., 2030)	Proposed managed lanes (Each dir., 2030)
South: North of I-635 to President George Bush Turnpike	2 - 3*	3	1	2 - 3	3	2	2 - 3	4	2
Middle: President George Bush Turnpike to Turbeville Rd.	2 - 3*	3	0	2 - 3	3** - 4	2	2 - 3	4	2
North: Turbeville Rd. to U.S. 380	2 - 3	2	0	2 - 3	3	0	2 - 3	3	1 - 2

* Discontinuous. ** PG&T to SH 121. *** Interim configuration relies primarily on use of existing pavement for expansion. Final configuration involves reconstruction of remainder of the corridor. TxDOT graphic

PROJECT CONTACTS



Texas Department of Transportation
 4777 East Highway 80
 Mesquite, TX 75150
 214-320-6100
Project Website: www.35Express.org



Kimberly Sims
 AGL Constructors
 Public Information Coordinator
 2420 S. Stemmons Frwy
 Lewisville, TX 75067
 214-483-7778

Tony Hartzel
 TxDOT DFW Strategic Projects
 Public Information Supervisor
 4777 E. Highway 80
 Mesquite, TX 75150
 214-320-4481
