



PROJECT INFORMATION SHEET

U.S. ARMY CORPS OF ENGINEERS

BUILDING STRONG

C-GLFER-Elkhart River & Christiana Creek Dams, Elkhart, IN


Description

The project is located in Elkhart County, in the City of Elkhart, Indiana. The Elkhart Dam fish passage and riverine restoration site is located northeast of Elkhart Avenue and Waterfall Drive, while the Christiana Creek Dam riverine restoration site is located northeast of East Crawford and Cassopolis Street. The Elkhart River and Christiana Creek are two tributaries to the St. Joseph River, which extends a total of 210 miles through portions of northern Indiana and southern Michigan before flowing into Lake Michigan. Both have dams located in Elkhart that substantially alter the character of the riverine water system; they have also played a central role in the decline of migratory aquatic species by severing their historic migration routes and preventing healthy recruitment. The dams effectively obstruct some 20-30 native fish species, including the state endangered Greater Redhorse and the highly prized Walleye. The restoration project would enable the passage of aquatic species to far reaching areas above the dams, improve the riverine habitat for endangered and threatened fish and mussel species, and stabilize the stream bank and naturalize sediment transport.

Congressional Interest

Walorski (IN-2); Senator Coats (IN), Senator Donnelly (IN)

Location Map & Picture

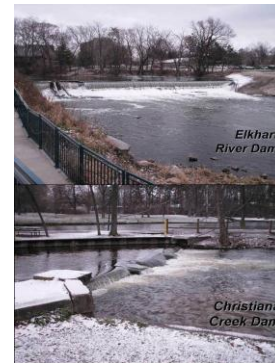

Non-Federal Project Sponsor

City of Elkhart, IN

Project Authority

Section 506 of WRDA 2000, as amended - Great Lakes Fishery and Ecosystem Restoration (GLFER)

Funding	Total	Federal	Non-Federal
Current Working Estimate:	\$ 2,200,000	\$ 1,430,000	\$ 770,000
Funds Allocated prior to FY16:	\$ 438,864	\$ 438,864	\$ 0
E and W Funds Allocated prior to FY16:	\$ 0	\$ 0	\$ 0
GLRI Funds Allocated prior to FY16:	\$ 438,864	\$ 438,864	\$ 0
FY16 Energy and Water Allocation:	\$ 0	\$ 0	\$ 0
FY16 GLRI Allocation:	\$ 75,000	\$ 75,000	\$ 0
FY17 Budget:	\$ 0	\$ 0	\$ 0
Funds required to complete (>FY17):	\$ 1,686,136	\$ 916,136	\$ 770,000

Stage

Design and Implementation

Status

Great Lakes Restoration Initiative (GLRI) funds were used to prepare the Detailed Project Report (DPR) and associated Environmental Assessment (EA). The DPR was approved by LRD in March 2014. Preparation of detailed plans and specs will commence upon execution of a Project Partnership Agreement (PPA). Per request by the City of Elkhart, the PPA will be delayed until mid-FY16, with construction award possible in FY17.

U.S. ARMY CORPS OF ENGINEERS - DETROIT DISTRICT

PM: Carl Platz, 616-842-5510 ext 25521, Carl.A.Platz@usace.army.mil

477 Michigan Ave., Detroit, MI 48226-2550

<http://www.lre.usace.army.mil>

Last Updated: 27-Jan-16
