

Sonic Enhanced Ash Agglomeration and Sulfur Capture

**Quarterly Report
January - March 1996**

RECEIVED
JUL 16 1996
OSTI

Work Performed Under Contract No.: DE-AC21-89MC26288

For
U.S. Department of Energy
Office of Fossil Energy
Morgantown Energy Technology Center
P.O. Box 880
Morgantown, West Virginia 26507-0880

By
Manufacturing and Technology Conversion International, Incorporated
P.O. Box 21
Columbia, Maryland 21045 - 0021

DISTRIBUTION OF THIS DOCUMENT IS UNLIMITED
April 1996

MASTER

DISCLAIMER

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

Available to the public from the National Technical Information Service, U.S. Department of Commerce, 5285 Port Royal Road, Springfield, VA 22161; phone orders accepted at (703) 487-4650.

PREFACE

This 27th Quarterly Technical Progress Report presents the results of work accomplished during the period January 1, 1996 - March 24, 1996 (January, February and March) under Contract No. DE-AC21-88MC26288 entitled "Sonic Enhanced Ash Agglomeration and Sulfur Capture."

During this reporting period, design and fabrication of the system continued.

TABLE OF CONTENTS

	<u>Page</u>
1.0 INTRODUCTION	1
1.1 PROJECT DESCRIPTION AND WORK STATUS	1
1.2 PROGRAM OBJECTIVES	2
1.3 SUMMARY STATUS FOR THE PERIOD	2
2.0 TECHNICAL DISCUSSION OF THE WORK ACCOMPLISHED DURING THE REPORTING PERIOD	3
3.0 PLANS FOR NEXT PERIOD	8

LIST OF FIGURES

	<u>Page</u>
FIGURE 1 SLAG HANDLING AND ASH DRAIN SECTIONS	4
FIGURE 2 REBURNING COAL INJECTOR	5
FIGURE 3 ASH RECYCLING SECTION	6

LIST OF TABLES

TABLE 1 DESIGN AND FABRICATION STATUS OF BIMODAL PDU	7
---	---

SECTION 1.0

INTRODUCTION

1.1 PROJECT DESCRIPTION AND WORK STATUS

A major concern with the utilization of coal in directly fired gas turbines is the control of particulate emissions and reduction of sulfur dioxide, and alkali vapor from combustion of coal, upstream of the gas turbine. Much research and development has been sponsored on methods for particulate emissions control and the direct injection of calcium-based sorbents to reduce SO₂ emission levels. The results of this research and development indicate that both acoustic agglomeration of particulates and direct injection of sorbents have the potential to become a significant emissions control strategy.

The Sonic Enhanced Ash Agglomeration and Sulfur Capture program focuses upon the application of an MTCI proprietary invention (Patent No. 5,197,399) for simultaneously enhancing sulfur capture and particulate agglomeration of the combustor effluent. This application can be adapted as either a "hot flue gas cleanup" subsystem for the current concepts for combustor islands or as an alternative primary pulse combustor island in which slagging, sulfur capture, particulate agglomeration and control, and alkali gettering as well as NO_x control processes become an integral part of the pulse combustion process.

The goal of the program is to support the DOE mission in developing coal-fired combustion gas turbines. In particular, the MTCI proprietary process for bimodal ash agglomeration and simultaneous sulfur capture will be evaluated and developed. The technology embodiment of the invention provides for the use of standard grind, moderately beneficiated coal and WEM for firing the gas turbine with efficient sulfur capture and particulate emission control upstream of the turbine. The process also accommodates injection of alkali gettering material if necessary. This is aimed at utilization of relatively inexpensive coal fuels, thus realizing the primary benefit being sought by direct firing of coal in such gas turbine systems. The proposed technology provides for practical, reliable,

and capital (and O&M) cost-effective means of protection for the gas turbine from impurities in the coal combustor effluent.

1.2 PROGRAM OBJECTIVES

The major objective of the Phase I test program is to confirm the feasibility of the MTCI bimodal particle size approach to enhance particulate control by acoustic ash agglomeration. An ancillary objective of the Phase I effort is to demonstrate and confirm the feasibility of an acoustic field to enhance sulfur capture by increasing sorbent reactivity. Phase I tests are designed to cover the frequency range between 50 and 1400 Hz, establish monomodal baseline performance as a benchmark from which to measure the degree of enhancement expected from the bimodal approach, and, finally, to confirm the effectiveness of low-frequency fields over high-frequency fields for realistic particulate streams.

The program will demonstrate the effectiveness of a unique approach which uses a bimodal distribution composed of large sorbent particles and fine fly ash particles to enhance ash agglomeration and sulfur capture at conditions found in direct coal-fired turbines. Under the impact of high-intensity sound waves, sorbent reactivity and utilization, it is theorized, will increase while agglomerates of fly ash and sorbents are formed which are readily collected in commercial cyclones. The work will extend the concept from the demonstration of feasibility (Phase I), through proof-of-concept (Phase II) to the construction (Phase III) of a coal-fired pulsed combustor with in-furnace sorbent injection. For Phase I, Pennsylvania State University will conduct studies for enhanced sulfur capture in The Combustion Laboratory and agglomeration tests in the High Intensity Acoustic Laboratory.

1.3 SUMMARY STATUS FOR THE PERIOD

During this reporting period, design and fabrication of the system continued.

SECTION 2.0

TECHNICAL DISCUSSION OF THE WORK ACCOMPLISHED DURING THE REPORTING PERIOD

2.1 TASK 2: ADDITIONAL TEST FACILITY MODIFICATIONS AND SHAKEDOWN TESTING

During this reporting period, work on design and fabrication continued. The design of the slag-handling and ash-drain sections was completed (Figure 1). The design and fabrication of the reburning coal injector was also completed (Figure 2). The pulse combustor air plenum has almost been completed (about 90%). Components of the ash recycling section are shown in Figure 3.

Fabrication of the structural support of the bimodal PDU was begun.

Table 1 shows the design and fabrication status of the bimodal unit and components.

PE stamped drawings and support data will be submitted to the Maryland State Chief Boiler Inspector for review and approval.

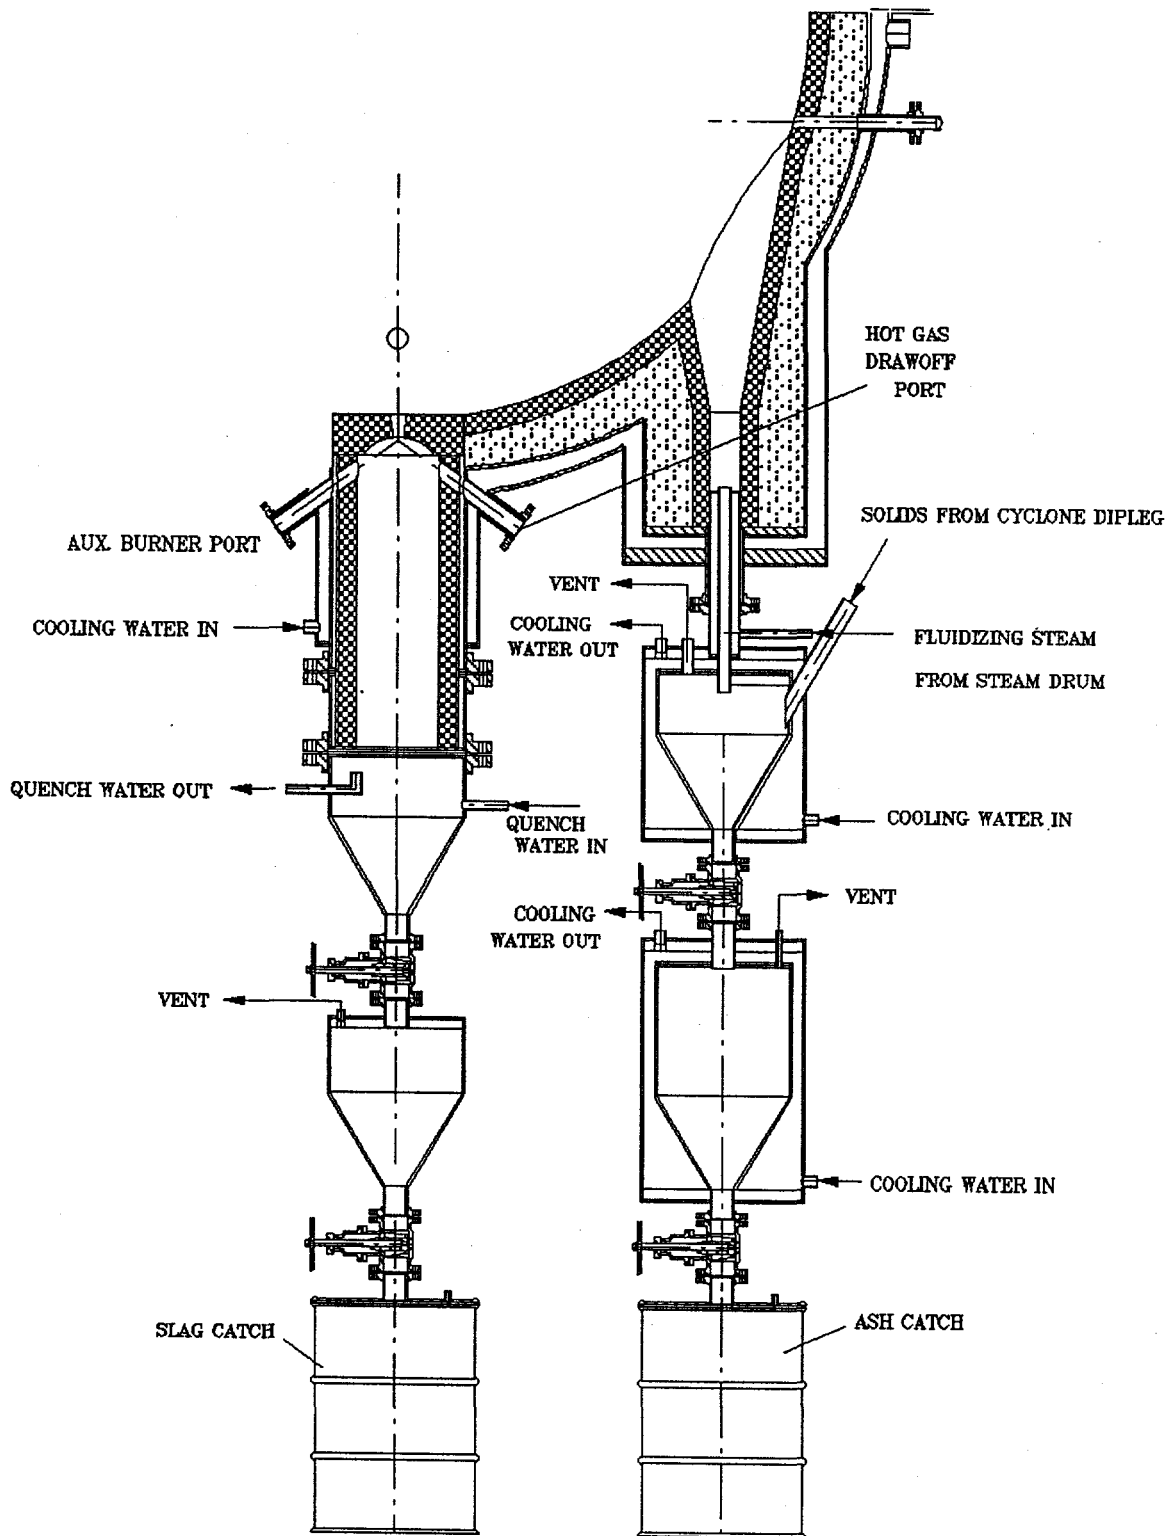


FIGURE 1: SLAG-HANDLING AND ASH DRAIN SECTIONS

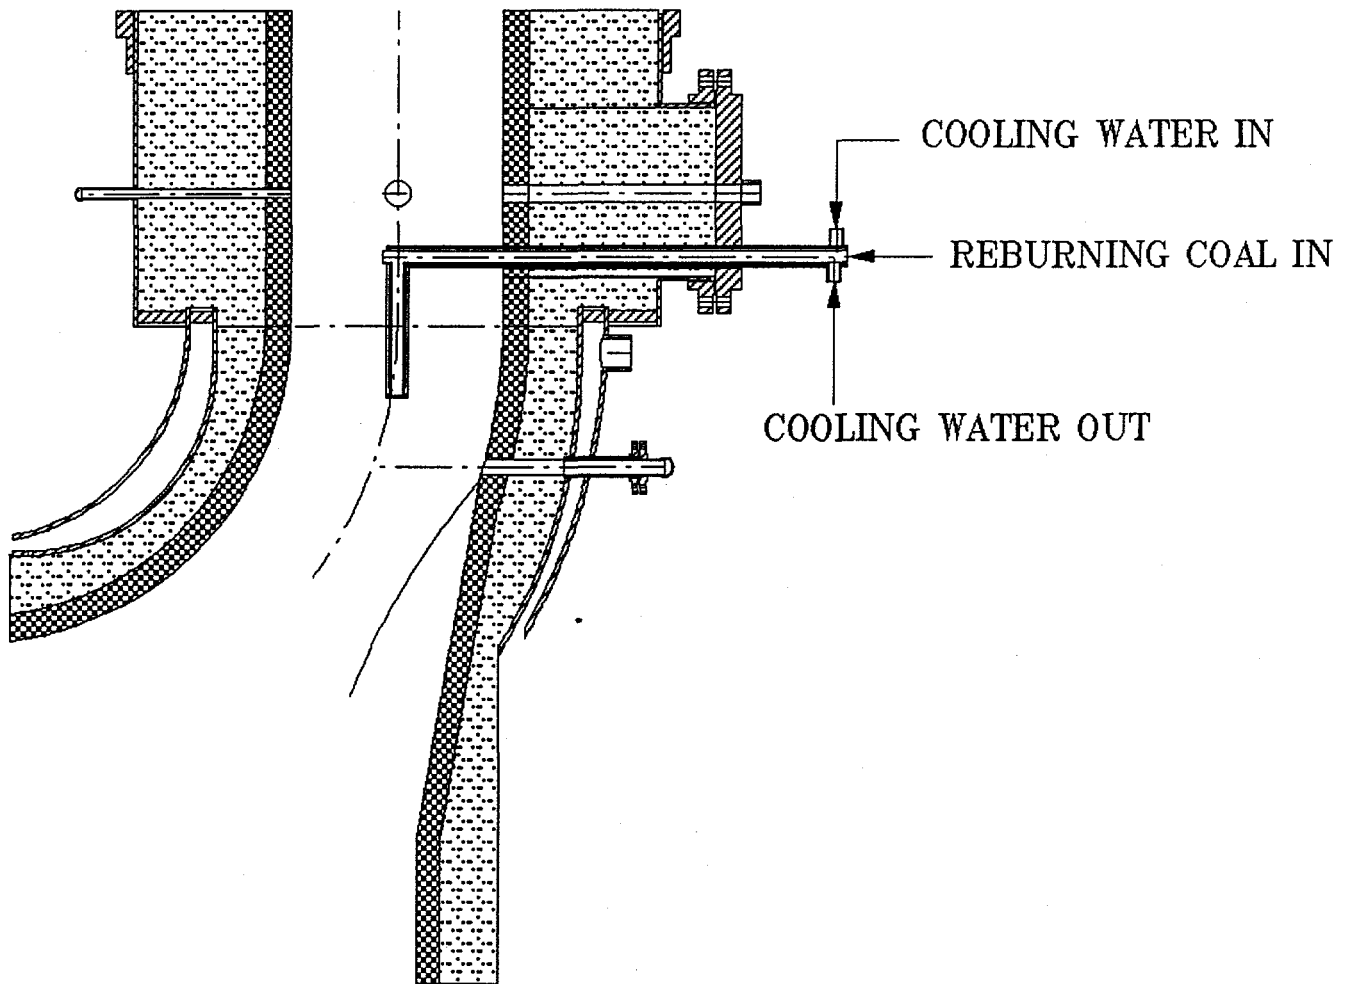


FIGURE 2: REBURNING COAL INJECTOR

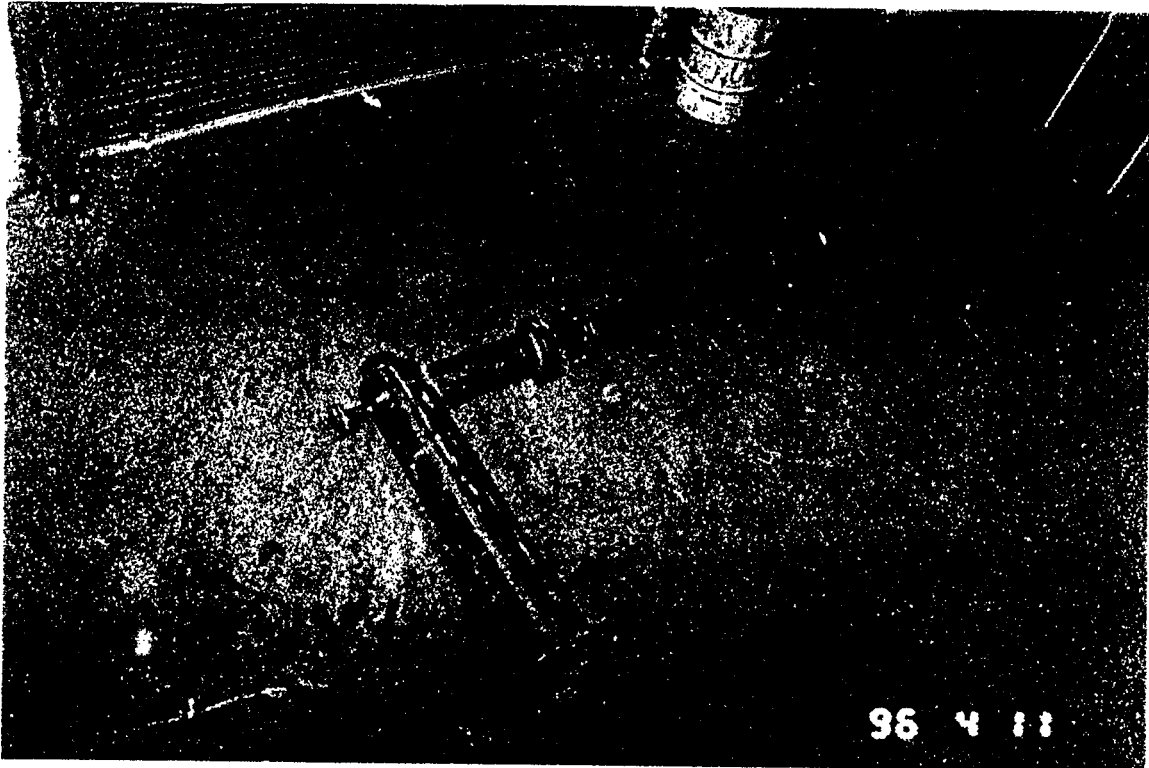


FIGURE 3: ASH RECYCLING SECTION

TABLE 1:
DESIGN AND FABRICATION STATUS OF BIMODAL PDU

Item No.	Description of Components	Design Accomplished, %	Fabrication Accomplished, %
1	Air plenum	100	90
2	Coal injector	100	100
3	Pilot burner	100	100
4	Aerovolve	100	100
5	Water jacket of pulse combustor	100	65
6	U-bend water jacket	100	100
7	Agglomeration chamber (60" dia.)	100	100
8	Slag-handling section	100	10
9	Ash drain section	100	10
10	Reburning coal injector	100	100
11	Primary cyclone	100	100
12	Secondary cyclone	*	*
14	Dipleg and ash recycle section	100	100
15	Refractory and insulation	100	8
16	Splitter of coal and air mixture	0	0
17	Flue gas heat exchanger	50	0
18	Steam drum	0	0
19	Air preheater in the flare	0	0
20	Structure	100	0
21	Instrumentation and control	70	0
22	Modification for pressure test	100	100
23	Concrete pad	100	100
24	Flanges for hydro testing	100	100
25	Hydrostatic test	-	100

* Primary cyclone of the previous configuration to be refurbished.

SECTION 3.0

PLANS FOR NEXT PERIOD

- Complete the design of the PDU.
- Complete the fabrication of the PDU components.
- Continue fabrication of the structure.
- Refractory-line the components.
