

March 2012 Construction Photos



Balfour Beatty laborers bolt on 84" diameter butterfly valve on discharge pipe.



Looking downstream at an overall view of the sump bay trash rack installation.

March 2012 Construction Photos



Balfour Beatty subcontractor Central Sierra Electric installing the cable tray at the pumping plant.



Installing geocell grid for oil spill containment basin of transformer at the switch yard.

March 2012 Construction Photos



Rigging the valve shaft for the 60" butterfly valve for pump #1.



Installing the torque tube at the 84" butterfly valve for pump #3.

March 2012 Construction Photos




Balfour Beatty laborers setting a pump motor on a pedestal with the assistance of a 120 ton crane.



Balfour Beatty subcontractor Corpro welding for cathodic protection system to discharge pipe.

March 2012 Construction Photos

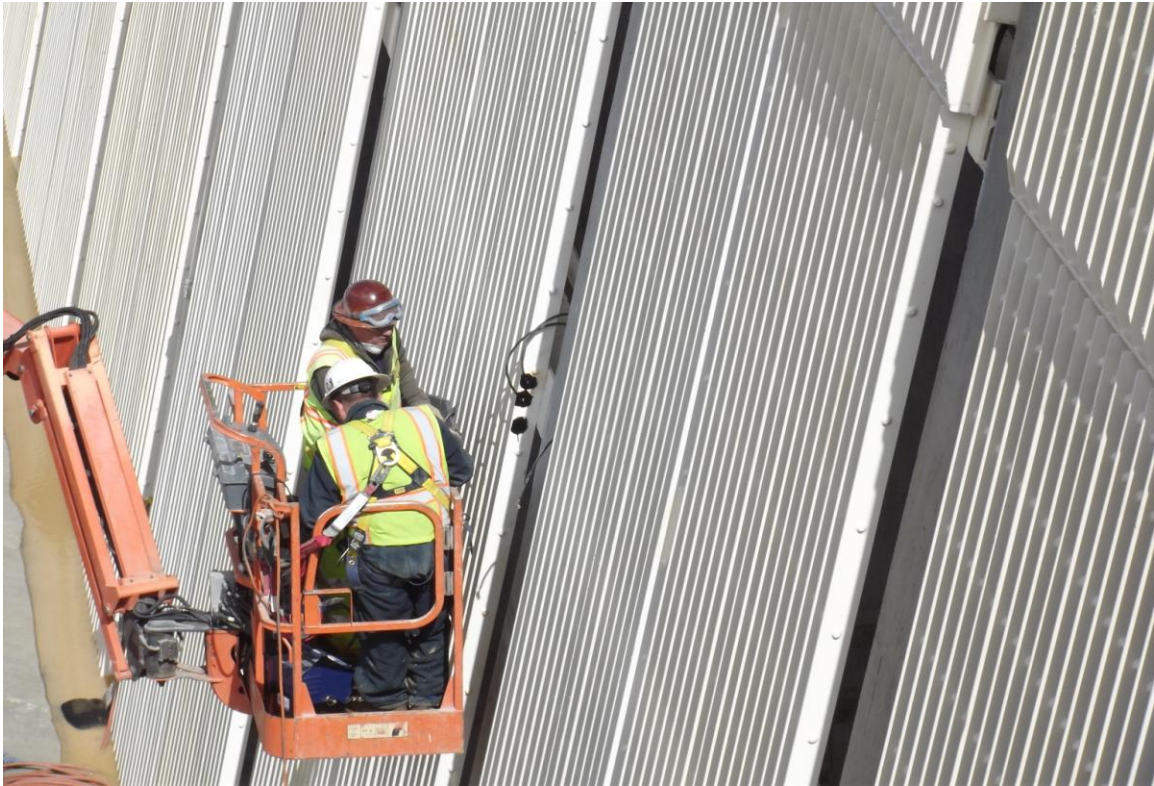

Balfour Beatty Crew touching up paint on trash rack at the forebay.



Balfour Beatty subcontractor Central Sierra electricians placing concrete dyed red in the duct bank.
