



UNITED STATES  
NUCLEAR REGULATORY COMMISSION  
WASHINGTON, D.C. 20555-0001

September 10, 1999

TO: Robert C. Pierson, Chief  
Special Projects Branch  
Division of Fuel Cycle Safety  
and Safeguards, NMSS

THRU: Melanie A. Galloway, Section Chief  
Enrichment Section  
Special Projects Branch  
Division of Fuel Cycle Safety  
and Safeguards, NMSS

Handwritten signature of Melanie A. Galloway in black ink.

FROM: Drew Persinko, Sr. Nuclear Engineer  
Special Projects Branch  
Division of Fuel Cycle Safety  
and Safeguards, NMSS

Handwritten signature of Drew Persinko in black ink.

SUBJECT: SUMMARY OF MEETING WITH DUKE COGEMA STONE & WEBSTER TO  
DISCUSS DESIGN AND LICENSE APPLICATION FOR THE MIXED OXIDE  
FUEL FABRICATION FACILITY

On August 31, 1999, the Nuclear Regulatory Commission (NRC) staff met with representatives from Duke Cogema Stone & Webster (DCS) and the Department of Energy (DOE) to discuss design of a mixed oxide fuel fabrication facility (MOX-FFF) and license application submittal schedules. The meeting agenda and slides used in the presentation are attached (Attachments 1 and 2, respectively). Also attached is a list of attendees (Attachment 3).

The meeting began with a brief update of the status of the MOX project by DCS followed by an update of the status of the Part 70 proposed rule and associated standard review plan and the MOX standard review plan by NRC. The Part 70 rule is out for public comment with the comment period closing on October 13, 1999; the staff is also accepting comments on the associated standard review plan. The MOX standard review plan is estimated to be completed in January 2000. DCS presented a design summary that included discussions of process and facility interfaces, the aqueous polishing process, the MOX fuel fabrication process, and preliminary design information in the structural, mechanical, electrical, I&C, safeguards and security and nuclear safety areas. Following the design presentation, participants held a discussion concerning licensing schedules. Preliminary schedules presented by the applicant call for an application to be submitted in September 2000, final design to be completed in March 2002, construction to be completed in March 2006, and startup in April 2006. NRC stated that the governing regulations are 70.23(a)(7), 70.23(a)(8) and 70.23(b). These regulations require that NRC approve the start of construction after it has determined that the design bases of the principal structures, systems, and components and the quality assurance program provide reasonable assurance of protection against natural phenomena and the consequences of potential accidents and after an environmental impact statement (EIS) has been completed. The regulations also require that, before a license is issued to operate a plutonium facility, the NRC must conclude that construction of the principal structures, systems, and components,

September 10, 1999

2

whose design bases were previously approved by the staff before construction, has been completed in accordance with the application. The staff has not determined the exact mechanism that it would use to allow the start of construction (e.g., letter, license), but the licensing process to be followed will be the same regardless of the mechanism. NRC stated that there can be one or two opportunities for a public hearing and that this is a function of the amount of information submitted by the applicant depending on the path chosen by the applicant. If, at the outset, complete information (design bases, design and operation) is submitted, it is possible to offer one opportunity for a hearing to cover all issues. Alternatively, if the initial submittal includes some lesser amount of information sufficient to support the decision to allow construction to commence but not enough to support issuance of a license to possess material and operate the facility, then there will be two opportunities for hearings. DCS and DOE indicated that a two-submittal approach was more likely due to full information not being available at the time the initial application is submitted.

Since the regulations require that the design bases be approved by NRC, as a minimum, before construction can commence, and Part 70 does not include a definition of design bases, the design bases definition in Part 50 was discussed. The staff concluded that it will review the definition of design bases and include a definition in the MOX standard review plan being developed. In the meantime, the applicant suggested that it will proceed using the Part 50 definition of design bases as a starting point. The NRC staff also suggested that some portions of the application and supporting information (e.g., quality assurance plan and certain computer validation reports) may be submitted before the application is submitted, to support the applicant's proposed schedule. In conclusion, staff suggested that the applicant formulate a revised schedule based on an overall licensing strategy considering information discussed at the meeting. That strategy is a function of the amount of information the applicant intends to include in its initial and subsequent submittals.

Concerning the MOX standard review plan, the applicant indicated that it may be beneficial to discuss the NRC's design bases in priority areas (e.g., criticality) before the draft MOX SRP is released in January 2000. The NRC indicated that it would support these types of meetings before the January 2000 issuance date for the MOX standard review plan for public comment; the applicant will provide a list of priority discussion areas.

The applicant asked how the NRC would address National Environmental Policy Act (NEPA) requirements for the licensing and construction of the MOX facility and if the NRC planned to provide comments on a DOE Environmental Impact Statement (EIS) on MOX. The NRC staff responded that an EIS would be necessary to satisfy NRC requirements under NEPA; the NRC anticipates reviewing DOE's MOX EIS within the context of the MOX license application to determine to what extent the NRC could adopt that work. Since the applicant may submit the DOE's EIS as its environmental report, the NRC will forgo commenting on the EIS at this time.

Attachments: 1. Agenda  
2. Slides  
3. Attendees

## AGENDA

### NRC / DUKE COGEMA STONE&WEBSTER (DCS) MOX MEETING August 31, 1999

- Introduction of NRC and DCS staff
- Project Status Update (DCS)
- Status Update of 10 CFR Part 70 and NUREG 1520 (NRC)
- Status Update of MOX SRP (NRC)
- MOX Preliminary Design Information Based on MELOX and LaHague (DCS)
- Schedule of Licensing Submittals and NRC Reviews, and Overall Project Design and Construction (DCS and NRC)
- Closing Remarks and Future Activities (DCS and NRC)



DUKE COGEMA  
STONE & WEBSTER

# **MOX Fuel Fabrication Project**

**presentation to**

**Nuclear Regulatory Commission  
Office of Nuclear Materials Safety & Safeguards**

**DUKE COGEMA STONE & WEBSTER**

**August 31, 1999**

---



## Meeting Objectives and Agenda

- Meeting Objectives
  - Reintroduce DCS & new NMSS MOX support staff
  - Present MOX fuel fabrication facility (MFFF) design
  - Discuss licensing details
- Agenda
  - Introduction of DCS and new NMSS staff DCS/NRC
  - Project status update Mathews (DCS)
  - Status update on 10CFR70, NUREG-1520 NRC
  - Presentation of MFFF design MFFF Design staff (DCS)
  - Licensing submittals and reviews - Round Table DCS/NRC/DOE
  - Identification/resolution of technical issues DCS/NRC

---

August 31, 1999

Page 1



## Opening Remarks

- Review of previous presentation (27 May 1999)
  - Introduction/Points of Contact
  - Overview of MOX project, fabrication facility
  - Discussion of licensing strategy

---

August 31, 1999

Page 2



# Introducing Duke Cogema Stone & Webster, LLC


From 27 May 1999 presentation

- Private-sector consortium contracted by DOE
- Mission: convert plutonium to spent nuclear fuel
  - Design, license, construct, and operate a MOX fuel fabrication facility (MFFF)
  - Perform qualification program for MOX fuel lead assemblies
  - Design shipping containers for MOX fuel assemblies
  - Irradiate MOX fuel at commercial reactors



# Duke, Cogema, Stone & Webster, LLC

From 27 May 1999 presentation



### MAJOR SUBCONTRACTORS





DUKE COGEMA  
STONE & WEBSTER

## DCS Organization/Points of Contact

DUKE COGEMA STONE & WEBSTER  
PO Box 31847  
Charlotte, NC 28231-1847

parcel address:  
400 South Tryon Street  
Charlotte, NC 28202

FAX:  
(704) 382-5815  
(704) 373-7838

**R H (Bob) Ihde**  
President & CEO  
**Toney A Mathews**  
Executive VP & COO

(704) 373-7811  
rhihde@dukeengineering.com

(704) 373-7833  
tamathew@dukeengineering.com

**Don B Blackburn**  
Project Development  
& Outreach

**Nareesh C Jan**  
Project Services  
& Administration

**R J (Jim) Braslett**  
Quality Assurance

**R A (Bob) Joyner**  
Chief Financial  
Officer

**Mary L Birch**  
Environment, Safety  
& Health

**Charles R Pollard**  
Project Control  
& Integration

(704) 373-7959  
ejbrabazon@dukeengineering.com

(704) 373-7820  
pshastings@dukeengineering.com

**George Meyers**  
Fuel Qualification  
and Design

**Richard H Clark**  
Fuel Irradiation

**Edward J Brabazon**  
Senior VP &  
Chief Engineer

**John E Matheson**  
Fuel Fabrication  
Services

**Peter S Hastings**  
Licensing Manager

**Joe M King**  
Construction  
Management

**Ray E Fortier**  
Facilities Design

**Jean-Marc Belmont**  
Process Design

(804) 832-3433  
jmatheson@framatech.com

From 27 May 1999 presentation

August 31, 1999

Page 5



DUKE COGEMA  
STONE & WEBSTER

## MOX Project Overview

- Complements immobilization as part of DOE's surplus plutonium disposition program
- MOX contract divided into four phases
  - Base contract: MFFF plant design and license application qualification program  
identification of utility modifications
  - Option one: construction of MFFF
  - Option two: startup and operation of MFFF  
irradiation of MOX fuel
  - Option three: deactivation

From 27 May 1999 presentation

August 31, 1999

Page 6



## Project Status

- Detailed planning, project baseline, Project Management Plan in DOE review (establishes baseline)
- Interactions with NRR by Fuel Qualification and Fuel Irradiation; qualification and irradiation plans well underway
- Initial Preliminary Design presented to DOE
- QA plan approved, development of QA procedures in progress
- MOX fuel assembly transportation package certification plan in DOE review

August 31, 1999

Page 7



## MOX Project Schedule Overview

- MFFF Final Design March 2002
- Complete Construction March 2006
- Facility Startup April 2006
- Commence batch irradiation  
at mission reactors September 2007

*(please note all dates are planning estimates)*

From 27 May 1999 presentation

August 31, 1999

Page 8





DUKE COGEMA  
STONE & WEBSTER

# MOX Fuel Fabrication Facility (MFFF)


Ed Brabazon  
MFFF Engineering Manager

---



DUKE COGEMA  
STONE & WEBSTER

## MOX FFF Design Organization

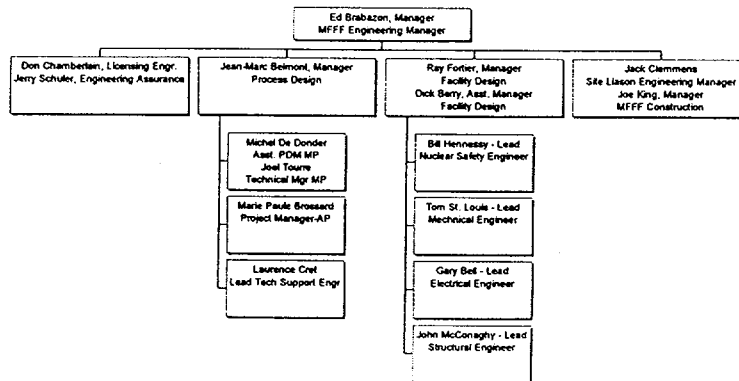

August 31, 1999

Page 10



DUKE COGEMA  
STONE & WEBSTER

## Design Summary

- General
- Major Assumptions
- Process / Facility Interfaces
- MFFF Interfaces with FQ, FI and PDCF
- Major Technical Accomplishments

August 31, 1999

Page 11



DUKE COGEMA  
STONE & WEBSTER

## General

- 36-month design schedule
- Major schedule milestones
- Major Components of Design
  - MOX Process Design
  - Aqueous Polishing Design
  - Facility Design
  - License Application

---

August 31, 1999

Page 12



DUKE COGEMA  
STONE & WEBSTER

## Major Assumptions

- MOX process (MP) based on MELOX design
- Aqueous Polishing (AP) based on La Hague experience
- Purchase selective equipment overseas
- Initiate equipment procurement in Month 37 (Part of Option 1)
- Will evaluate need for long lead procurement
- Baseline for Pu isotopics composition

---

August 31, 1999

Page 13



DUKE COGEMA  
STONE & WEBSTER

## Process / Facility Interfaces

- Process Design develops
  - Process flow diagrams
  - Equipment sizing
  - Initial machine location drawings
- Facility Design develops U.S. Criteria and BOP design
- Process Design developing building layouts
- Facility Design developing initial generic site plan
- Work split on process equipment design based on Type I, II, or III classification

---

August 31, 1999

Page 14



DUKE COGEMA  
STONE & WEBSTER

## Process / Facility Interfaces (cont.)

- Both develop equipment specifications (systematic transfer of responsibility).
- Process Group will review and approve the design of process equipment by Facility Group

---

August 31, 1999

Page 15



DUKE COGEMA  
STONE & WEBSTER

## MFFF Interfaces with FQ, FI and PDCF

- Pu isotopics
- Pu impurities
- Pu loading w%
- Pu density
- Host site agreements
- Specification for fuel shipping cask

---

August 31, 1999

Page 16



DUKE COGEMA  
STONE & WEBSTER

## Major Technical Accomplishments - Aqueous Polishing Building

- Documentation of process choices
- Define process design criteria
- Perform lessons learned from La Hague
- Establish flow diagram
- Outline of description notes
- Perform preliminary criticality calculations notes
- Preliminary sizing of process units for input to general layout

---

August 31, 1999

Page 17



DUKE COGEMA  
STONE & WEBSTER

## Major Technical Accomplishments - MOX Process (MP) Building

- Basic principles of plant layout
- Preliminary general flow chart
- Draft safety basis of design
- Draft MP design requirements
- Perform lessons learned from MELOX
- Preliminary sizing of process units for input to general layout
- Perform preliminary criticality and thermal calculations notes

---

August 31, 1999

Page 18



DUKE COGEMA  
STONE & WEBSTER

## Major Technical Accomplishments - Facility Design

- Drafted design criteria for :
  - Nuclear Technology
  - Structural, civil and geotechnical
  - Mechanical
  - Electrical, S&S and I&C
- Developed conceptual site plan

---

August 31, 1999

Page 19



DUKE COGEMA  
STONE & WEBSTER

## QUALITY ASSURANCE

### MOX Project Quality Assurance Plan

- Quality Levels
- COGEMA QA Plan
- Design Control
- Design Verification

---

August 31, 1999

Page 20



DUKE COGEMA  
STONE & WEBSTER

## Design Features & Design Criteria

- Aqueous Polishing
- MOX Process
- Facilities

---


August 31, 1999

Page 21



DUKE COGEMA  
STONE & WEBSTER

## Aqueous Polishing and MOX Process main steps

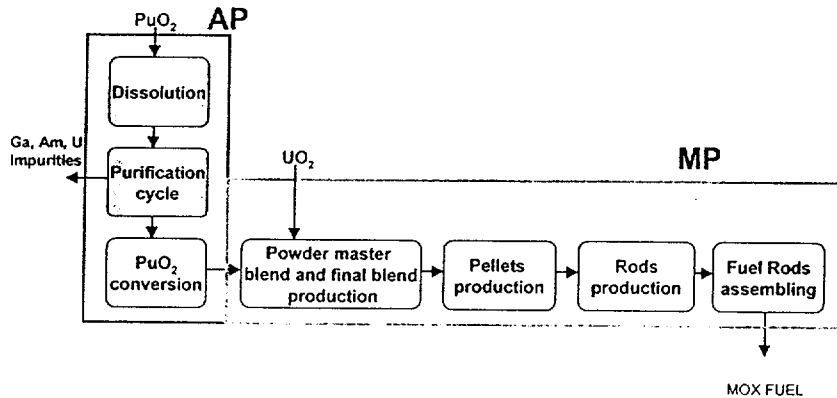

August 31, 1999

Page 22



DUKE COGEMA  
STONE & WEBSTER

## Aqueous Polishing Process

step 1.  $\text{PuO}_2$  Dissolution by **electro-generated Ag(II)**

Process selected because it is very efficient,  
independent of  $\text{PuO}_2$  powder characteristics,

step 2. Pu Purification by **solvent extraction**

Process selected because it yields very little Pu  
leakage and has a very high gallium  
decontamination factor .

August 31, 1999

Page 23





DUKE COGENA  
STONE & WEBSTER

## Aqueous Polishing Process

### step 3. Conversion into $\text{PuO}_2$ by oxalate calcination

Process selected because it yields a  $\text{PuO}_2$  powder  
routinely used for MOX fabrication

This process will be continuous



DUKE COGENA  
STONE & WEBSTER

## Aqueous Polishing: Pu Characteristics W-GRADE Pu

- Input (Oxide powder from PDCF)
  - granulometry: 100% < 500  $\mu\text{m}$   
99% > 5  $\mu\text{m}$
  - Isotopy: (criticality calculations)  $^{239}\text{Pu}$ : < 96%;  
 $^{240}\text{Pu}$ : > 4%;
  - Specific gravity (criticality calculations): < 7
- Impurities
  - $^{241}\text{Am}$  < 0.7%
  - Ga < 12000  $\mu\text{g/g}$  of Pu
  - others impurities section H4 of SOW



## Aqueous Polishing: Pu Characteristics W-GRADE Pu

- Output (Sinterable Oxide powder)
  - Isotopy: (criticality calculations)  
 $^{239}\text{Pu}$  : <96% ;  $^{240}\text{Pu}$  : > 4% ;
  - Specific area: ~10 m<sup>2</sup>.g<sup>-1</sup>
  - Granulometry: ~14 μm
  - $^{241}\text{Am}$  < 5 ppm
  - Ga < 0.1 μg/g of Pu
  - Specific gravity: ~1.7
  - Specific gravity (criticality calculations): <3.5
  - Humidity content (criticality calculations) : 3%



DUKE COGEMA  
STONE & WEBSTER

## DISSOLUTION PROCESS MAIN EQUIPMENT

### DECANNING EQUIPMENT (located in glove boxes)

Designed to allow the opening of ARIES Type cans (crimped lid) and BNFL Type cans (screwed lid)

It is assumed that the ARIES convenience can will be modified to reduce Pu waste (to be determined with PDCF)

### DISSOLVER (located in a glove box)

Geometrically safe equipment

Made of TITANE to eliminate corrosion problems

Volume: ~ 56L

### FILTER (located in a glove box)

To remove any remaining PuO<sub>2</sub> (The dissolution is complete under normal operation)

Below the smallest particle diameter

### RECEIVING VESSEL (located in a limited access room)

Made of TITANE to eliminate corrosion problems

Geometrically safe equipment



DUKE COGEMA  
STONE & WEBSTER

## PURIFICATION PROCESS MAIN EQUIPMENT

### **PULSED COLUMNS for purification** (located in a limited access room)

- Extraction
- Acid scrubbing
- Pu stripping
- Raffinates diluent washing

This equipment is used at the UP2-800 and UP3 plants.  
The HETS is less than one meter and is constant (UP3 has operated for 10 years).

### **MIXER SETTLERS for solvent regeneration** (located in a compartment topped by a glove-box)

- Pu barrier
- Solvent regeneration steps
  - sodium carbonate washing
  - soda washing
  - nitric acid washing

---

August 31, 1999

Page 28



DUKE COGEMA  
STONE & WEBSTER

## CONVERSION PROCESS MAIN EQUIPMENT

### **PRECIPITATORS** (2 in the polishing facility)

- Located in a glove box
- Pyrex stirred bowl
- Magnetic stirrer

### **FILTER**

- Located in a glove box
- Flat, under vacuum filter

### **FURNACE**

- Located in a glove box
- Electrically heated cylinder
- Rotary screw located inside the furnace moves the powder
- The screw speed is adjusted to control the mean residence time in the calcination section

---

August 31, 1999

Page 29



## CONVERSION PROCESS MAIN EQUIPMENT

- **HOMOGENIZERS**
  - Located in a glove box
  - 2 geometrically safe tumbling mixers
  - Capacity 24 kg ( about one day of production)
  - Sized to cool the powder.

---

August 31, 1999

Page 30



## CANNING MAIN EQUIPMENT

### INTERMEDIATE CAN

Same dimensions as the La Hague convenience can, to reuse COGEMA canning equipment (proven technology and existing design)

Screwed or expendable seal lid (TBD)

### CANNING SYSTEM

Located in Glove boxes  
Reuse of the existing canning head of La Hague T4 facility

### TRANSFER TO THE MP

Pneumatic transfer  
for security reasons  
to avoid decontamination of the reusable cans

---

August 31, 1999

Page 31

## Aqueous Polishing Design Criteria



DUKE COGEMA  
STONE & WEBSTER

Principle design criteria for Aqueous Polishing process are:

- Transfer of proven dissolution, purification, conversion processes
- Transfer of proven technology from La Hague plant, or Marcoule plant ~80 % of process equipment
- Weapon grade Pu received from PDCF
- Aqueous Polishing process throughput: 3.5T/Year
- Waste strategy (EIS is bounding)

---

August 31, 1999

Page 32

## MOX Process



DUKE COGEMA  
STONE & WEBSTER

- A-MIMAS Principles
- Flowchart of production line
- Typical process units
  - Primary dosing
  - Secondary dosing

---

August 31, 1999

Page 33



## MOX PROCESS GENERAL FLOW CHART

- Main bases for the flow chart are :
- Sole type fuel assembly design (PWR)
- Pu content in primary blend : 20 %
- Scraps recycling rate capability : 16 % (in final product)
- Operating period for the entire MOX process : 42 weeks / yr
- Process charged Pu into commercial quality fuel : 99.5 %



## MOX PROCESS LAYOUT MAIN DEVELOPMENT AND ADAPTATION FROM MELOX

Incorporated in the present layout :

- Room arrangement based on contamination hazard
- Heavy units located on ground floor
- Process areas C3 surrounded by corridors
- No C3 process areas on building perimeter
- Electrical and control cabinets close to the related process units



DUKE COGEMA  
STONE & WEBSTER

## MOX Process Design Criteria

Principle design criteria for MOX process are :

- Transfer of proven A-MIMAS process
- Transfer of proven technology from MELOX ~80 % of process equipment
- Weapon grade Pu
- U.S. Plant throughput : 70 MTHM / yr
- Fuel specification according to FRAGEMA technical file
- 99.5 % of process charged Pu into commercial quality fuel
- Waste strategy (EIS is bounding)

---

August 31, 1999

Page 36



DUKE COGEMA  
STONE & WEBSTER

## Facilities Design

- Design Features
- Design Criteria

---

August 31, 1999

Page 37



DUKE COGEMA  
STONE & WEBSTER

## Site Concept - Design Features

- Personnel access
- Commercial truck deliveries
- Change rooms, rest rooms and lunch room outside the MMA
- SSTs will transport oxide to the MFFF truck bay.
- SSTs will transport MOX fuel assemblies offsite from MFFF truck bay.


August 31, 1999

Page 38



DUKE COGEMA  
STONE & WEBSTER

## Facility Features - Conceptual Site Layout

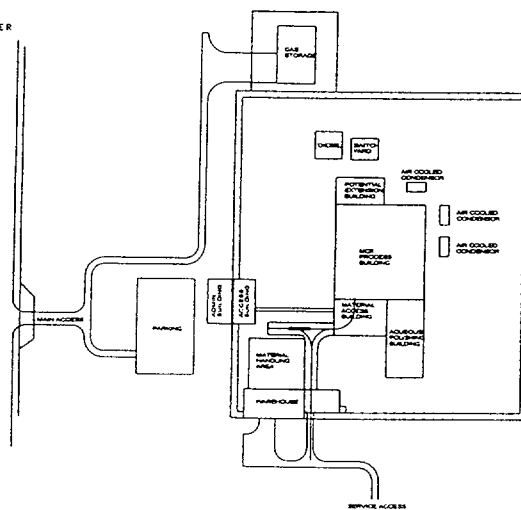

August 31, 1999

Page 39





DUKE COGEMA  
STONE & WEBSTER

## Facility Design Criteria

- Draft Basis of Design documents developed
  - Structural
  - Mechanical
  - Electrical / I&C/S&S
  - Nuclear Safety
- Designate
  - quality classifications
  - general requirements
  - applicable codes and standards
  - specific requirements

---

August 31, 1999

Page 40



DUKE COGEMA  
STONE & WEBSTER

## Structural

- Draft BOD documents prepared
  - Structural Design
  - Architectural Design
  - Site/Geotechnical Design
- No significant differences compared to normal DOE/NRC Practices
- Codes & Standards consistent with NRC expectations
- Acceptance Criteria consistent with risk-based safety classification

---

August 31, 1999

Page 41



DUKE COGEMA  
STONE & WEBSTER

## Structural

- Structural Design BOD will be referenced/invoked by individual SSC description
- Architectural Design will be conventional quality and address facility access, occupancy and site planning
- Site/Geotechnical BOD defines foundation design requirements
- Site/geotechnical BOD sets site configuration requirements and relationships between facilities

---

August 31, 1999

Page 42



DUKE COGEMA  
STONE & WEBSTER

## Mechanical

- Fluid Systems BOD
- HVAC Systems BOD
- Building Service Systems BOD
- Fire Safety BOD
- Equipment BOD
- Seismic BOD

---

August 31, 1999

Page 43



DUKE COGEMA  
STONE & WEBSTER

## Mechanical

- Establishes Design Requirements for systems and equipment
- Establishes applicable design Codes and Standards
- Establishes U.S. Requirements for glovebox design
- Functional safety & quality requirement documents
- Incorporates Host Site Requirement

---

August 31, 1999

Page 44



DUKE COGEMA  
STONE & WEBSTER

## Electrical

- Electrical Basis of Design
- I&C Basis of Design
- Safeguards and Security Basis of Design

---

August 31, 1999

Page 45



DUKE COGEMA  
STONE & WEBSTER

## Electrical

- General description of the electrical system layout
  - Normal standby emergency power sources
  - Electrical system availability
- Applicable Codes and Standards
- Raceway design requirements
- Wire and Cable design requirements
- Exterior Utility Service
- Interior Utility Service

---

August 31, 1999

Page 46



DUKE COGEMA  
STONE & WEBSTER

## Electrical

- Grounding
- Lighting
- Standby and Emergency Power
- Protection Philosophy
- Separation and Physical Independence

---

August 31, 1999

Page 47



DUKE COGEMA  
STONE & WEBSTER

## Electrical Systems

- Communications and Alarm Systems
  - The requirements for the various communications sub-systems used within the facility as well as offsite communications methods will be described
- Heat Tracing and Freeze Protection
- Cathodic Protection

---

August 31, 1999

Page 48



DUKE COGEMA  
STONE & WEBSTER

## Instrumentation and Controls

- General Requirements
  - Provides general requirements for instrument and control
- Codes, Standards, And Guides
  - Identifies NRC Requirements and Guidelines
  - Identifies Industry Codes and Standards (ANS, EPRI, IEEE, ISA, NEMA, NFPA, SAMA, UL)

---

August 31, 1999

Page 49



DUKE COGENA  
STONE & WEBSTER

## Instrumentation and Controls

- Instrumentation Systems
  - Monitor variables and systems over their anticipated ranges of operation
  - Display instrumentation provides accurate, complete, and timely information pertinent to system status
  - Graphics displays represent process equipment schematically.

---

August 31, 1999

Page 50



DUKE COGENA  
STONE & WEBSTER

## Instrumentation and Controls

- Control and Protection Systems
  - Prevent the unmonitored release of radioactive material and prevent the inadvertent occurrence of a criticality
  - The Plant Control System is PLC based
  - The Plant Protection System is PLC and hardwired based distributed control system independent of the control system

---

August 31, 1999

Page 51



DUKE COGEMA  
STONE & WEBSTER

## Safeguards and Security

- General Requirements
  - Threats
  - Protection of Special Nuclear Material & Vital Equipment
  - Security & Restricted Access Areas
- Applicable Codes and Standards
  - Provides definition of applicable DOE orders and manuals, NRC required documents and industry codes and standards

---

August 31, 1999

Page 52



DUKE COGEMA  
STONE & WEBSTER

## Safeguards and Security

- Specific Requirements
  - Intrusion Detection and Assessment Systems
  - Access Control & Entry/exit Inspection
  - Barriers & Locks
  - Secure Storage
  - Communication Maintenance Power
  - Nuclear Material Control & Accounting Safeguards

---

August 31, 1999

Page 53



DUKE COGENA  
STONE & WEBSTER

## Nuclear Safety

- Integrated Safety Analysis
- Nuclear Criticality Safety
- Environmental Permitting
- Radiation Protection
- Emergency Preparedness
- Deactivation
- Waste Management

---

August 31, 1999

Page 54



DUKE COGENA  
STONE & WEBSTER

## Nuclear Safety

- Integrated Safety Analysis
  - Based on requirements from proposed 10 CFR 70 changes (6/2/99), NUREG-1520, NUREG-1513, OSHA, EPA
- Nuclear Criticality Safety
  - Accidental criticality prevention, double contingency, crit monitors, NCS admin control program described
- Environmental Requirements
  - Air, surface water, drinking water, RCRA, noise control are described.

---

August 31, 1999

Page 55





## Nuclear Safety

- Radiation Protection
  - RP design features are described, including an ALARA Design: facility layout, rad zone maps, access control, containment and confinement, shielding
  - Includes Rad monitoring: area, airborne, and effluent
  - Also Health Physics: facilities and equipment, outside/host site support
- Emergency Preparedness
  - Host Site: site Emergency Plan input
  - Emergency response organization, facilities, equipment



## Nuclear Safety

- Deactivation
  - Deactivation is an intermediate step between shutdown & decommissioning
- Waste Management
  - Includes TRU waste storage, glovebox dust abatement, shipping containers, deactivation
  - WIPP and host site WAC



DUKE COGEMA  
STONE & WEBSTER

# MFFF Design Topics





DUKE COGEMA  
STONE & WEBSTER

## Safety

---

- Preliminary Hazards Analysis (PHA)
  - Good engineering practice
  - Early identification of significant impacts on the MOX FFF design
  - Support of the initial identification of IROFS
  - Support of functional classification of equipment
  - Identify initial bounding hazards and accidents for initial screening process

---

August 31, 1999

Page 59



DUKE COGEMA  
STONE & WEBSTER

## Safety

---

- Evolving 10 CFR Part 70.61
  - Extension of performance requirements in 10 CFR Part 20
  - General incorporation of accident performance requirements
  - Additional requirements with regard to worker safety
  - Clarification of chemical safety performance requirements
- Issues associated with worker dose
  - May impact MELOX design to address worker dose
  - May add complexity to the design
  - May lead to operations and maintenance concerns
  - Requires detailed analysis

---

August 31, 1999

Page 60



DUKE COGEMA  
STONE & WEBSTER

## Safety

---

### Chemical Process Safety/ Monitoring

- 29 CFR 1910 - OSHA worker safety
  - Memorandum of Understanding (MOU) between NRC and the Occupational Safety and Health Administration (OSHA)
- 40 CFR 68 - EPA Risk Management Programs
  - Development of Risk Management Plan
- Aqueous Polishing chemical monitoring and control

---

August 31, 1999

Page 61



DUKE COGEMA  
STONE & WEBSTER

## Nuclear Criticality Safety

---

- Criticality Safety Programs
- Criticality Safety Criteria
- Criticality Control
- Evaluation Methodology
- Benchmark Determination

---

August 31, 1999

Page 62



DUKE COGEMA  
STONE & WEBSTER

## Criticality Safety Programs

---

- Administrative programs in accordance with ANS-8.19-1996, Administrative Practices for Nuclear Criticality Safety
- QA program in accordance with ANS-8.19-1996, Administrative Practices for Nuclear Criticality Safety
- Training program in accordance with ANS-8.20-1991, Nuclear Criticality Safety Training
- Operational inspections, audits, assessments, and investigations function to be regularly performed in accordance with standard NCS principles

---

August 31, 1999

Page 63



DUKE COGEMA  
STONE & WEBSTER

## Criticality Safety Criteria

---

- Double contingency principle compliance
- Criticality Analysis
  - Upper Safety Limit (USL)
    - Administrative safety margin,  $\Delta k_m$
    - Account for method bias and uncertainty based on statistical analysis of benchmark experiment results
  - Worst-case treatment or statistical accounting for design, mechanical, material, and fabrication uncertainties
- Single parameter limits of ANSI/ANS-8.1

---

August 31, 1999

Page 64



## Criticality Control

---

- Criticality Control Modes
  - Geometry control whenever possible
  - Mass and moderation control when required for process and operability reasons



## Nuclear Criticality Safety Evaluation Methodology

---

- NCSEs prepared according to standard US procedures and criticality methodologies (based on ANSI/ANS-8.1 as invoked by RG 3.71)
- U.S. standard criticality code (KENO) and neutron cross-sections included in SCALE 4.4 applied
- NCSEs originated by the Process Group
- NCSEs independently reviewed by the Facility Group



DUKE COGEMA  
STONE & WEBSTER

## Benchmark Determination

---

- Process selection & data analysis
- Validation
- Sensitivity and uncertainty techniques
- Available benchmark experiments

---

August 31, 1999

Page 67



DUKE COGEMA  
STONE & WEBSTER

## Criticality Summary

---

- Standard US Criticality Safety Evaluation Methodology
- Procedure has been prepared to ensure standard US methodology is used
- Standard US criticality code (KENO/Scale 4.4) will be used
- Criticality calculations will be validated using the latest methods of benchmark validity determination including parameter trending analysis and ORNL methods
- Standard administrative uncertainties will be used
- Nuclear Criticality Safety Evaluations will be originated by the Process Group and independently reviewed by the Facility Group
- Criticality Safety Administrative Programs will be used on the MFFF

---

August 31, 1999

Page 68



DUKE COGEMA  
STONE & WEBSTER

## Radiation Protection

---

- Regulatory
  - 10CFR70, Domestic Licensing of Special Nuclear Material
  - 10CFR20, Standard for Protection Against Radiation
- Primary Guidance documents
  - Regulatory Guides
  - NUREGs
  - ANSI Standards
  - ICRP Publications

---

August 31, 1999

Page 69



DUKE COGEMA  
STONE & WEBSTER

## Radiation Protection

---

- Removes  $^{241}\text{Am}$  [ $^{241}\text{Am}/(^{241}\text{Am} + \text{Pu Total})$ ] < 0.0005%
- Automated operations
- Major radiation sources in shielded cubicles
- High maintenance equipment separated
- Radioactive source material removed for maintenance

---

August 31, 1999

Page 70





DUKE COGEMA  
STONE & WEBSTER

## Radiation Protection

---

- Exposure limited through automation and remote control
- Biological shields placed between radiation sources and operators
- Reduced radiation
  - PuO<sub>2</sub> Powder
  - C-Pu/W-Pu  $\approx 5$  X DER
- Same shielding as MELOX - reduced occupational exposure
- Occupational exposure goal: ALARA

---

August 31, 1999

Page 71



DUKE COGEMA  
STONE & WEBSTER

## Radiation Protection

---

### Shielding Calculations

- Based on MELOX results of shielding and dose calculations
  - Revise to support design changes
  - Perform calculation to support new designed units
- Computer codes (U.S.)
  - SCALE 4.3 or 4.4
  - MCNP 4B or 4C

---

August 31, 1999

Page 72

## Radiation Protection

---

- Radiation Monitoring - Selected Equipment
  - External Radiation
    - Local Area Monitors (Gamma & Neutron)
  - Internal Radiation
    - Continuous Air Monitors - movable/ near breathing zone
    - Continuous - General area airborne sampling - laboratory analysis
    - Operator foot-pedal for glove-box entries
      - Moveable - covers all glove-ports
      - Notification for glove tear/other problems
      - Remote alarms - Health Physics & Control Room
- Particulate Monitoring

## Confinement Systems Design

---

### Static Confinement

- Confinement barriers
  - First confinement system
    - Solution-containing vessels, powder-containing equipment completed by gloveboxes or cells (AP)
  - Second confinement system
    - Process rooms and building



DUKE COGEMA  
STONE & WEBSTER

## Confinement Systems Design

---

### Dynamic Confinement

- Confinement Zones Exhaust & Depressurization Systems for MFF and Polishing Buildings include:
  - Glovebox Nitrogen Blanketing
  - Primary Confinement Zone C4 Exhaust (Very High Depressurization THD)
  - Secondary Confinement Zone C3 Exhaust (High Depressurization HD)
  - Tertiary Confinement Zone C2 Exhaust (Moderate Depressurization MD)
  - Clean Areas Exhaust System Zone C1 (Conventional HVAC system)
  - Number of HEPA filters on exhaust depends on contamination risk

---

August 31, 1999

Page 75



DUKE COGEMA  
STONE & WEBSTER

## Fire Safety Design Features at MFFF

---

- Fire Areas With Minimum of 2 Hour Rated Fire Barriers
- Automatic and Manual Fire Suppression Capabilities
- Automatic Fire Detection Systems throughout
- Facility Wide Fire Alarms throughout
- Fire Prevention

---

August 31, 1999

Page 76



DUKE COGEMA  
STONE & WEBSTER

## Electrical System

### MAJOR FEATURES

- Redundant Preferred (Normal) Power Feeds
- Essential and Emergency Diesel Generators
- Electrical Separation Per IEEE 384


August 31, 1999

Page 77



DUKE COGEMA  
STONE & WEBSTER

## Simplified Electrical One-Line

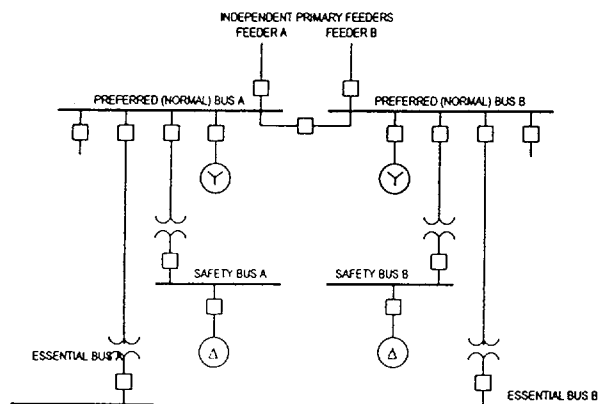

August 31, 1999

Page 78



## Instrument and Controls

### MAJOR FEATURES


- Control By Programmable Logic Controllers With Operator Interfaces
- Control is Unitized
- MMIS Provides Supervision and Data Storage
- Redundancy When Required
- Safety Trips Hardwired

August 31, 1999

Page 79



## Control System Architecture

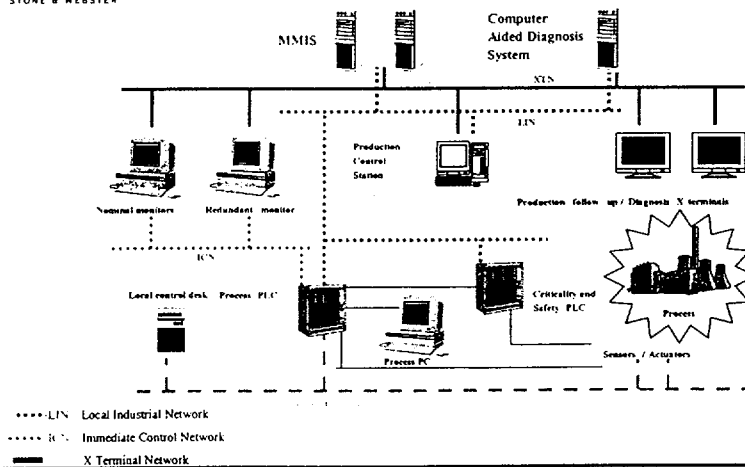

August 31, 1999

Page 80

## Safeguards

---

- MAJOR FEATURES
- Measurement, Control and Accountability Program in Accordance with 10 CFR Part 74, Subpart E
- Fundamental Nuclear Material Control Plan Will be Prepared In Accordance with NUREG-1280
- Program Will Use Classic Safeguards Techniques
- IAEA Interface via 10 CFR Part 75


## Security

---

### MAJOR FEATURES

- Security program will be in accordance with Department of Energy Orders
- MOX Fuel Fabrication Facility will be constructed at a DOE site and will be protected by DOE contracted security forces
- Level of integration of the Fuel Fabrication Facility security system into the host site security system will be determined after the Record of Decision

# THE ANMMAS FUEL FABRICATION PROCESS AT MELOX PLANT

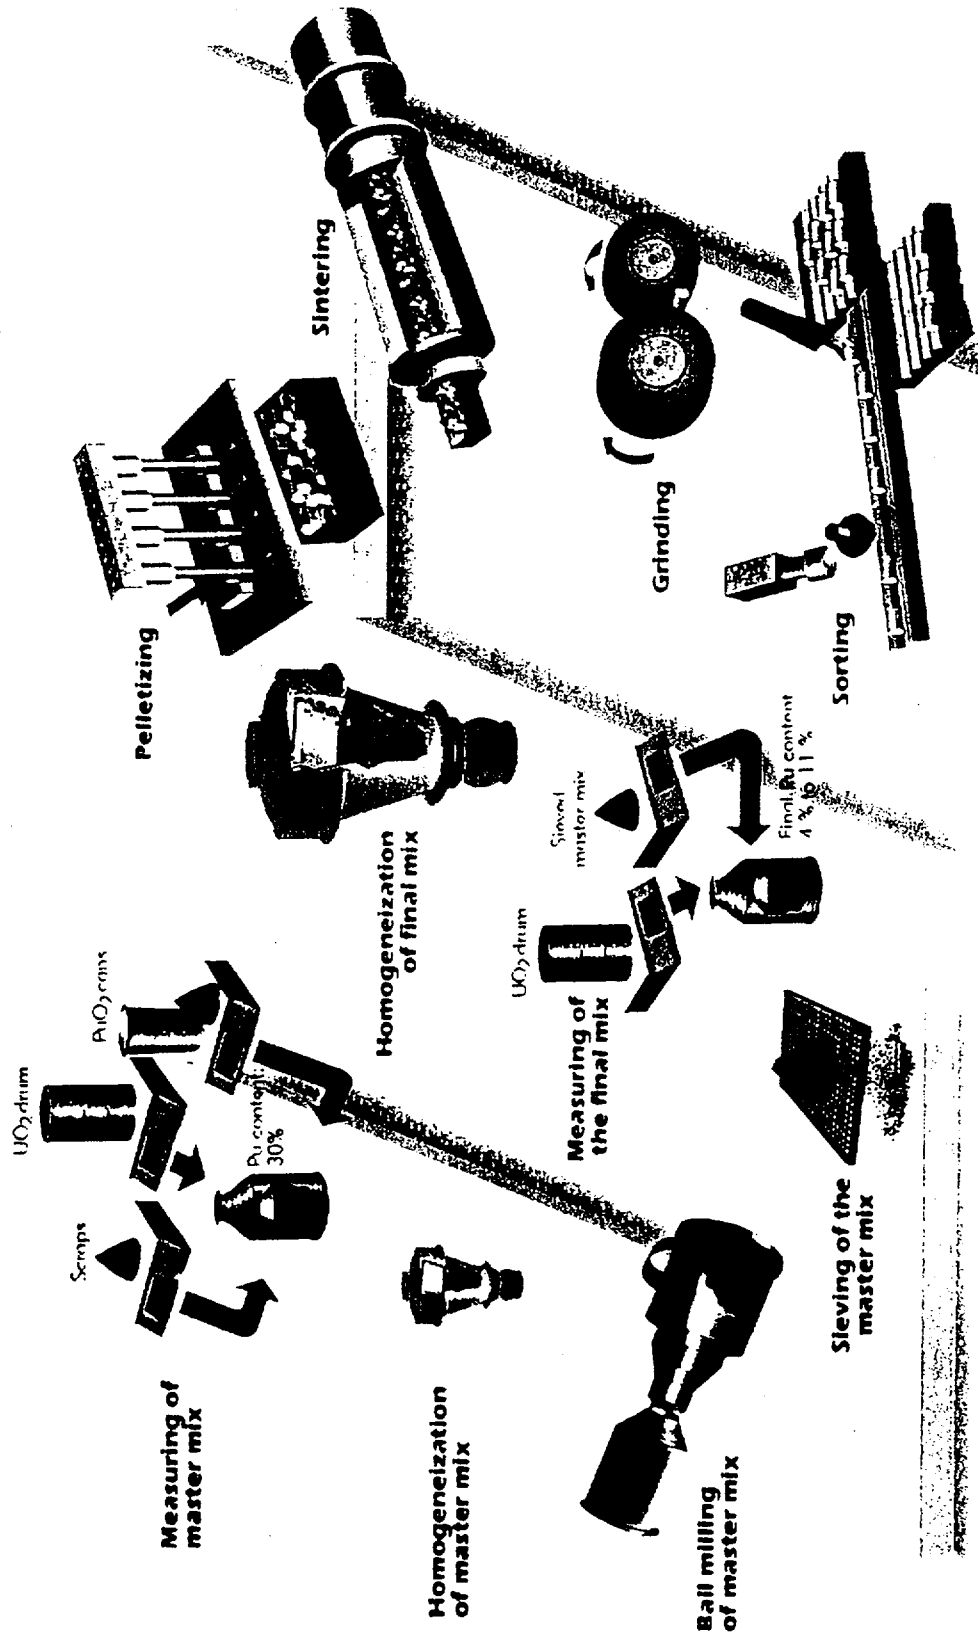



DUKE COGEMA  
STONE & WEBSTER

# MFFF Licensing Round Table Discussion







DUXE COHEN  
STONE & WEBSTER

---

## MFFF Licensing Round Table Discussion

---



DUXE COHEN  
STONE & WEBSTER

## Construction Authorization and Operating License

---

- §70.23(b): requires "Commission approval" for construction of a plutonium facility
- Information required for submittal described in §70.22(f) (design basis information)
- How will NRC go about authorizing construction?
- How does new ISA requirement impact process?

## ATTENDEES

<u>NAME</u>	<u>AFFILIATION</u>	<u>ADDRESS/PHONE</u>
Amy Bryce	NRC	Washington, DC 20555 301-415-5848
Andrew Persinko	NRC	301-415-6522
Melanie Galloway	NRC	301-415-7266
Robert Pierson	NRC	301-415-7192
Rex Wescott	NRC	301-415-6727
Michael Kelly	NRC	301-415-8137
Tom Pham	NRC	301-415-8154
Lawrence Berg	NRC	301-415-6215
Fred Burrows	NRC	301-415-8110
Albert Wong	NRC	301-415-7906
Charles Cox	NRC	301-415-6755
M. Srinivasan	NRC	301-415-5676
Yen-Ju Chen	NRC	301-415-5615
Rocio Castaneira	NRC	301-415-8103
Wayne Burnside	NRC	301-415-2211
Ed Brabazon	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-7959
Ray Fortier	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-8245
Toney Mathews	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-7832

<u>NAME</u>	<u>AFFILIATION</u>	<u>ADDRESS/PHONE</u>
Jamie Johnson	DOE	MD-12 1000 Independence Ave. Washington, DC 20585 202-586-5960
Patrick Rhoads	DOE	MD-12 1000 Independence Ave. Washington, DC 20585 202-586-7859
Finis Southworth	DCS	MD-01 1000 Independence Ave. Washington, DC 20585 202-586-0149
Peter Hastings	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-7820
Don Williams	ORNL	PO Box 2009 Oak Ridge, TN 37831 423-574-8710
Faris Badwan	LANL	PO Box 1660 Los Alamos, NM 87545 505-665-5984
Bill Hennessy	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-8235
Richard Berry	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-8248
John McConaghy	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-3021
Gary Bell	DCS	400 S. Tryon St. Charlotte, NC 28202 704-373-7962

<u>NAME</u>	<u>AFFILIATION</u>	<u>ADDRESS/PHONE</u>
Steven Dolley	NCI	1000 Conn Ave, NW #804 Washington, DC 20036 202-822-8444
Mary Olson	NIRS	1424 16 <sup>th</sup> St., NW #404 Washington, DC 20036 202-328-0002
Felix Killar, Jr.	NEI	1776 I St, NW Suite 400 Washington, DC 20006 202-739-8126
Charles Sanders	FCF	PO Box 11646 Lynchburg, VA 24506 804-832-5216
Edmund Kelly	NFS	1700 Rockville Pike #400 Rockville, MD 20852 301-770-5510
Kathy Martin	DOE	1000 Independence Ave. Washington, DC 20585 202-586-6975
Becky Apter	DCS	400 S. Tryon St. Charlotte, NC. 28201
Laurence Oret	DCS	SGN St. Quentin-En Yvelines 78182 Cedex France
Lionel Gaiffe	DCS	SGN St. Quentin-En Yvelines 78182 Cedex France
Michel Dedonder	DCS	SGN St. Quentin-En Yvelines 78182 Cedex France
