

FY 2013 MAINTENANCE DREDGING

PROJECT: Gulf Intracoastal Waterway
 SUBPROJECT: IHNC Lock Forebay
 PROJECT MANAGER: Victor Landry
 PHONE: (504) 862-2407
 LOCAL SPONSOR: U.S. Government has sufficient interest

DESCRIPTION OF WORK:


Maintain forebay to -31.5' MLG (with an additional 3' of advance maintenance)

HISTORICAL DREDGING FREQUENCY: Annually
 LAST DREDGED: 2011
 TYPE OF DREDGE: Cutterhead
 ESTIMATED QUANTITY: 75,000 CY
 ESTIMATED COST: \$500,000

ADVERTISE: Jan 2013
 OPEN BIDS: TBD
 AWARD: TBD
 START WORK: TBD
 DURATION: 7 days

DREDGING REACH: Lock Forebay
 DISPOSAL AREA: Mississippi River
 DISPOSAL TYPE: Open Water
 REMARKS: Dredged Material discharged beyond the -55' Depth Contour
 NOTE: This work is done as part of the New Orleans Harbor Contract

GULF INTRACOASTAL WATERWAY INNER HARBOR NAVIGATION CANAL LOCK FOREBAY

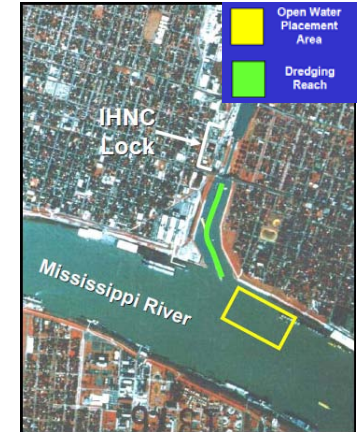

PROJECT AUTHORITY: River and Harbor Act of 24 July 1946, Senate Document 242, 79th Congress, 2nd Session, and prior R&H Acts; River and Harbor Act of 23 October 1962, House Document 556, 87th Congress, 2nd Session.

NEPA DOCUMENTATION	FONSI	PUBLIC NOTICE	WATER QUALITY CERTIFICATION	
FEIS O&M	4-Feb-77	19-Feb-75		21-Feb-79
SIR#11 Advance Maintenance & Allowable Overdepth	20-Sep- 85	28-Oct-86		

* revised Water Quality Certificate

Recent Dredging History Of GIWW – IHNC LOCK FOREBAY

Fiscal Year	Disposal Area	Dredging Quantity (CY)
2001	Mississippi River Open Water	22,500
2002	Mississippi River Open Water	6,551
		107,008
2003	NO DREDGING	
2004	Mississippi River Open Water	14,807
2005	NO DREDGING	
2006	Mississippi River Open Water	32,480
2007	Mississippi River Open Water	36,085
2008	Mississippi River Open Water	35,641
2009	Mississippi River Open Water	52,073
2010	Mississippi River Open Water	6,100
		81,610
2011	Mississippi River Open Water	81,469

