



Barrier Berm Project – Daily Report

Day 173

Document: 139551-PMD-173-S

Date Prepared: November 21, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W8 Berm – November 16, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 20 November

Vessel	Cubic Yards (CY) Handled
East	
Cutter Alaska	1,854
Subtotal East	1,854
West	
Cutter EW Ellefsen	26,291
Cutter Texas	17,600
Subtotal West	43,891
Total	45,745

- Alaska down 17.5 hours for repairs


Today – 21 November

- Berm placement operations to continue on W8 and W10.
- E4 production to resume as soon as repairs are completed.

Tomorrow – 22 November

- Today's operational activities to continue tomorrow.

All Dredges Weekly Volume

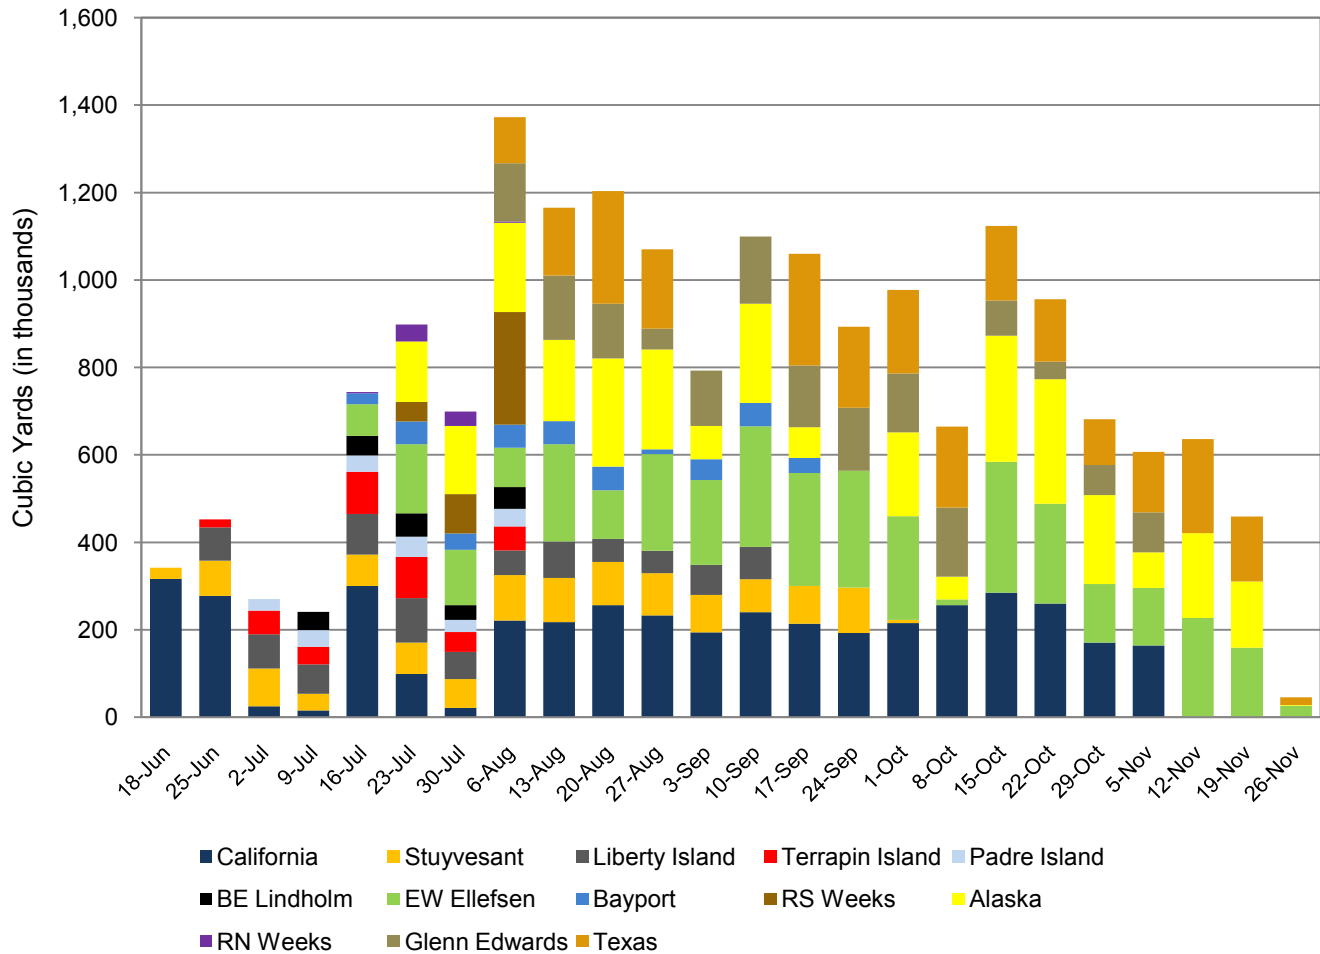

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California*	4,175,650	
Cutter EW Ellefsen	3,452,824	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,982,613	
Cutter Texas	2,454,682	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards*	1,593,128	162
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	18,454,220	951

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,716,400
W8	1,204,865
W9	2,281,314
W10	1,755,171
W11	0
Borrow Operations	8,496,470
Totals	18,454,220

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	30,996
W8	8,259
W9	12,449
W10	13,930
W11	0
Totals	65,634

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



W10 Berm – November 16, 2010



E4 North Berm – November 16, 2010
